

Anx B – Work Completion Report

Company	AMTZ Medpolis Square 4554 Pvt Ltd	Name of contractor	Simhaa Constructions	Sl. No. site bills reg.	104
Project/site	AMS4554	Nature of work	Civil works for Level 04	Dt. site bills reg.	15-09-2025
Block no.	AMS4554	Work done from date	01-08-2025	M-codex bill ID.	
WO no.	20250829031	Work done to date	13-09-2025	WO issued ?	Yes
WO date	29-08-2025	Contractor bill no.	57	GST bill required?	Yes

Sl. No.	Unit/floor no	Details of work	Qty	Units	Rate ID	Rate	Amount
1	AMS4554/ Level 04	Brickwork - 150 MM (Fal G)	5709.45	Sft		93.75	5,35,260.94
2	AMS4554/ Level 04	Brickwork - 100 MM (Fal G)	1974.56	Sft		78.75	1,55,496.60
3	AMS4554/ Level 04	Brickwork - 100 MM (AAC)	1264.24	Sft		90.00	1,13,781.60
4	AMS4554/ Level 04	6" Mullions	553.34	Rft		140.00	77,467.60
5	AMS4554/ Level 04	8" Mullions	13.70	Rft		171.25	2,346.13
6	AMS4554/ Level 04	6" Lintels	34.45	Rft		207.50	7,148.38
7	AMS4554/ Level 04	4" Lintels	23.30	Rft		171.25	3,990.13
8	AMS4554/ Level 04	Internal Plastering	19740.83	Sft		45.00	8,88,337.35
9	AMS4554/ Level 04	Staircase ceiling plastering	1230.80	Sft		45.00	55,386.00
10	AMS4554/ Level 04	10mm Bar Anchoring work	656.00	No's		118.36	77,644.16
11	AMS4554/ Level 04	12mm Bar Anchoring work	90.00	No's		170.86	15,377.40
12	AMS4554/ Level 04	16mm Bar Anchoring work	60.00	No's		227.81	13,668.60
							19,45,905
						Add GST @	18%
						Total amount including taxes for work done	22,96,168

Remarks		
Approved by project manager	Approved by Director/E&D team	
Sign:	Sign:	
Date:	Date:	

APPROVED BY

15 SEP 2025

Notes: 1. This form must be typed. 2. This word form even if work order is not issued. 3. Use this form even if work order is not issued. 4. Attach measurement and estimate sheets only if required i.e., details cannot be entered at greater than 10k QS manager and directors approval is required. 6. For bill amount less than 10k any QS team member may sign and in place of director sign of respective E&D member to be taken. 7. Director include – Soham, Anand Mehta (for GHT + GMR), Sachin (for Vivopolis), B. anand Kumar (for NGH + NRK). 8. Entry of rate ID is mandatory. 9. This sheet must be sent within 2 working days of work completion (with or without contractors bill). 10. Contractors to send scanned copy of bill to site and QS by email. 11. Contractors must submit original bills at HO (can be sent by courier).

MEASUREMENT SHEET												
Company Name:		AMTZ Medpolis Square 4554 Pvt Ltd			Approved by:			N. Leela Venkatesh				
Project:		AMS4554			Sign:							
Work Description :		Civil works for Level 04			Work start date:			01-08-2025				
Contractor:		Simhaa Constructions			Work end date:			13-09-2025				
Prepared By:		Leela Venkatesh			Date :			15-09-2025				
S No.	Item Head	Item Description			A	B	C	D	E	F=AxBxCxD	G	H=Sum of F
			Length	Width	Height	Nos.	Unit wt/mtr	Quantity	Units			Item Head Total
1	Civil Works	Brickwork - 150 MM (Fal G)	1.00	1.00	1.00	-	-	5709.45	Sft			5,709.45
2	Civil Works	Brickwork - 100 MM (Fal G)	1.00	1.00	1.00	-	-	1974.56	Sft			1,974.56
3	Civil Works	Brickwork - 100 MM (AAC)	1.00	1.00	1.00	-	-	1264.24	Sft			1,264.24
4	Civil Works	6" Mullions	1.00	1.00	1.00	-	-	553.34	Rft			553.34
5	Civil Works	8" Mullions	1.00	1.00	1.00	-	-	13.70	Rft			13.70
6	Civil Works	6" Lintels	1.00	1.00	1.00	-	-	34.45	Rft			34.45
7	Civil Works	4" Lintels	1.00	1.00	1.00	-	-	23.30	Rft			23.30
8	Civil Works	Internal Plastering	1.00	1.00	1.00	-	-	19740.83	Sft			19,740.83
9	Civil Works	Staircase ceiling plastering	1.00	1.00	1.00	-	-	1230.80	Sft			1,230.80
10	Civil Works	10mm Bar Anchoring work	1.00	1.00	1.00	-	-	656.00	No's			656.00
11	Civil Works	12mm Bar Anchoring work	1.00	1.00	1.00	-	-	90.00	No's			90.00
12	Civil Works	16mm Bar Anchoring work	1.00	1.00	1.00	-	-	60.00	No's			60.00
										TOTAL		7,746.25


APPROVED BY

15 SEP 2025
LEELA VENKATESH.N.
Project Manager

Tax Invoice

e-Invoice

IRN : ae936b0536e0fee54d9197c8cd2e5fb7cba090802f61fcff-
bc62d17e83caf4ac
Ack No : 112526572153042
Ack Date : 3-Sep-25

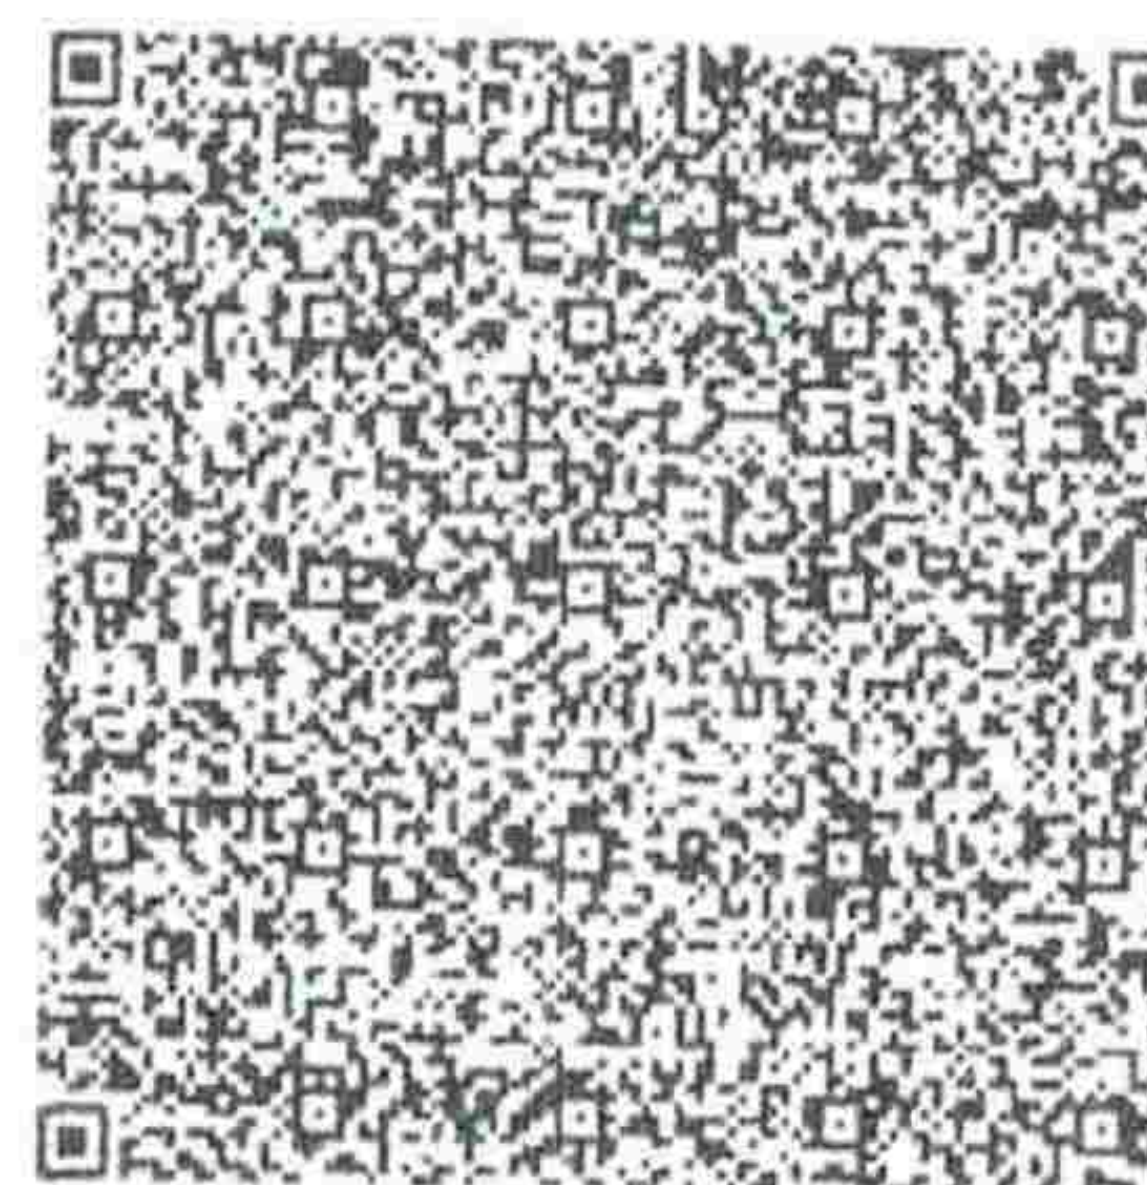**Simhaa Constructions (2025-26)**

Plot No. 2, Block-B, Auto Nagar
Visakhapatnam
GSTIN/UIN: 37ABMFS6706L1ZJ
State Name : Andhra Pradesh, Code : 37
E-Mail : simhaaconstructions@rediffmail.com
Buyer (Bill to)

AMTZ Medpolis Square 4554 Pvt. Ltd

VM Steel Project Town Ship Sub Post Office
Ground, Plot No. D1-56, HUB Building, AMTZ Campus,
Pragathi Maidan, Visakhapatnam
GSTIN/UIN : 37AAXCA5420G1ZG
State Name : Andhra Pradesh, Code : 37

Invoice No

57

Delivery Note

Dated

3-Sep-25

Mode/Terms of Payment

Reference No. & Date

SC/AMS/4554/RA 62 dt. 3-Sep-25

Buyer's Order No

20250829031

Dispatch Doc No

Dated

29-Aug-25

Delivery Note Date

Dispatched through

Destination

Terms of Delivery

Sl No	Particulars	HSN/SAC	Quantity	Rate	per	Amount
1	Contract Receipt (2025-26) RA 62 for Civil Constructions of RCC Building at AMTZ Medpolis Square 4554 Visakhapatnam. (Civil Works for Level 04/slab06 For Amtz 4554)	995415				19,46,080.91
	CGST - Output 9%				9 %	1,75,147.28
	SGST - Output 9%				9 %	1,75,147.28
	Total					₹ 22,96,375.47

Amount Chargeable (in words)

E & O.E

INR Twenty Two Lakh Ninety Six Thousand Three Hundred Seventy Five and Forty Seven paise Only

HSN/SAC	Taxable Value	Central Tax Rate	Central Tax Amount	State Tax Rate	State Tax Amount	Total Tax Amount
995415	19,46,080.91	9%	1,75,147.28	9%	1,75,147.28	3,50,294.56
Total	19,46,080.91		1,75,147.28		1,75,147.28	3,50,294.56

Tax Amount (in words) : **INR Three Lakh Fifty Thousand Two Hundred Ninety Four and Fifty Six paise Only**
Remarks

RA 62 for Civil Constructions of RCC Building at AMTZ
Medpolis Sqaure 4554 Visakhapatnam. (Civil Works for
Level 04 / Slab 06 for Amtz 4554.)

for Simhaa Constructions (2025-26)

This is a Computer Generated Invoice



Authorised Signatory

Civil Contract for RCC works for the project AMTZ Medpolis Square 4554 at AMTZ,
Visakhapatnam

RA - 62



SIMHAA CONSTRUCTIONS
Visakhapatnam

SIMHAA CONSTRUCTIONS

RA 62

DATE: 02.09.2025

Name of the work: Civil works for Construction of RCC building at AMTZ Medpolis Square 4554, Visakhapatnam.

Name of the Contractor : M/s Simhaa Constructions


P. O Number : 20250829031, on Dt: 29 Aug 2025

" Civil works for Level_04/Slab 06 for AMTZ 4554. "

Sl. NO	Item Name	Uom	P.O Qty	Rate	up to Previous	QUANTITY This Bill Qty	Total	Total Value of Work	Amount up to Previous	Present Bill
1	CONST - CIVIL 9891 - Construction - Civil - - -Miscellaneous - -LS Works include: BW_6" {5,668 sft @ 93.75rs}, BW_4" {2,204 sft @ 78.75 rs}, BW_4" AAC {909 sft @ 90.00 rs}, Internal Plastering {22579 sft @ 45.00 rs}, Mullions_6" {553 rft @ 140.00 rs}, Mullions_8" {14 rft @ 171.25 rs}, Lintel_6" {34rft @ 207.50 rs}, Lintel_4" {23 rft @ 171.25 rs}, Anchoring Works_10mm {656 no's @ 118.36 rs}, Anchoring Works_12mm {198 no's @ 170.86rs}, Anchoring works_16mm {132 no's @ 227.81 rs}.	L.S	100	20672.20	-	94.140	94.140	19,46,080.91	-	19,46,080.91
Total								1946080.91	-	1946080.91

Total Value of present Bill 1946080.91
Add GST @ 18% 350294.56
Total 2296375.47

{ Amount In Words : Twenty Two Lakhs Ninety Six Thousand Three Hundredend Seventy Five Rupees and Four Seven Paise Only }

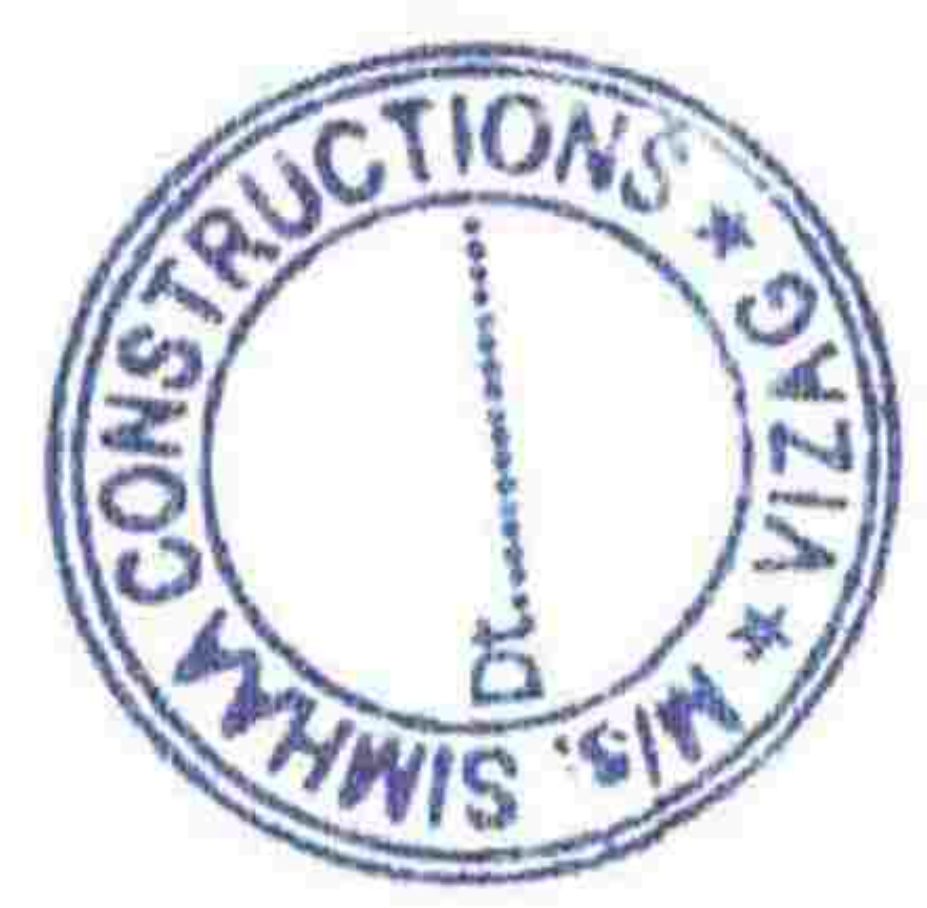

Name of Agency : M/s SIMHAA CONSTRUCTIONS

Project: AMTZ Medpolis Square 4554 Pvt.Ltd.

Work: " Civil works for Level_04/Slab 06 for AMTZ 4554."

RAR No: 62

SUMMARY

Sl. NO	Description of Item	UOM	Qty	Rate	Amount	Remarks
1	150 mm Brickwork - Fal G	Sft	5709.45	93.75	535260.94	
2	100 mm Brickwork - Fal G	Sft	1974.56	78.75	155496.60	
3	100 mm Brickwork - AAC	Sft	1264.24	90.00	113781.60	
4	6" Mullions	Rft	553.34	140.00	77467.60	
5	8" Mullions	Rft	13.70	171.25	2346.13	
6	6" Lintels	Rft	34.45	207.50	7148.38	
7	4" Lintels	Rft	23.30	171.25	3990.13	
8	Internal Plastering	Sft	19740.83	45.00	888337.35	
9	Staircase Ceiling plastering	Sft	1230.80	45.00	55386.00	
10	10mm Bar Anchoring work	No's	656.00	118.36	77644.16	
11	12mm Bar Anchoring work	No's	90.00	170.86	15377.40	
12	16mm Bar Anchoring work	No's	60.00	227.81	13668.60	

Total Taxable Value - As per Work Done 1945904.87

Total Taxable Value -As Per WO 2067220.00

Measurable Qty of Work Unit 94.140 C/o to Abstract



Handwritten signature in blue ink.

Name of Agency : M/s SIMHAA CONSTRUCTIONS
 Project: AMTZ Medpolis Square 4554 Pvt.Ltd.
 Work: " Civil works for Level 04/Slab 06 for AMTZ 4554."
 RAR No: 62

MEASUREMENT SHEET

Sl no	Item Head	Item Description	L	W	D	Nos	Qty	UOM	Remarks
1	150mm Brickwork	Grid E - 01 to 07							
		Duct Inner Wall up to TB Bottom Lvl	31.415		3.000	1	94.245	Sqm	
		Deduct Mullions 150x150	0.150		3.000	-11	-4.950	Sqm	
		Deduct Mullions 200x150	0.200		3.000	-1	-0.600	Sqm	
		Grid A - 01 to 7							
	150mm wall	Duct Inner Wall - up to TB Bottom Lvl	26.865		3.000	1	80.595	Sqm	
		Staircase - South Wall - 6" wall	3.400		4.475	1	15.215	Sqm	
		MLB	3.400		0.450	-1	-1.530	Sqm	
		Deduct S16	3.400		1.200	-1	-4.080	Sqm	
		Deduct Mullions 150x150	0.150		3.000	-9	-4.050	Sqm	
		Passenger Lift	2.000		4.175	1	8.350	Sqm	
		FR Lift	2.000		4.175	1	8.350	Sqm	
		Grid 1- A to E (Excl. Duct)							
		Grid 1- A to E (Excl. Duct)	31.500		4.175	1	131.513	Sqm	
		Deduct S18 [2.65x1.80]-02 no's	2.650		1.950	-2	-10.335	Sqm	
		Deduct S17 [2.80x1.80]-05 no's	2.800		1.950	-5	-27.300	Sqm	
		Deduct S19 [2.80x3.0]-01 no's	2.800		3.000	-1	-8.400	Sqm	
		deduct Duct Inner Wall - above TB Lvl	2.150		1.175	-1	-2.526	Sqm	
		Deduct Mullion (150x150)-12 no's	0.150	0.150	3.000	-12	-5.400	Sqm	
		Grid 7- A to E (East)							
		E7 - Duct Inner Wall - up to TB Bottom Lvl	0.650		3.000	1	1.950	Sqm	
		D7 - Duct Inner Wall - up to TB Bottom Lvl	2.105		3.000	1	6.315	Sqm	
		A7 - Duct Inner Wall - up to TB Bottom Lvl	0.650		3.000	1	1.950	Sqm	
		Deduct Mullion (150x150)-4 no's	0.150	0.150	3.000	-4	-1.800	Sqm	
		N-E Block Internal BW							
		Walls Along E-E axis							
		Outer L wall @ North - Fire Tower to PHE Shaft	8.100		4.475	1	36.248	Sqm	
		Deduct FD2B [1.80x2.40]-01	1.800		2.550	-1	-4.590	Sqm	
		Deduct OP at FHS Shaft above 1.20m	1.200		3.275	-1	-3.930	Sqm	
		Outer L wall @ South - Staircase Wall - Double wall	2.400		4.475	2	21.480	Sqm	
		Deduct MLB	2.400		0.450	-2	-2.160	Sqm	
		Outer L wall @ North - Fire Tower to Elec Shaft	6.400		4.475	1	28.640	Sqm	
		Deduct FD2B [1.80x2.40]-01	1.800		2.550	-1	-4.590	Sqm	
		Deduct Shaft Opening above 1.20m to RB Rm	3.000		3.275	-1	-9.825	Sqm	
		PHE - Shaft Wall - @ South	1.500		4.475	1	6.713	Sqm	
		PHE - Shaft Wall - @ West	3.200		4.475	1	14.320	Sqm	
		deduct OP - 0.90x2.40	0.900		2.550	-1	-2.295	Sqm	



[Handwritten signature]

Name of Agency: M/s SIMHAA CONSTRUCTIONS
 Project: AMTZ Medpolis Square 4554 Pvt.Ltd.
 Work: " Civil works for Level_04/Slab 06 for AMTZ 4554."
 RAR No: 62

MEASUREMENT SHEET

Sl no	Item Head	Item Description	L	W	D	Nos	Qty	UOM	Remarks
		Walls Along I-I axis							
		Wall @ grid 5-5	4.850		4.475	1	21.704	Sqm	
		Wall in b/w Toilet Exhaust & FHS Shaft	0.850		4.475	1	3.804	Sqm	
		FHS Shaft - @ East Wall	0.850		1.200	1	1.020	Sqm	
		Wall in b/w - Fire Tower & Stair	6.300		4.475	1	28.193	Sqm	
		Deduct FD2B [1.20x2.40]-01	1.200		2.550	-1	-3.060	Sqm	
		Elec Shaft Wall @ East side	0.800		4.475	1	3.580	Sqm	
		grid 6- D to D'	4.880		4.475	1	21.838	Sqm	
		Deduct Mullions [1.50x1.50]-05	0.150	0.150	2.400	-5	-1.800	Sqm	
		S-W Block Internal BW							
		Walls Along A-A axis							
		Outer L wall @ North	5.350		4.475	1	23.941	Sqm	
		Deduct FD [1.80x2.40]-01	1.800		2.550	-1	-4.590	Sqm	
		Wall in b/w - Elec & FHS shaft	0.750		4.475	1	3.356	Sqm	
		Wall in b/w - Elec & PHE shaft	0.650		4.475	1	2.909	Sqm	
		Walls Along 2-2 axis							
		Wall at Grid 2	6.000		4.475	1	26.850	Sqm	
		Wall in b/w - Stair & Lobby	3.500		4.475	1	15.663	Sqm	
		Deduct FD [1.20x2.150]-01	1.200		2.300	-1	-2.760	Sqm	
		Wall in b/w - Lift Lobby & Shaft	3.500		4.475	1	15.663	Sqm	
		Deduct HC [0.90x1.20]-01	0.900		1.350	-1	-1.215	Sqm	
		Outer Wall @ East	6.195		4.475	1	27.723	Sqm	
		Dedu Shaft Opening above 1.20m to RB Btm	2.300		3.275	-1	-7.533	Sqm	
		Deduct OP [0.90x2.5]-01	0.900		2.650	-1	-2.385	Sqm	
Total Qty in Sqm							530.421		
Total Qty in Sft							5,709.448	Sft	

2	100mm Brickwork								
		Grid A - 01 to 7							
	100mm wall	Staircase - South Wall - 2nd wall	3.400		4.475	1	15.215	Sqm	
	100mm wall	MIB	3.400		0.450	-1	-1.530	Sqm	
	100mm wall	Deduct SI6	3.400		1.200	-1	-4.080	Sqm	
		N-E Block Internal BW							
	100mm wall	Staircase - North wall (double wall)	2.400		4.475	2	21.480	Sqm	
	100mm wall	Staircase - South wall (at Column)	1.600		4.475	1	4.475	Sqm	
		Walls Along E-E axis							
		Partition Wall @ Women & Men Toilet	1.000		5.225	2	10.450	Sqm	
		Partition Wall @ Men Toilet	2.205		5.225	1	11.521	Sqm	
		Deduct [0.75 x 2.10]-01	0.750		2.250	-1	-1.688	Sqm	



Name of Agency : M/s SIMHAA CONSTRUCTIONS
 Project: AMTZ Medpolis Square 4554 Pvt.Ltd.
 Work: " Civil works for Level_04/Slab 06 for AMTZ 4554."
 RAR No: 62

MEASUREMENT SHEET

Sl.no	Item Head	Item Description	L	W	D	Nos	Qty	UOM	Remarks
		Outer L wall @ North	3.900		4.475	1	17.453	Sqm	
		Deduct GD2G [1.50x2.40]-01	1.500		2.550	-1	-3.825	Sqm	
		Offset Walls # GD2G	0.400		5.225	2	4.180	Sqm	
		Wall @ HWC/Ante Room	5.950		5.225	1	31.089	Sqm	
		Deduct ND [0.90x2.40]-02 no's	0.900		2.550	-2	-4.590	Sqm	
		Outer L wall @ South	7.400		4.475	1	33.115	Sqm	
		Walls Along I-I axis							
		Outer S wall @ West	4.450		5.225	1	23.251	Sqm	
		Wall in b/w- HWC & Ante Room	2.050		5.225	1	10.711	Sqm	
		Deduct ND-I [1.10x2.40]-01 no's	1.100		2.550	-1	-2.805	Sqm	
		Wall in b/w- Women & Men	4.250		4.475	1	19.019	Sqm	
Total Qty in Sqm							183.441		
Total Qty in Sft							1,974.560	Sft	

3	100mm AAC 600x100x200 Brickwork	Grid E - 01 to 07							
	AAC	Wall in b/w Duets - above Tie Beam	25.300		1.175	1	29.728	Sqm	
		Grid A - 01 to 7							
	AAC	Wall in b/w Duets - above Tie Beam	22.000		1.175	1	25.850	Sqm	
		Grid 7- A to E (East)							
	AAC	Wall in b/w Duets -above Tie Beam - D to E	6.545		1.025	1	6.709	Sqm	
		C to D	6.450		1.025	1	6.611	Sqm	
		B to C	7.825		1.025	1	8.021	Sqm	
		A to B	7.275		1.025	1	7.457	Sqm	
		Grid 1- A to E (Excl. Duct)							
		Grid 1- A to E (Excl. Duct)	28.150		1.175	1	33.076	Sqm	
Total Qty in Sqm							117.451		
Total Qty in Sft							1,264.244	Sft	

3	Mullions 150x150	N-E Block Internal BW							
		FD2B [1.80x2.40]-02*2	2.400			4	9.600	Rmt	
		FD2B [1.80x2.40]-01*1	2.400			1	2.400	Rmt	
		S-W Block Internal BW							
		FD [1.20x2.150]-01*01	2.150			1	2.150	Rmt	
		FD [1.80x2.40]-01*02	2.400			2	4.800	Rmt	
		Mullions at grid E @ Duets	4.175			11	45.925	Rmt	
		Mullions at grid A @ Duets	4.175			9	37.575	Rmt	
		Mullions at grid 1E-1A	4.175			12	50.100	Rmt	
		Mullions at grid 7E-7A	1.025			4	16.400	Rmt	
Total Qty in Rmt							168.650		
Total Qty in Rft							553.341	Rft	



Name of Agency : M/s SIMHAA CONSTRUCTIONS
 Project: AMTZ Medpolis Square 4554 Pvt.Ltd.
 Work: " Civil works for Level_04/Slab 06 for AMTZ 4554."
 RAR No: 62

MEASUREMENT SHEET

Sl.no	Item Head	Item Description	L	W	D	Nos	Qty	UOM	Remarks
-------	-----------	------------------	---	---	---	-----	-----	-----	---------

3	Mullions [2000x150]	Mullions at grid E -a Ducts	4.175			1	4.175	Rmt	
		Total Qty in Rmt					4.175		
		Total Qty in Rft					13.698	Rft	
4	Lintels [150mm wide]	N-E Block Internal BW							
		FD2B [1.80x2.40]-02	1.800			2	3.600		
		[1.20x2.40]	1.350			1	1.350		
		at FHS Shaft	1.200			1	1.200		
		S-W Block Internal BW							
		FD2B [1.80x2.40]-01	1.800			1	1.800		
		[1.20x2.40]	1.350			1	1.350		
		at PHE Shaft	1.200			1	1.200		
		Total Qty in Rmt					10.500		
		Total Qty in Rft					34.451	Rft	

5	Lintels [100mm wide]	ND [0.90x2.40]-02 no's	1.300			2	2.600		
		Toilet Door [0.75 x 2.10]-01	1.000			1	1.000		
		ND-1 [1.10x2.40]-01 no's	1.500			1	1.500		
		HH [0.85x1.20]-01+01-02	1.000			2	2.000		
		Total Qty in Rmt					7.100		
		Total Qty in Rft					23.295	Rft	

6	Internal Plastering	Internal Plastering up to Tie Beam Level Only							
		grid E-01 to 07	62.700		3.300	1	206.910		
		column Sides-05*2	0.750		4.475	10	33.563		
		S6 [4.4x3.0]-05 no's	4.400		3.000	-5	-66.000		
		Add Jambs	10.400	0.150		5	7.800		
		S16 [3.3x3.0]-01 no's	3.300		3.000	-1	-9.900		
		Add Jambs	9.300	0.150		1	1.395		
		Tie beam Top Plaster -a- Duct Portion							
		grid E-1 Duct	4.400	0.150		1	0.660		
		grid E-2 Duct	3.600	0.150		1	0.540		
		grid E-3 Duct	0.950	0.150		1	0.143		
		grid E-4 Duct	2.775	0.150		1	0.416		
		grid E-5 Duct	2.375	0.150		1	0.356		
		grid E-6 Duct	2.425	0.150		1	0.364		
		grid E-7 Duct	2.725	0.150		1	0.409		
		grid E-8 Duct	1.575	0.150		1	0.236		

B. Jagadeesh



Name of Agency : M/s SIMHAA CONSTRUCTIONS
 Project: AMTZ Medpolis Square 4554 Pvt.Ltd.
 Work: " Civil works for Level 04/Slab 06 for AMTZ 4554."
 RAR No: 62

MEASUREMENT SHEET

Sl no	Item Head	Item Description	L	W	D	Nos	Qty	UOM	Remarks
		grid E6 Duct	3.575	0.150		1	0.536		
			0.725	0.150		1	0.109		
		grid E7 Duct	4.350	0.150		1	0.653		
		grid A-01 to 2	10.100		3.300	1	33.330		
		column Sides-01*1	0.700		4.475	1	3.133		
		S6 [4.4x3.0]-01 no's	4.400		3.000	-1	-13.200		
		Add Jambs	10.400	0.150		1	1.560		
		Tie beam Top Plaster @ Duct Portion	4.400	0.150		1	0.660		
		grid A-03 to 7	43.350		3.300	1	143.055		
		S6 [4.4x3.0]-04 no's	4.400		3.000	-4	-52.800		
		Add Jambs	10.400	0.150		1	1.560		
		Tie beam Top Plaster @ Duct Portion							
		grid A3 Duct	0.575	0.150		1	0.086		
			2.775	0.150		1	0.416		
		grid A4 Duct	2.375	0.150		1	0.356		
			2.425	0.150		1	0.364		
		grid A5 Duct	2.725	0.150		1	0.409		
			1.575	0.150		1	0.236		
		grid A6 Duct	3.575	0.150		1	0.536		
			0.725	0.150		1	0.109		
		grid A7 Duct	4.350	0.150		1	0.653		
		column Sides-03*2+1	0.750		3.300	7	17.325		
		grid I-A to E	35.700		3.300	1	117.810		
		Deduct S18 [2.65x1.80]-02 no's	2.650		1.800	-2	-9.540		
		Add Jambs	8.900	0.150		2	2.670		
		Deduct S17 [2.80x1.80]-05 no's	2.800		1.800	-5	-25.200		
		Add Jambs	9.200	0.150		5	6.900		
		Deduct S19 [2.80x3.0]-01 no's	2.800		3.000	-1	-8.400		
		Add Jambs	11.600	0.150		1	1.740		
		Tie beam Top Plaster @ Duct Portion							
		grid I-C Duct	1.055	0.150		1	0.158		
			1.090	0.150		1	0.164		
		column Sides-03*2	0.750		4.475	6	20.138		
		grid 7- A to F	35.700		3.450	1	123.165		
		Deduct Opening							
		grid 7-A to B	7.275		3.000	-1	-21.825		
		Add Jambs	13.275	0.200		1	2.655		
		grid 7- B to C	7.825		3.000	-1	-23.475		
		Add Jambs	13.825	0.200		1	2.765		
		grid 7- C to D	6.450		3.000	-1	-19.350		
		Add Jambs	12.450	0.200		1	2.490		
		grid 7- D to E	6.550		3.000	-1	-19.650		

Bygda



Name of Agency : M/s SIMHAA CONSTRUCTIONS
 Project: AMTZ Medpolis Square 4554 Pvt.Ltd.
 Work: " Civil works for Level 04/Slab 06 for AMTZ 4554."
 RAR No: 62

MEASUREMENT SHEET

Sl.no	Item Head	Item Description	L	W	D	Nos	Qty	UOM	Remarks
		Add Jambs	12.550	0.200		1	2.510		
		Column Sides-3*2	0.900		4.475	6	24.165		
		Tie beam Top Plaster at Duct Portion							
		grid 7-D Duct	1.225	0.200		1	0.245		
			0.575	0.200		1	0.115		
		grid 7-A Duct	0.500	0.200		1	0.100		
		grid 7-E Duct	0.500	0.200		1	0.100		
		Internal Columns till RB Btm	0.924	0.900	4.475	13	212.222		
		N-E Block							
		Walls Along E-F axis							
		Outer L wall at North	15.900		5.225	1	83.078	Sqm	
		Deduct FD2B[1.80x2.40]-01	1.800		2.400	-0.5	-2.160	Sqm	
		Deduct OP at Elec Shaft above 1.20m	1.600		3.275	-0.5	-2.620	Sqm	
		Deduct GD2G[1.50x2.40]-01	1.500		2.400	-0.5	-1.800	Sqm	
		Offset Walls # GD2G	0.400		5.225	4	8.360	Sqm	
		Outer L wall at South	18.680		5.225	1	97.603	Sqm	
		Deduct FD2B[1.80x2.40]-01	1.800		2.400	-0.5	-2.160	Sqm	
		Dedu Shaft Opening above 1.20m to RB Btm	3.000		3.275	-0.5	-4.913	Sqm	
		Walls Along I-I axis							
		East Wall at grid 6	6.980		5.225	1	36.471	Sqm	
		column offsets	0.150		5.225	1	0.784	Sqm	
			0.750		5.225	1	3.919	Sqm	
		West Side wall at grid 4 side	4.750		5.225	1	24.819	Sqm	
		Staircase Hall	6.400	3.400	5.400	1	105.840	Sqm	
		Deduct FD2B[1.20x2.40]-01	1.200		2.400	-0.5	-1.440	Sqm	
		Fire Tower	6.500	3.200	5.225	1	101.365	Sqm	
		Deduct FD2B[1.20x2.40]-02	1.200		2.400	-1	-2.880	Sqm	
		deduct Lift Openings	2.000		4.475	-2	-17.900	Sqm	
		PHS Shaft [0.85x1.40]	0.850	1.400	5.400	1	16.740	Sqm	
		ELLC Shaft [0.85x1.60]	0.850	1.600	5.400	1	26.460	Sqm	
		Deduct OP at Elec Shaft above 1.20m	1.600		3.275	-0.5	-2.620	Sqm	
		Shaft [3.0x0.85]	3.000	0.850	5.400	1	41.580	Sqm	
		Dedu Shaft Opening above 1.20m to RB Btm	3.000		3.275	-0.5	-4.913	Sqm	
		PHF Shaft [3.15x1.30]	3.150	1.300	5.400	1	48.060	Sqm	
		deduct OP-0.90x2.40	0.900		2.400	-0.5	-1.080	Sqm	
		Men Toilet [3.45 x 4.25]	4.250	3.450	5.225	1	80.465	Sqm	
		Deduct [0.75 x 2.40]-01	0.750		2.100	-0.5	-0.788	Sqm	
		Deduct ND [0.90x2.40]-01 no's	0.900		2.400	-0.5	-1.080	Sqm	
		WC Inside [0.920x1.20]	0.920	1.200	5.225	1	22.154	Sqm	
		Deduct [0.75 x 2.40]-01	0.750		2.100	-0.5	-0.788	Sqm	
		Ante Room [2.05x3.70]	2.050	3.700	5.225	1	60.088	Sqm	

By Ag. dt. 28



Name of Agency : M/s SIMHAA CONSTRUCTIONS
 Project: AMTZ Medpolis Square 4554 Pvt.Ltd.
 Work: " Civil works for Level_04/Slab 06 for AMTZ 4554."
 RAR No: 62

MEASUREMENT SHEET

Sl no	Item Head	Item Description	L	W	D	Nos	Qty	UOM	Remarks
		Deduct ND [0.90x2.40]-02no's	0.900		2.400	-1	-2.160	Sqm	
		Deduct GD2G[1.50x2.40]-01	1.500		2.400	-0.5	-1.800	Sqm	
		ND-1 [1.10x2.40]-01 no's	1.100		2.400	-0.5	-1.320	Sqm	
		Women Toilet [3.55x2.45]	3.550	2.450	5.225	1	62.700	Sqm	
		Deduct ND [0.90x2.40]-01no's	0.900		2.400	-0.5	-1.080	Sqm	
		Partition Wall @ Women Toilet	1.000		5.225	2	10.450	Sqm	
		HWC [2.05x2.05]	2.050	2.050	5.225	1	42.845	Sqm	
		ND-1 [1.10x2.40]-01 no's	1.100		2.400	-0.5	-1.320	Sqm	
		Partition Wall @ men Toilet	1.000		5.225	2	10.450	Sqm	
		S-W Block							
		Outer Phenphery							
		North Face	9.330		5.225	1	48.749	Sqm	
		Deduct FD2B[1.80x2.40]-01	1.800		2.400	-0.5	-2.160	Sqm	
		West wall face	7.050		5.225	1	36.836	Sqm	
		column offsets	0.150		5.225	1	0.784	Sqm	
			0.750		5.225	1	3.919	Sqm	
		East wall face	6.950		5.225	1	36.314	Sqm	
		Deduct Elee Shaft OP	2.300		3.275	-1	-7.533	Sqm	
		Add Jambs	11.150	0.150		1	1.673	Sqm	
		Deduct PHE OP [0.90x2.5]-01	0.900		2.500	-0.5	-1.125	Sqm	
		Stairease Hall [3.40 x 6.70]	6.700	3.400	5.400	1	109.080	Sqm	
		Deduct FD2B[1.50x2.40]-01	1.500		2.400	-0.5	-1.800	Sqm	
		Deduct S16[2.20x1.20]-01	3.300		1.200	-1	-3.960	Sqm	
		Add Jambs	9.000	0.150		1	1.350	Sqm	
		Lift Lobby [4.20 x 3.50]	4.200	3.500	5.225	1	21.945	Sqm	
		Deduct FD2B[1.50x2.40]-02	1.500		2.400	-1	-3.600	Sqm	
		Deduct IH[0.85x1.20]-01	0.850		1.200	-0.5	-0.510	Sqm	
		deduct Lift Openings	2.000		4.475	-2	-17.900	Sqm	
		FHS Shaft [0.75x1.00]	1.000	0.750	5.400	1	18.900	Sqm	
		Deduct IH[0.85x1.20]-01	0.850		1.200	-0.5	-0.510	Sqm	
		Elee Shaft [2.30x0.75]	2.300	0.750	5.400	1	32.940	Sqm	
		Deduct Shaft OP	2.300		3.275	-1	-15.065	Sqm	
		Add Jambs	11.150	0.150		1	1.673	Sqm	
		PHE Shaft [2.30x0.65]	2.300	0.650	5.400	1	31.860	Sqm	
		Deduct PHE OP [0.90x2.5]-01	0.900		2.500	-0.5	-1.125	Sqm	
	Tie beam Top offset Plastering @ AAC Masonry	Grid E - 01 to 07							
	AAC	Wall in b/w Ducts - above Tie Beam	28.300	0.050		1	1.265	Sqm	
		Grid A - 01 to 7							
	AAC	Wall in b/w Ducts - above Tie Beam	22.000	0.050		1	1.100	Sqm	
		Grid 7- A to E (East)							
	AAC	Wall in b/w Ducts - above Tie Beam - D to E	6.545	0.050		1	0.327	Sqm	



Signature

Name of Agency : M/s SIMHAA CONSTRUCTIONS
 Project: AMTZ Medpolis Square 4554 Pvt.Ltd.
 Work: " Civil works for Level_04/Slab 06 for AMTZ 4554,"
 RAR No: 62

MEASUREMENT SHEET

Sl no	Item Head	Item Description	L	W	D	Nos	Qty	UOM	Remarks
		C to D	6.450	0.050		1	0.323	Sqm	
		B to C	7.825	0.050		1	0.391	Sqm	
		A to B	7.275	0.050		1	0.364	Sqm	
		Grid I- A to E (Excl. Duct)							
		Grid I- A to E (Excl. Duct)	28.150	0.050		1	1.408	Sqm	
Total Qty in Sqm							1833.97		
Total Qty in Sft							19740.83	Sft	

7	Anchoring & Lockset Mullions [150x150]	10 mm dia	Dia	No.of Bars	No.of Members		Total Qty		
		N-E Block Internal BW							
		FD2B[1.50x2.40]-02*2	10mm bars	4	4		16.00	No's	
		FD2B[1.50x2.40]-01*1	10mm bars	4	1		4.00	No's	
		S-W Block Internal BW							
		FD[1.50x2.150]-01*01	10mm bars	4	1		4.00	No's	
		FD[1.80x2.40]-01*02	10mm bars	4	2		8.00	No's	
		Mullions at grid F @ Ducts	10mm bars	4	12	4	192.00	No's	
		Mullions at grid A @ Ducts	10mm bars	4	9	4	144.00	No's	
		Mullions at Grid 1A-1F	10mm bars	4	3	4	48.00	No's	
			10mm bars	4	4	1	16.00	No's	
		Mullions at grid 7 @ Ducts	10mm bars	4	12	4	192.00	No's	
		Lintel at FD - @ Staircase Hall	10mm bars	4	2	4	32.00	No's	
Total Qty in No's							656.00	No's	

8	Anchoring & Lockset	12 mm dia	Dia	No.of Bars	No.of Members		Total Qty		
		Anchoring for Tie Beam at Grid F	12mm bars	3	6	2	36.00	No's	
		Anchoring for Tie Beam at Grid A	12mm bars	3	5	2	30.00	No's	
		Anchoring for Tie Beam at Grid I	12mm bars	3	4	2	24.00	No's	
Total Qty in No's							90.00	No's	

9	Anchoring & Lockset	16 mm dia	Dia	No.of Bars	No.of Members		Total Qty		
		Anchoring for Tie Beam at Grid F	16mm bars	2	6	2	24.00	No's	
		Anchoring for Tie Beam at Grid A	16mm bars	2	5	2	20.00	No's	
		Anchoring for Tie Beam at Grid I	16mm bars	2	4	2	16.00	No's	
Total Qty in No's							60.00	No's	

10	Ceiling Plastering @ Staircase	Staircase 1	L	W	Area	No's	Qty		
		Flight-I&III+Landing-Typical 2 nos - Bottom Surface	6.989	1.600		2	22.365	Sqm	
		Side-1			1.950	2	3.899	Sqm	1949673



B. Jagadeesh


Name of Agency : M/s SIMHAA CONSTRUCTIONS
 Project: AMTZ Medpolis Square 4554 Pvt.Ltd.
 Work: " Civil works for Level_04/Slab 06 for AMTZ 4554."
 RAR No: 62

MEASUREMENT SHEET

Sl no	Item Head	Item Description	L	W	D	Nos	Qty	UOM	Remarks
		Side-2			0.957	2	1.914	Sqm	957173
		Flight-II&IV+Landing-Typical 2 no.s - Bottom Surface	6.989	1.600		2	22.365	Sqm	
		Side-1			1.950	2	3.899	Sqm	1949673
		Side-2			0.920	2	1.839	Sqm	919673
		Landing	2.220	0.200		2	0.888	Sqm	
		Landing	2.050	0.200		2	0.820	Sqm	
		Staircase II							
		Flight-I&III+Landing-Typical 2 no.s - Bottom Surface	6.789	1.600		2	21.725	Sqm	
		Side-1			1.900	2	3.799	Sqm	1899673
		Side-2			0.920	2	1.839	Sqm	919673
		Flight-II&IV+Landing-Typical 2 no.s - Bottom Surface	6.789	1.600		2	21.725	Sqm	
		Side-1			1.900	2	3.799	Sqm	1899673
		Side-2			0.919	2	1.839	Sqm	919394
		Landing	2.020	0.200		2	0.808	Sqm	
		Landing	2.050	0.200		2	0.820	Sqm	
Total Qty in Sqm							114.34		
Total Qty in Sft							1230.80	Sft	




Signature

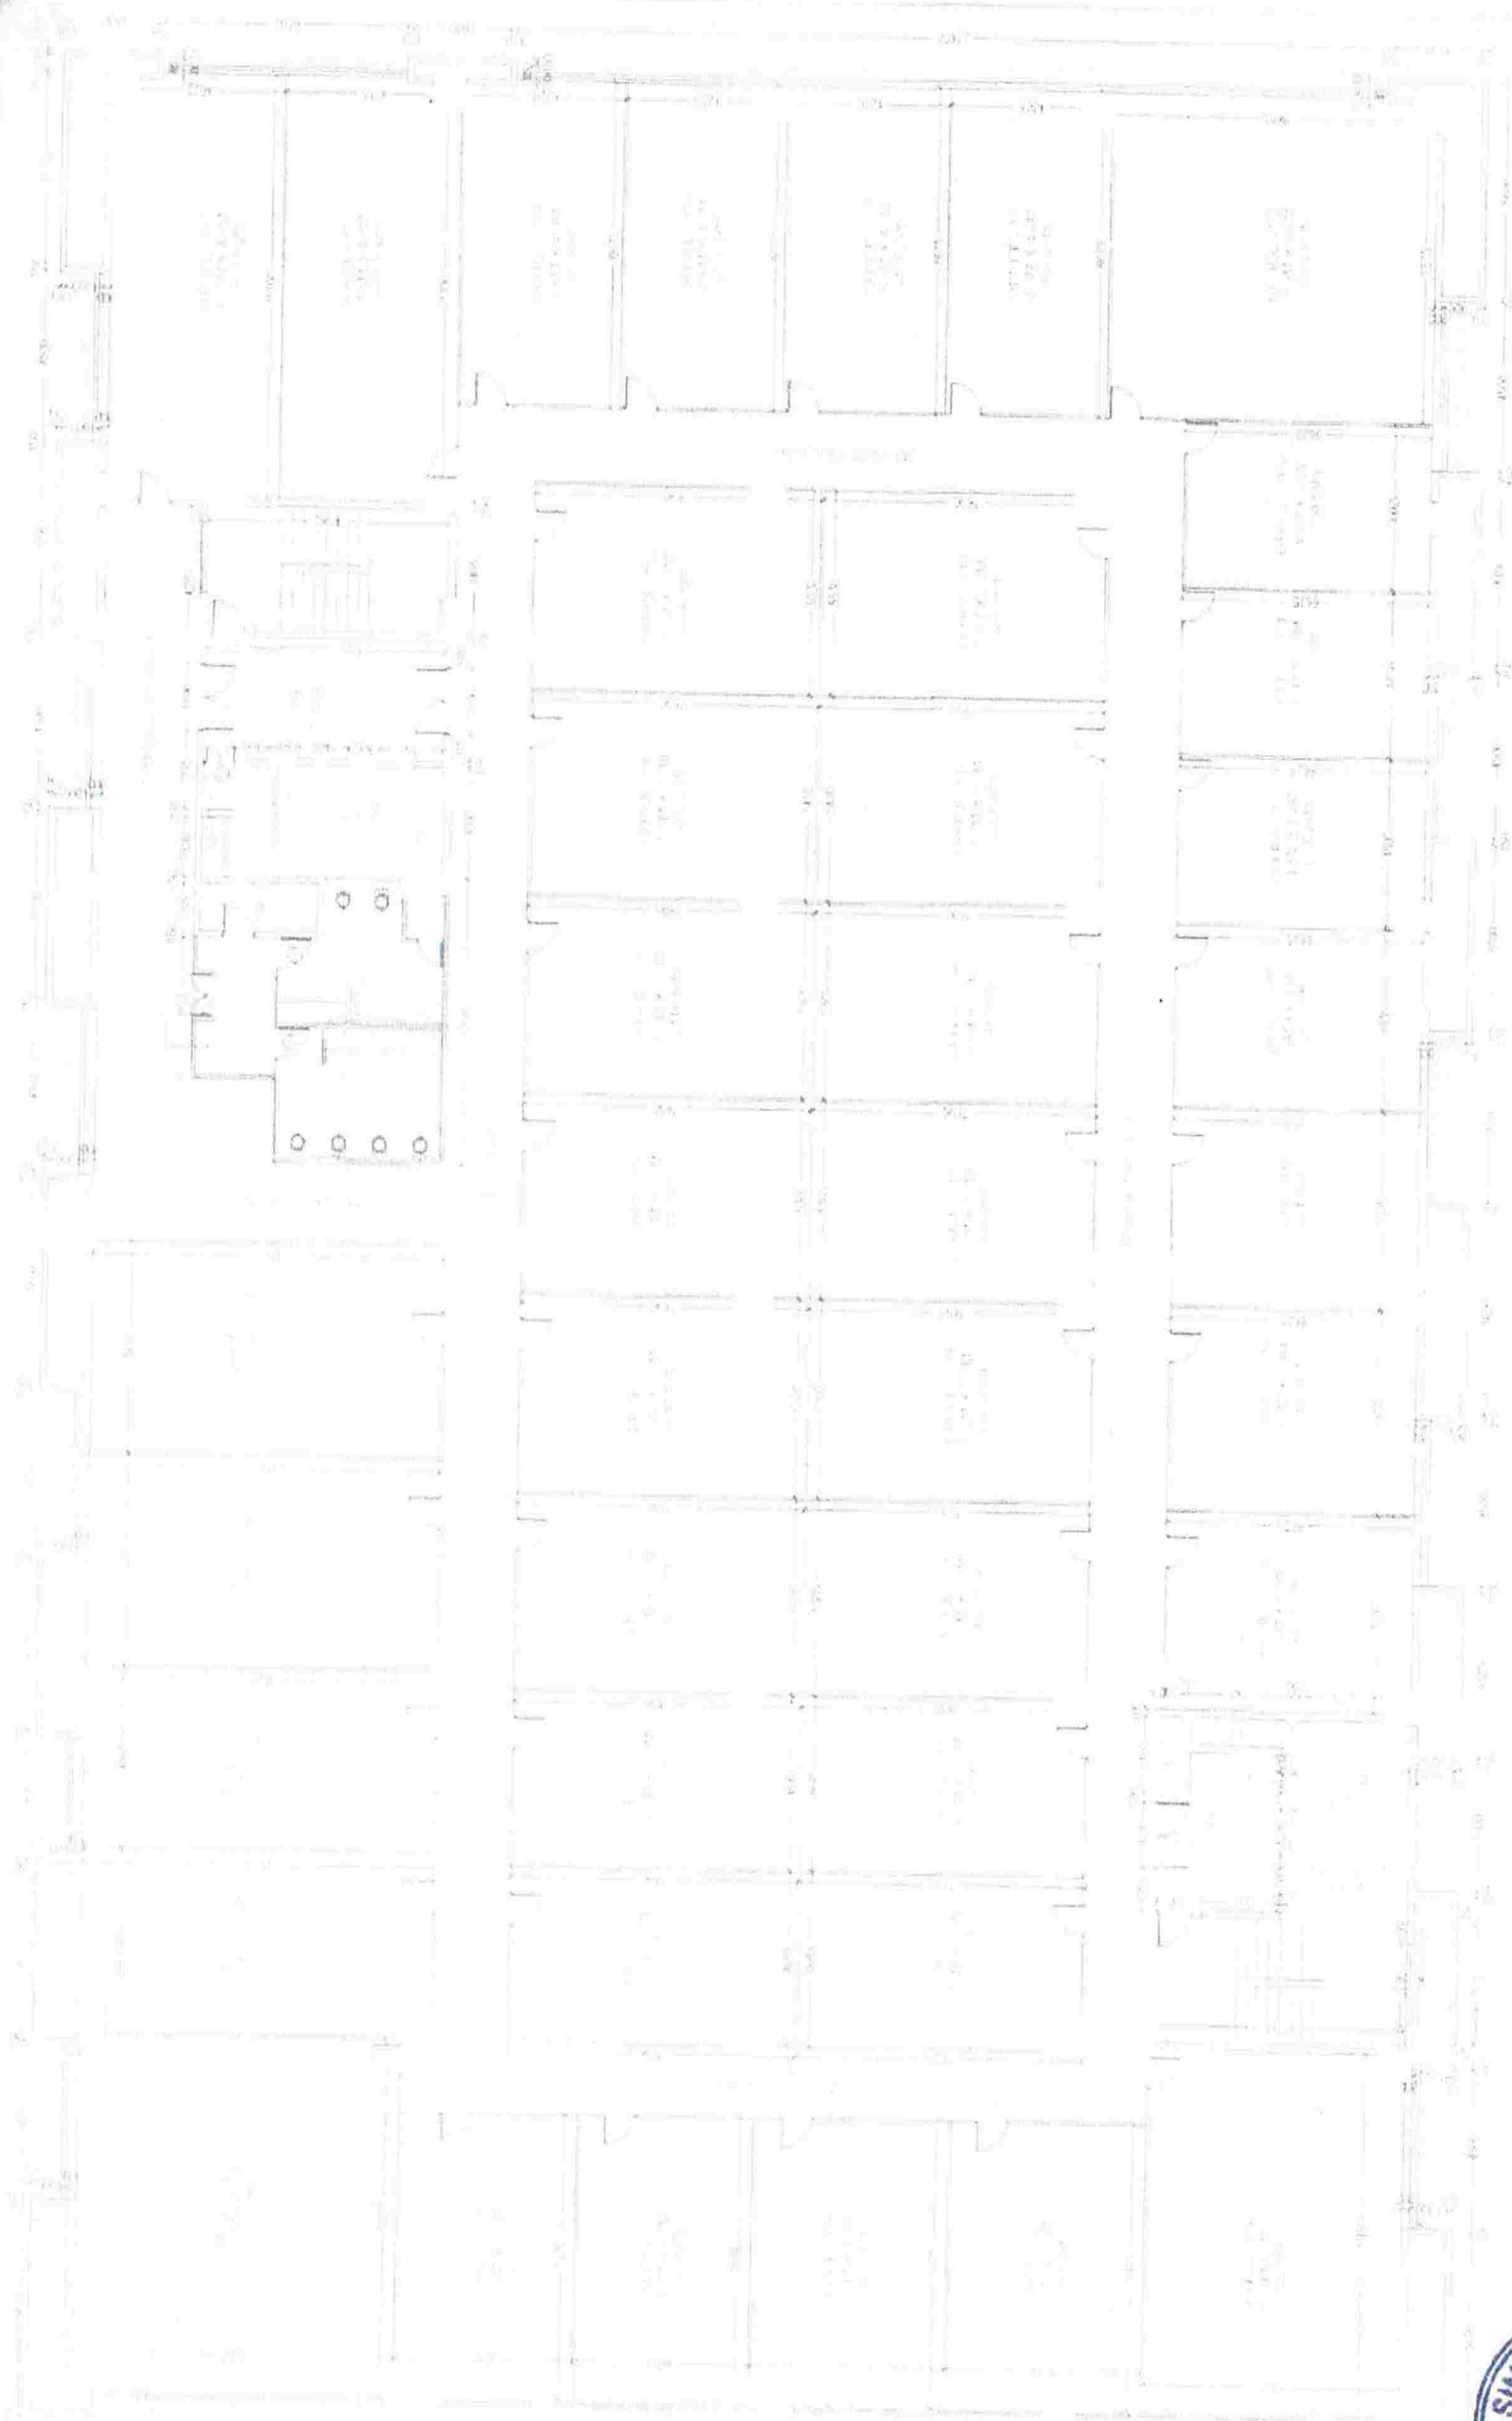

Internal wall thickness 70mm

Owners & Developers	Date	Drawn by	Checked by
Modi Properties Private Limited	30/07/20	Ar. Mani	Modi Properties & Investments Pvt. Ltd
Project Name & Phase	Approved By	Scale	Project No.
Modi Properties Private Limited	30/07/20	1:100	4554

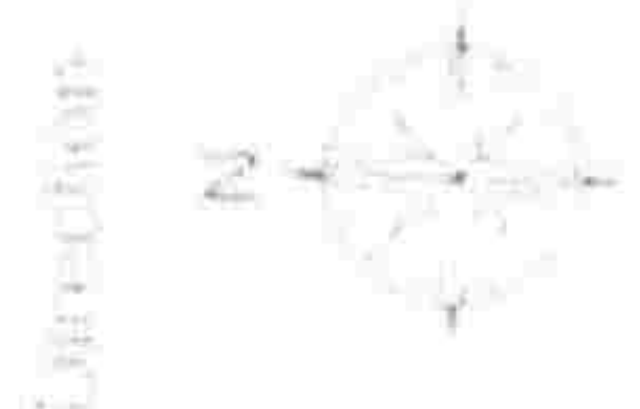

3RD FLOOR FLOOR PLAN
