

Internal memo no. 903/35/A
Annexure - B
RMC pour report

Company/ firm:	Modi Reality Mallapur LLP	Block No.:E Block	Towards E Block column 3 concreting purpose
Project:	Gulmohar Residency	Flat / Villa no.:	-
Supplier:	KN Infra	Slab no.:	Towards E Block column 3 concreting purpos
Requisition nos.:	20240403038	A. Estimated quantity:	68M3(M25)
PO nos.:	20240403050	B. Requisition quantity:	68M3
	Sign of Adm'n	C. Actual quantity poured	48M3
	Sign of Project Manger	D. Difference (C-A)	20M3

Details of RMC pour

Sl.	Date	Time of dispatch h from RMC plant	Time of receipt at site	Time of pour	Quantity poured	Batch no.	Specified wt @2400 kgs/m3	Measured weight (kgs)	Short fall in weight in kgs	Deduction for shortfall in Rs.	7 day cube test strength in kN/m2	28 days cube test strength in kN/m2
1.	17.04.24	10:20	14:08	14:20	8	19200	18970	-230				
2.	17.04.24	12:00	12:43	13:05	7	16800	17210	+410				
3.	17.04.24	13:39	17:16	17:30	6.5	15600	15990	+390				
4.	17.04.24	17:23	20:54	21:10	3	7200	7340	+140				
5.	03.05.24	09:10	13:00	13:15	3.5	8400	8760	+360				
6.	25.05.24	10:51	12:58	13:05	8	19200	19410	+210				
7.	25.05.24	11:13	14:56	15:05	8	19200	19000	-200				
8.	25.04.24	14:01	18:09	18:20	4	9600	9720	+120				
Total:					48	115200	116400	1200				
Remarks	Po not to be closed											

Note: 1. Report to be sent on a daily basis to purchase@modiproperties.com and report-audit@modiproperties.com. 2. Report must be prepared during pour and not later. 3. Report must be sent within one working day. 4. Multiple report can be sent for one PO. 5. Weigh all vehicles. 6. 6 cubic meters vehicle should have a net weight of 14,110 kgs @ 2,400kgs/ m3. If the shortfall is more than 50 kgs per load purchase to debit supplier shortfall amount on pro-rata basis. 7. Site to calculate shortfall. 8. Maintain original report + weightment slips + pour reports + test reports + photographs at

No: 294, Ramapally (V), Keesara(M)
Pin Dist - 501 301

Email: kninfra1@gmail.com

Ph. No: 9100999994/9100755567

DELIVERY CHALLAN

Customer Name: GULMOHAR RESIDENCY			D.C. No: 0244		Date: 25-05-2024
Delivery Site: MALLAPUR			Truck No: TS08UG4353		Mode: PUMP
S.No:	Description	Qty	Units	Cum. Qty	Remarks
1	M 25 RMC	8	Cum	8	-
Other Documents Enclosed:			For Office use only		
1)			Driver Name:		RAMESH CH
2)			Signature:		
Note: No alterations will be accepted without supplier & Customer Signatures alongwith reasons					
Received above material in good condition					
Customer Signature			fo K N INFRA Authorised Signatory		

FORWARD
MODI REALTY MALLAPUR
Water No: **15800** Dtd **25/5/24**
MRN No: **80240527019**
Received By...

Key No: 294, Ramapally (V), Keesara(M)
edchel Dist - 501 301

NFRA



Email : kninfra1@gmail.com
Ph. No: 9100999994/9100755567

DELIVERY CHALLAN

Customer Name: GULMOHAR RESIDENCY
D.C. No: 0245
Date: 25-05-2024

Delivery Site: MALLAPUR
Truck No: TS08UG4350
Mode: PUMP

S.No:	Description	Qty	Units	Cum. Qty	Remarks
-------	-------------	-----	-------	----------	---------

2	M 25 RMC	8	Cum	16	-
---	----------	---	-----	----	---

Other Documents Enclosed:


Driver Name: SRI SHAILAM
Signature:

Note: No alterations will be accepted without supplier & Customer Signatures alongwith reasons.
Received above material in good condition

Customer Signature

Authorised Signatory

to K N INFRA

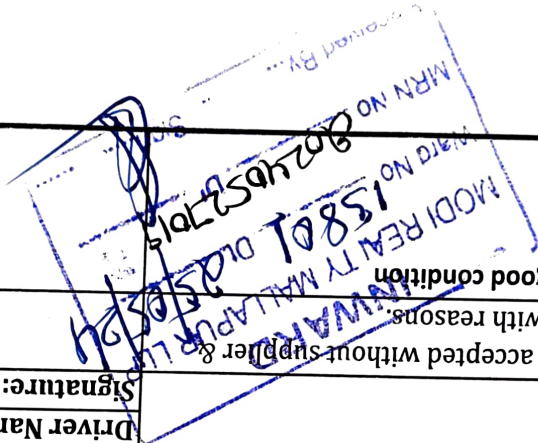

Survey No: 294, Ramapally (V), Keesara(M)
Medchel Dist - 501 301

Email : kninfra1@gmail.com

Ph. No: 9100999994/9100755567

KN INFRA

ENGINEER'S CONCRETE



DELIVERY CHALLAN

Customer Name: GULMOHAR RESIDENCY		D.C. No: 0248		Date: 25-05-2024	
Delivery Site: MALLAPUR		Truck No: TS08UG7853		Mode: PUMP	
S.No:	Description	Qty	Units	Cum. Qty	Remarks
3	M 25 RMC	4	Cum	20	-
Other Documents Enclosed:					
1) Driver Name: RAUF					
2) Signature:					
Note: No alterations will be accepted without supplier's					
Customer Signatures along with reasons					
Received above material in good condition					
Customer Signature		to K N INFRA			
Authorised Signatory					
