

Construction Division
Additions & Alteration Charges Approval Form

Company Name:		MRMLLP	Site	Gulmohar Residency
Name of the customer		MVN ABHISHEK RAO		
Villa/ Flat No.		H-507		
Sl.No	Description	Amount		
1	Total extra Charges	-		
2	Total refundable amount	1166		
3	Net amount to be charges (if any)			
4	Net amount to be refunded (if any)	1166		
Remarks : Refund				
One thousand one hundred sixty six rupees only				
Approved by Project Manager		Approved by Design Team		Approved by MD
Date		Date		Date
Sign:		Sign:		Sign:
Note: 1. Enclose measurement & estimate sheet. 2. Send scanned copy by email to plans@...				
Maintain originals in A&A of customers at site				

Note: 1. Enclose measurement & estimate sheet. 2. Send scanned copy by email to plans@modiproperties.com & CR. 3. Maintain originals in A&A of customers at site.

ESTIMATE SHEET						
Company Name:	MRMLP					
Project:	Gulmohar Residency					
Work Description:	Extra Specs					
Flat No.	H-507					
Prepared By	Niharika					
Date:	07-08-2024					
S No.	Item Head	Item Description	Quantity	Units	Rate	Amount
	Refund					
1	Tiles	Kitchen dado	33.33	sft	35.00	1166.55
					Total	1166.55
		Total Amount in Words = One Thousand One Hundred Sixty Six Rupees only				

Quality Control Check Report. Stage: After Finishing Stage III (Apartments)

Flat No	H-507	Other	—	Sl. No.	42839
Company	MEN-UP	Project	GMR	Phase	—
Prepared by	Saikiran	Sign	<i>[Signature]</i>	Date	13/03/2024
Project Manager	Aravindan	Sign	<i>[Signature]</i>	Date	13/03/2024
Previous stage report no.	42750	Report filed and signed by PM		Yes ☒ No ☐	
Checked By MD on		MD Sign		For filling	Yes ☐ No ☐

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after :

- Completing stage II works.
- Complete works like doors, windows, grills, electrical wiring, switches, french door glass, etc.
- In case of modular kitchen provide platform, granite and dado and modular kitchen in this stage.
- Provide video door phone in this stage.
- Possession for wood work cannot be given until QC check for stage III is completed and all corrections mentioned in the report are made.

Miscellaneous check:

Modular kitchen to be provided	☒ Yes ☐ No	Modular kitchen provided	☐ Yes ☐ No
Modular kitchen workman ship	☐ Good ☐ Avg ☐ Poor	Modular kitchen granite & dado workman ship & finishing	☐ Good ☐ Avg ☐ Poor
Video door phone /wifi cam to be provided	☒ Yes ☐ No	Video door phone/wifi cam provided	☐ Yes ☒ No
Painting marks and drops are cleaned from floor, windows, walls.			☐ Good ☐ Avg ☒ Poor

MODI REALTY MALLAPURAM LLP
 Sy No. 19, Marthapuram,
 HYDRABAD - 500 076

Draft finishing..check.report.apts. stage III .dt 17-10-2020 ver5

Quality Control Check Report. Stage: After Finishing Stage III (Apartments)

Quality Control Check Report. Stage: After Finishing Stage III (Apartments)													
		Rate the quality of (Good ✓, Avg ✕, Poor - needs correction ✕✕, NA)											
S No	Room	Door, door knob & door stopper fitting	Door, door knob & door stopper cleaning	Window grills & quality	Window grills fitting & finishing	Windows quality	Window fitting & finishing	Balcony railing quality & finishing	French door quality & fitting	CP jali quality and fitting	Edge building	Switch boards fitting & covering with plastic covers	Junction box covers painting
1	Bedroom 1 M. Bed	✓	✓	✓	✕	✓	✓	✓	✓	✓	✓	✓	✕
2	Bedroom 2 G. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 3 C. Bed	✓	✓	✓	✕	✓	✓	✓	✓	✓	✓	✓	✕
4	Drawing	✓	✕	✓	✕	✓	✓	✓	✓	✓	✓	✓	✕
5	Dining	✓	✕	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕	✓	✓
7	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Utility / balcony 2	✓	✓	✓	✕	✓	✓	✓	✓	✓	✓	✓	✓
9	Utility / balcony 3	✓	✕	✓	✕	✓	✓	✓	✓	✓	✕	✓	✕
10	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Toilet 1 M. Toi	✓	✓	✓	✕	✓	✓	✓	✓	✓	✕	✓	✓
12	Toilet 2 C. Toi	✓	✓	✓	✕	✓	✓	✓	✓	✓	✓	✓	✓
13	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕
14	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
15	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓

Remarks

NOTE :- (1) main door, Granite soffit was not provided.
(2) DB Box covers & Junction box covers to be placed at couple of places.

Quality Control Check Report. Stage: After Finishing Stage II (Apartments)

Flat No	H-507	Other	-	Sl. No.	92750
Company	MEM-UP	Project	hmr	Phase	-
Prepared by	Sarkisan	Sign	Sarkisan	Date	27/10/2024
Project Manager	Abrindan	Sign	[Signature]	Date	27/10/2024
Previous stage report no.		-		Report filed and signed by PM	☐ Yes ☒ No
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.					

Inspection should be done after:

- Completion of flooring, bathroom/utility tiles, first coat of paint.
- Completion of doors, windows, grills, electrical wiring, switches must be done in next stage
- False ceiling must be completed before flooring.
- Kitchen platform, granite and dado must be completed where modular kitchen is not provided.
- Provide granite soffit for main door and balconies in this stage.

Certified that all corrections mentioned in the QC Report have been completed. Work can proceed to next Stage.

Project In-charge	Sign	Date

Miscellaneous check:

Main door fixed with lock & stopper	☒ Yes ☐ No		
Granite soffit for balcony required	☒ Yes ☐ No	Granite soffit for balcony provided	☒ Yes ☐ No
Balcony granite soffit workmanship	☐ Good ☒ Avg ☐ Poor	Balcony granite soffit edge polishing	☐ Good ☒ Avg ☐ Poor
Granite soffit for main door required	☒ Yes ☐ No	Granite soffit for main door provided	☐ Yes ☒ No
Main door granite soffit workmanship	☐ Good ☐ Avg ☒ Poor	Main door granite soffit edge polishing	☐ Good ☐ Avg ☒ Poor

S No	Room	Rate the quality of (Good ✓, Avg X, Poor - needs correction XX, NA)												
		Workmanship of tiling	White cement filling around CPVC lines	Corners finishing	Finishing near doors	Finishing on top of tiles	Finishing near ventilators	Step at bathroom entrance / utility	Step for shower / pot wash	Tile joint grouting	Granite platform finishing and edge polishing	Granite platform slope	Granite platform height	Finishing under granite platform
1	Toilet 1 M. Eid	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 2 C. Toi	✓	X	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 4	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Wash basin in dining area	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Other													
9	Other													
Remarks		NOTE:-1) Main door Granite soffit not provided.												

Quality Control Check Report **Draft After Finishing Stage II (Painting)**

Quality Control Check Sheet														
Start After Finishing Stage II (Painting)														
Flooring & painting		Rate the quality of (Good =, Avg X, Poor - needs correction N/A)												
S No	Room	Color variation of floor tiles	Flooring workman ship & grouting	Skirting size (3")	Skirting workmanship	Plastering above skirting	Plastering & finishing of walls	Crack filling	Left Finishing	Windows check	General quality of painting & finishing	Door & frame painting quality	Door handling, upper and painting quality	Edge handling
1	Bedroom 1 G-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Bedroom 2 G-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 3 C-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Other	✓	✓	✓	✓	✓	✓	✓	X	✓	✓	✓	✓	✓
12	Other													
Remarks		(1) General painting & door paintings to be done by customer itself.												
		(2) Flat to be clean.												

Quality Control Check Report. Stage: After Plastering (Apartments)

Flat No.	H-507	Other	—	Sl. No.	42084
Company	MM-LLP	Project	CMK	Phase	—
Prepared by	SATKIRAN	Sign	<i>Sat</i>	Date	20-07-2023
Project Manager	NARENDAR/SRINIVAS	Sign	<i>Nare</i>	Date	20-07-2023
Previous stage report no.	—	Report filed and signed by PM?			☐ Yes ☒ No
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.					

Inspection should be done after:

- brickwork & 2 coats plastering is completed
- after cleaning the villa.
- Water proofing, screeding in bathrooms is completed.
- before starting painting, tiling & flooring.

Plastering Check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark X for minor mistake that requires minor correction.
3. Mark XX for major mistake that requires correction by replacement or re-fixing.
4. Mark XXX for major mistake that cannot be corrected.
5. 9" unplastered area from SFL should be left including in common areas and terraces.
6. Windows must be checked with templates. Plastering must be 3mm margin for lippum work. Tolerance 1/4".
7. Provision of tiles in bathrooms, kitchen & wash areas (rough plastering).
8. Check size of sink bowl. Hole should be 1" to 2" larger. (Tolerance: 1")
9. All doors frames should have 1/2" grooves.
10. Sill top must be of uniform thickness, correct height, at one level & without broken edges.

Certified that all corrections mentioned in the QC Report have been completed. Work can Proceed to next Stage.

Project In-charge	Sign	Date
<i>[Signature]</i>		

Quality Control Check Repot.

Stage: After Plastering (Apartments)

S No	Room	Skirting Provision (✓ or ✗)	Furnishing around door frame (✓ or ✗)	Beams & columns finishing (✓ or ✗)	Finishing of lofts (✓ or ✗)	Electricity junctions finishing (✓ or ✗)	Windows check (✓ or ✗)	Tiles provision (✓ or ✗)	Sink provision & size (✓ or ✗)	Grooves for door frames (✓ or ✗)	Balcony & terrace sill top finishing (✓ or ✗)	Screeding in bathroom & utility (✓ or ✗)	Screeding in 6" above FFL? (✓ or ✗)
1	Bedroom 1 - Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 - Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 - Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 - Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 - Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✗	✓	✓	✓
7	Bedroom 4	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Toilet 4	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Lobby 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Balcony	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Utility	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
15	Portico	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
16	Kitchen	✓	✓	✓	✓	✓	✗	✗	✓	✓	✓	✓	✓
17	Other												
Remarks													

Quality Control Check Report. Stage: After Brickwork (Apartments Lab Spaces)

Flat No.	H-502	Others	—	Sl No.	41451
Company	MRM-UP	Project	GMR	Phase	—
Prepared by	SATKIPAN	Sign	<i>[Signature]</i>	Date	06-03-2023
Project Manager	RAM PRASAD	Sign	<i>[Signature]</i>	Date	06-03-2023
Previous Stage report no.	—	Report filed and signed by PM?			☐ Yes ☒ No
Apartment No.		Other	<i>[Signature]</i>	other	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.					

Inspection should be done after:

- brickwork is completed
- chicken mesh fixed
- after cleaning the apartment
- electrical conducting work is completed

Brickwork Check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✕ for minor mistake that requires minor correction.
3. Mark ✕✕ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✕✕✕ for major mistake that cannot be corrected.
5. Wall thickness should be as per plan. Use of 4", 6" & 8" blocks must be checked.
6. All walls should have 2 beds of about 2" to 3" thickness with one no. 6 mm or 8 mm rod with M15 CC.
7. Chicken mesh should be used in each and every joint between RCC & Brickwork.
8. Joint between brickwork & beam on external side must be filled.
9. Check room dimensions with working plan. (Tolerance: 1")
10. Diagonals of each room shall be equal. (Tolerance: 2")
11. Balcony sill level should be 3'3" from SFL. (Tolerance: 1")
12. Check room height with specified height. (Tolerance: 1")
13. Check plumb of walls wherever it appears to be out of plumb. (Tolerance: 1/2")
14. Specify the No. of beams which are not aligned by more than 1" in a room.
15. Door frames must have black Japan coating and wood primer /pellambar – at cost of painter.

Certified that all corrections mentioned in the QC Report have been completed. Work can proceed to next stage.

[Signature] *[Signature]* *[Signature]*

Quality Control Check Report.

Stage: After Brickwork (Apartments/ Lab Spaces)

S No	Room	Wall thickness (✓ or ✗)	Beds in walls (✓ or ✗)	Chicken mesh (✓ or ✗)	External brickwork & beam joint (✓ or ✗)	Room Dimensions (✓ or ✗)	Room Dimensions Difference in inches	Diagonal (✓ or ✗)	Diagonal Difference in inches	Balcony sill level (✓ or ✗)	Room Height (✓ or ✗)	Plumb of walls (Good/ Avg./ Bad)	Alignment of beams and walls - Nos.
1	Bedroom 1 m. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 m. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	Avg	✓
3	Bedroom 2 G. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 C. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 C. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	Avg	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	Avg	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	Avg	✓
14	Other												
15	Other												
Remarks NOTE:- 1) Central level bed's was not providing properly at couple of walls.													

Quality Control Check Report.		Stage: After Brickwork (Apartments/ Lab Spaces)
Quality of edges and corners in all rooms?	☐ Good ☒ Avg. ☐ Bad	
Specify rooms that need correction:		
Misc. Checks.		
Was 3.75 CFT proportion box provided?	☒ Yes ☐ No	
Condition of proportion box?	☐ Good ☒ Avg. ☐ Bad	
Was the Apartment cleaned before starting brick work?	☐ Yes ☐ No ☒ Cant' say	
Is the Apartment cleaned for plastering?	☒ Yes ☐ No	
Wastage?	☐ High ☒ Medium ☐ Low	
Storage of building material like bricks sand and cement.	☐ Good ☒ Avg. ☐ Bad	
Drum (200 ltrs) provided for curing in each flat?	☒ Yes ☐ No	
Remarks:		

Door Frames & Windows check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. Window template depth should be between 2 to 2 1/2" after plastering.
6. Lintel level should be 7'3" from SFL & 7' from FFL. (Tolerance 1"). Lintel should be as per standard design.
7. Lofts should be at a height of 7' to 7'3" from FFL. Kitchen platform thickness should be 2". SFL to bottom 31". (Tolerance 1")
8. Slopes of lofts and kitchen platforms to be checked by using 12' spirit level and check height from floor from 2 or 3 points.
9. Thickness of platforms & lofts should be between 2 & 2.5".
10. Provide single layer table brick at bottom of each door frame without threshold.
11. Check Z angle template size (Z angle for bathroom ventilators not required in new projects).
12. Window opening must be checked with MS square pipe templates of 2 sizes for inner and outer openings.
13. Z angle template must be 1" from brick wall surface from the inner side.

Quality Control Check Report.

Stage: After Brickwork (Apartments/ Lab Spaces)

S No	Room	Door size, face and position (✓ or ✗)	Brick at bottom of door frame (✓ or ✗)	Door frame hold fast provision and fasteners (✓ or ✗)	Door level design & level (✓ or ✗)	Door diagonal check (✓ or ✗)	Door Plumb - two sides (✓ or ✗)	Windows level design & level, Sill level (✓ or ✗)	Windows size (✓ or ✗)	Windows - template depth & diagonal (✓ or ✗)	Windows - template red inside painting (✓ or ✗)	Loft & Kitchen platform height (✓ or ✗)	Loft & Kitchen platform slope (✓ or ✗)	Door size, face and position (✓ or ✗)
1	Bedroom 1 m. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 G. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 C. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 k. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other													
15	Other													
Remarks: NOTE :- 1) Kitchen platforms not casted.														
2) As per customer request, utility door position was changed.														

GULMOHAR RESIDENCY

Sy. No. 19, Mallapur Village, Uppal, Hyderabad.
Owned & Developed by: M/s. Modi Realty Mallapur LLP.
Head office: 5-4-187/3&4 M G Road Secunderabad.


Details of Additions & Alterations

Flat No	707	Block no.	4	' , '
Flat Area	sft	Type	Deluxe / Luxury	
Buyer Name	Mr. AA.S. RAGHAVA M V N A B H I S H E K			
Phone No.	8754640872	Email		

RA2


I hereby confirm that I have given the details of the minor additions and alterations that are required in the above referred flat in the pages attached herein. Please complete the changes suggested by me. I agree to pay the charges, if any, for the additions and alterations that I have asked you to make, as per the rates suggested by you. I shall deliver all the materials that are required to be provided by me at the site on or before _____.

In case I fail to deliver these items to the site by the specified date, you may complete the works in the flat as per the standard items provided by you.

Buyers sign		Engg. Sign	
Date:	07/5/23	Date	

Note:

1. Colour shades of paints may vary from batch to batch & company to company. The Builder will not take responsibility of quality of work for dark shades especially green & blue.
2. Shade / colour of natural material like marble and granite can't be guaranteed and may vary from lot to lot. Cracks like appearance in marble is a natural feature and Builder shall not be responsible for repairs or replacement.
3. Availability of bathroom or flooring tiles of the same type /colour/make can not be guaranteed and closest possible type/colour/make may be used in its place.
4. No further change shall be permitted from this day.
5. Please sign on all pages.

Buyer's sign: 

Engg. Sign:

Date:

Choice of colours:

Changes in flooring:

- 1) M.T - Luna
- 2) C.T - Malaysian
- 3) Kitchen wall of - ceiling 1044
floor 1 - ceiling 1044
- 4) Hall & Dining & 3. bed room - 2x2 - vitrified tile,
- 5) Balcony - ceiling 1044.
- 6) utility wall - balance white
flooring - malarpa offwhite / .

Buyers Sign
19/6/23

Engg. Sign:

Date:

Changes in electrical points: (mark on plan)

Same as SDC.

Choice of Bathroom tiles, CP fittings & Sanitary ware:

Buyer's Sign: 
19/6/23


Engg. Sign:

Date:



S.NO	ITEM	SYMBOL	HEIGHTS from F.F.L
1.	Distribution Board & Switch board	□	7' TO 7'6"
2.	Switch board	□	4' OR 4'6"
3.	Wall power/switch light	○	7' TO 7'6"
4.	5 amps plug point	●	2'
5.	Ceiling fan	⊙	6'6" OR 7'
6.	Exhaust fan	⊙	7'
7.	15 amps plug point	⊙	7' OR 3'6" OR 7'
8.	Television point	⊙	3'
9.	Telephone point	⊙	7'
10.	Ceiling light	⊙	4'6"
11.	Ceiling fan	⊙	4'6"
12.	Bed Push	⊙	6"
13.	Ceiling light	⊙	7'
14.	WiFi Camera	⊙	7'
15.	AC Compressor	⊙	7' TO 7'6"
16.	AC Blower	⊙	4' TO 4'6"
17.	Switch board with 5A socket	⊙	4' TO 4'6"

Note - Switch boards next to bed side must be @ 3.6' from center of bed

LEGEND:-

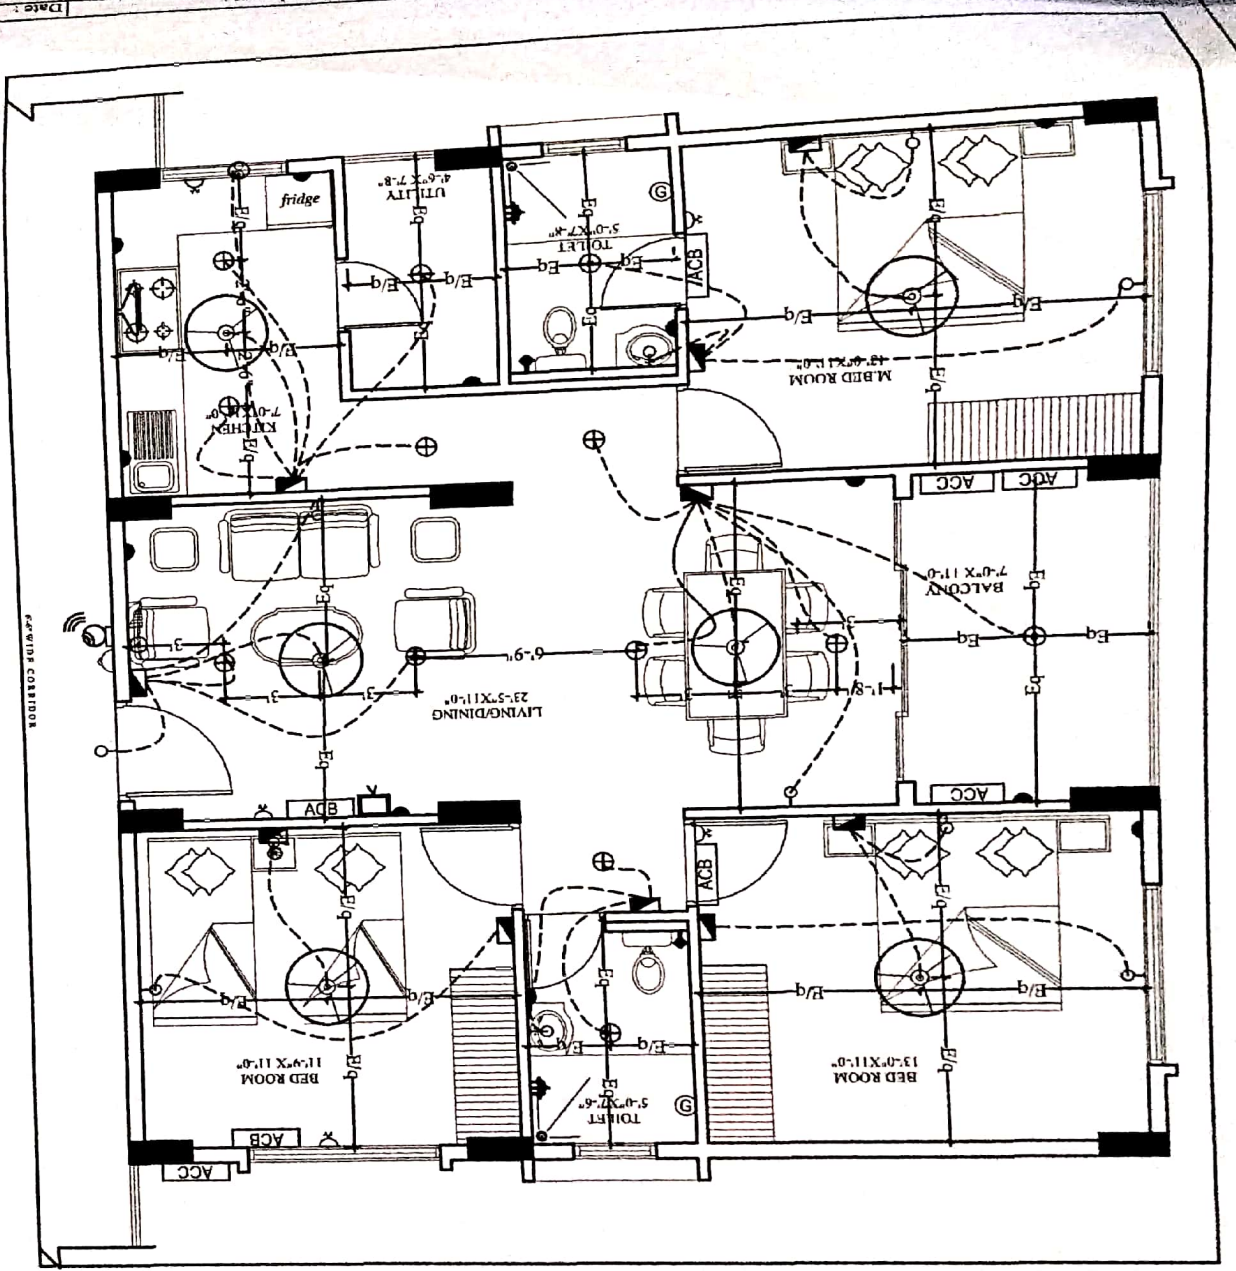


19/06/22

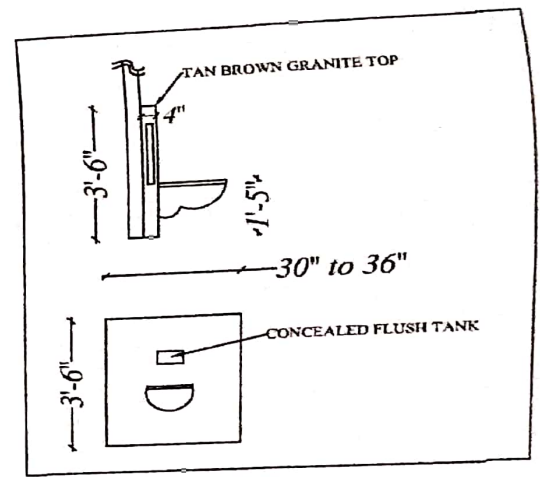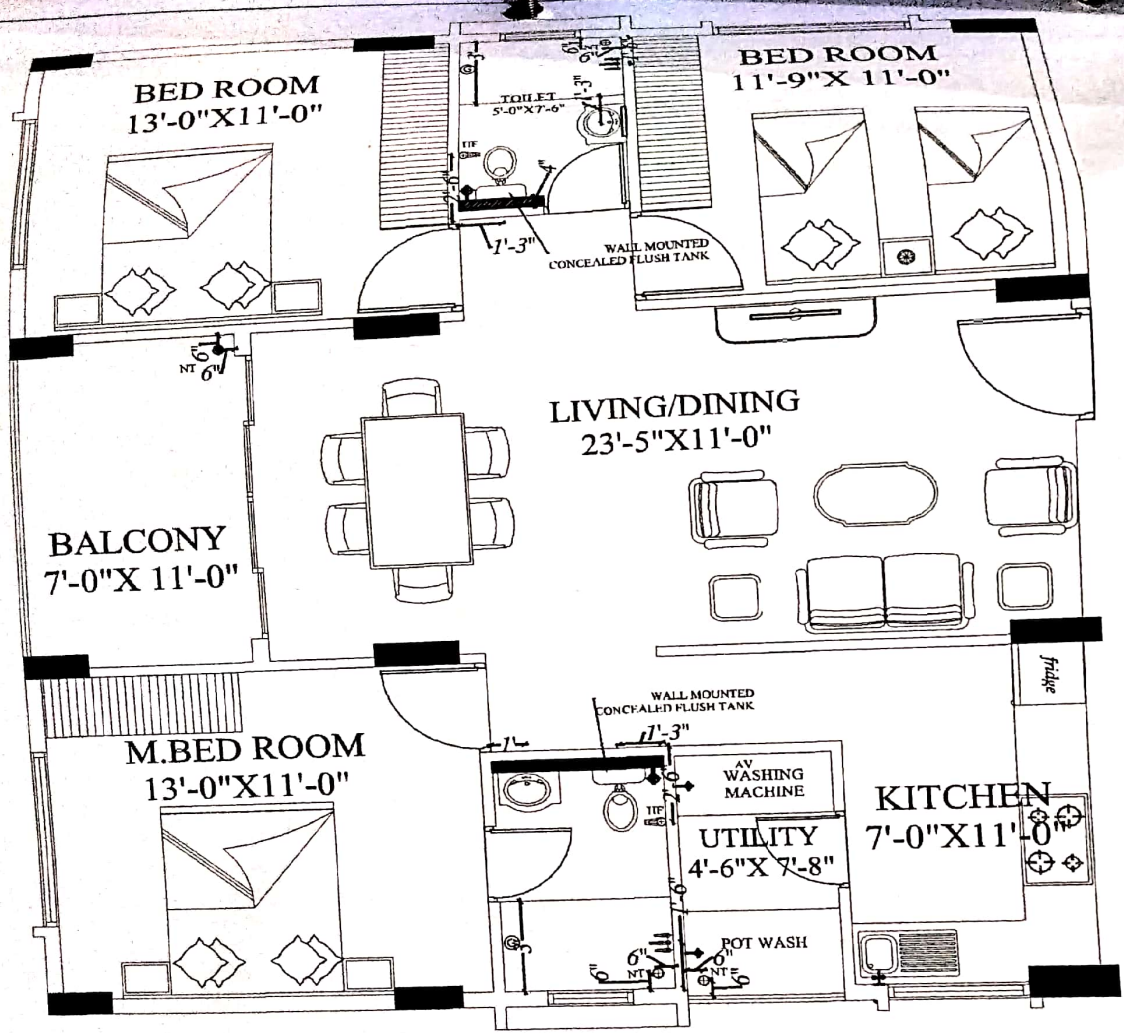

LEGEND

+	HEALTH FAUCET
⚡	ANGLE VALVE
⊙	NANI TRAP
○	3" RAIN WATER PIPE
⊕	GEASER POINT
≡	WALL MIXTURE
⦿	TAP / LONG BODY

Description	Direction	Owners & Developers :	Date :	16.09.20	Promoted by
PLUMBING PLAN-1360 Sft (A1-TYPE)		Modi Reality Mallapur LLP	Prepared By :	Jayapradha	Modi Properties Pvt Ltd
		Project Name & Phase :	Approved By :	Soham Modi	
		Gulmohar Residency	Scale :	N.T.S	Phone:+91-40-66335551

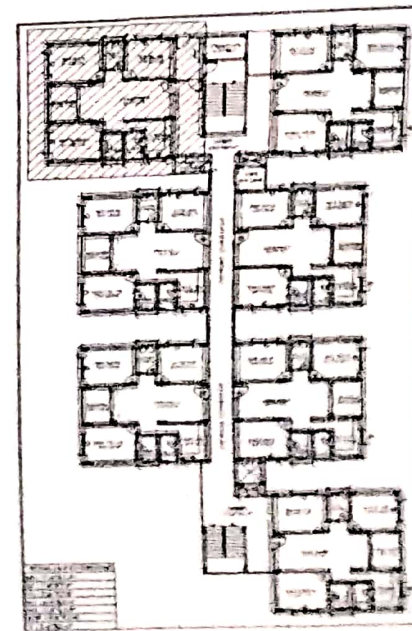

Scanned with OKEN Scanner
