


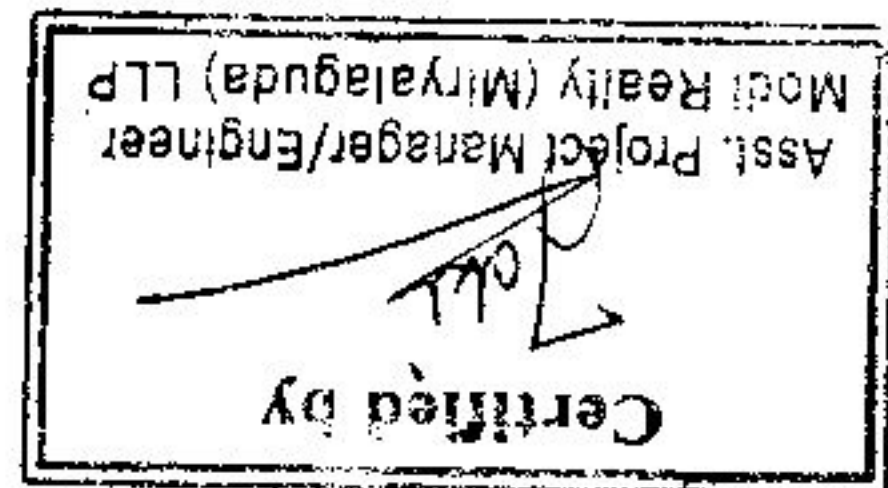

Annexure - B - Send Weekly		Details of hire charges		Name of contractor		ASHOK CONSTRUCTIONS		Company name		MRMLLP		Project name		AVR Gulmohar Homes		Date		5/3/2021		Period		From 25/02/2021 To 4/3/2021		Amount											
Sl. No.		Equipment Type		Quantity		Rate		Units		Amount		1		JCB		14.56		900.00		Hour		13,104		2		Tractor		1.00		1,800.00		Engage		1,800	
Total																																			
Payment approved by MD:																																			
Prepared by:																																			
Name		Zakir																																	
Date		5/3/2021																																	

Anx - C - Material received

Annexure - C - send weekly									
Details of material received									
Name of contractor		ASHOK CONSTRUCTIONS							
Company name		MRMLLP							
Project name		AVR Gulmohar Homes							
Date		5/3/2021							
Period		From: 25-02-2021		To: 4/3/2021					
Sl No	Material type	Received date	Inward no	Quantity	Units	Rate	Amount		
1	METAL - 20 mm	25-02-2021	297	12.00	TONS	630.00	7,560		
2	Red Brick	25-02-2021	568	1,000.00	No's	6.50	6,500		
3	Red Brick	25-02-2021	570	2,000.00	No's	6.50	13,000		
4	Solid Brick-6 x 8 x 16	25-02-2021	571	185.00	No's	30.00	5,550		
5	Solid Brick-6 x 8 x 16	25-02-2021	571	65.00	No's	30.00	1,950		
6	Solid Brick-6 x 8 x 16	25-02-2021	572	1,141.00	No's	30.00	34,230		
7	Solid Brick-4 x 8 x 16	26-02-2021	573	887.00	No's	20.00	17,740		
8	SAND/STONE DUST	27-02-2021	298	25.67	TONS	630.00	16,172		
9	SAND/STONE DUST	28-02-2021	299	26.48	TONS	630.00	16,682		
10	CEMENT BAGS	1/3/2021	574	530.00	Bags	350.00	185,500		
11	Solid Brick-4 x 8 x 16	2/3/2021	575	892.00	No's	30.00	26,760		
12	Solid Brick-6 x 8 x 16	3/3/2021	576	2,200.00	No's	30.00	66,000		
13	Solid Brick-6 x 8 x 16	3/3/2021	577	190.00	No's	30.00	5,700		
14	SAND/STONE DUST	3/3/2021	300	25.79	TONS	630.00	16,248		
15	Total						419,592		
16	Payment approved by MD								
Prepared by:				Approved by:		MID's approval			
Name	Zakir								
Date	5/3/2021								

Certified by

[Signature]

Asst. Project Manager/Engineer
Modi Realty (Miryalaguda) LLP

Anx - D - Milestone report

Annexure - D - send weekly												
Mile stone report for CR-												
Company name:		MRMLLP										
Project name:		AVR Gulmohar Homes										
Date:		5/3/2021										
Note:		Prepare the statement for all the villas in the project										
S No	Villa no- 4BHK)	Type (2, 3, 4BHK)	SBUA	Work start date	Completion of plinth	Completion of RCC	Completion of brickwork and plastering	Completion of stage I	Completion of stage II	Completion of stage III	Completion of stage IV	Date of physical possession
1	1	3BHK	2,340	9/Aug/19	5/Oct/19	21/Jan/20	8/Aug/20	8/Jan/21				
2	2	4BHK	2,340	27/Apr/17	8/Aug/17	2/Jan/18	10/Apr/18	9/Aug/18	14/Aug/18	14/Aug/18	7/Sep/18	
3	3	2BHK	1,250	27/Apr/17	9/Feb/17	29/12/2017	10/Apr/18	17/May/19	1/Sep/18	7/Sep/18	11/Nov/18	
4	4	2BHK	1,250	27/Apr/17	16/Aug/17	29/12/2017	24/Apr/18					
5	5	2BHK	1,250	27/Apr/17	16/Aug/17	6/Jan/18	8/May/18					
6	6	3BHK	2,340	27/Apr/17	25/Jul/17	22/May/18	14/Feb/19	22/May/20	17/Oct/20	24/Dec/20		
7	7	3BHK	2,340	27/Apr/17	5/Aug/17	29/May/18	25/Apr/19	7/Mar/20	17/Oct/20	17/Dec/20		
9	9	2 BHK	1,250	16/Sep/17	10/Oct/17	6/Jan/18	15/May/18	6/Nov/18	27/Mar/19	20/Jul/19	1/Jan/20	20/Jan/20
10	10	2BHK	1,250	18/Aug/18	27/Oct/18	3/Jan/19	10/Jan/20	22/May/20				
11	11	2BHK	1,250	19/Aug/18	23/Oct/18	20/Dec/18	20/Jul/19	22/May/20				
12	12	2BHK	1,250	30/Jul/18	10/Sep/18	13/Nov/18	6/Jun/20	19/Nov/20				
13	13	2 BHK	1,250	4/Jul/18	10/Sep/18	30/Oct/18	23/May/20	19/Nov/20				
14	14	2 BHK	1,250	4/Jul/18	20/Nov/18	11/Jan/19	23/May/20	27/Nov/20				
15	15	3BHK	2,340	29/Aug/18	20/Jul/19	10/Sep/19	22/May/20	26/Sep/20	17/Dec/20			
16	16	3BHK	2,340	11/Jul/18	22/Nov/18	7/Feb/19	11/Nov/20					
17	17	2BHK	1,250	6/Aug/18	6/Dec/18	19/Jan/19	10/Jan/20	18/Jul/20	17/Oct/20	5/Dec/20		
18	18	3BHK	2,340	29/Jul/19	20/Nov/19	4/Jul/20						
19	19	3BHK	2,340	31/Jul/19	23/Nov/19	22/May/20						
20	20	2BHK	1,250	27/Aug/18	5/Jan/19	9/Feb/19	8/Aug/20	16/Dec/20				
21	21	2 BHK	1,250	16/Sep/17	10/Oct/17	29/Jan/18	19/May/18	4/Dec/18	31/Mar/19	23/Jul/19		
22	22	2 BHK	1,250	30/May/17	20/Sep/17	29/Jan/18	29/May/18	18/Aug/18	7/Mar/19	14/Aug/19	20/Aug/20	25/Feb/20
23	23	3BHK	2,340	23/Jul/18	7/Feb/19	25/Jun/19	11/Sep/20	8/Jan/21				
24	24	3BHK	2,340	31/Jul/19	28/Nov/19	18/Sep/20						
25	25	3BHK	2,340	7/Aug/19	4/Jan/20	23/May/20						
26	26	3BHK	2,265	23/May/19	13/Dec/19	27/Feb/20	5/Oct/20	8/Jan/21				
27	27	3BHK	2,340	8/Aug/18	24/Nov/18	22/May/20						
28	28	3BHK	2,340	7/Aug/18	27/Nov/18	6/Jun/20						
29	29	2BHK	1,250	25/Dec/18	2/Feb/19	9/Feb/19	4/Sep/19	15/Feb/20	27/Jun/20	26/Sep/20		
30	30	2 BHK	1,250	30/May/17	14/Nov/17	22/Mar/18	30/Nov/18	30/Jan/19	25/Apr/19	14/Aug/19	25/Oct/20	31/Oct/20

Anx - D - Milestone report

S No	Villa no- 4BHK	Type (2, 3, 4BHK)	SBUA	Work start date	Completion of plinth	Completion of RCC	Completion of brickwork and plastering	Completion of stage I	Completion of stage II	Completion of stage III	Completion of stage IV	Date of physical possession
31	31	2BHK	1,250	26/Dec/18	5/Feb/19	16/Mar/19	21/Dec/19	5/Dec/20	4/Mar/21			
32	32	4 BHK	2,340	12/Dec/17	19/Dec/17	23/Feb/18	13/Jun/18	6/Nov/18	19/Jun/19	17/Aug/19		
33	33	2BHK	1,250	23/Apr/19	5/Jun/19	8/Feb/19	17/Dec/19	6/Feb/20	25/Jul/20	8/Aug/20	10/Oct/20	20/Oct/20
34	34	2 BHK	1,250	9/Jul/18	13/Jun/19	16/Jul/19	16/Nov/19	28/Jan/20	18/Jun/20	8/Aug/20	1/Nov/20	20/Nov/20
35	35	2 BHK	1,250	15/Sep/17	6/Oct/17	6/Feb/18	27/Sep/18	13/Nov/18	16/Oct/19	20/Dec/19		
36	36	3BHK	2,340	25/Aug/18	30/Aug/19	28/Jan/20	22/May/20	19/Nov/20				
37	37	2BHK	1,250	24/Jul/17	17/Nov/17	6/Feb/18	11/Dec/18	19/Jun/19	30/Oct/19	21/Dec/19		
38	38	4 BHK	2,340	7/Jan/19	26/Feb/19	9/Apr/19	10/Jan/20					
39	39	4BHK	2,340	7/Jan/19	23/Feb/19	31/Mar/19	10/Jan/20					
40	40	3-BHK	2,340	10/Jun/18	10/Jul/18	23/Feb/19	17/Dec/20					
41	41	2-BHK	1,250	5/Jun/18	26/Jun/18	3/Oct/18	19/Jun/19	15/Feb/20	11/Sep/20	26/Sep/20		
42	42	3BHK	2,340	20/Jul/18	12/Nov/19	5/Oct/20						
43	43	3BHK	2,340	25/Jul/19	2/Nov/19	21/Dec/19						
44	44	2 BHK	1,250	29/May/19	30/Oct/19	15/Feb/20	8/Aug/20	16/Dec/20				
45	45	3BHK	2,340	11/Jul/19	25/Oct/19	4/Jul/20						
46	46	3BHK	2,340	10/Jul/19	16/Oct/19	23/May/20	17/Oct/20					
47	47	3BHK	2,340	28/Apr/19	20/Sep/19	20/Nov/19	22/May/20	5/Oct/20	4/Mar/21			
48	48	2 BHK	1,250	15/Sep/17	26/Oct/17	6/Mar/18	3/Jul/18	13/Nov/18	11/May/19	27/Aug/19		
49	49	3BHK	2,340	6/Jul/19	20/Aug/19	20/Dec/19	16/Dec/20	17/Dec/20	3/Mar/21			
50	50	2 BHK	2,340	4/Sep/19	4/Sep/19	6/Feb/20	8/Aug/20	17/Dec/20				
51	51	3BHK	2,340	25/06/2019	24/Aug/19	5/Dec/20						
52	52	3BHK	2,340	26/Jun/19	1/Oct/19	11/Nov/20						
53	53	2BHK	1,250	29/May/19	27/Aug/19	15/Feb/20	18/Sep/20	16/Dec/20				
54	54	3BHK	2,340	9/Jul/19	13/Jul/19	7/Mar/20						
55	55	4BHK	2,430	21/Jul/18	17/Aug/19	5/Nov/19	16/Dec/20					
56	56	2 BHK	1,250	21/Jul/18	2/Jan/19	26/Jul/19	28/Oct/20	5/Feb/21				
57	57	2 BHK	1,250	16/Oct/17	28/Nov/17	24/Mar/18	19/Feb/19	18/Sep/19	14/Nov/19	20/Dec/19		
58	58	2 BHK	1,250	18/Jul/18	18/Aug/18	17/Dec/20						
59	59	4BHK	2,340	16/May/19	9/Jul/19	13/Sep/19	4/Jul/20	12/Feb/21				
60	60	2BHK	1,250	21/Jul/18	22/Aug/18	12/Jul/19	11/Nov/20	17/Dec/20				
61	61	2 BHK	1,250	15/Sep/17	14/Oct/17	24/Apr/18	29/Sep/18	22/Nov/18	24/May/19	27/Aug/19		
62	62	2 BHK	1,250	24/Jul/17	15/Dec/17	17/Mar/18	15/Nov/18	30/Jan/19	29/Jun/19	25/Sep/19	27/Jul/20	15/Aug/20
63	63	2 BHK	1,250	8/Nov/17	19/Dec/17	6/Mar/18	15/Nov/18	19/Feb/19	25/Sep/19	23/Dec/19	27/Jul/20	15/Aug/20
64	64	2 BHK	1,250	15/Sep/17	14/Oct/17	23/Feb/18	15/Nov/18	19/Feb/19	19/Jun/19	28/Sep/19	8/Aug/20	18/Aug/20
65	65	3BHK	2,340	15/Jun/18	21/Jul/18	15/Nov/18	7/Sep/19	8/Aug/20				

Anx - D - Milestone report

S No	Villa no-	Type (2, 3, 4BHK)	SBU/A	Work start date	Completion of plinth	Completion of RCC	Completion of brickwork and plastering	Completion of stage I	Completion of stage II	Completion of stage III	Completion of stage IV	Date of physical possession
66	66	3BHK	2,340	7/Jun/18	5/Jul/18	30/Nov/18	7/Sep/19	23/May/20	5/Dec/20	17/Dec/20		
67	67	3BHK	2,340	16/Jun/18	24/Jul/18	17/Dec/20						
68	68	3BHK	2,340	23/Dec/18	19/Jun/19	14/Nov/19	25/Jul/20	5/Feb/21				
69	69	3BHK	2,340	14/Jun/18	26/Jul/18	30/Jul/19	12/Feb/21					
70	70	3BHK	2,340	14/Jun/18	28/Jul/18	30/Jul/19	12/Feb/21					
71	71	2 BHK	1,250	31/Jul/17	7/Jul/18	1/Sep/18	10/Jun/20	17/Dec/20				
72	72	2BHK	1,250	2/Jul/18	15/Nov/18	5/Feb/21						
73	73	2 BHK	1,250	5/Jul/18	4/Aug/18	13/Oct/18						
74	74	2 BHK	1,250	15/Sep/17	2/Nov/17	3/Mar/18	22/Dec/18	24/May/19	16/Nov/19	11/Jun/20	1/Jun/20	23/Jun/20
75	75	2 BHK	1,250	18/May/18	19/Jun/18	19/Sep/18	11/Jun/19	20/Sep/19	14/Nov/19	23/Jun/20		
76	76	2 BHK	1,250	8/Nov/17	9/Dec/17	3/Mar/18	2/Mar/19	25/Apr/19	4/Sep/19	28/Jun/20		
77	77	2BHK	1,250	30/Nov/17	17/Mar/18	16/May/18	15/May/18	30/Nov/18	25/Apr/19	13/Sep/19	5/Oct/19	18/Aug/20
78	78	2BHK	1,250	7/May/19	6/Jul/19	17/Aug/19	10/Jun/20	15/Feb/20	14/Jul/20	8/Aug/20	15/Oct/20	22/Oct/20
79	79	2 BHK	1,250	26/Oct/17	24/Nov/17	24/Mar/18	15/Dec/18	11/May/19				
80	80	2 BHK	1,250	26/Oct/17	6/Dec/17	24/Mar/18	4/Dec/18	24/May/19	18/Sep/19	5/Oct/19		
81	81	3BHK	2,340	21/Jun/18	7/Aug/18	20/Sep/19	11/Sep/20	4/Mar/21				
82	82	3BHK	2,340	18/Jun/18	24/Aug/18	30/Aug/19	11/Nov/20	12/Feb/21				
83	83	2BHK	1,250	14/May/19	19/Oct/2019	1/Oct/19	10/Jun/20	18/Jun/20	17/Oct/20	11/Nov/20		
84	84	2 BHK	1,250	26/Jun/18	25/Aug/18	3/Nov/18	11/Nov/20	17/Dec/20				
85	85	3BHK	2,340	16/May/19	29/Jun/19	13/Dec/19	11/Sep/20	12/Feb/21				
86	86	2 BHK	1,250	13/Dec/17	13/Jun/18	22/Aug/18	11/May/19	5/Nov/19	28/Jun/20	27/Feb/20		
87	87	2 BHK	1,250	25/Jun/18	29/Aug/18	26/Dec/18	25/Oct/19	28/Nov/19	1/Feb/20	22/May/20		
88	88	2 BHK	1,250	26/Oct/17	21/Nov/17	5/Jun/18	18/Sep/19	13/Dec/19	28/Jun/20	27/Feb/20		
89	89	3BHK	2,340	3/Jun/19	13/Sep/19	13/Dec/19	8/Aug/20	26/Sep/20				
90	90	3BHK	2,340	24/Jun/19	10/Sep/19	7/Nov/19	10/May/19	4/Jul/20				
91	91	2BHK	1,250	15/Sep/17	10/Mar/18	7/Jul/18	11/May/19	12/Oct/19	21/Jun/20	27/Feb/20	8/Aug/20	20/Sep/20
92	92	3BHK	2,340	18/Nov/17	3/Jul/18	11/Dec/18	13/Nov/19	14/Nov/19	8/Aug/20	10/May/20		

Certified by

 Asst. Project Manager/Engineer
 Modi Realty (Mira-Vasindia) LLP
