

PURCHASE DIVISION
Advice for approval for credit to supplier

(2)

Date:	28/09/2021	Prepared by:	MINISH
PO/WO no.	79892	PO / WO Date.	04/09/2021
Supplier Name	SL RMC PLANT	PO/WO amount	2,40,500/-
Firm/Company	Mehra & Modi Realty, KOKKURUP	Project	G+M
Sl. No.		Bill Date	Bill amount
1.	158	07/09/2021	1,96,100/-
2.			
3.			
4.			

Amount A – Bills total(Excluding Transport & Hamali Charges):

1,96,100/-

Sl. No.	DC No	DC. Date	MRN No.	DC matches MRN
1.				☐ Yes ☐ No
2.				☐ Yes ☐ No
3.				☐ Yes ☐ No
4.				☐ Yes ☐ No

ROUTING Report Enclosed

Amount B – Other Credits :-

Amount C – Other Debits :-

4,957/-

Amount D (D=A+B-C) – Amount to be credited to the supplier:

1,91,143/-

Amount E – PO / WO value:

2,40,500/-

Amount F – Difference (A – E):

49,357/-

Quantity received as per PO /WO	☐ Yes ☐ Excess received ☒ Short received ☐ Other (explained below)
Is difference between PO / Bill acceptable?	☒ Yes ☐ No (explained below)
Excess / short material received	☒ Approved – within acceptable limits ☐ No (explained below)
Close PO / W?O	☒ Yes ☐ No – wait for balance material ☐ No (explained below)
Advance paid / PDC given (deduct when paying)	☐ Yes – Rs. _____/- ☒ No
Payment – due date	07/10/2021

Remarks: PO to close 12 cu/mtr qty loss received & shortage material for 3,215 kg.

Approved by	Purchase Officer	Purchase Manager	Procurement Manager	M D	Accounts – register of bill	Accountant	Accounts Manager
Sign:				APPROVED BY			
Date			28/9/21	28 SEP 2021			
				SOHAM MODI			

Notes: 1. In case amount to be credited to supplier and the bills total does not match prepare JV for debit or credit. 2. Attach additional sheets if quantity of bills or DCs is more than the space provided. Clearly mark the space provided with 'see attachment'. 3. Purchase Officer can approve Pos/Wos upto Rs. 5,000/-, Purchase Manager and Procurement Manager to approve all bills from 5,000/- to 1,00,000/- . 4. Attach JV, Office copy of PO/WO, DCs and bills to this advice. 5. In Amount A, exclude

shortage of material

Subject: shortage of material

From: minish <minish@modiproperties.com>

Date: 28-09-2021, 12:12 PM

To: slrmcplant@gmail.com

To,

Mr Venkatesh,

SL RMC Plant,

Dear Sir,

We recieved short material againstn your Invoice No 158 Dt 07/09/21 for 3,215 kgs. Against our PO No 79892 Dt 04/09/21, we are deducting Rs 4,957/-for the same.

Please Note.

--

Regards,

Minish Parikh

Manager-Procurement | +91 95155 46784 | minish@modiproperties.com

Modi Properties Pvt. Ltd. | www.modiproperties.com

5-4-187/ 3 & 4, M G Road, Secunderabad - 03 | +91 40 66335551

Don't just buy a flat or villa! Buy a great lifestyle!

We build affordable flats & villas in gated communities.


28/09/21



SL RMC PLANT

READY-MIX CONCRETE

Tax Invoice

SI Rmc Plant Sy No719/2 Devaryamjal (Village) Shameerpet (M) Medchal(D) Gstin:36ADNFS2288J1ZF GSTIN/UIN: 36ADNFS2288J1ZF State Name : Telangana, Code : 36 E-Mail : slrmcplant@gmail.com Buyer Mehta & Modi Realty Kowkur LLP 5-4-187/3&4, II nd floor, MG Road, Soham Mansion, Secunderabad-500003 GSTIN/UIN : 36ABLFM7631F1Z3 State Name : Telangana, Code : 36	Invoice No.	Dated
	158	7-Sep-2021
	Supplier's Ref.	Mode/Terms of Payment
	79892	Other Reference(s)
Buyer's Order No.	Dated	
	Terms of Delivery	

SI No.	Description of Goods	HSN/SAC	Part No.	Quantity	Rate	per	Amount
1	M20	38245010		53.00 cbm	3,135.59	cbm	1,66,186.27
	Output CGST @9 %					9 %	14,956.76
	Output SGST @9%					9 %	14,956.76
	Round Off						0.21
Total				53.00 cbm			₹ 1,96,100.00

Amount Chargeable (in words)

E. & O.E

INR One Lakh Ninety Six Thousand One Hundred Only

HSN/SAC	Taxable Value	Central Tax		State Tax		Total Tax Amount
		Rate	Amount	Rate	Amount	
38245010	1,66,186.27	9%	14,956.76	9%	14,956.76	29,913.52
Total	1,66,186.27		14,956.76		14,956.76	29,913.52

Tax Amount (in words) : **INR Twenty Nine Thousand Nine Hundred Thirteen and Fifty Two paise Only**

Remarks:
04.09.2021

Declaration

We declare that this invoice shows the actual price of the goods described and that all particulars are true and correct.

Company's Bank Details

Bank Name : Lakshmi Vilas Bank

A/c No. : 0136360000001393

Branch & IFS Code : As Rao Nagar & LAVB0000136

Customer's Seal and Signature



This is a Computer Generated Invoice



Purchase Order

Page(s) 1 Of 2

04-09-2021 10:04:01 AM

Original / Office Copy / Purchase Div.Copy

From Company : **Mehta & Modi Realty Kowkur LLP**
5-4-187/3&4, II nd floor, MG Road, Soham Mansion, Secunderabad-500003
G S T No. : 36ABLFM7631F1Z3

Supplier Details

SL RMC PLANT

Sy.No.719/2,Devaryamjal Shameerpet,Medchal.

7207255678

Doc No	79892	140731
Doc Date	04-09-2021	
Quote No	NIL	
Quote Date	23-08-2021	
SupplyType	Supply	

Kind Attn : MR P. VENKATESHWARA RAO

Purchase Order for the Supply of following Items.

Item Name	Qty	Rate	Dis%	GST%	Amount
1 1013 - Building material - Ready Mix Concrete - NA - cu. mtrs. M-20	65.00	3,700.00	0.00	0.00	240,500.00
Total Order Value . . .					240,500.00

Rupees : Two Lakh(s) Fourty Thousand Five Hundred Only.

Terms and Conditions :-

Specification / Brand	All items shall be of ___ brand/company
Payment Terms	Within 30 days of delivery.
Tax	All taxes included in above price.
Delivery Date	Next Working Day.
Delivery Location	Greenwood Heights Sy no: 196, Kowkur. Phone: 040-66335551
Penalty For Delay	Nil
Transportation Cost	Included in the above price.
Warranty	Nil
Advance Paid	NIL
Other Terms	Payment as per actual receipt of material.Above Order for site perpural CC road&south centre gate inside area CC road laying work purpose.
Completion Date	NA
Measurment	Nil
Security	Nil
Remarks	Delivery at GHT Kowkur Contact Person Mr Suresh-9502232100.

3,215 x 3,700 = 4957/-
2,400
28/9/21

For **Mehta & Modi Realty Kowkur LLP**

Authorised Signatory

Name :

04/09/2021

Name :

Accepted the above Terms And Conditions

For **SL RMC PLANT**

Date : _/_/

Subject: cancellation

From: minish <minish@modiproperties.com>

Date: 04-09-2021, 9:42 AM

To: asuresh@modiproperties.com, taigareadymix@gmail.com

To,

Mr Dileep Narayan,

Taiga Readymix,

Dear Sir,

We are cancelling the PO No 79892 Dt 23/08/2021 for M-20 RMC, as you are unable to deliver the material on time, this is for Information.

Please Note.

--

Regards,

Minish Parikh

Manager-Procurement | +91 95155 46784 | minish@modiproperties.com

Modi Properties Pvt. Ltd. | www.modiproperties.com

5-4-187/ 3 & 4, M G Road, Secunderabad - 03 | +91 40 66335551

Don't just buy a flat or villa! Buy a great lifestyle!

We build affordable flats & villas in gated communities.

Purchase Order

Page(s) 1 Of 1

23-08-2021 10:04:35 AM

Origin:



79892

13.08.21 2:25:58

From Company : **Mehta & Modi Realty Kowkur LLP**
5-4-187/3&4, II nd floor, MG Road, Soham Mansion, Secunderabad-500003
G S T No. : 36ABLFM7631F1Z3

Cancelled.

Supplier Details

Taiga Readymix
Medchal Pudoor Village, sy nos, 618/A Pudoor, Medchal
Mandal, Medchal, Malkajgiri Dist-Pincode-501401

7331166966

8019671079

Doc No	79892	140731
Doc Date	23-08-2021	
Quote No	NIL	
Quote Date	23-08-2021	
SupplyType	Supply	

Kind Attn : J.Dileep Narayan

Purchase Order for the Supply of following Items.

Item Name	Qty	Rate	Dis%	GST%	Amount
1 1013 - Building material - Ready Mix Concrete - MA - cu. mtrs. M-20	65.00	3,700.00	0.00	0.00	240,500.00
Total Order Value . . .					240,500.00

Rupees : Two Lakh(s) Fourty Thousand Five Hundred Only.

Terms and Conditions :-

Specification / Brand All items shall be of brand/company**Payment Terms** Within 30 days of delivery.**Tax** All taxes included in above price.**Delivery Date** Next Working Day.**Delivery Location** Greenwood Heights

Sy no: 196, Kowkur.

Phone. 040-66335551

Penalty For Delay Nil**Transportation Cost** Included in the above price.**Warranty** Nil**Advance Paid** NIL**Other Terms** Payment as per actual receipt of material. Above Order for site perpurat CC road & south centre gate inside area CC road laying work purpose.**Completion Date** NA**Measurment** Nil**Security** Nil**Remarks** Delivery at GHT Kowkur Contact Person Mr Suresh-9502232100.

For MDs APPROVAL

- ☒ High Value/quantity beyond limits.
- ☒ Po/Req. processed-post approval.
- ☐ Approval for technical details/clarification
- ☐ Replenishing SSSLP stock
- ☐ Other

For **Mehta & Modi Realty Kowkur LLP**

Authorised Signatory

Accepted the above Terms And Conditions

For **Taiga Readymix**Name : 23/08/2021

Name : _____

Date : __/__/__

1136

Requisition Form

Company Name:		MMR Kowkur llp		Date:		19-08-2021	
Site & Phase :		GHT		Time:		11.00	
Supplier				Req. No.		140731	
Material required before date:			23-08-2021		ID No.		68579

No	Description	Size	Quantity	Units	Inward No	Date
1	RMC	M 20 Grade	65	Cubic meter	3,700/	
2						
3						
4						
5						
6						
7						
8						
9						
10						

Remarks: - For GHT Site Perpural CC Road & South Center gate inside area CC Road laying work Purpose

Sign. & Date		A Suresh		Approved by			
		19-08-2021		Sign. & Date			

Note: On receipt of material at site write inward number and date in last 2 columns.




RMC pour report

Company/ firm:	MMRKLLP	Project:	GHT	A. Estimated quantity:	65 Cu Mtrs
Flat / Villa no.:	Peripheral Road	Block No.:	B-Block	B. Requisition quantity:	65 Cu Mtrs
Slab no.:	MAIN ROAD	PO Nos.	79892	C. Actual quantity poured:	54 cum
Requisition nos.:	140731	Supplier:	SL RMC Plant	D. Difference (C-A):	11 Cu-mtrs
Sign of security		Sign of Admin		Sign of Project manager	
Date	06-09-2021	Date	06-09-2021	Date	06-09-2021

Details of RMC pour

Sl. No	Date	Time	Quantity poured	Dc No. / Batch no.	Specified weight (@ 2,400 kgs per meter cube	Measured weight (kgs)	Short fall in weight in kgs	Inward no.	MRN No.
1.	04-09-2021	10:29	6cum	1898	14400kgs	13410	✓ 990kgs	11467	95638
2.	04-09-2021	11:48	6cum	1899	14400kgs	13960	✓ 440kgs	11469	95639
3.	04-09-2021	13:31	6cum	1906	14400kgs	13855	✓ 545kgs	11470	95690
4.	04-09-2021	14:46	6cum	1910	14400kgs	13810	✓ 590kgs	11471	95689
5.	04-09-2021	16:21	6cum	1915	14400kgs	13750	✓ 650kgs	11472	95687
6.	04-09-2021	16:25	6cum	1916	14400kgs	13165	1235kgs	11474	95988
7.	04-09-2021	16:50	7cum	1917	16800kgs	16450	350kgs	11475	95989
8.	04-09-2021	19:05	6cum	1922	14400kgs	14410	390kgs	11476	95990
9.	04-09-2021	21:05	5cum	1924	12000kgs	11600	400kgs	11477	95991
10.									
11.									
Total:			54cum		1,29,600kgs	1,24,410Kgs	5590Kgs		
Remarks:	67 SEP 2021								

Note: 1. Report to be sent on completion of each slab or footing for a block or villa. 2. Report must be sent within one working day with relevant documents attached. 3. Weigh all vehicles. 4. 6 m cu vehicles weight less than 14,100 kgs - deduct amount in bill. 5. Calculate short fall in weight. 6. If short fall is more than 10% of specified weight, write shortfall as Nil. 6. Ensure that relevant totals are entered.





SL RMC PLANT
READY-MIX CONCRETE

DELIVERY CHALLAN

Plot No. 26, S.S. Villas,
Markandeya Nagar, Kapra,
Hyderabad,
Telangana - 500 062.

D.C. No. : 1898

To, M/s. GREEN WOOD HEIGHTS.

Date : 4/9/21.


Vehicle No. : TS 08 UE 8893.

S.No.	Grade	PARTICULARS	Qty.	Cum.	Value
1	M20	TIME: 9:45 AM INWARD Inward No: 11467 Dt: 04/08/21 MRN No: 95983 Dt: 6/9/21 Received By: Sign:  MEHTA & MODI REALTY CORPORATION LLP	6m ³	6m ³	Dump.

For **SL RMC PLANT**

Receiver's Signature

10.29


Authorised Signatory



SRI VENKATESWARA WEIGH BRIDGE

Sy.No. 1, Plot No. 8, Yapral Village, Alwal Mandal
Medchal Dist. Telangana State.

24
HOURS
SERVICE

FULLY ELECTRONIC & COMPUTERISED 80 TONNE WEIGH BRIDGE

SERIAL No. : 3111	VEHICLE No. : TS08UE 8893
GROSS : 25510 Kg.	DATE: 04/09/2021 TIME: 10:29
TARE : 12100 Kg.	DATE: 04/09/2021 TIME: 11:54
NETT : 13410 Kg.	

150/-

Party's Signature

Weighment Charges

Operator's Signature

* Our responsibility ceases once the vehicle leaves the platform.
వాహనము ప్లాట్ ఫారం విడిచిన తర్వాత మా బాధ్యత లేదు.



Schwing Stetter
MCI 360 Control System

STETTER

Autographic / Batch Report / Delivery Note

Batch Date	4-Sep-21	Plant Serial No	M1-25
Batch time	9:40	Batch End Time	9:48
		Batcher Name	STETTER
Batch No	12281	Truck Driver	***
Customer	GREEN WOOD HEIGHTS	Production Qty:	6.00
Site address	KAIWKOOR	Returned Qty:	0.00
Recipe Code	M20 GREEN WOOD HEIGHTS	Total Ordered Qty:	0.00
Recipe Name	M20 GREEN WOOD HEIGHTS	With This Load	6.00
Truck No	TS 08 UE 8893	Batch Size:	1.00

	SAND	SAND	12MM	20MM	Agg5	Agg6	Cem1	Cem2	Cem3	Cem4	Cem5	Water	Ice	Slurry	Silice	Admix1	Admix1 2	Admix2	Admix2 2
Recipe	0	800	440	670	0	0	250	70	0	0	0	165	0	0	0	2.50	0.0	0.0	0.0
Target	0	800	440	670	0	0	250	70	0	0	0	165	0	0	0	2.50	0.0	0.0	0.0
9:41	0	800	440	670	0	0	250	70	0	0	0	165	0	0	0	2.50	0.0	0.0	0.0
9:42	0	801	441	669	0	0	251	72	0	0	0	166	0	0	0	2.50	0.0	0.0	0.0
9:43	0	800	440	670	0	0	250	70	0	0	0	165	0	0	0	2.51	0.0	0.0	0.0
9:45	0	802	442	672	0	0	252	71	0	0	0	167	0	0	0	2.50	0.0	0.0	0.0
9:46	0	800	440	670	0	0	250	70	0	0	0	165	0	0	0	2.52	0.0	0.0	0.0
9:47	0	801	441	671	0	0	251	72	0	0	0	166	0	0	0	2.50	0.0	0.0	0.0

Total

Act	0	4804	2644	4022	0	0	1504	425	0	0	0	994	0	0	0	15.03	0	0	0
Tar	0	4800	2640	4020	0	0	1500	420	0	0	0	990	0	0	0	15	0	0	0

Moisture Corection & Other Component Corection

G1Moi	G2Moi	G3Moi	G4Moi	G5Moi	G6Moi	C1 cor	C1 cor	C3.co	C4 cor	C5.co	W1 Cor	W2	Si Cor	Adm11	Adm12 c	Adm21	Adm22 c
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0

INWARD	
Inward No: 11467	Dr: 6/10/21
MRN No: 95983	Dr: 6/11/21
Received By:	Sign:
MENTA & MODI REALTY KOWKUR LLP	



SL RMC PLANT
READY-MIX CONCRETE

DELIVERY CHALLAN

Plot No. 26, S.S. Villas,
Markandeya Nagar, Kapra,
Hyderabad,
Telangana - 500 062.

D.C. No. : 1899

Date : 4/9/21

To, GREEN WOOD HEIGHTS

KOWKUR

Vehicle No. : TS 08UE 7860

S.No.	Grade	PARTICULARS	Qty.	Cum.	Value
2	M20	TIME : 10:10 AM,	6M ³	12M ³	DUMP.

INWARD	
Inward No: 17469	Di: 04/09/21
MRN No: 95986	Di: 8/9/21
Received By:	Sign: [Signature]
MEHTA & MODI REALTY KOWKUR LLP	

Receiver's Signature

For **SL RMC PLANT**

[Signature]
Authorised Signatory



SRI VENKATESWARA WEIGH BRIDGE

Sy.No. 1, Plot No. 8, Yapral Village, Alwal Mandal
Medchal Dist. Telangana State.

24
HOURS
SERVICE

FULLY ELECTRONIC & COMPUTERISED 80 TONNE WEIGH BRIDGE

SERIAL No. : 3113

VEHICLE No.: TS08UE 7860

GROSS : 25625 kg.

DATE: 04/09/2021 TIME: 11:48

TARE : 11665 kg.

DATE: 04/09/2021 TIME: 12:45

NETT : 13960 kg.

Party's Signature

Weighment Charges

Operator's Signature

* Our responsibility ceases once the vehicle leaves the platform.
వాహనము ప్లాట్ ఫారం విడిచిన తర్వాత మా బాధ్యత లేదు.

Inward No: 17469



Schwing stetter
MCI 360 Control System

STETTER

Autographic / Batch Report / Delivery Note

Batch Date 4-Sep-21

Plant Serial No M1-25

Batch time 10:07

Batch End Time: 10:15

Batcher Name STETTER

Batch No: 12282

Truck Driver ***

Customer: GREEN WOOD HEIGHTS

Production Qty: 6.00

Site address: KAWKOOR

Returned Qty: 0.00

Recipe Code: M20 GREEN WOOD HEIGHTS

Total Ordered Qty: 0.00

Recipe Name M20 GREEN WOOD HEIGHTS

With This Load 12.00

Truck No TS 08 UE 7860

Batch Size 1.00

	SAND1	SAND2	12MM	20MM	Agg5	Agg6	Cem1	Cem2	Cem3	Cem4	Cem5	Water	Ice	Slurry	Silice	Admix1	Admix1 2	Admix2	Admix2 2
Recipe	0	800	440	670	0	0	250	70	0	0	0	165	0	0	0	2.50	0.0	0.0	0.0
Target	0	800	440	670	0	0	250	70	0	0	0	165	0	0	0	2.50	0.0	0.0	0.0
10:08	0	802	442	670	0	0	252	70	0	0	0	165	0	0	0	2.50	0.0	0.0	0.0
10:09	0	801	441	672	0	0	251	72	0	0	0	166	0	0	0	2.50	0.0	0.0	0.0
10:10	0	800	440	670	0	0	250	70	0	0	0	165	0	0	0	2.51	0.0	0.0	0.0
10:12	0	801	441	672	0	0	252	71	0	0	0	167	0	0	0	2.50	0.0	0.0	0.0
10:13	0	800	440	670	0	0	250	70	0	0	0	165	0	0	0	2.51	0.0	0.0	0.0
10:14	0	802	439	672	0	0	250	69	0	0	0	166	0	0	0	2.51	0.0	0.0	0.0

Total

Act	0	4806	2643	4026	0	0	1505	422	0	0	0	994	0	0	0	15.03	0	0	0
Tar	0	4800	2640	4020	0	0	1500	420	0	0	0	990	0	0	0	15	0	0	0

Moisture Corection & Other Component Corection

G1Moi	G2Moi	G3Moi	G4Moi	G5Moi	G6Moi	C1.cor	C1.cor	C3.cor	C4.cor	C5.cor	W1 Cor	W2	Si Cor	Adm11.c	Adm12.c	Adm21.c	Adm22.c
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0

INWARD	
Inward No: 11469	Dr: 04/09/21
MRN No: 95994	Dr: 06/09/21
Received By:	Sign:
MEHTA & MODI REALTY KOWKUR LLP	



SL RMC PLANT
READY-MIX CONCRETE

DELIVERY CHALLAN

Plot No. 26, S.S. Villas,
Markandeya Nagar, Kapra,
Hyderabad,
Telangana - 500 062.


D.C. No. : 1906

To, Green wood Heights

Date : 4/9/2021

M/s. kawkoor.

Vehicle No. : TS 08 UE 8893

S.No.	Grade	PARTICULARS	Qty.	Cum.	Value
3	M20	Time :- 12:35	6 M ³	18 M ³	Dump.
INWARD Inward No. 11470 Dt: 04/09/21 Inward No. 95985 Dt: 6/9/21 Received By:  13:31 For SL RMC PLANT Mandali Authorised Signatory					
Receiver's Signature					



SRI VENKATESWARA WEIGH BRIDGE

Sy.No. 1, Plot No. 8, Yaprall Village, Alwal Mandal
Medchal Dist. Telangana State.

24
HOURS
SERVICE

FULLY ELECTRONIC & COMPUTERISED 80 TONNE WEIGH BRIDGE

SERIAL No. 3115	VEHICLE No.: TS08UE 8893
GROSS 25460 Kg.	DATE: 04/09/2021 TIME: 13:31
TARE 11605 Kg.	DATE: 04/09/2021 TIME: 14:41
NETT 13855 Kg.	
150/- Party's Signature	Weighment Charges
	Operator's Signature

* Our responsibility ceases once the vehicle leaves the platform.
వాహనము ప్లాట్ ఫారం విడిచిన తర్వాత మా బాధ్యత లేదు.

STETTER

Autographic / Batch Report / Delivery Note

Batch Date	4 Sep-21	Plant Serial No	M1-25
Batch time	12:35	Batch End Time	12:43
		Batcher Name	STETTER
Batch No	12289	Truck Driver	***
Customer	GREEN WOOD HEIGHTS	Production Qty	6.00
Site address	KAWKOOR	Returned Qty	0.00
Recipe Code	M20 GREEN WOOD HEIGHTS	Total Ordered Qty	0.00
Recipe Name	M20 GREEN WOOD HEIGHTS	With This Load	18.00
Truck No	TS 08 UE 8893	Batch Size	1.00

	SAND1	SAND2	12MM	20MM	Agg5	Agg6	Cem1	Cem2	Cem3	Cem4	Cem5	Water	Ice	Slurry	Silice	Admix1	Admix1.2	Admix2	Admix2.2
Recipe	0	800	440	670	0	0	250	70	0	0	0	165	0	0	0	2.50	0.0	0.0	0.0
Target	0	800	440	670	0	0	250	70	0	0	0	165	0	0	0	2.50	0.0	0.0	0.0
12:36	0	800	440	670	0	0	250	70	0	0	0	167	0	0	0	2.50	0.0	0.0	0.0
12:37	0	801	441	669	0	0	251	71	0	0	0	166	0	0	0	2.51	0.0	0.0	0.0
12:38	0	799	440	670	0	0	250	70	0	0	0	165	0	0	0	2.51	0.0	0.0	0.0
12:40	0	801	441	672	0	0	252	71	0	0	0	167	0	0	0	2.50	0.0	0.0	0.0
12:41	0	800	440	670	0	0	251	70	0	0	0	165	0	0	0	2.51	0.0	0.0	0.0
12:42	0	801	439	671	0	0	250	72	0	0	0	164	0	0	0	2.51	0.0	0.0	0.0
Total																			
Act	0	4802	2641	4022	0	0	1504	424	0	0	0	994	0	0	0	15.04	0	0	0
Tar	0	4800	2640	4020	0	0	1500	420	0	0	0	990	0	0	0	15	0	0	0

Moisture Correction & Other Component Correction

G1Moi	G2Moi	G3Moi	G4Moi	G5Moi	G6Moi	C1.cor	C1.cor	C3.cor	C4.cor	C5.cor	W1 Cor	W2	Si Cor	Adm11.c	Adm12.c	Adm21.c	Adm22.c
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0





SL RMC PLANT
READY-MIX CONCRETE

DELIVERY CHALLAN

Plot No. 26, S.S. Villas,
Markandeya Nagar, Kapra,
Hyderabad,
Telangana - 500 062.

D.C. No.: 1910

To, Green wood Heights

M/s. Kawleer

Date: 4/9/2021

Vehicle No.: TS08 UE 8894

S.No.	Grade	PARTICULARS	Qty.	Cum.	Value
4	M20	Time: 13:35	6 M3	24 M3	puwf.
INWARD Inward No: <u>7471</u> Dt: <u>04/09/21</u> MRN No: <u>95996</u> Dt: <u>04/09/21</u> Received By: <u>[Signature]</u> Sign: <u>[Signature]</u> MEHTA & MODI REALTY KOWKUR LLP					

For **SL RMC PLANT**
Manoj

Authorised Signatory



SRI VENKATESWARA WEIGH BRIDGE

Sy.No. 1, Plot No. 8, Yaprak Village, Alwal Mandal
Medchal Dist. Telangana State.



FULLY ELECTRONIC & COMPUTERISED 80 TONNE WEIGH BRIDGE

3119 SERIAL No.:		TS08UE 8894 VEHICLE No.:	
GROSS : 25210	Kg.	DATE: 04/09/2021	TIME: 14:46
TARE : 11400	Kg.	DATE: 04/09/2021	TIME: 15:39
NETT : 13810	Kg.		
150/-			
Party's Signature		Operator's Signature	

* Our responsibility ceases once the vehicle leaves the platform.
వాహనము ప్లాట్ ఫారం విడిచిన తర్వాత మా బాధ్యత లేదు.

STETTER

Autographic / Batch Report / Delivery Note

Batch Date 4-Sep-21
Batch time 13:35

Plant Serial No M1-25
Batch End Time: 13:43
Batcher Name STETTER

Batch No 12293

Truck Driver ***

Customer: GREEN WOOD HEIGHTS

Production Qty: 6.00

Site address KAWKOOR

Returned Qty: 0.00

Recipe Code M20 GREEN WOOD HEIGHTS

Total Ordered Qty: 0.00

Recipe Name M20 GREEN WOOD HEIGHTS

With This Load 24.00

Truck No TS 08 UE 8894

Batch Size : 1.00


	SAND1	SAND2	12MM	20MM	Agg5	Agg6	Cem1	Cem2	Cem3	Cem4	Cem5	Water	Ice	Slurry	Silice	Admix1	Admix1.2	Admix2	Admix2.2
Recipe	0	800	440	670	0	0	250	70	0	0	0	165	0	0	0	2.50	0.0	0.0	0.0
Target	0	800	440	670	0	0	250	70	0	0	0	165	0	0	0	2.50	0.0	0.0	0.0
13:36	0	802	440	670	0	0	250	70	0	0	0	165	0	0	0	2.51	0.0	0.0	0.0
13:37	0	801	442	671	0	0	252	71	0	0	0	166	0	0	0	2.50	0.0	0.0	0.0
13:38	0	800	440	670	0	0	250	70	0	0	0	165	0	0	0	2.51	0.0	0.0	0.0
13:40	0	803	442	672	0	0	252	71	0	0	0	166	0	0	0	2.50	0.0	0.0	0.0
13:41	0	800	440	670	0	0	250	70	0	0	0	165	0	0	0	2.52	0.0	0.0	0.0
13:42	0	800	442	671	0	0	252	71	0	0	0	166	0	0	0	2.50	0.0	0.0	0.0

Total

Act	0	4806	2646	4024	0	0	1506	423	0	0	0	993	0	0	0	15.04	0	0	0
Tar	0	4800	2640	4020	0	0	1500	420	0	0	0	990	0	0	0	15	0	0	0

Moisture Correction & Other Component Correction

G1Moi	G2Moi	G3Moi	G4Moi	G5Moi	G6Moi	C1.cor	C1.cor	C3.cor	C4.cor	C5.cor	W1 Cor	W2	Si Cor	Adm11.c	Adm12.c	Adm21.c	Adm22.c
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0

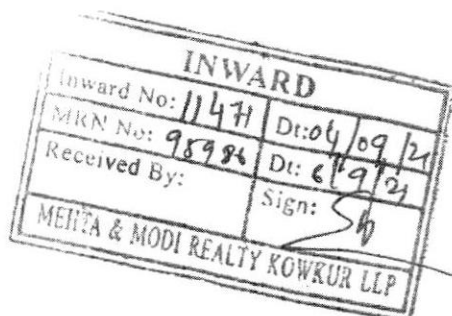



SL RMC PLANT
READY-MIX CONCRETE

DELIVERY CHALLAN

Plot No. 26, S.S. Villas,
Markandeya Nagar, Kapra,
Hyderabad,
Telangana - 500 062.

D.C. No.: 1915

Date: 4/9/2021

To, Green wood heights

kawkoor.

Vehicle No.: TS08 UE 7859

pono: 79892-140731

S.No.	Grade	PARTICULARS	Qty.	Cum.	Value
5	M20	Time: 15:30	6 M3	30 M3	Dump
INWARD Inward No: 11472 Dt: 04/09/21 Vehicle No: 95988 Dt: 6/9/21 Received By: Sign: RENTA & MODI REALTY KONGUR LLP For SL RMC PLANT Manoj Receiver's Signature Authorised Signatory					



SRI VENKATESWARA WEIGH BRIDGE

Sy.No. 1, Plot No. 8, Yaprail Village, Alwal Mandal
Medchal Dist. Telangana State.

24
HOURS
SERVICE

FULLY ELECTRONIC & COMPUTERISED 80 TONNE WEIGH BRIDGE

SERIAL No: 3120	VEHICLE No.: TS08UE 7859
GROSS 25450 Kg.	DATE: 04/09/2021 TIME: 16:21
TARE 11700 Kg.	DATE: 04/09/2021 TIME: 17:57
NETT 13750 Kg.	

150/-
Party's Signature

Weighment Charges

Operator's Signature

* Our responsibility ceases once the vehicle leaves the platform.

వాహనము ప్లాట్ ఫారం విడిచిన తర్వాత మా బాధ్యత లేదు.

STETTER

Autographic / Batch Report / Delivery Note

Batch Date	4-Sep-21	Plant Serial No	M1-25
Batch time	15:25	Batch End Time:	15:33
		Batcher Name	STETTER
Batch No :	12300	Truck Driver	***
Customer:	GREEN WOOD HEIGHTS	Production Qty:	6.00
Site address:	KAWKOOR	Returned Qty:	0.00
Recipe Code :	M20 GREEN WOOD HEIGHTS	Total Ordered Qty:	0.00
Recipe Name	M20 GREEN WOOD HEIGHTS	With This Load	30.00
Truck	TS 08 UE 7859	Batch Size :	1.00

	SAND1	SAND2	12MM	20MM	Agg5	Agg6	Cem1	Cem2	Cem3	Cem4	Cem5	Water	Ice	Slurry	Silice	Admix1	Admix1.2	Admix2	Admix2.2
Recipe	0	800	440	670	0	0	250	70	0	0	0	165	0	0	0	2.50	0.0	0.0	0.0
Target	0	800	440	670	0	0	250	70	0	0	0	165	0	0	0	2.50	0.0	0.0	0.0
15:26	0	801	442	670	0	0	252	72	0	0	0	165	0	0	0	2.50	0.0	0.0	0.0
15:27	0	801	441	671	0	0	251	71	0	0	0	166	0	0	0	2.51	0.0	0.0	0.0
15:28	0	802	440	670	0	0	250	70	0	0	0	165	0	0	0	2.52	0.0	0.0	0.0
15:30	0	801	441	672	0	0	252	71	0	0	0	167	0	0	0	2.50	0.0	0.0	0.0
15:31	0	800	440	670	0	0	251	70	0	0	0	165	0	0	0	2.51	0.0	0.0	0.0
15:32	0	802	441	672	0	0	253	69	0	0	0	166	0	0	0	2.52	0.0	0.0	0.0

Total

Act	0	4807	2645	4025	0	0	1509	423	0	0	0	994	0	0	0	15.06	0	0	0
Tar	0	4800	2640	4020	0	0	1500	420	0	0	0	990	0	0	0	15	0	0	0

Moisture Corection & Other Component Corection

G1Moi	G2Moi	G3Moi	G4Moi	G5Moi	G6Moi	C1 cor	C1 cor	C3 cor	C4 cor	C5 cor	W1 Cor	W2	Si Cor	Adm11 c	Adm12 c	Adm21 c	Adm22 c
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0

INWARD	
Inward No: 11472	Di: 04/09/21
MRN No: 95998	Di: 06/09/21
Received By:	Sign:
MEHTA & MOUJI REAL ESTATE LLP	



SL RMC PLANT
READY-MIX CONCRETE

DELIVERY CHALLAN

Plot No. 26, S.S. Villas,
Markandeya Nagar, Kapra,
Hyderabad,
Telangana - 500 062.

D.C. No.: **1918**

Date: **4/9/2021**

To, **Green wood Heights**

M/s. **Kowkoot**

Vehicle No.: **TS08 UE 8893** pono: **79892-140731**

S.No.	Grade	PARTICULARS	Qty.	Cum.	Value
		6 M² Time:- 15:40	6 M³	36 M³	Dump.

INWARD

Inward No: **11474** Dt: **04/09/21**

MRN No: **95987** Dt: **6/9/21**

Received By: **SB** Sign: **SB**

MERTA & MODI REALTY KOWKOOT LLP

For **SL RMC PLANT**
Manchay

Receiver's Signature

Authorised Signatory



SRI VENKATESWARA WEIGH BRIDGE

Sy.No. 1, Plot No. 8, Yaprail Village, Alwal Mandal
Medchal Dist. Telangana State.

24 HOURS SERVICE

FULLY ELECTRONIC & COMPUTERISED 80 TONNE WEIGH BRIDGE

SERIAL No.: 3122	VEHICLE No.: TS08UE 8893
GROSS 25265 Kg.	DATE: 04/09/2021 TIME: 16:25
TARE 12100 Kg.	DATE: 04/09/2021 TIME: 17:53
NETT 13165 Kg.	

150/-

Party's Signature

Weighment Charges

Operator's Signature

* Our responsibility ceases once the vehicle leaves the platform.
వాహనము ప్లాట్ ఫారం విడిచిన తర్వాత మా బాధ్యత లేదు.

MRN No: **95987** Dt: **04/09/21**

Received By: **SB** Sign: **SB**

MERTA & MODI REALTY KOWKOOT LLP

STETTER

Autographic / Batch Report / Delivery Note

Batch Date 4-Sep-21 Plant Serial No M1-25
Batch time 15:35 Batch End Time 15:43
Batcher Name STETTER

Batch No 12301 Truck Driver ***
Customer GREEN WOOD HEIGHTS Production Qty 6.00
Site address KAWKOOR Returned Qty 0.00
Recipe Code M20 GREEN WOOD HEIGHTS Total Ordered Qty 0.00
Recipe Name M20 GREEN WOOD HEIGHTS With This Load 36.00
Batch Size 1.00

Recipe	Target	SAND1	SAND2	12MM	20MM	Agg5	Agg6	Cem1	Cem2	Cem3	Cem4	Cem5	Water	Ice	Slurry	Silice	Admix1	Admix2	Admix2.2
Recipe	0	300	440	670	0	0	0	250	70	0	0	0	165	0	0	0	2.50	0.0	0.0
Target	0	800	440	670	0	0	0	250	70	0	0	0	165	0	0	0	2.50	0.0	0.0
15.36	0	801	439	669	0	0	0	250	70	0	0	0	165	0	0	0	2.52	0.0	0.0
15.37	0	800	441	671	0	0	0	251	71	0	0	0	166	0	0	0	2.51	0.0	0.0
15.38	0	802	440	670	0	0	0	250	70	0	0	0	165	0	0	0	2.52	0.0	0.0
15.40	0	801	441	672	0	0	0	252	71	0	0	0	164	0	0	0	2.50	0.0	0.0
15.41	0	800	440	670	0	0	0	251	70	0	0	0	165	0	0	0	2.51	0.0	0.0
15.42	0	801	440	669	0	0	0	250	72	0	0	0	166	0	0	0	2.52	0.0	0.0
Total	0	4805	2641	4021	0	0	0	1504	424	0	0	0	991	0	0	0	15.08	0	0
Act	0	4800	2640	4020	0	0	0	1500	420	0	0	0	990	0	0	0	15	0	0
Tar	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0

Moisture Correction & Other Component Correction

G1Mol G2Mol	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
G3Mol G4Mol	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
G5Mol G6Mol	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
C1.corr	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
C3.corr	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
C4.corr	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
C5.corr	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
W1 Cor	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
W2 Si Cor	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
Admix1	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
Admix12.c	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
Admix21.c	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
Admix22.c	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0


INWARD

Forward No: 11424 Date: 04/09/21

MKN No: 9598 Date: 04/09/21

Received By: Sign: 58

MEHTA & MODI REALTY KOWKUR LLP



SL RMC PLANT
READY-MIX CONCRETE

DELIVERY CHALLAN

Plot No. 26, S.S. Villas,
Markandeya Nagar, Kapra,
Hyderabad,
Telangana - 500 062.

D.C. No. : **1917**

Date : **4/9/2021**

To,
M/s.

Green wood Heights

Kowkoo

Vehicle No. :

TS 08 UE 8894

pono. : **79892-140731**

S.No.	Grade	PARTICULARS	Qty.	Cum.	Value
7	M20	Time :- 16:50	7 M ³	42 M ³	Dump.

INWARD	
Inward No: 11475	Di: 04/09/21
No. of Nos: 95981	Di: 6/9/21
Received By:	Sign:
MEHTA & MODI REALTY KOWKUR LLP	

Receiver's Signature

For **SL RMC PLANT**
Manch

Authorised Signatory

STETTER

Autographic / Batch Report / Delivery Note

Batch Date	4-Sep-21	Plant Serial No	M1-25
Batch time	16:47	Batch End Time:	16:55
		Batcher Name	STETTER
Batch No.	12303	Truck Driver	***
Customer	GREEN WOOD HEIGHTS	Production Qty:	6.00
Site address:	KAWKOOR	Returned Qty:	0.00
Recipe Code	M20 GREEN WOOD HEIGHTS	Total Ordered Qty:	0.00
Recipe Name	M20 GREEN WOOD HEIGHTS	With This Load	42.00
TS No	TS 08 UE 8894	Batch Size :	1.00


	SAND1	SAND2	12MM	20MM	Agg5	Agg6	Cem1	Cem2	Cem3	Cem4	Cem5	Water	Ice	Slurry	Silice	Admix1	Admix1.2	Admix2	Admix2.2
Recipe	0	800	440	670	0	0	250	70	0	0	0	165	0	0	0	2.50	0.0	0.0	0.0
Target	0	800	440	670	0	0	250	70	0	0	0	165	0	0	0	2.50	0.0	0.0	0.0
16:48	0	802	441	672	0	0	252	72	0	0	0	167	0	0	0	2.50	0.0	0.0	0.0
16:49	0	800	441	671	0	0	251	71	0	0	0	166	0	0	0	2.51	0.0	0.0	0.0
16:50	0	802	440	670	0	0	250	70	0	0	0	165	0	0	0	2.52	0.0	0.0	0.0
16:52	0	801	441	672	0	0	252	71	0	0	0	164	0	0	0	2.50	0.0	0.0	0.0
16:53	0	800	442	670	0	0	251	70	0	0	0	165	0	0	0	2.51	0.0	0.0	0.0
16:54	0	802	440	671	0	0	251	69	0	0	0	164	0	0	0	2.50	0.0	0.0	0.0

Total

Act	0	4807	2645	4026	0	0	1507	423	0	0	0	991	0	0	0	15.04	0	0	0
Tar	0	4800	2640	4020	0	0	1500	420	0	0	0	990	0	0	0	15	0	0	0

Moisture Corection & Other Component Corection

G1Moi	G2Moi	G3Moi	G4Moi	G5Moi	G6Moi	C1.cor	C1.cor	C3.cor	C4.cor	C5.cor	W1 Cor	W2	Si Cor	Adm11.c	Adm12.c	Adm21.c	Adm22.c
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0





SL RMC PLANT
READY-MIX CONCRETE

DELIVERY CHALLAN

Plot No. 26, S.S. Villas,
Markandeya Nagar, Kapra,
Hyderabad,
Telangana - 500 062.

D.C. No. : 1922

Date : 4/9/2021

To,

M/s.

Green wood Heights.

Kawkoor.

Vehicle No. :

TS 08 UE 8893

pono:-79892-140731

S.No.	Grade	PARTICULARS	Qty.	Cum.	Value
8	1720	Time:-19:05	6 m ³	48 m ³	Dumb.

INWARD	
Inward No. 11678	Date 4/9/21
M/R No. 95990	5/9/21
Received By:	Sign:
MEHTA & MODI READY MIX CONCRETE LLP	

Receiver's Signature

For **SL RMC PLANT**
Mandela

Authorised Signatory

STETTER

Autographic / Batch Report / Delivery Note

Batch Date	4-Sep-21	Plant Serial No	M1-25
Batch time	19:00	Batch End Time	19:08
Batcher Name	STETTER	Batcher Name	STETTER
Batch No	12308	Truck Driver	***
Customer	GREEN WOOD HEIGHTS	Production Qty:	6.00
Site address	KAWKOOR	Returned Qty:	0.00
Recipe Code	M20 GREEN WOOD HEIGHTS	Total Ordered Qty:	0.00
Recipe Name	M20 GREEN WOOD HEIGHTS	With This Load	48.00
Truck No	TS 08 UE 8893	Batch Size:	1.00

Recipe	SAND1	SAND2	12MM	20MM	Agg5	Agg6	Cem1	Cem2	Cem3	Cem4	Cem5	Water	Ice	Slurry	Slice	Admix1	Admix2	Admix2	Admix2
Target	600	440	670	0	0	0	250	70	0	0	0	165	0	0	0	2.50	0.0	0.0	0.0
19:01	601	441	672	0	0	0	250	72	0	0	0	165	0	0	0	2.50	0.0	0.0	0.0
19:02	600	442	671	0	0	0	251	71	0	0	0	166	0	0	0	2.51	0.0	0.0	0.0
19:03	602	440	670	0	0	0	250	70	0	0	0	165	0	0	0	2.50	0.0	0.0	0.0
19:05	601	441	672	0	0	0	252	71	0	0	0	164	0	0	0	2.50	0.0	0.0	0.0
19:06	600	441	670	0	0	0	250	70	0	0	0	165	0	0	0	2.51	0.0	0.0	0.0
19:07	600	440	672	0	0	0	251	72	0	0	0	166	0	0	0	2.50	0.0	0.0	0.0
Total	4804	2645	4027	0	0	0	1504	476	0	0	0	991	0	0	0	15.02	0	0	0
Act	4800	2640	4020	0	0	0	1500	470	0	0	0	990	0	0	0	15	0	0	0
Tar	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0

Moisture Correction & Other Component Correction

G1Mo: G2Mo:	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
G3Mo: G4Mo:	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
G5Mo: G6Mo:	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
C1 cor:	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
C2 cor:	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
C3 cor:	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
C4 cor:	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
C5 cor:	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
W1 Cor:	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
W2:	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
Sl Cor:	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
Admix1:	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
Admix2:	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
Admix2:	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
Admix2:	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0

INWARD

INWARD NO: 1446

RECEIVED BY: 9599D

DATE: 4/9/21

TIME: 5/9/21

19:05



SL RMC PLANT
READY-MIX CONCRETE

DELIVERY CHALLAN

Plot No. 26, S.S. Villas,
Markandeya Nagar, Kapra,
Hyderabad,
Telangana - 500 062.

D.C. No. : 1924

Date : 4/9/2021

To,
M/s.

Green wood Heights

Kowkur

Vehicle No. :

TS 08 UE 8894

pono: 79892-140731

S.No.	Grade	PARTICULARS	Qty.	Cum.	Value
9	M20	Time:- 21:05	5 M3	53 M3	Dump.

INWARD	
Inward No: 11477	Dr: 04/09/21
MRN No: 75991	Dr: 6/9/21
Received By:	Sign: [Signature]
MEHTA & MODI REALTY KOWKUR LLP	

Receiver's Signature

For **SL RMC PLANT**
Mandali

Authorised Signatory

STETTER

Autographic / Batch Report / Delivery Note

Batch Date	4-Sep-21	Plant Serial No	M1-25
Batch time	21:00	Batch End Time	21:08
		Batcher Name	STETTER
Batch No	12310	Truck Driver	***
Customer	GREEN WOOD HEIGHTS	Production Qty	5.00
Site address	KAWKOOR	Returned Qty	0.00
Recipe Code	M20 GREEN WOOD HEIGHTS	Total Ordered Qty	0.00
Recipe Name	M20 GREEN WOOD HEIGHTS	With This Load	53.00
TS No	TS 08 UE 8894	Batch Size	1.00

	SAND1	SAND2	12MM	20MM	Agg5	Agg6	Cem1	Cem2	Cem3	Cem4	Cem5	Water	Ice	Slurry	Slime	Admix1	Admix1.2	Admix2	Admix2.2
Recipe	0	800	440	670	0	0	250	70	0	0	0	165	0	0	0	2.50	0.0	0.0	0.0
Target	0	800	440	670	0	0	250	70	0	0	0	165	0	0	0	2.50	0.0	0.0	0.0
21:01	0	800	440	669	0	0	252	72	0	0	0	165	0	0	0	2.50	0.0	0.0	0.0
21:02	0	800	442	671	0	0	251	71	0	0	0	166	0	0	0	2.51	0.0	0.0	0.0
21:03	0	800	440	670	0	0	250	70	0	0	0	165	0	0	0	2.50	0.0	0.0	0.0
21:05	0	800	442	672	0	0	252	71	0	0	0	164	0	0	0	2.50	0.0	0.0	0.0
21:06	0	800	441	671	0	0	250	70	0	0	0	165	0	0	0	2.51	0.0	0.0	0.0

Total

Act	0	8008	2205	3353	0	0	1255	354	0	0	0	825	0	0	0	12.50	0	0	0
Tar	0	8000	2200	3350	0	0	1250	350	0	0	0	825	0	0	0	12.5	0	0	0

Moisture Corection & Other Component Corection

G1Moi	G2Moi	G3Moi	G4Moi	G5Moi	G6Moi	C1.cor	C1.cor	C3.cor	C4.cor	C5.cor	W1 Cor	W2	Si Cor	Adm11.c	Adm12.c	Adm21.c	Adm22.c
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0

INWARD	
Inward No: 11477	Date: 04/09/21
MRN No:	Dr:
Received By:	Sign:
MENTA & MODI REALTY KOWKOR LLP	

RMC pour report

Company/ firm:	MMRKLLP	Project:	GHT	A. Estimated quantity:	65 Cu Mtrs
Flat / Villa no.:	Peripheral Road	Block No.:	B-Block	B. Requisition quantity:	65 Cu Mtrs
Slab no.:	MAIN ROAD	PO Nos.	79892	C. Actual quantity poured:	54 cum
Requisition nos.:	140731	Supplier:	SL RMC Plant	D. Difference (C-A):	11 Cu mtrs
Sign of security		Sign of Admin		Sign of Project manager	
Date	06-09-2021	Date	06-09-2021	Date	06-09-2021

Details of RMC pour

Sl. No	Date	Time	Quantity poured	Dc No. / Batch no.	Specified weight (@ 2,400 kgs per meter cube	Measured weight (kgs)	Short fall in weight in kgs	Inward no.	MRN No.
1.	04-09-2021	10:29	6cum	1898	14400kgs	13410	990kgs	11467	95638
2.	04-09-2021	11:48	6cum	1899	14400kgs	13960	440kgs	11469	95639
3.	04-09-2021	13:31	6cum	1906	14400kgs	13855	545kgs	11470	95690
4.	04-09-2021	14:46	6cum	1910	14400kgs	13810	590kgs	11471	95689
5.	04-09-2021	16:21	6cum	1915	14400kgs	13750	650kgs	11472	95687
6.	04-09-2021	16:25	6cum	1916	14400kgs	13165	1235kgs	11474	95988
7.	04-09-2021	16:50	7cum	1917	16800kgs	16450	350kgs	11475	95989
8.	04-09-2021	19:05	6cum	1922	14400kgs	14410	390kgs	11476	95990
9.	04-09-2021	21:05	5cum	1924	12000kgs	11600	400kgs	11477	95991
10.									
11.									
Total:			54cum		1,29,600kgs	1,24,410Kgs	5590Kgs		
Remarks:	APPROVED 7 SEP 2021 A. SHRESTHA Certified by: N. Shrawan Asst. Engineer MENTA & MOON REALTY KONGUR LLP								

Note: 1. Report to be sent on completion of each slab or footing for a block or villa 2. Report must be sent within one working day with relevant documents attached 3. Weigh all vehicles 4. 6 m cu vehicles weight less than 14,100 kgs - deduct amount in bill 5. Calculate short fall in weight as per internal memo no. 912/70/b dated 10.09.2017 6. Shortfalls within permissible limits, write shortfall as Nil. 6. Ensure that relevant totals are entered.
