

Anx B – Work Completion Report

Company	AMTZ Medpolis Square 4554 Pvt Ltd	Name of contractor	Simhaa Constructions	Sl. No. site bills reg.	166
Project/site	AMS4554	Nature of work	RCC Works	Dt. site bills reg.	24-11-2025
Block no.	AMS4554	Work done from date	01-10-2025	M-codex bill ID.	
WO no.	20251022015	Work done to date	20-10-2025	WO issued ?	Yes
WO date	22-10-2025	Contractor bill no.	90	GST bill required?	Yes

Sl. No.	Unit/floor no	Details of work		Qty	Units	Rate ID	Rate	Amount
1	AMS4554	CONST - RCC 7205 - Construction - Footing - Shuttering - Sqm (Labour charges for the shuttering works)		50.04	Sqm	RCC 193	425.00	21,267.00
2	AMS4554	CONST - RCC 2523 - Construction - Footing - Bar Bending - Ton (Labour charges for the bar bending work)		0.47	Ton	RCC 175	9,436.00	4,434.92
3	AMS4554	CONST - RCC 2640 - Construction - Footing - Concreting - Material - cum (Charges for the RCC M20 material)		5.93	Cum	RCC 191	4,347.00	25,777.71
4	AMS4554	CONST - RCC 5898 - Construction - Footing - Concreting - Labour - cum (Labour charges for the RCC M20 concrete works)		5.93	Cum	RCC 194	725.00	4,299.25
5	AMS4554	CONST - RCC 2744 - Construction - Footing PCC - Concreting - Labour - cum (Labour charges for the PCC M10 laying works in footings)		2.59	Cum	RCC 188	565.00	1,463.35
6	AMS4554	CONST - RCC 6417 - Construction - Footing PCC - Concreting - Material - cum (Charges for the PCC M10 material)		2.59	Cum	RCC 192	3,956.00	10,246.04
								67,488
							Add GST @	18%
							Total amount including taxes for work done	79,636

Remarks:	
Approved by project manager	Approved by QS team
Sign: 	Sign:
Date: 21/10/2025	Date:

Notes: 1. This sheet replaces installation report and advice for credit to contractors. 2. This word form must be typed. 3. Use this form even if work order is not issued. 4. Attach measurement and estimate sheets only if required i.e., details cannot be entered above 5000 sqm and amount greater than 10k QS manager and directors approval is required. 6. For bill amount less than 10k any QS team member may sign and in place of director sign of respective E&D member to be taken. 7. Director include - Sonali, Anand Mehta (for GHT + GMR), Sachin (for Vivopolis), B. anand Kumar (for NGH + NRK). 8. Entry of rate ID is mandatory. 9. This sheet must be sent within 2 working days of work completion (with or without contractors bill). 10. Contractors to send scanned copy of bill to site and QS by email. 11. Contractors must submit original bills at HO (can be sent by courier).

MEASUREMENT SHEET												
Company Name:		AMTZ Medpolis Square 4554 Pvt Ltd			Approved by:			N. Leela Venkatesh				
Project:		AMS4554			Sign:							
Work Description :		RCC works for East compound wall			Work start date:			01-10-2025				
Contractor:		Simhaa Constructions			Work end date:			20-10-2025				
Prepared By:		N. Leela Venkatesh			Date :			24-11-2025				
S No.	Item Head	Item Description			A	B	C	D	E	F=AxBxCxDxG	Units	H=Sum of F Item Head Total
			Length	Width	Height	Nos.	Unit wt/mtr	Quantity				
1	RCC Works	CONST - RCC 7205 - Construction - Footing - Shuttering - Sqm (Labour charges for the shuttering works)	1.00	1.00	1.00	-	-	50.04	-		Sqm	50.04
2	RCC Works	CONST - RCC 2523 - Construction - Footing - Bar Bending - Ton (Labour charges for the bar bending work)	1.00	1.00	1.00	-	-	0.47	-		Ton	0.47
3	RCC Works	CONST - RCC 2640 - Construction - Footing - Concreting - Material - cum (Charges for the RCC M20 material)	1.00	1.00	1.00	-	-	5.93	-		Cum	5.93
4	RCC Works	CONST - RCC 5898 - Construction - Footing - Concreting - Labour - cum (Labour charges for the RCC M20 concrete works)	1.00	1.00	1.00	-	-	5.93	-		Cum	5.93
5	RCC Works	CONST - RCC 2744 - Construction - Footing PCC - Concreting - Labour - cum (Labour charges for the PCC M10 laying works in footings)	1.00	1.00	1.00	-	-	2.59	-		Cum	2.59
6	RCC Works	CONST - RCC 6417 - Construction - Footing PCC - Concreting - Material - cum (Charges for the PCC M10 material)	1.00	1.00	1.00	-	-	2.59	-		Cum	2.59
											TOTAL	67.55

APPROVED BY


(Signature)

14 NOV 2025

LEELA VENKATESH.N.
Project Manager

Tax Invoice

e-Invoice



IRN : 4a574e185d58213ca9a6ae199d7e313cfb5f390ca5cc6d-57c56c96854c7034c9
Ack No : 112527741487188
Ack Date : 21-Nov-25

Simhaa Constructions (2025-26)

Plot No 2, Block-B, Auto Nagar
Visakhapatnam
GSTIN/UIN 37ABMFS6706L1ZJ
State Name : Andhra Pradesh, Code : 37
E-Mail : simhaaconstructions@rediffmail.com
Buyer (Bill to)

AMTZ Medpolis Square 4554 Pvt. Ltd

VM Steel Project Town Ship Sub Post Office
Ground, Plot No D1-56, HUB Building, AMTZ Campus,
Pragathi Maidan, Visakhapatnam
GSTIN/UIN : 37AAXCA5420G1ZG
State Name : Andhra Pradesh, Code : 37

Invoice No.

90

Delivery Note

Reference No. & Date

SC/AMS/4554/RA 85 dt. 21-Nov-25

Buyer's Order No

20251022015

Dispatch Doc No

Dispatched through

Terms of Delivery

Dated

21-Nov-25

Mode/Terms of Payment

Other References

Dated

22-Oct-25

Delivery Note Date

Destination

SI No	Particulars	HSN/SAC	Quantity	Rate	per	Amount
1	Contract Receipt (2025-26) RA 85 for Civil Contract for RCC Works for the project AMTZ Medpolis Square 4554, Visakhapatnam, RCC works fro the eastern Compound wall of AMTZ 4554.	995415				67,488.27
	CGST - Output 9%				9 %	6,073.94
	SGST - Output 9%				9 %	6,073.94
Total						₹ 79,636.15
Amount Chargeable (in words)						E & O E
INR Seventy Nine Thousand Six Hundred Thirty Six and Fifteen paise Only						
HSN/SAC		Taxable Value	Rate	CGST Amount	SGST/UTGST Rate	Total Tax Amount
995415		67,488.27	9%	6,073.94	9%	12,147.88
Total		67,488.27		6,073.94		12,147.88

Tax Amount (in words) : **INR Twelve Thousand One Hundred Forty Seven and Eighty Eight paise Only**

for Simhaa Constructions (2025-26)

Remarks

RA 85 RCC works fro the eastern Compound wall of AMTZ 4554.

This is a Computer Generated Invoice

For M/s. **SIMHAA CONSTRUCTIONS**

Authorized Signatory

(KAN RAJU)
Managing Partner

Civil Contract for RCC works for the project AMTZ Medpolis Square 4554 at AMTZ,
Visakhapatnam

RA - 85

SIMHAA CONSTRUCTIONS
Visakhapatnam

SIMHAA CONSTRUCTIONS

RA 85

DATE: 21.11.2025

Name of the work: Civil works for Construction of RCC building at AMTZ Medpolis Square 4554, Visakhapatnam.

Name of the Contractor : M/s Simhaa Constructions

P. O Number : 20251022015 on Dt: 22 Oct 2025

"RCC Works for the Eastern compound wall of AMTZ 4554 "

Sl. NO	Item Name	Uom	P.O Qty	Rate	QUANTITY		Amount	
					up to Previous	This Bill Qty	Total Value of Work	up to Previous
1	CONST- RCC 7205 - Construction - Footing - Shuttering--sqm Labour charges for the shuttering works. Read UOM as Sqm.	Sqm	50	425.00	-	50.040	21,267.00	-
2	CONST - RCC 2523 -Construction - Footing -Bar Bending--Ton Labour charges for the bar bending works. Read UOM as MT.	Ton	1	9436.00	-	0.470	4,434.92	-
3	CONST - RCC 2640 - Construction - Footing - Concreting - Material-- cum Charges for the RCC(m20) material. Read UOM as Cum.	Cum	6	4347.00	-	5.930	25,777.71	-
4	CONST - RCC 5898 - Construction- Footing -Concreting - Labour--cum Labour charges for the RCC (M20) concrete works. Read UOM as Cum.	Cum	6	725.00	-	5.930	4,299.25	-
5	CONST - RCC 2744 - Construction - Footing PCC -Concreting - Labour -cum Labour charges for the PCC (M10) laying works in footings. Read UOM as Cum.	Cum	3	565.00	-	2.590	1,463.35	-
6	CONST - RCC 6417 - Construction - Footing PCC-Concreting - Material--cum Charges for the PCC (M10) Material. Read UOM as Cum.	Cum	3	3956.00	-	2.590	10,246.04	-
Total							67488.27	-

Total

67488.27

67488.27

Total Value of present Bill

Add GST @ 18%

12147.89

Total

79636.16

{ Amount In Words : Seventy Nine Thousand Six Hundred Thirty Six Rupees and One Six Paise Only }

For M/s. SIMHAA CONSTRUCTIONS

(KAN RAJU)
 Managing Partner

Name of Agency : M/s SIMHAA CONSTRUCTIONS

Project: AMTZ Medpolis Square 4554 Pvt.Ltd.

Work: RCC Works for the Eastern compound wall of AMTZ 4554.

RAR No: 85

SUMMARY

S.No	Item Head	Item Description	Units	Quantity	Sub Total	Remarks
1	PCC_M10	Footings	Cum	1.270		
		Plinth Beam	Cum	1.320		
					2.590	
2	Shuttering	Footings	Sqm	12.260		
		Col. up to PB	Sqm	13.780		
		PB	Sqm	16.960		
		Col. above PB	Sqm	7.040		
					50.040	
3	RCC-M20	Footings	Cum	2.800		
		Col. up to PB	Cum	0.790		
		PB	Cum	1.940		
		Col. above PB	Cum	0.400		
					5.930	
4	4" BW	4" BW	Sft	257.170		
					257.170	
5	Steel	Footings, Columns & PB	MT	0.464		
					0.470	

For M/s. SIMHAA CONSTRUCTIONS


(HAN RAJUN)
Managing Partner

Name of Agency : M/s SIMHAA CONSTRUCTIONS
 Project: AMTZ Medpolis Square 4554 Pvt.Ltd.
 Work: RCC Works for the Eastern compound wall of AMTZ 4554.
 RAR No: 85

Measurment sheet

PCC

Footings PCC

S.No	Description	Unit	Nos	L	W	D	Qty	Remarks
1	East side	Cft	11	3.500	3.500	0.333	44.917	
Total							44.917 Cft	1.270 Cum

PB-PCC

S.No	Description	Unit	Nos	L	W	D	Qty	Remarks
1	East side	Cft	1	111.975	1.250	0.333	46.656	
Total							46.656 Cft	1.320 Cum

RCC

Footings RCC

S.No	Description	Unit	Nos	L	W	D	Qty	Remarks
1	East side	Cft	11	3.000	3.000	1.000	99.000	
Total							99.000 Cft	2.800 Cum

Columns up to PB Bottom-RCC

S.No	Description	Unit	Nos	L	W	D	Qty	Remarks
1	East side	Cft	11	0.750	0.750	4.495	27.813	
Total							27.813 Cft	0.790 Cum

PB-RCC

S.No	Description	Unit	Nos	L	W	D	Qty	Remarks
1	East side	Cft	1	121.725	0.750	0.750	68.470	
Total							68.470 Cft	1.940 Cum

Columns above PB-RCC

S.No	Description	Unit	Nos	L	W	D	Qty	Remarks
1	East side	Cft	11	0.750	0.750	2.297	14.211	
Total							14.211 Cft	0.400 Cum

For M/s. SIMHAA CONSTRUCTIONS


 (RAN RAJU)
 Managing Partner

<u>Measurment sheet</u>								
<u>Shuttering</u>								
Footings Shuttering								
S.No	Description	Unit	Nos	L	W	D	Qty	Remarks
1	East side	Sft	11	3.000	3.000	1.000	132.000	
Total							132.000 Sft 12.260 Sqm	
Columns up to PB Bottom-Shuttering								
S.No	Description	Unit	Nos	L	W	D	Qty	Remarks
1	East side	Sft	11	0.750	0.750	4.495	148.334	
Total							148.334 Sft 13.780 Sqm	
PB-Shuttering								
S.No	Description	Unit	Nos	L	W	D	Qty	Remarks
1	East side	Sft	1	121.725		0.750	182.588	2 sides
Total							182.588 Sft 16.960 Sqm	
Columns above PB-Shuttering								
S.No	Description	Unit	Nos	L	W	D	Qty	Remarks
1	East side	Sft	11	0.750	0.750	2.297	75.791	
Total							75.791 Sft 7.040 Sqm	
BW above PB -100 mm								
S.No	Description	Unit	Nos	L	W	D	Qty	Remarks
1	East side	Sft	1	111.975		2.297	257.173	
Total							257.170 Sft	
BW under Plinth beam-200 mm								
S.No	Description	Unit	Nos	L	W	D	Qty	Remarks
1	East side	Sft	1	111.975		2.494	279.217	
Total							279.220 Sft	
Transom - 150 mm x 100 mm								
S.No	Description	Unit	Nos	L	W	D	Qty	Remarks
1	East side	rft	1	121.725			121.725	
Total							122.000 rft	
Levels								
	drive way	11.10						
	PB Top	11.48						

For M/s. SIMHAA CONSTRUCTIONS


 (KAN RAJU)
 Managing Partner

<u>Measurment sheet</u>			
Footing Btm	9.58		
PB Btm	11.25		
Col ht below PB		1.37 Meters	
EW	9.48	1.62 m	
col above PB	12.18	0.70 Meters	
BW btm lvl	10.49	0.76 Meters	
bw above PB	12.18		

For M/s. SIMHAA CONSTRUCTIONS


 (KAN RAJU)
 Managing Partner

RA - 85 - BBS - East Compound wall

RA - 85 - BBS - East Compound wall																									
Member	Size			Bar Detail	Dia	Spacing Of Bar	Bend/ Deep Length (ft)	Cover (inch)	Overlap	Bar Shape	Bend Deductions				Cutting Length (ft)	No. of Bars			Total Length (ft)	Total Length with Dia. (m)					
	L (ft)	B (ft)	H (ft)								45°	90°	135°	180°		No. of Bars	No. of Members	Total Nos.		8	10	12	16	20	25
F1	3.000	3.000	1.000	Main Bot.	10 mm	8 inch c/c	0.667	2			0.666		3.868	6	8	11	66	255.310	255.310						
				Main Top.	10 mm		0.667				0.666		3.868	6	8	11	66	255.310	255.310						
Columns up to PB LVL																									
Columns at Conventional BW	0.750	0.750	6.245	Col bars	10 mm			1.5					7.078	4	8	11	44	311.445	311.445						
				Stirrups	10 mm	8 inch c/c			1.640		0.066	0.068	2.304	0	8	11	00	236.076	236.076						
Columns above PB LVL																									
Columns at Conventional BW	0.750	0.750	2.297	Col bars	10 mm			1.5					5.453	4	8	11	44	239.912	239.912						
				Stirrups	10 mm	8 inch c/c			5.906		0.066	0.068	2.304	6	8	11	66	157.084	157.084						
PB East	121.725	0.750	0.756	Top Main	12 mm			1	5.906		0.079		128.390	2	8	1	2	256.780	256.780	256.780					
Nos	19	0		Bot Main	12 mm				5.906		0.079		128.390	2	8	1	2	256.780	256.780	256.780					
Width	0.750	0.000	8 inch c/c	Stirrups	8 mm	8 inch c/c					0.052	0.079	2.648	162	8	1	162	429.024	429.024						
Total Length (ft)																		429.024	1456.938	513.559	0.000	0.000	0.000	0.000	
Unit Weight In (Kg/ft)																		0.120	0.188	0.271	0.481	0.752	1.175	1.175	

For M/s. SIMHAA CONSTRUCTION



(KAN RAJU)
Managing Partner

RA - 85 - BBS - East Compound wall																									
Member		Size		Bar Detail		Dia mm	Spacing Of Bar	Bend Devp Length		Cover	Overlap	Bar Shape	Bend Deductions			Cutting Length	No. of Bars			Total Length	Total Length with Dia. (m)				
		L (ft)	B (ft)	H (ft)	Particular Pacing of Bar			ft	(inch)				45°	90°	135°		180°	No. of Bars	No. of Members		Total Nos.	8	10	12	16
															Total Weight In (KG)			51.483	273.904	139.175	0.000	0.000	0.000		
															Total Weight per 1m			0.051	0.274	0.139	0.000	0.000	0.000		
															Total in (MT)			0.464							


For M/s. SIMHAA CONSTRUCTIONS


KAN RAJU
Managing Partner

Compound Wall Estimation

Column at Every 10' 10.00 ft

Data	Side	Total Length	L(m)	L(ft)	No.of Columns
				Total	
1	East Side	37.10	37.10	121.73	11
Total no.of columns					11

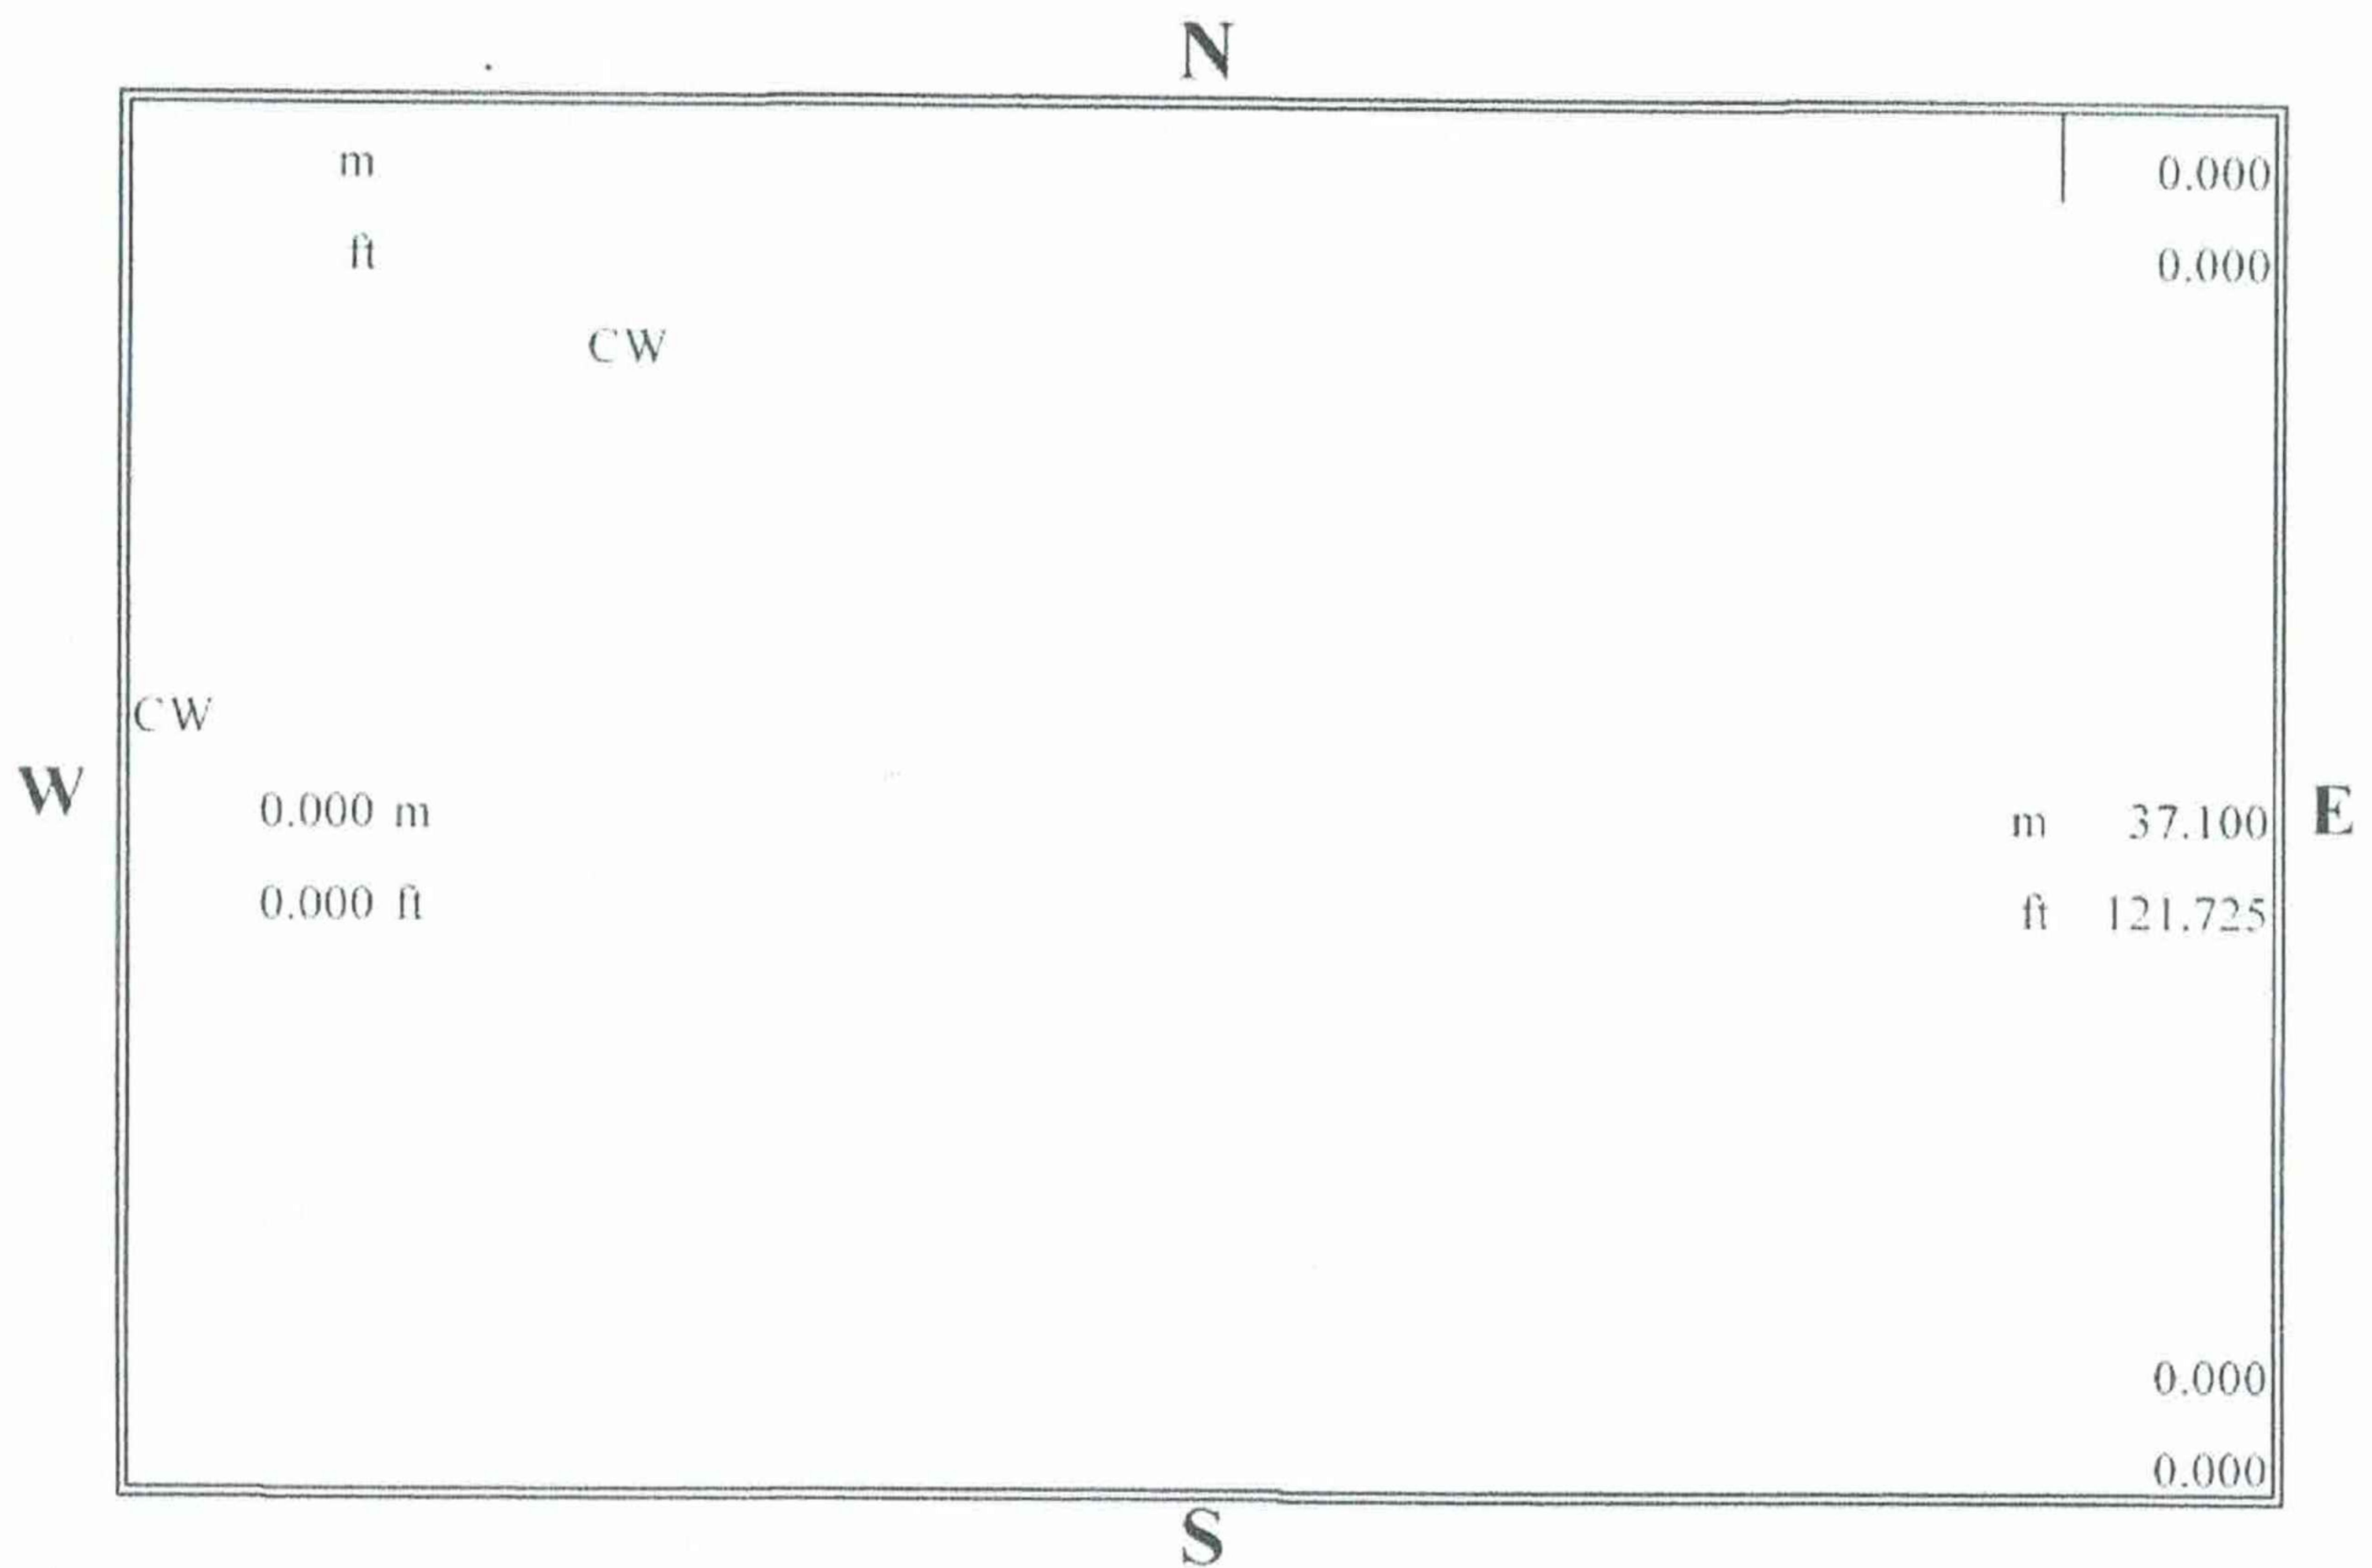

For M/s. SIMHAA CONSTRUCTIONS

(Signature)
 (KAN RAJU)
 Managing Partner
