

Construction Division
Additions & Alteration Charges Approval Form

Company Name:	Modi Properties Pvt Ltd	Site	May Flower Platinum
Name of the customer	Nukala Sarika		
Villa/ Flat No.	A-708		
Sl.No	Description	Amount	
1	Total extra Charges	42,180=00	
2	Total refundable amount	5,256=00	
3	Net amount to be charges (if any)	36,924=00	
4	Net amount to be refunded (if any)	—	
Remarks :			
Approved by Project Manager	Approved by Design Team	Approved by MD	
Date 14/2/2022	Date	Date	
Sign: 	Sign:	Sign:	

Note: 1. Enclose measurement & estimate sheet. 2. Send scanned copy by email to plans@modiproperties.com & CR. 3. Maintain originals in A&A of customers at site.

ESTIMATE SHEET									
Company Name:	MPL								
Project:	May Flower Platinum								
Work Description:	Extra Specs								
Flat No.	A-708								
Prepared By	K. Narendar Reddy								
Date:	11-02-2022								
S No.	Item Head	Item Description	Quantity	Units	Rate	Amount	Item Head Total		
1	UPVC Window	Mesh Provision for windows	68.00	sft	60.00	4080.00			
2	Big Tiles laying	Big Tiles laying	635.00	sft	60.00	38100.00			
		Sub Total A					42180		
	Refund								
1	Granite	Granite	28.00	sft	55.00	1540.00			
2	Kitchen dado tiles	Kitchen dado tiles	40.00	sft	35.00	1400.00			
3	SS Sink	SS Sink	1.00	no	2316.00	2316.00			
		Sub Total A					5256		
		Grand Total (A-B)					36924		
Amount in words - Thirty Six Thousand Nine Hundred and Twenty Four Rupees only.									

Reddy

APPROVED BY
14 FEB 2022
S. V. Subha Reddy
Project Manager

Quality Control Check Report Stage After Finishing Stage III (Apartments)

Flat No A-708 28208

Company MPL MFP

Prepared by T.Vinod Kumar 20/08/21

Project Manager Subba Reddy 20/08/21

Previous stage report no 27424 Yes No

Checked By AHD on 27/4/24 Yes No

Report filed and signed by PM T.Vinod Kumar 20/08/21

For filing Yes No

Recommendation:

- ☒ Stop further work. Submit ATR on QC report to QC team. Proceed only after received by QC.
- ☒ Stop further work. Proceed with work after taking corrections pointed out in the QC report. ATR not required.
- ☒ Proceed with further work only after taking corrections pointed out in the QC report. ATR not required.
- ☒ Proceed with further work. ATR not required.
- ☒ Inspection should be done after:
- ☒ Completing stage of work.
- ☒ Complete works like doors, windows, grills, electrical wiring, switches, french door glass, etc.
- ☒ In case of modular kitchen provide platform, granite and dado and modular kitchen in this stage.
- ☒ Provide video door phone in this stage.
- ☒ Possession for work cannot be given until QC check is complete in all categories as per the approved plan.

Miscellaneous check:

Modular kitchen to be provided ☒ Yes ☐ No ☐ Avg ☐ Poor ☐ Good ☐ Avg ☐ Poor

Modular kitchen workman ship ☒ Yes ☐ No ☐ Avg ☐ Poor ☐ Good ☐ Avg ☐ Poor

Video door phone w/fi cam to be provided ☒ Yes ☐ No ☐ Avg ☐ Poor ☐ Good ☐ Avg ☐ Poor

Painting marks and drops are cleaned from floor windows, walls ☒ Yes ☐ No ☐ Avg ☐ Poor ☐ Good ☐ Avg ☐ Poor

Certified that all corrections mentioned in the QC report have been completed. Work can proceed to next stage.

Project in-charge	Sign	Date
<u>T.Vinod Kumar</u>	<u>T.Vinod Kumar</u>	<u>20/08/21</u>

Quality Control Check Report. Stage: After Finishing Stage III (Apartments)

Rate the quality of (Good ✓, Avg. X, Poor - needs correction XX, XN)													
S No.	Room	Door, door knob & door stopper fitting	Door, door knob & door stopper cleaning	Window grills & quality	Window grills fitting & finishing	Windows quality	Window fitting & finishing	Balcony railing quality & finishing	French door quality & fitting	CP joint quality and fitting	Edge building	Switch boards fitting & covering with plastic covers	Junction box covers painting
1	Bedroom 1 - M. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Bedroom 2 - C. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 3 - G. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility - balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Utility - balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Utility - balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Toilet 1 - M. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Toilet 2 - C. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Toilet 3 - G. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
15	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓

Remarks

1. In G. Toi 1 no. of wall tile is broken.

2. In Utility grill not fixed.

3. In balcony for railing, glass not fixed.

4. In Dining Seepage started.

ATR on Quality Control Check Repot. (Apartments)

Flat No	A-708	QC report stage	Stage-2	Sl. No.	37424
Company	MPL	Project	MFP	Phase	
Prepared by	Sravani.k	Sign	<i>[Signature]</i>	Date	5/4/21
Project Manager	Subbaredy.s.v	Sign	<i>[Signature]</i>	Date	5/4/21
Receipt by QC date	3/4/21	Sign		Other	
Receipt at HO date		Sign		Other	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation that was made by QC:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team.

Notes:

1. Attach a copy of the QC report to this sheet.
2. Circle each correction with a red pen – tick (✓) each circle for work completed and cross (X) each circle where work has not been completed.
3. Give remarks for each case where work has not completed on this sheet.
4. Make 2 copied of the ATR – send one to MD and other to QC.
5. Enclose required photographs – hard copy.

Remarks:

17 AU works are completed.

Quality Control Check Report. Stage: After Finishing Stage II (Apartments)

Flat No	A-708		Other	Sl. No.	37424
Company	MPL		Project	Phase	-
Prepared by	T. Vinod Kumar		Sign	Date	03-04-21
Project Manager	Subba Reddy		Sign	Date	03-04-21
Previous stage report no.			37166	Report filed and signed by PM	☒ Yes ☐ No
Checked By MD on			MD Sign	For filling	☐ Yes ☐ No
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☐ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.					

Inspection should be done after:

- Completion of flooring, bathroom /utility tiles, first coat of paint.
- Completion of doors, windows, grills, electrical wiring, switches must be done in next stage
- False ceiling must be completed before flooring.
- Kitchen platform, granite and dado must be completed where modular kitchen is not provided.
- Provide granite soffit for main door and balconies in this stage.

Miscellaneous check:

Main door fixed with lock & stopper	☐ Yes ☒ No	Granite soffit for balcony provided	☒ Yes ☐ No
Granite soffit for balcony required	☒ Yes ☐ No	Balcony granite soffit edge polishing	☐ Good ☒ Avg ☐ Poor
Balcony granite soffit workmanship	☐ Good ☒ Avg ☐ Poor	Granite soffit for main door provided	☐ Yes ☐ No
Granite soffit for main door required	☐ Yes ☐ No	Main door granite soffit edge polishing	☐ Good ☐ Avg ☐ Poor
Main door granite soffit workmanship	☐ Good ☐ Avg ☐ Poor		

Quality Control Check Repot. Stage: After Finishing Stage II (Apartments)

Flooring & painting		Rate the quality of (Good ✓, Avg. X, Poor - needs correction XX, NA)												
S No	Room	Color variation of floor tiles	Flooring workmanship & grouting	Skirting size (3")	Skirting workmanship	Plastering above skirting	Plastering & finishing of walls	Crack filling	Loft Finishing	Windows check	General quality of painting & finishing	Door & frame painting quality	Door beading, luppam and painting quality.	Edge building
1	Bedroom 1 M. Bed	✓	✓	✓	✓	✓	✓	-	-	✓	✓	✓	✓	✓
2	Bedroom 2- C. Bed	✓	✓	✓	✓	✓	✓	-	-	✓	✓	✓	✓	✓
3	Bedroom 3- G. Bed	✓	✓	✓	✓	✓	✓	-	-	✓	✓	✓	✓	✓
4	Drawing	✓	✓	✓	✓	✓	✓	-	-	✓	✓	✓	✓	✓
5	Dining	✓	✓	✓	✓	✓	✓	-	-	-	✓	-	-	✓
6	Lobby 1--	-	-	-	-	-	-	-	-	-	-	-	-	-
7	Utility / balcony 1	-	-	-	-	-	-	-	-	-	-	-	-	-
8	Utility / balcony 2-	✓	✓	✓	-	-	✓	-	-	-	✓	✓	✓	✓
9	Utility / balcony 3-	-	-	-	-	-	-	-	-	-	-	-	-	-
10	Kitchen	✓	✓	✓	✓	✓	✓	-	✓	✓	✓	-	-	✓
11	Other													
12	Other													
Remarks		Note:-1. In C.Bed, Kitchen Skirting piece is missing.												
		2. In M.Bed Skirting piece is broken.												
		3. In kitchen Dado tile provision is provided with 18"												

4. In drawing & dining finishing works (Painting) to be done for couple of places.
5. In balcony flooring not done as per M.D.six approval

Quality Control Check Report. Stage: After Plumbing & Electrical (Apartments)

Flat No.	A-708	Other	Sl. No.	37166
Company	MPL	Project	Phase	m
Prepared by	Akhrel	Sign	Date	25/2/21
Project Manager	Subba Reddy	Sign	Date	25/2/21
Previous stage report no.		36569	Report filed and signed by PM?	☒ Yes ☐ No
Additions & alterations sheet date		7/6/20	All pages signed by engineer & customer?	☒ Yes ☐ No
Checked By MD on		MD Sign	For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- after cleaning the apartment.
- before starting painting, tiling & flooring.
- electrical conduct, waterproofing & plumbing work is completed (for stage II only).
- additions & alterations is finalized and signed. In case there are no additions and alterations printout of email by PM to CR confirming the same must be filed.
- additions & alterations sheets to be transferred to QC file. QC to check if A&A are made as per request.

Certified that all corrections mentioned in the QC report have been completed. Work can proceed to next stage.

After Plumbing & Electrical Check.

Notes:

1. Mark ☒ for correct or minor mistake which does not require correction
2. Mark ☒ for minor mistake that requires minor correction.
3. Mark ☒ for major mistake that requires correction by replacement or re-fixing.
4. Mark ☒ for major mistake that cannot be corrected.
5. Location of CPVC & PVC fittings must be checked as per measurements given in circular. Tolerance 1".
6. Location, height and spirit level of electrical points must be checked as per measurements given in circular & plan. Tolerance 1".
7. Civil work near pipes in balcony & utility must be neat and mortar should be removed from the pipes.
8. Water proofing must cover all pipes & check height above SFL.
9. Fasteners must be used as specified in circular. Especially check fixing of PVC pipes.
10. Height of DB box must be 6" below false ceiling level or 12" below slab level.
11. In case of many changes in civil work, electrical work and plumbing work, a new drawing must be prepared at HO and approved by MD.

Project in-charge	Sign	Date
<i>Subba Reddy</i>	<i>[Signature]</i>	26/2/2021

Quality Control Check Report. Stage: After Plumbing & Electrical (Apartments)

S No	Room	Civil work near pipes in balcony & utility ⁷ (✓ or ✕)	CPVC & PVC Check ⁵ (✓ or ✕)	Electrical points check ⁶ (✓ or ✕)	Water proofing check ⁸ (✓ or ✕)	Proper use of fasteners check ⁹ (✓ or ✕)	Placement of DB ¹⁰ (✓ or ✕)	Placement of Generator changeover (✓ or ✕)
1	Bedroom MB	—	—	✓	—	—	—	—
2	Toilet 1 MT	✓	✓	✓	✓	—	—	—
3	Bedroom 2 KB	—	—	✓	—	—	—	—
4	Toilet 2 CT	✓	✓	✓	✓	—	—	—
5	Bedroom 3 CB	—	—	✓	—	—	—	—
6	Toilet 3 KT	✓	✓	✓	✓	—	—	—
7	Drawing	—	—	✓	—	—	✓	✓
8	Dining	—	—	✓	—	—	—	—
9	Lobby 1	—	—	—	—	—	—	—
10	Utility / balcony 1	—	—	✓	—	✓	—	—
11	Utility / balcony 2	✓	✓	✓	✓	✓	—	—
12	Utility / balcony 3	—	—	—	—	—	—	—
13	Kitchen	✓	✓	✓	—	—	—	—
14	Other							
15	Other							
Remarks								


Remarks on additions & alteration sheet:


Signed by engineer,	☒ Yes ☐ No	Signed by customer,	☒ Yes ☐ No
Revised drawing required from HO	☐ Yes ☒ No	Approved revised drawing attached	☐ Yes ☒ No

Quality Control Check Report. Stage: After Plumbing & Electrical (Apartments)

Miscellaneous check

Screeding done on walls upto 12" outside bathroom/utility	☒ Yes ☐ No
Bathroom /utility filled with 4" water for water proof check	☐ Yes ☒ No
Hole packing done around all pipes in ceiling and internal walls	☒ Yes ☐ No
Remarks:	

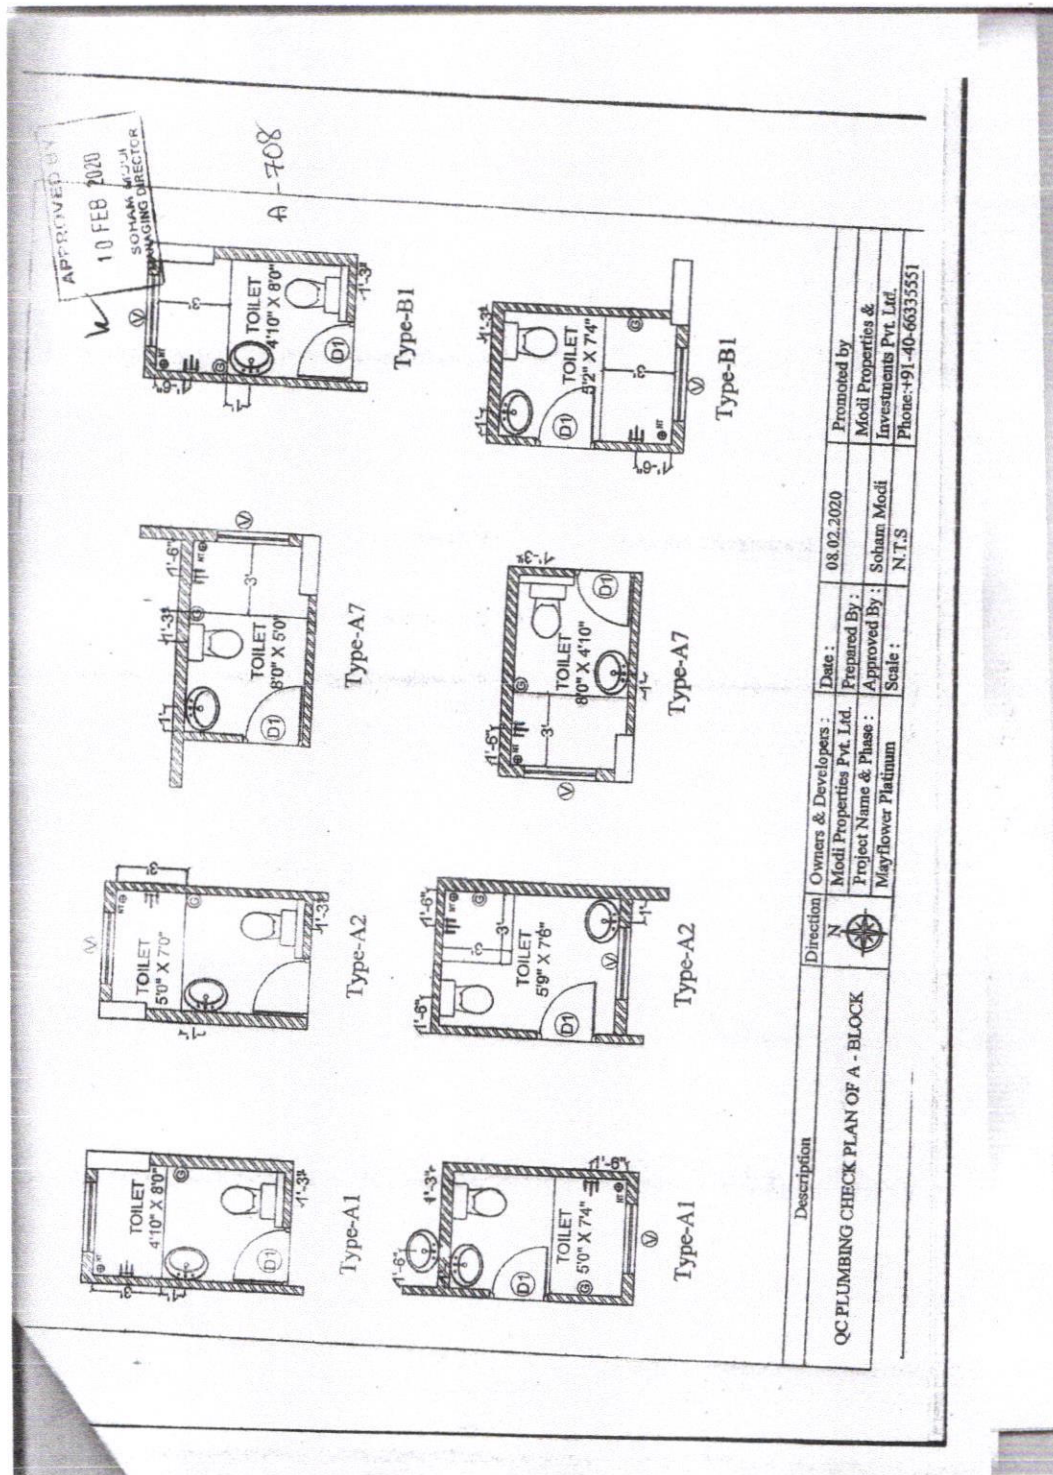



Quality Control Check Report. Stage: After Plastering (Apartments)

Flat No.	A-708	Other	Sl. No.	36569
Company	MPL	Project	Phase	-
Prepared by	T. Vinod Kumar	Sign	Date	08-12-20
Project Manager	Subba Reddy	Sign	Date	08-12-20
Previous stage report no.		36212	Report filed and signed by PM? <i>Yes</i>	
Checked By MD on		MD Sign	For filling ☐ Yes ☐ No	

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
☐ Proceed with further work. ATR not required.

Inspection should be done after:

- brickwork & 2 coats plastering is completed
- after cleaning the villa.
- Water proofing, screeding in bathrooms is completed.
- before starting painting, tiling & flooring.

Plastering Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. 9" unplastered area from SFL should be left including in common areas and terraces.
6. Windows must be checked with templates. Plastering must be 3mm margin for lippum work. Tolerance 1/4".
7. Provision of tiles in bathrooms, kitchen & wash areas (rough plastering).
8. Check size of sink bowl. Hole should be 1" to 2" larger. (Tolerance: 1")
9. All doors frames should have 1/2" grooves.
10. Sill top must me of uniform thickness, correct height, at one level & without broken edges.

Certified that all corrections mentioned in the QC report have been completed. Work can proceed to next stage.

Project in-charge	Sign	Date
<i>[Signature]</i>		9/12/2020

Quality Control Check Report. Stage: After Plastering (Apartments)

S No	Room	Skirting Provision (✓ or ✗)	Furnishing around door frame (✓ or ✗)	Beams & columns finishing (✓ or ✗)	Finishing of lofts (✓ or ✗)	Electricity junctions finishing (✓ or ✗)	Windows check (✓ or ✗)	Tiles provision (✓ or ✗)	Sink provision & size (✓ or ✗)	Grooves for door frames (✓ or ✗)	Balcony & terrace sill top finishing (✓ or ✗)	Screeding in bathroom & utility (✓ or ✗)	Screeding in 6" above FFL? (✓ or ✗)
1	Bedroom + M. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet + M. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 - C. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 - C. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 - G. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3 - G. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Bedroom 4 -	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Toilet 4 -	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Lobby + Pufa	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Lobby 2 -	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Terrace/balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Terrace/balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
15	Terrace/balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
16	Portico	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
17	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
18	Other Utility	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
Remarks													

Quality Control Check Report. Stage: After Brickwork (Apartments)

Flat No.	A-708	Others	—	Sl. No.	36212
Company	MPL	Project	MFP	Phase	—
Prepared by	G. RAJESH	Sign	<i>GR</i>	Date	16/10/20
Project Manager	Subha Reddy	Sign	<i>SR</i>	Date	16/10/20
Previous stage report no.	35958	Report filed and signed by PM?		☒ Yes ☐ No	
Apartment No.		Other			
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☐ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☒ Proceed with further work. ATR not required.

Inspection should be done after:

- brickwork is completed
- chicken mesh fixed
- after cleaning the apartment
- electrical conducting work is completed

Brickwork Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. Wall thickness should be as per plan. Use of 4", 6" & 8" blocks must be checked.
6. All walls should have 2 beds of about 2" to 3" thickness with one no. 6 mm or 8 mm rod with M15 CC.
7. Chicken mesh should be used in each and every joint between RCC & Brickwork.
8. Joint between brickwork & beam on external side must be filled.
9. Check room dimensions with working plan. (Tolerance: 1")
10. Diagonals of each room shall be equal. (Tolerance: 2")
11. Balcony sill level should be 3" from SFL. (Tolerance: 1")
12. Check room height with specified height. (Tolerance: 1")
13. Check plumb of walls where ever it appears to be out of plumb. (Tolerance: 1/2")
14. Specify the No. of beams which are not aligned by more than 1" in a room.
15. Door frames must have black Japan coating and wood primer / pellambar - at cost of painter.

Certified that all corrections mentioned in the QC report have been completed. Work can proceed to next stage.

Project in-charge	Sign	Date
S.V. S. Neeloh	<i>SVS</i>	16/10/20

Quality Control Check Report. Stage: After Brickwork (Apartments)

S No	Room	Wall thickness (✓ or ✗)	Beds in walls (✓ or ✗)	Chicken mesh (✓ or ✗)	External brickwork & beam joint (✓ or ✗)	Room Dimensions (✓ or ✗)	Room Dimensions Difference in inches	Diagonal (✓ or ✗)	Diagonal Difference in inches	Balcony sill level (✓ or ✗)	Room Height (✓ or ✗)	Plumb of walls (Good/Avg./Bad)	Alignment of beams and walls - Nos.
1	Bedroom 1 M.B	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	Avg	✓
2	Toilet 1 M.T	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	"	✓
3	Bedroom 2 K.B	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	"	✓
4	Toilet 2 K.T	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	"	✓
5	Bedroom 3 G.B	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	"	✓
6	Toilet 3 G.T	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	Good	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	"	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	"	✓
9	Lobby + Porch	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	"	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	Avg	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	"	✓
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	"	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	"	✓
14	Other												
15	Other												
Remarks													

Quality Control Check Report. Stage: After Brickwork (Apartments)

Quality of edges and corners in all rooms?	☐ Good ☒ Avg. ☐ Bad
Specify rooms that need correction:	

Misc. Checks.

Was 3.75 CFT proportion box provided?	☒ Yes ☐ No
Condition of proportion box?	☐ Good ☒ Avg. ☐ Bad
Was the Apartment cleaned before starting brick work?	☒ Yes ☐ No ☐ Can't say
Is the Apartment cleaned for plastering?	☒ Yes ☐ No
Wastage?	☐ High ☒ Medium ☐ Low
Storage of building material like bricks sand and cement.	☐ Good ☒ Avg. ☐ Bad
Drum (200 lts) provided for curing in each flat?	☒ Yes ☐ No
Remarks:	

Door Frames & Windows check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. Window template depth should be between 2 to 2 1/2" after plastering.
6. Lintel level should be 7'3" from SFL & 7' from FFL. (Tolerance 1")
7. Lofts should be at a height of 7' to 7'3" from FFL. Kitchen plat from should be at a height of 32" or 33" from FFL and 35" or 36" from SFL. (Tolerance 1")
8. Slopes of lofts and kitchen platforms to be checked by using 12" spirit level and check height from floor from 2 or 3 points.
9. Thickness of platforms & lofts should be between 2 & 2.5"
10. Provide single layer table brick at bottom of each door frame without threshold.

Quality Control Check Report Stage: After Brickwork (Apartments)

S No	Room	Door size, face and position (✓ or ✗)	Brick at bottom of door frame (✓ or ✗)	Door lentil level (✓ or ✗)	Door diagonal check (✓ or ✗)	Door Plumb - two sides (✓ or ✗)	Door frame black Japan/ wood primer/Peelambar check (✓ or ✗)	Windows lentil & sill level (✓ or ✗)	Windows size (✓ or ✗)	Windows - template depth & diagonal (✓ or ✗)	Windows - template powder coated (✓ or ✗)	Loft & Kitchen platform required? (Yes or No)	Loft & Kitchen platform provided (✓ or ✗ or NA)	Loft & Kitchen platform slope (✓ or ✗)
1	Bedroom 1 M.B	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M.T	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 K.B	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 K.T	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 G.B	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3 G.T	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby + Pooja	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other													
15	Other													
Remarks:														



MAYFLOWER PLATINUM

Survey no. 82/1, Mallapur, Hyderabad – 500 076.
Owned & Developed by: M/s. Modi Properties Pvt. Ltd.
Head office; 5-4-187/3&4 M G Road Secunderabad.

Details of Additions & Alterations

Flat No	708	Block no.	'A'
Flat Area	1800 sft	Type	Deluxe / Luxury
Buyer Name	Nukala Sarika		
Phone No.	8978989799/8440510004	Email	m.kumar4@sti.co.in

I hereby confirm that I have given the details of the minor additions and alterations that are required in the above referred flat in the pages attached herein. Please complete the changes suggested by me. I agree to pay the charges, if any, for the additions and alterations that I have asked you to make, as per the rates suggested by you. I shall deliver all the materials that are required to be provided by me at the site on or before _____. In case I fail to deliver these items to the site by the specified date, you may complete the works in the flat as per the standard items provided by you.

Buyers sign		Engg. Sign	
Date:	26/8/2020	Date	26/8/2020

Note:

1. Colour shades of paints may vary from batch to batch & company to company. The Builder will not take responsibility of quality of work for dark shades especially green & blue.
2. Shade / colour of natural material like marble and granite can't be guaranteed and may vary from lot to lot. Cracks like appearance in marble is a natural feature and Builder shall not be responsible for repairs or replacement.
3. Availability of bathroom or flooring tiles of the same type /colour/make can not be guaranteed and closest possible type/colour/make may be used in its place.
4. No further change shall be permitted from this day.
5. Please sign on all pages.

Buyers sign:

Engg. Sign:

Date:

26/8/2020

Choice of colours:

Same as model flat A 106

Changes in flooring:

- 1) Same as Model flat A 106, Drawing to Dining hall (big tiles) 3 Bedroom 2x2 roofed tiles.
- 2) Flooring same as model flat include MBR flooring.

Buyers sign:



Engg. Sign:




20/6/2020
Date:

Changes in electrical points: (mark on plan)

Kitchen Entrance wall 1 extra plug point.

Choice of Bathroom tiles, CP fittings & Sanitary ware:

Same as model flat A106

Buyers sign: 

Engg. Sign: 

26/8/20
Date:

Changes in kitchen platform: (mark on plan)

Same as model flat A 106

Other Changes:

— all room in Mesh with windows —

Buyers sign:




Engg. Sign:



Date:

26/8/20

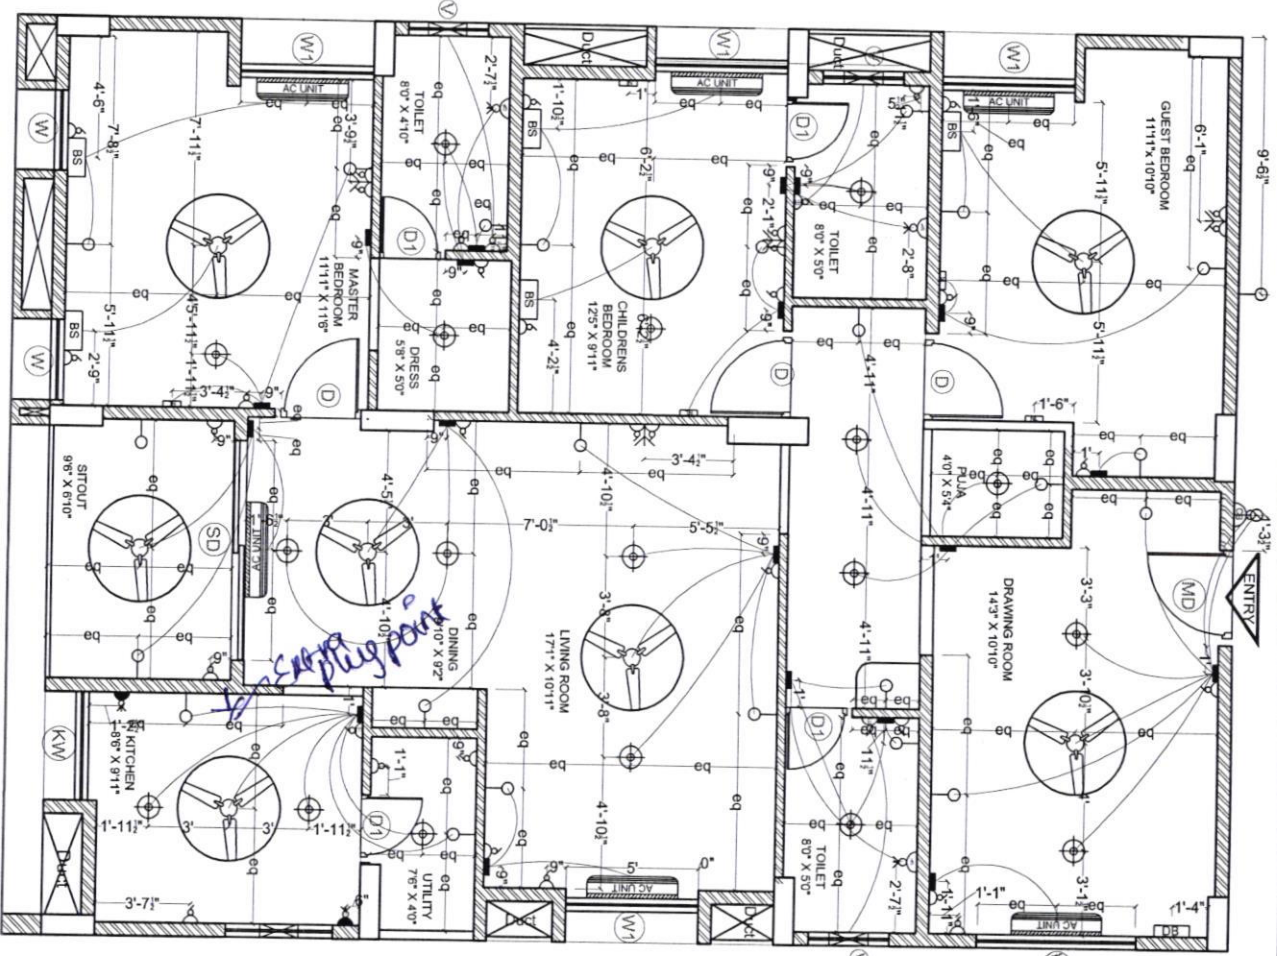

Handwritten signatures and notes in blue ink.

ELECTRICAL LEGEND		
SYMBOL	DESCRIPTION	MOUNTING HT.
	5 amp outlet with switch on raw power	3'-6" from FFL
	Geyser Point	8'-3" from FFL
	15 amp outlet with switch on raw power (for fridge)	below counter
	Wall light	6'-6" from FFL
	Ceiling fan	ceiling ht
	TV point	3'-6" from FFL
	Telephone point	3'-6" from FFL
	LAN / Ethernet	3'-6" from FFL
	Ceiling light	ceiling ht
	Switch board	4'-6" from FFL
	Bed Side Switch board	2'-0" from FFL
	Distribution board	5'-6" from FFL
	Exhaust point	7'-6" from FFL
	AC Point	8'-0" from FFL
	AC Unit	as per standard
	Ceiling bell switch	4'-6" from FFL
	Ceiling bell	8'-0" from FFL
	Exhaust	7'-0" from FFL

Description

Direction

Owners & Developers :

Date :

02.12.2019

Promoted by

ELECTRICAL PLAN OF FLAT-A8




BNC Estates
Project Name & Phase :

Mayflower Grande

Prepared By :
Approved By :

Soham Modi
N.T.S

Modi Properties & Investments Pvt. Ltd.
Phone:+91-40-66335551

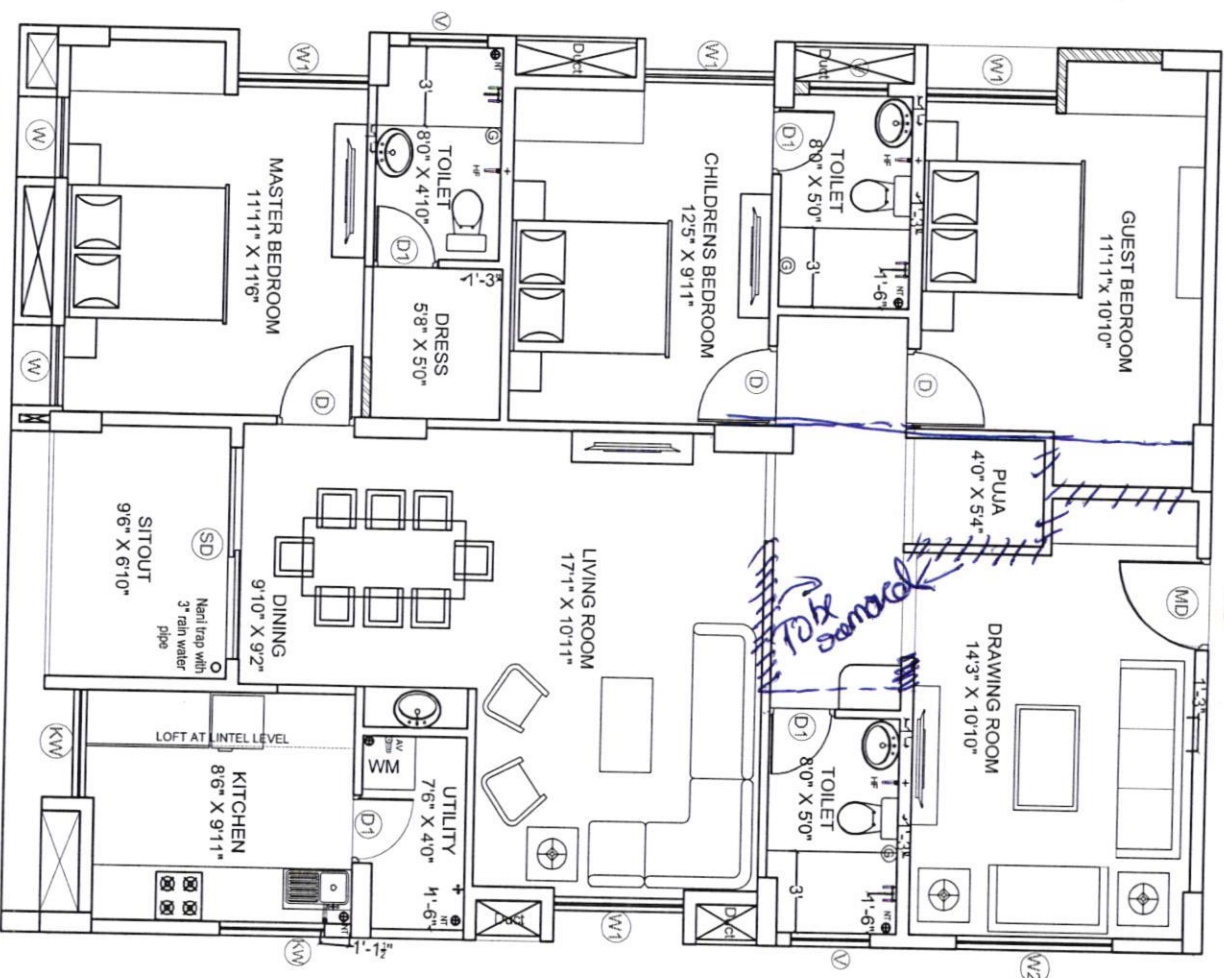

LEGEND

+	HEALTH FAUCET
◊	ANGLE VALVE
●	NANI TRAP
○	3" RAIN WATER PIPE
⊙	GEYSER POINT
⊞	WALL MIXTURE
+	TAP / LONG BODY

Handwritten signature and date: 09.01.2020

Description

Direction

Owners & Developers :

Date :

09.01.2020

Promoted by

PLUMBING PLAN OF A8




Modi Properties Pvt. Ltd.
Project Name & Phase :
Mayflower Platinum

Prepared By :
Approved By :
Scale :

Soham Modi
N.T.S

Modi Properties &
Investments Pvt. Ltd.
Phone: +91 40-66335551

A8

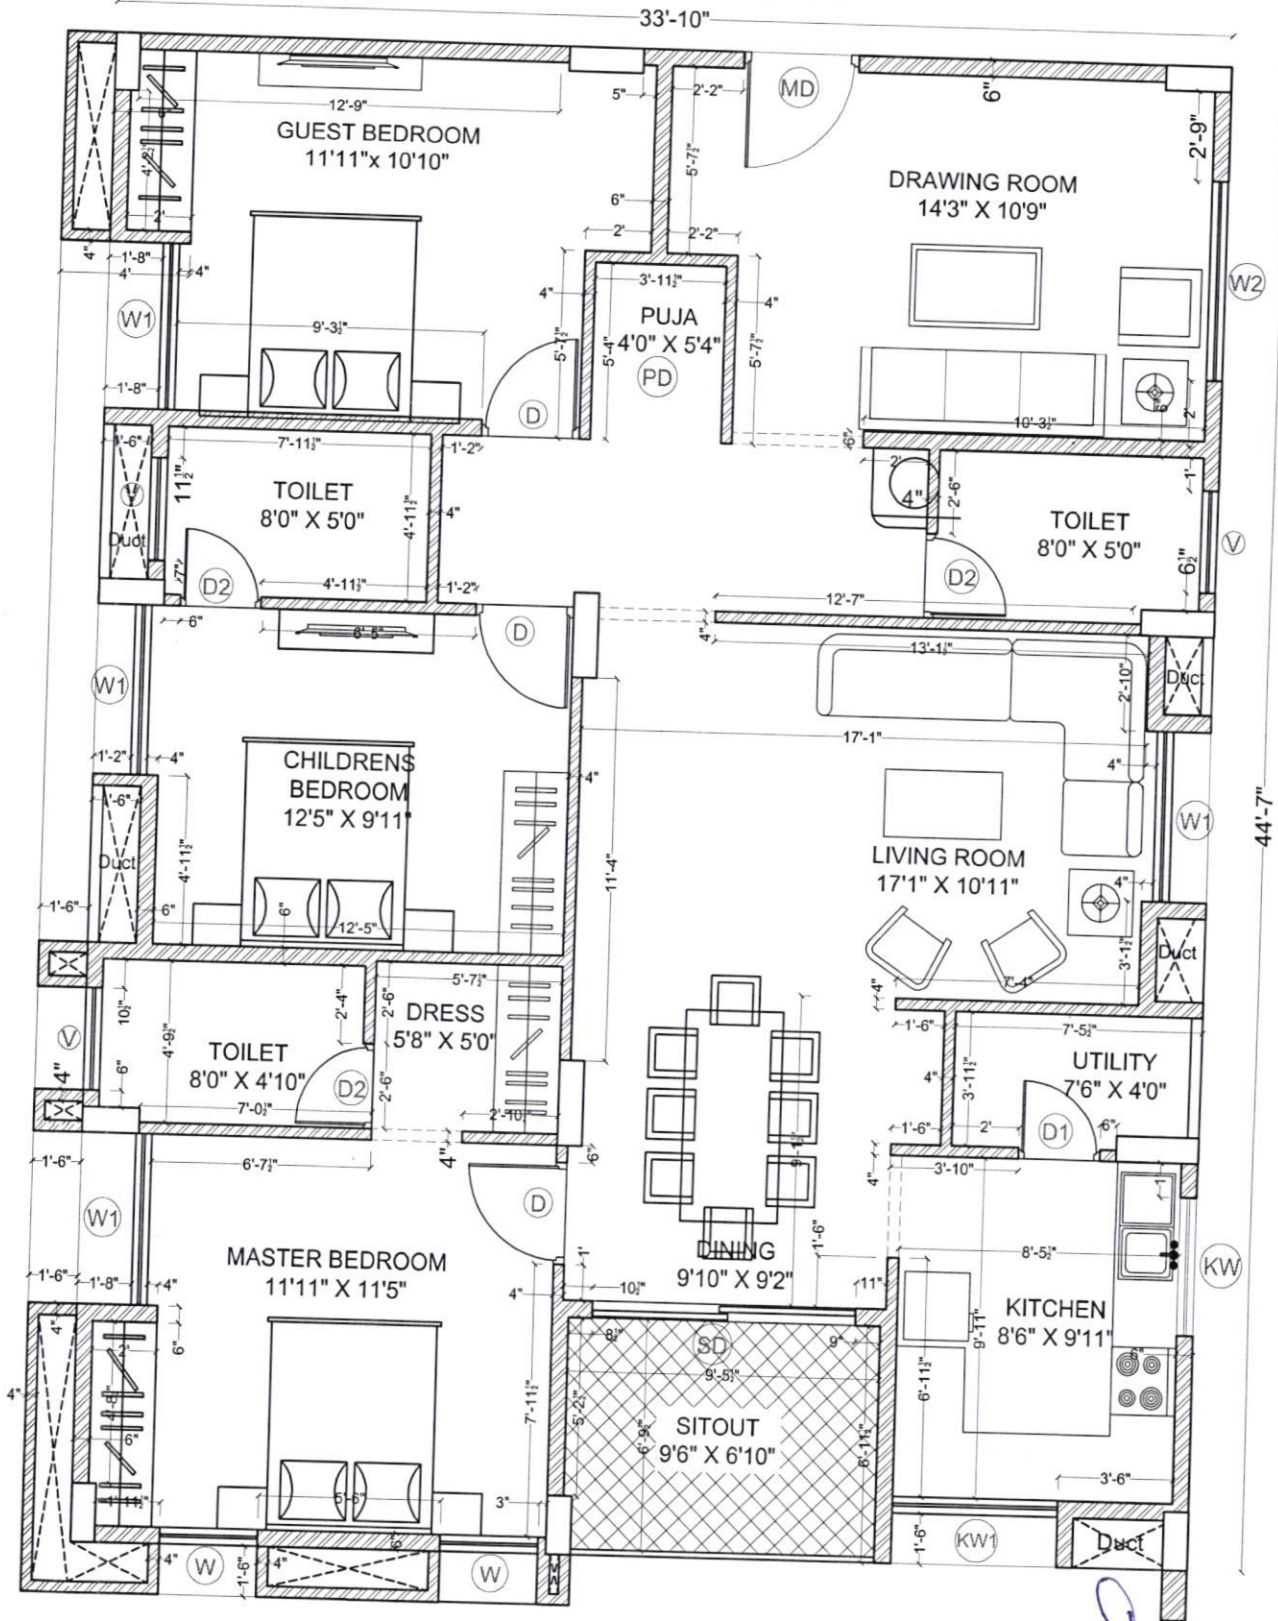

ant had *Shravan G*

Description	Direction	Owners & Developers :	Date :	18.03.2020	Promoted by
WORKING DRAWING OF FLAT.NO.A-8		Modi Properties Pvt Ltd.	Prepared By :		Modi Properties Pvt. Ltd Phone:+91-40-66335551
		Project Name & Phase :	Approved By :	Soham Modi	
		MAYFLOWR PLATINUM	Scale :	N.T.S	
