

MAYFLOWER PLATINUM

Survey no. 82/1, Mallapur, Hyderabad – 500 076.
Owned & Developed by: M/s. Modi Properties Pvt. Ltd.
Head office; 5-4-187/3&4 M G Road Secunderabad.

Details of Additions & Alterations

Flat No	108	Block no.	'A'
Flat Area	1800 sft	Type	Deluxe / Luxury
Buyer Name	A Mohan Ganesh/G.Sita Madhavi		
Phone No.	9849028941/9949469853(C), 040-48574237	Email	gsitamadhavi@gmail.com

I hereby confirm that I have given the details of the minor additions and alterations that are required in the above referred flat in the pages attached herein. Please complete the changes suggested by me. I agree to pay the charges, if any, for the additions and alterations that I have asked you to make, as per the rates suggested by you. I shall deliver all the materials that are required to be provided by me at the site on or before _____. In case I fail to deliver these items to the site by the specified date, you may complete the works in the flat as per the standard items provided by you.

Buyers sign	<i>Situmth</i>	Engg. Sign	<i>Gravand</i>
Date:	2/7/2020	Date	09/06/2020

Note:

1. Colour shades of paints may vary from batch to batch & company to company. The Builder will not take responsibility of quality of work for dark shades especially green & blue.
2. Shade / colour of natural material like marble and granite can't be guaranteed and may vary from lot to lot. Cracks like appearance in marble is a natural feature and Builder shall not be responsible for repairs or replacement.
3. Availability of bathroom or flooring tiles of the same type /colour/make can not be guaranteed and closest possible type/colour/make may be used in its place.
4. No further change shall be permitted from this day.
5. Please sign on all pages.

Buyers sign:

Engg. Sign:

Date:

Choice of colours:

Same as model flat - A 106

Changes in flooring:

No additional cost for ceiling & only the floor tiles.

1) MBR & Drawing & living for additional same as A 106.

3) We need three exhaust fans in three bathroom.

Buyers sign:

[Signature]

Engg. Sign:

[Signature]

Date:

02/12/2020

Changes in electrical points: (mark on plan)

Extra in kitchen 2 points 5amp, 16amp



Choice of Bathroom tiles, CP fittings & Sanitary ware:

- 1) MBR WC change to EWC to SWC
- 2) Door frame bigger at common bathroom.



Buyers sign:

Blank


Engg. Sign:

[Signature]

02/4/2020


Changes in kitchen platform: (mark on plan)

→ same as model flat



Other Changes:

- ① ~~Common~~ wall removing at Drawing room wall same as living wall (marked as plan)
- ② all windows - 3 track with mesh.



Buyers sign:

Stenul


Engg. Sign:

Alfauad

Date:


02/11/2020

A8

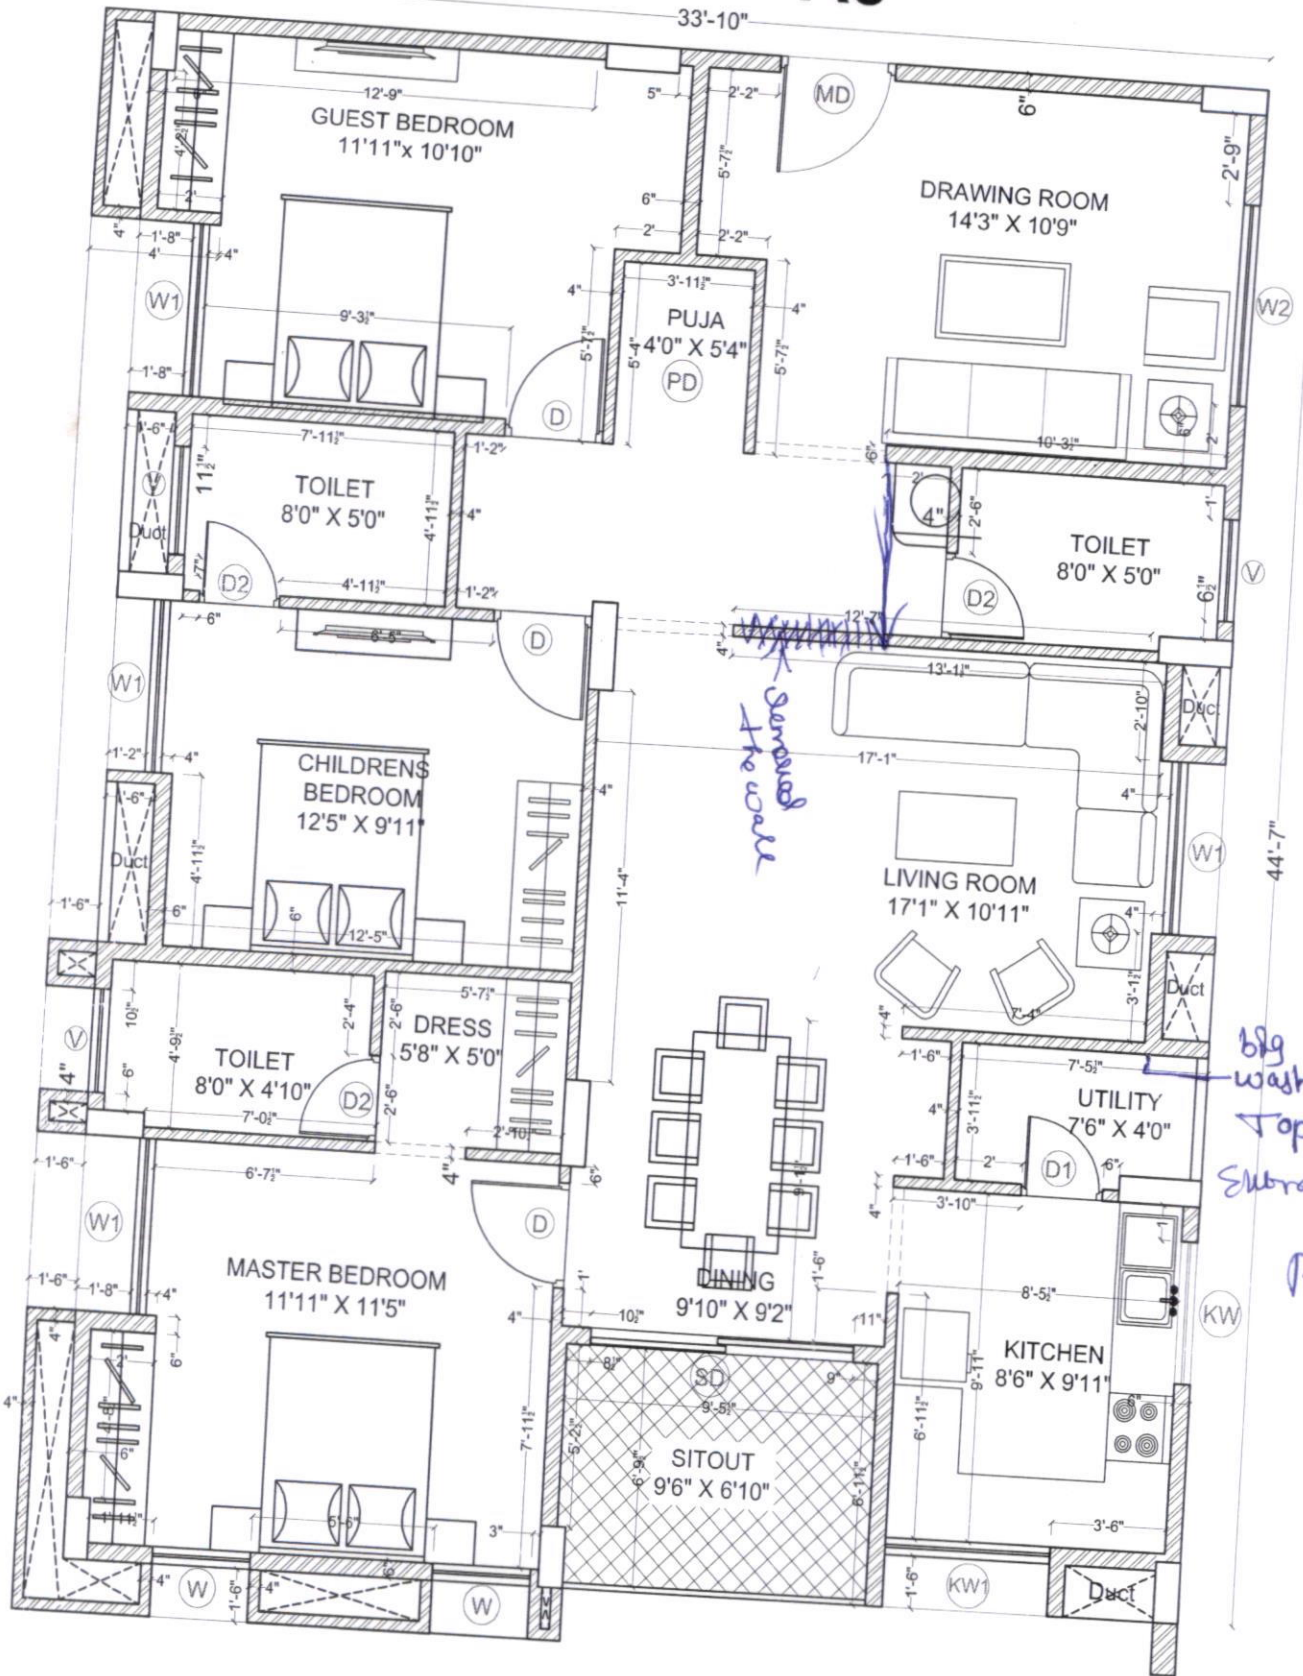

Sitout *Good* *02/11/2020*

Description	Direction	Owners & Developers :	Date :	18.03.2020	Promoted by
WORKING DRAWING OF FLAT.NO.A-8	N 	Modi Properties Pvt Ltd. Project Name & Phase :	Prepared By :		

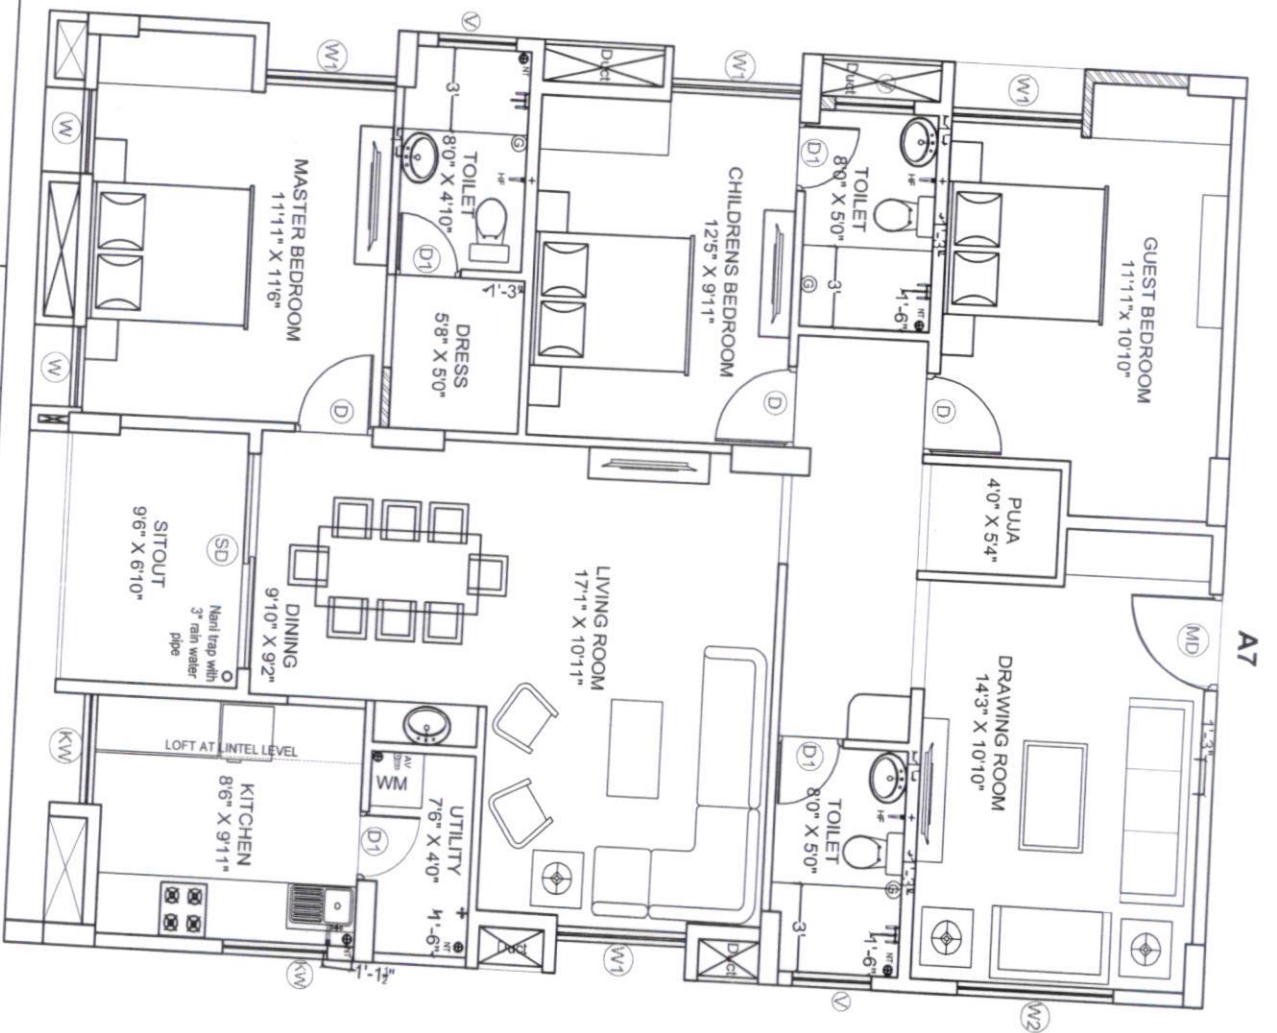

LEGEND

+	HEALTH FAUCET
⊥	ANGLE VALVE
●	MAN TRAP
○	3" RAIN WATER PIPE
⊕	GEASER POINT
E	WALL MIXTURE
+	TAP / LONG BODY

PLUMBING PLAN OF A8

Description

Direction

Owners & Developers :

Date :

Prepared By :

09.01.2020

Promoted by



Modi Properties Pvt. Ltd.
Project Name & Phase :
Mayflower Platinum

Approved By :

Soham Modi


Investments Pvt. Ltd.

Scale :

N.T.S

Phone: +91-40-66335551

Handwritten notes:
09/01/20
K. J. J.
St. J.

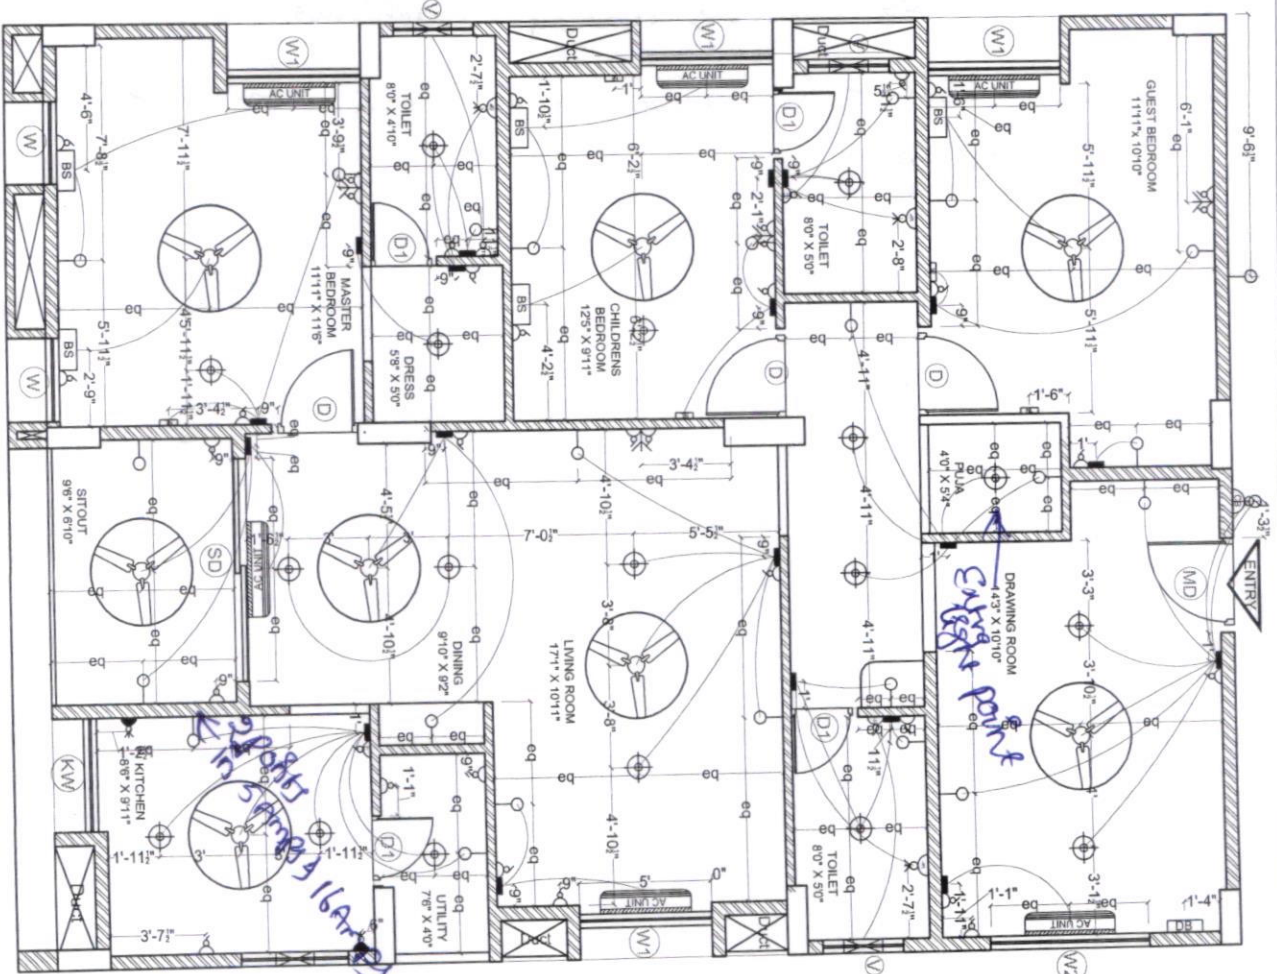

ELECTRICAL LEGEND		
SYMBOL	DESCRIPTION	MOUNTING HT.
	5 amp outlet with switch on raw power	3'-6" from FFL
	Geyser Point	8'-3" from FFL
	15 amp outlet with switch on raw power (for fidge)	below counter
	Wall light	6'-6" from FFL
	Ceiling fan	ceiling ht.
	TV point	3'-6" from FFL
	Telephone point	3'-6" from FFL
	LAN / Ethernet	3'-6" from FFL
	Ceiling light	ceiling ht.
	Switch board	4'-6" from FFL
	Bed Side Switch board	2'-0" from FFL
	Distribution board	5'-6" from FFL
	Exhaust point	7'-6" from FFL
	AC Point	8'-0" from FFL
	AC Unit	as per standard
	Ceiling bell switch	4'-6" from FFL
	Ceiling bell	8'-0" from FFL
	Exhaust	7'-0" from FFL

Description

Direction

Owners & Developers :

Date :

02.12.2019

Promoted by

BNC Estates

Prepared By :

Modi Properties & Investments Pvt. Ltd.

Project Name & Phase :

Approved By :

Phone: +91-40-66335551



Mayflower Grande

Signature

N.T.S

ELECTRICAL PLAN OF FLAT-A8

Signature
02/12/2019

Quality Control Check Report. Stage: After Finishing Stage III (Apartments)

Flat No	A-108	Other	Sl. No.	38004
Company	MPL	Project	Phase	
Prepared by	T.Vinod Kumar	Sign	Date	19-07-21
Project Manager	Subba Reddy	Sign	Date	19-07-21
Previous stage report no.	37121	Report filed and signed by PM	☒ Yes ☐ No	
Checked By MD on	MD Sign	For filling	☐ Yes ☐ No	

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after :

- Completing stage II works.
- Complete works like doors, windows, grills, electrical wiring, switches, french door glass, etc.
- In case of modular kitchen provide platform, granite and dado and modular kitchen in this stage.
- Provide video door phone in this stage.
- Possession for wood work cannot be given until QC check for stage III is completed and all corrections mentioned in the report are made.

Certified that all corrections mentioned in the QC report have been completed. Work can proceed to next stage.

Project in-charge	Sign	Date
T.Vinod Kumar	[Signature]	20/7/2021

Miscellaneous check:

Modular kitchen to be provided	☒ Yes ☐ No	Modular kitchen provided	☐ Yes ☒ No
Modular kitchen workman ship	☐ Good ☐ Avg ☐ Poor	Modular kitchen granite & dado workman ship & finishing	☐ Good ☐ Avg ☐ Poor
Video door phone /wifi cam to be provided	☒ Yes ☐ No	Video door phone/wifi cam provided	☐ Yes ☒ No
Painting marks and drops are cleaned from floor, windows, walls.	☐ Good ☐ Avg ☒ Poor		

Quality Control Check Report. Stage: After Finishing Stage III (Apartments)

Rate the quality of (Good ✓, Avg. X, Poor – needs correction XX, NA)													
S No	Room	Door, door knob & door stopper fitting	Door, door knob & door stopper cleaning	Window grills & quality	Window grills fitting & finishing	Windows quality	Window fitting & finishing	Balcony railing quality & finishing	French door quality & fitting	CP jali quality and fitting	Edge building	Switch boards fitting & covering with plastic covers	Junction box covers painting
1	Bedroom 1-M. Bed	X	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Bedroom 2-C. Bed	✓	✓	✓	X	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 3-C. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	X	✓
4	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	X	✓	✓
5	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Lobby 1- Pooja	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Utility / balcony 2	XX	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Toilet 1- M. Toi	X	X	✓	X	✓	✓	✓	✓	✓	✓	X	✓
12	Toilet 2- C. Toi	✓	✓	✓	X	✓	✓	✓	✓	✓	✓	✓	✓
13	Toilet 3- C. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other												
15	Other												

Remarks: Note: 1. In utility door to be changed

2. In utility grill not fitted.

3. In balcony for railing glass not fitted.

4. Painting work to be improve.

Construction Division
Additions & Alteration Charges Approval Form

Company Name:	Modi Properties Pvt Ltd	Site	May Flower Platinum
Name of the customer	A- mohan Laxesh / G. Sita Madhavi		
Villa/ Flat No.	A- 108		
Sl.No	Description	Amount	
1	Total extra Charges	51,390 = ~	
2	Total refundable amount	—	
3	Net amount to be charges (if any)	51,390 = ~	
4	Net amount to be refunded (if any)	—	
Remarks :			
Approved by Project Manager		Approved by Design Team	
Date: 20/10/2021		Date	
Sign: 		Sign:	
		Approved by MD	
		Date	
		Sign:	

Note: 1. Enclose measurement & estimate sheet. 2. Send scanned copy by email to plans@modiproperties.com & CR. 3. Maintain originals in A&A of customers at site.

ESTIMATE SHEET

ESTIMATE SHEET								
Company Name:		MPL		Approved by:				
Project:		May Flower Platinum		Sign:				
Work Description:		Extra Specs						
Flat No.		A-108						
Prepared By		K. Narendar Reddy						
Date:		20-10-2021						
S No.	Item Head	Item Description		Quantity	Units	Rate	Amount	Item Head Total
1	Electrical points	5amps Switch & socket point near in kitchen		1.00	nos	450.00	450.00	
2	Big Tiles laying	Drawing, Dining, Living, Master Bedroom		849.00	Sft	60.00	50940.00	
		Total						51390.00
	Amount in words - Fifty One Thousand Three Hundred and Ninety Rupees only							

MEASUREMENT SHEET

MEASUREMENT SHEET										
Company Name:		MPL		Approved by:						
Project:		May Flower Platinum		Sign:						
Work Description:		Extra Specs								
Flat No.		A-108								
Prepared By		K. Narendar Reddy								
Date:		20-10-2021								
S No.	Item Head	Item Description		Length	Width	Height	Nos.	Quantity	Units	Item Head Total
1	Electrical points	5amps Switch & socket point near in kitchen		1.00	1.00	1.00	1.00	1.00	nos	1.00
2	Big Tiles laying	Drawing room		306.00	1.00	1.00	1.00	306.00	sft	
		Living and Dining		329.00	1.00	1.00	1.00	329.00	sft	
		Master Bedroom		214.00	1.00	1.00	1.00	214.00	sft	
										849.00

Quality Control Check Repot. Stage: After Finishing Stage II (Apartments)

Flat No	A-108	Other	Sl. No.	3721
Company	mfp	Project	Phase	-
Prepared by	G. SRINIVAS Rao.	Sign	Date	15/02/21
Project Manager	Subba Reddy.	Sign	Date	15/02/21
Previous stage report no.	36658	Report filed and signed by PM	☒ Yes ☐ No	
Checked By MD on		MD Sign	For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- Completion of flooring, bathroom /utility tiles, first coat of paint.
- Completion of doors, windows, grills, electrical wiring, switches must be done in next stage
- False ceiling must be completed before flooring.
- Kitchen platform, granite and dado must be completed where modular kitchen is not provided.
- Provide granite soffit for main door and balconies in this stage.

Certified that all corrections mentioned in the QC report have been completed Work can proceed to next stage.

Project in-charge	Sign	Date
<i>[Signature]</i>	<i>[Signature]</i>	16/2/2021

Miscellaneous check:

Main door fixed with lock & stopper	☒ Yes ☐ No	Granite soffit for balcony provided	☒ Yes ☐ No
Granite soffit for balcony required	☒ Yes ☐ No	Balcony granite soffit edge polishing	☐ Good ☒ Avg ☐ Poor
Balcony granite soffit workmanship	☐ Good ☒ Avg ☐ Poor	Granite soffit for main door provided	☐ Yes ☐ No
Granite soffit for main door required	☐ Yes ☐ No	Main door granite soffit edge polishing	☐ Good ☐ Avg ☐ Poor
Main door granite soffit workmanship	☐ Good ☐ Avg ☐ Poor		

Quality Control Check Repot. Stage: After Finishing Stage II (Apartments)

		Rate the quality of (Good ✓, Avg. X, Poor – needs correction XX, NA)												
Tiling & granite work		Workmanship of tiling	White cement filling around CPVC lines	Corners finishing	Finishing near doors	Finishing on top of tiles	Finishing near ventilators	Step at bathroom entrance / utility	Step for shower / pot wash	Tile joint grouting	Granite platform finishing and edge polishing	Granite platform slope	Granite platform height	Finishing under granite platform
S No	Room													
1	Toilet 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 4	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Wash basin in dining area	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Other													
9	Other													
Remarks														

Quality Control Check Report. Stage: After Finishing Stage II (Apartments)

Flooring & painting		Rate the quality of (Good ✓, Avg. ✕, Poor – needs correction ✕ ✕, NA)												
S No	Room	Color variation of floor tiles	Flooring workman ship & grouting	Skirting size (3")	Skirting workmanship	Plastering above skirting	Plastering & finishing of walls	Crack filling	Loft Finishing	Windows check	General quality of painting & finishing	Door & frame painting quality	Door beading, luppam and painting quality	Edge building
1	Bedroom 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Bedroom 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
Remarks														

Quality Control Check Repot. Stage: After Plumbing & Electrical (Apartments)

Flat No.	A-108	Other	Sl. No.	36658
Company	MPL	Project	Phase	
Prepared by	S. SRINIVAS RAO	Sign	Date	18/12/20
Project Manager	Subba Reddy	Sign	Date	18/12/20
Previous stage report no.		35346	Report filed and signed by PM?	☒ Yes ☐ No
Additions & alterations sheet date		09/06/20	All pages signed by engineer & customer?	☒ Yes ☐ No
Checked By MD on		MD Sign	For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- after cleaning the apartment.
- before starting painting, tiling & flooring.
- electrical conduct, waterproofing & plumbing work is completed (for stage II only).
- additions & alterations is finalized and signed. In case there are no additions and alterations printout of email by PM to CR confirming the same must be filed.
- additions & alterations sheets to be transferred to QC file. QC to check if A&A are made as per request.

Certified that all corrections mentioned in the QC report have been completed Work can proceed to next stage.

After Plumbing & Electrical Check.

Notes:

1. Mark ☒ for correct or minor mistake which does not require correction
2. Mark ☒ for minor mistake that requires minor correction.
3. Mark ☒ for major mistake that requires correction by replacement or re-fixing.
4. Mark ☒ for major mistake that cannot be corrected.
5. Location of CPVC & PVC fittings must be checked as per measurements given in circular. Tolerance 1".
6. Location, height and spirit level of electrical points must be checked as per measurements given in circular & plan. Tolerance 1".
7. Civil work near pipes in balcony & utility must be neat and mortar should be removed from the pipes.
8. Water proofing must cover all pipes & check height above SFL.
9. Fasteners must be used as specified in circular. Especially check fixing of PVC pipes.
10. Height of DB box must be 6" below false ceiling level or 12" below slab level.
11. In case of many changes in civil work, electrical work and plumbing work, a new drawing must be prepared at HO and approved by MD.

Project in-charge	Sign	Date
Subba Reddy		21/12/2020

Quality Control Check Report. Stage: After Plumbing & Electrical (Apartments)

S No	Room	Civil work near pipes in balcony & utility ⁷ (✓ or ✕)	CPVC & PVC Check ⁵ (✓ or ✕)	Electrical points check ⁶ (✓ or ✕)	Water proofing check ⁸ (✓ or ✕)	Proper use of fasteners check ⁹ (✓ or ✕)	Placement of DB ¹⁰ (✓ or ✕)	Placement of Generator changeover (✓ or ✕)
1	Bedroom 1 - B.B.	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 - B.T.	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 - B.B.	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 - B.T.	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 - B.B.	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3 - B.T.	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓
9	Lobby 1	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓
14	Other POOSA	✓	✓	✓	✓	✓	✓	✓
15	Other	✓	✓	✓	✓	✓	✓	✓
Remarks								


Remarks on additions & alteration sheet:

Signed by engineer,	☒ Yes ☐ No	Signed by customer,	☒ Yes ☐ No
Revised drawing required from HO	☐ Yes ☒ No	Approved revised drawing attached	☐ Yes ☒ No


Quality Control Check Report. Stage: After Plumbing & Electrical (Apartments)

Miscellaneous check


Screeding done on walls upto 12" outside bathroom/utility	☒ Yes	☐ No
Bathroom /utility filled with 4" water for water proof check	☒ Yes	☐ No
Hole packing done around all pipes in ceiling and internal walls	☒ Yes	☐ No
Remarks:		

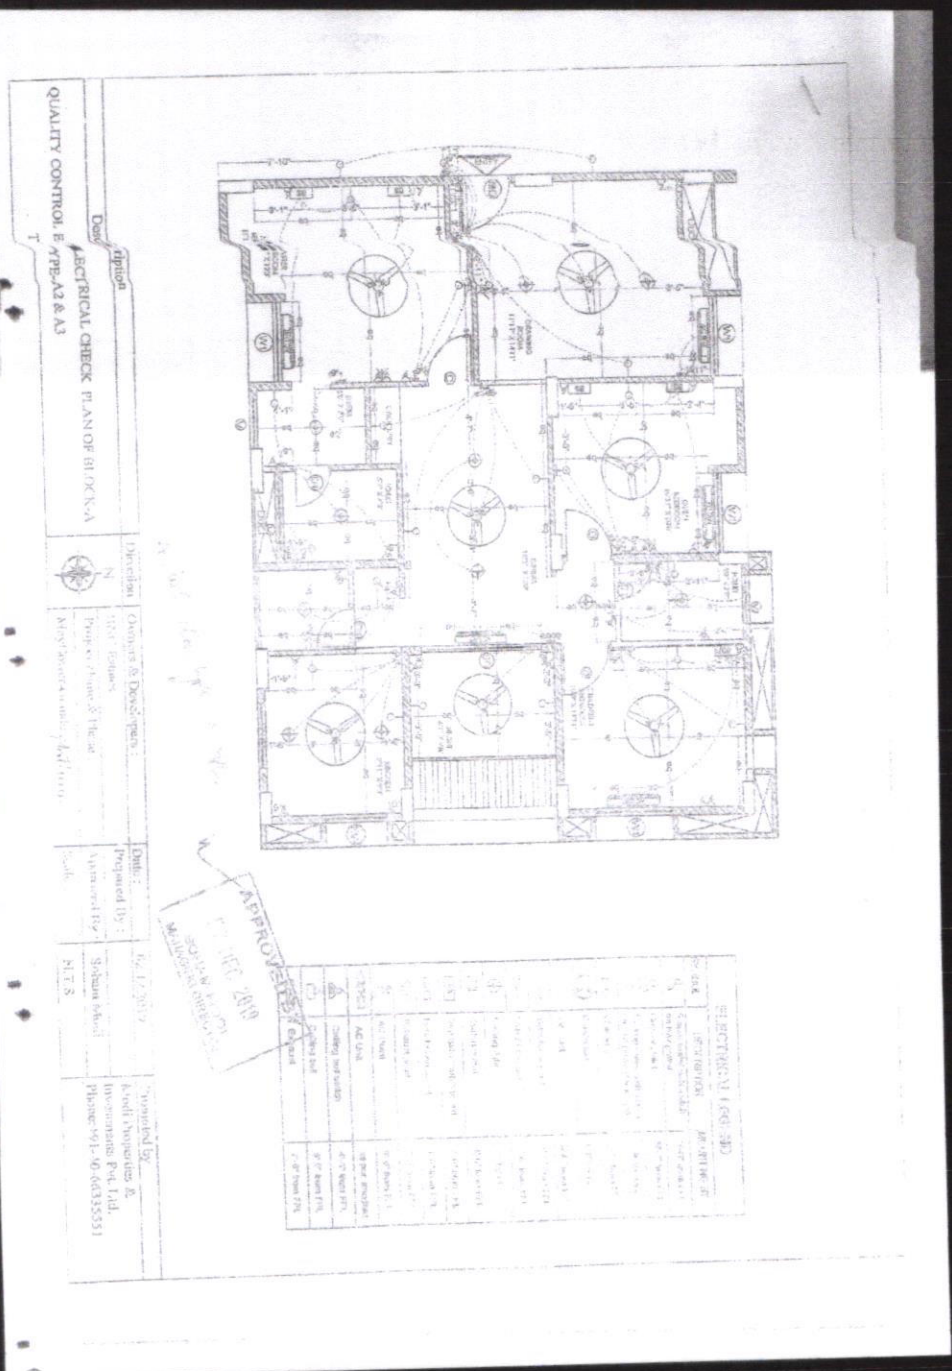


APPROVED BY
10 FEB 2020
SOHAM MODI
MANAGING DIRECTOR




Type-A1




Type-A2




Type-A7




Type-B1




Type-A1



Type-A2



Type-A7



Type-B1

A - 108 plumb type - 3 mpl

Description	Direction	Owners & Developers :	Date :	Promoted by
QC PLUMBING CHECK PLAN OF A - BLOCK	N	Modi Properties Pvt. Ltd.	08.02.2020	Modi Properties & Investments Pvt. Ltd.
		Project Name & Phase :	Prepared By :	
		Mayflower Platinum	Approved By :	
			Scale :	
				Phone: +91-40-66335551

Quality Control Check Report. Stage: After Plastering (Apartments)

Flat No.	A-108	Other	Sl. No.	35346
Company	MPL	Project	Phase	-
Prepared by	T. Vinod Kumar	Sign	Date	06/05/20
Project Manager	Subba Reddy	Sign	Date	06/05/20
Previous stage report no.	35187	Report filed and signed by PM?	☒ Yes ☐ No	
Checked By MD on		MD Sign	For filling	☐ Yes ☐ No
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.				

Inspection should be done after:

- brickwork & 2 coats plastering is completed
- after cleaning the apartment.
- water proofing, screeding in bathrooms is completed.
- before starting painting, tiling & flooring.

Plastering Check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. 9" unplastered area from SFL should be left including in common areas and terraces.
6. Windows must be checked with templates. Plastering must be 3mm margin for lippum work. Tolerance 1/4".
7. Provision of tiles in bathrooms, kitchen & wash areas (rough plastering).
8. Check size of sink bowl. Hole should be 1" to 2" larger. (Tolerance: 1")
9. All doors frames should have 1/2" grooves.
10. Sill top must be of uniform thickness, correct height, at one level & without broken edges.

Certified that all corrections mentioned in the QC report have been completed. Work can proceed to next stage.

Project in-charge	Sign	Date
S. V. S. Reddy	[Signature]	20/05/20

Quality Control Check Report. Stage: After Plastering (Apartments)

S No	Room	Skirting Provision (✓ or X)	Finishing around door frame (✓ or X)	Beams & columns finishing (✓ or X)	Finishing of lofts (✓ or X)	Electrical junctions finishing (✓ or X)	Window check ⁶ (✓ or X)	Tiles provision (✓ or X)	Sink provision & size (✓ or X)	Grooves for door frames (✓ or X)	Balcony & terrace sill top finishing (✓ or X)	Screeding in bathroom & utility (✓ or X)	Screeding in 6" above FFL? (✓ or X)
1	Bedroom 1 M. Bed	✓	✓	✓	-	✓	✓	✓	-	✓	-	✓	✓
2	Toilet 1 M.T.	-	✓	✓	-	✓	✓	✓	-	✓	-	✓	✓
3	Bedroom 2 G. Bed	✓	✓	✓	-	✓	✓	✓	-	✓	-	✓	✓
4	Toilet 2 C.T.	-	✓	✓	-	✓	✓	✓	-	✓	-	✓	✓
5	Bedroom 3 G. Bed	✓	✓	✓	-	✓	✓	✓	-	✓	-	✓	✓
6	Toilet 3-	-	-	✓	-	✓	✓	✓	-	✓	-	✓	✓
7	Drawing	✓	✓	✓	-	✓	✓	✓	-	✓	-	✓	✓
8	Dining	✓	✓	✓	-	✓	✓	✓	-	✓	-	✓	✓
9	Lobby 1-	-	-	-	-	-	-	-	-	-	-	-	-
10	Utility / balcony 1	✓	-	✓	-	✓	✓	✓	-	✓	✓	✓	✓
11	Utility / balcony 2	-	✓	✓	-	✓	✓	✓	-	✓	-	✓	✓
12	Utility / balcony 3	-	-	-	-	-	-	-	-	-	-	-	-
13	Kitchen	✓	-	✓	✓	✓	✓	✓	-	-	-	✓	✓
14	Other												
15	Other												
Remarks		1. In both toilets chipping is done for walls, but not packed. 2. In G. Bed plastering at template not done. 3. In kitchen chipping is done for kitchen wall & it was not packed. 4. Kitchen platform not casted.											

Quality Control Check Report. Stage: After Brickwork (Apartments)

Flat No.	A-108	Others	Sl. No.	35187
Company	MPL	Project	Phase	—
Prepared by	G. RAJESH	Sign	Date	21/01/2020
Project Manager	Subba Reddy	Sign	Date	21/01/2020
Previous stage report no.	34708	Report filed and signed by PM?	Yes ☒ No ☐	
Apartment No		Other	Yes ☐ No ☐	
Checked By MD on	MD Sign	Forfilling	Yes ☐ No ☐	

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- brickwork is completed
- chicken mesh fixed
- after cleaning the apartment
- electrical conducting work is completed

Brickwork Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. Wall thickness should be as per plan. Use of 4", 6" & 8" blocks must be checked.
6. All walls should have 2 beds of about 2" to 3" thickness with one no. 6 mm or 8 mm rod with M15 CC.
7. Chicken mesh should be used in each and every joint between RCC & Brickwork.
8. Joint between brickwork & beam on external side must be filled.
9. Check room dimensions with working plan. (Tolerance: 1")
10. Diagonals of each room shall be equal. (Tolerance: 2")
11. Balcony sill level should be 3'3" from SFL. (Tolerance: 1")
12. Check room height with specified height. (Tolerance: 1")
13. Check plumb of walls where ever it appears to be out of plumb. (Tolerance: 1/2")
14. Specify the No. of beams which are not aligned by more than 1" in a room.
15. Door frames must have black Japan coating and wood primer / pellambar — at cost of painter.

Certified that all corrections mentioned in the QC report have been completed. Work can proceed to next stage.

Project Charge	Sign	Date
S.V.S. Reddy		23/01/2020

Quality Control Check Report. Stage: After Brickwork (Apartments)

S No	Room	Wall thickness (✓ or ✗)	Beds in walls (✓ or ✗)	Chicken mesh (✓ or ✗)	External brickwork & beam joint (✓ or ✗)	Room Dimensions (✓ or ✗)	Room Dimensions Difference in inches	Diagonal (✓ or ✗)	Diagonal Difference in inches	Balcony sill level (✓ or ✗)	Room Height (✓ or ✗)	Plumb of walls (Good/Avg./Bad)	Alignment of beams and walls - Nos.
1	Bedroom 1 M.B	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M.T	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 K.B	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 K.T	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 G.B	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3 C.T	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby L.	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other												
15	Other												
Remarks													

Quality Control Check Repot. Stage: After Brickwork (Apartments)

Quality of edges and corners in all rooms?	☐ Good ☒ Avg. ☐ Bad
Specify rooms that need correction:	

Misc. Checks.

Was 3.75 CFT proportion box provided?	☒ Yes ☐ No
Condition of proportion box?	☐ Good ☒ Avg. ☐ Bad
Was the Apartment cleaned before starting brick work?	☒ Yes ☐ No ☐ Cant' say
Is the Apartment cleaned for plastering?	☒ Yes ☐ No
Wastage?	☐ High ☒ Medium ☐ Low
Storage of building material like bricks sand and cement.	☐ Good ☒ Avg. ☐ Bad
Drum (200 lts) provided for curing in each flat?	☒ Yes ☐ No
Remarks:	

Door Frames & Windows check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✕ for minor mistake that requires minor correction.
3. Mark ✕✕ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✕✕✕ for major mistake that cannot be corrected.
5. Window template depth should be between 2 to 2 ½" after plastering.
6. Lintel level should be 7'3" from SFL & 7' from FFL. (Tolerance 1")
7. Lofts should be at a height of 7' to 7'3" from FFL. Kitchen plat from should be at a height of 32" or 33" from FFL and 35" or 36" from SFL. (Tolerance 1")
8. Slopes of lofts and kitchen platforms to be checked by using 12" spirit level and check height from floor from 2 or 3 points.
9. Thickness of platforms & lofts should be between 2 & 2.5".
10. Provide single layer table brick at bottom of each door frame without threshold.

Quality Control Check Report. Stage: After Brickwork (Apartments)

S No	Room	Door size, face and position (✓ or X)	Brick at bottom of door frame (✓ or X)	Door lintel level (✓ or X)	Door diagonal check (✓ or X)	Door Plumb - two sides (✓ or X)	Door frame black Japan/wood primer/Peelambar check (✓ or X)	Windows lintel & sill level (✓ or X)	Windows size (✓ or X)	Windows - template depth & diagonal (✓ or X)	Windows - template powder coated (✓ or X)	Loft & Kitchen platform required? (Yes or No)	Loft & Kitchen platform provided (✓ or X or NA)	Loft & Kitchen platform slope (✓ or X)
1	Bedroom 1	M.B	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1	M.T	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2	K.B	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2	K.T	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3	G.B	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	C.T	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing		✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining		✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby 1		✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1		✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2		✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3		✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen		✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other													
15	Other													
Remarks:														

company	Mpl	Proposed A&A										
Project : May Flower Platinum												
type of flat luxury												
Proposed A&A												
S.No	flat no	choice of colours	changes in flooring	changes in electrical point	choice of bathrooms, tiles, cp fittings&sanitary	changes in kitchen platform	other changes					
1												
	A-108	same as model flat A 105	same as model flat	same as model flat A 106	same as model flat A 106	same As model flat 106	Nil					
