

Construction Division
Additions & Alteration Charges Approval Form

Company Name:	Modi Properties Pvt Ltd	Site	May Flower Platinum
Name of the customer	G. Bhaskar Vinay		
Villa/ Flat No.	C - 1003		
Sl.No	Description	Amount	
1	Total extra Charges	Nil	
2	Total refundable amount	-	
3	Net amount to be charges (if any)	-	
4	Net amount to be refunded (if any)	-	
Remarks :			
Approved by Project Manager		Approved by Design Team	
Date 17/5/2022		Date	
Sign: [Signature]		Sign:	

Note: 1. Enclose measurement & estimate sheet. 2. Send scanned copy by email to plans@modiproperties.com & CR. 3. Maintain originals in A&A of customers at site.

ATR on Quality Control Check Repot. (Apartments)

Flat No	C-103	QC report stage		Sl. No.	39092
Company	MPL	Project	MFP	Phase	-
Prepared by	N. Subhash	Sign		Date	17-03-22
Project Manager	Subbar Reddy	Sign		Date	17-03-22
Receipt by QC date		Sign		Other	
Receipt at HO date		Sign		Other	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation that was made by QC:

☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.

☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team.

Notes:

1. Attach a copy of the QC report to this sheet.
2. Circle each correction with a red pen – tick (✓) each circle for work completed and cross (X) each circle where work has not been completed.
3. Give remarks for each case where work has not completed on this sheet.
4. Make 2 copied of the ATR – send one to MID and other to QC.
5. Enclose required photographs – hard copy.

Remarks:

Remarks: All works completed

Quality Control Check Report. Stage: After Finishing Stage III (Apartments)

Flat No	C-103	Other	Sl. No.	39092
Company	MPL	Project	Phase	-
Prepared by	T. Vinod Kumar	Sign	Date	05-01-22
Project Manager	Subba Reddy	Sign	Date	05-01-22
Previous stage report no.	38377	Report filed and signed by PM	☒ Yes ☐ No	
Checked By MD on	MD Sign	For filling	☐ Yes ☐ No	

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☐ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after :

- Completing stage II works.
- Complete works like doors, windows, grills, electrical wiring, switches, french door glass, etc.
- In case of modular kitchen provide platform, granite and dado and modular kitchen in this stage.
- Provide video door phone in this stage.
- Possession for wood work cannot be given until QC check for stage III is completed and all corrections mentioned in the report are made.

Miscellaneous check:

Modular kitchen to be provided	☒ Yes ☐ No	Modular kitchen provided	☐ Yes ☒ No
Modular kitchen workman ship	☐ Good ☐ Avg ☐ Poor	Modular kitchen granite & dado workman ship & finishing	☐ Good ☐ Avg ☐ Poor
Video door phone /wifi cam to be provided	☒ Yes ☐ No	Video door phone/wifi cam provided	☐ Yes ☒ No
Painting marks and drops are cleaned from floor, windows, walls.	☐ Good ☒ Avg ☐ Poor		

Quality Control Check Report. Stage: After Finishing Stage III (Apartments)

S No	Room	Rate the quality of (Good ✓, Avg. X, Poor - needs correction ✗, NA)											
		Door, door knob & door stopper fitting	Door, door knob & door stopper cleaning	Window grills & quality	Window grills fitting & finishing	Windows quality	Window fitting & finishing	Balcony railing quality & finishing	French door quality & fitting	CP jali quality and fitting	Edge building	Switch boards fitting & covering with plastic covers	Junction box covers painting
1	Bedroom 1- M. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Bedroom 2 C. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 3- Gr. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Lobby	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Toilet 1- M. Toi	✓	✓	✓	✓	✓	✗	✗	✓	✓	✓	✓	✓
12	Toilet 2- C. Toi	✓	✓	✓	✓	✓	✗	✗	✓	✓	✓	✓	✓
13	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other												
15	Other												

Remarks Note: 1. Except kitchen all rooms, seepage started. completed

2. In M. Toi one number of wall tile missing. completed

3. In balcony for french door mosquito mesh not provided. completed

4. In balcony for railing glass missing not provided. completed

5. In utility grill not fixed. completed

Draft finishing. check report. apts. stage III dt 17-10-2020 ver5

6. In Kitchen for double & glass painting for balcony. completed.

Quality Control Check Report. Stage: After Finishing Stage II (Apartments)

Flat No	C-103	Other	Sl. No.	38377
Company	MPL	Project	Phase	
Prepared by	T. Vinod Kumar	Sign	Date	16-09-21
Project Manager	Subba Reddy	Sign	Date	16-09-21
Previous stage report no.	37499	Report filed and signed by PM	☒ Yes ☐ No	
Checked By MD on	MD Sign	For filling	☐ Yes ☐ No	

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- Completion of flooring, bathroom /utility tiles, first coat of paint.
- Completion of doors, windows, grills, electrical wiring, switches must be done in next stage
- False ceiling must be completed before flooring.
- Kitchen platform, granite and dado must be completed where modular kitchen is not provided.
- Provide granite soffit for main door and balconies in this stage.

Certified that all corrections mentioned in the QC report have been completed. Work can proceed to next stage.

Project in-charge	Sign	Date
<i>[Signature]</i>		17/9/2021

Miscellaneous check:

Main door fixed with lock & stopper	☒ Yes ☐ No	Granite soffit for balcony provided	☒ Yes ☐ No
Granite soffit for balcony required	☒ Yes ☐ No	Balcony granite soffit edge polishing	☐ Good ☒ Avg ☐ Poor
Balcony granite soffit workmanship	☐ Good ☒ Avg ☐ Poor	Granite soffit for main door provided	☐ Yes ☐ No
Granite soffit for main door required	☐ Yes ☐ No	Main door granite soffit edge polishing	☐ Good ☐ Avg ☐ Poor
Main door granite soffit workmanship	☐ Good ☐ Avg ☐ Poor		

Quality Control Check Report. Stage: After Finishing Stage (Apartments)

Tiling & granite work		Rate the quality of (Good ✓, Avg. X, Poor - needs correction XX, NA)												
S No	Room	Workmanship of tiling	White cement filling around CPVC lines	Corners finishing	Finishing near doors	Finishing on top of tiles	Finishing near ventilators	Step at bathroom entrance / utility	Step for shower / pot wash	Tile joint grouting	Granite platform finishing and edge polishing	Granite platform slope	Granite platform height	Finishing under granite platform
1	Toilet 1- M.Toi	✓	✓	✓	✓	X	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 2- C.Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Toilet 3-	-	-	-	-	-	-	-	-	-	-	-	-	-
4	Toilet 4-	-	-	-	-	-	-	-	-	-	-	-	-	-
5	Wash basin in dining area	-	-	-	-	-	-	-	-	-	-	-	-	-
6	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Other													
9	Other													
Remarks		Note:- 1. In M.Toi (1) no of wall tile broken.												

Quality Control Check Repot. Stage: After Finishing Stage II (Apartments)

S No	Room	Rate the quality of (Good ✓, Avg. ✕, Poor – needs correction ✕✕, N/A)											
		Flooring workman ship & grouting	Skirting size (3")	Skirting workmanship	Plastering above skirting	Plastering & finishing of walls	Crack filling	Loft Finishing	Windows check	General quality of painting & finishing	Door & frame painting quality	Door beading, luppam and painting quality.	Edge building
1	Bedroom 1 - M. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Bedroom 2 - C. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 3 - G. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Lobby 1 -	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Utility / balcony 2 -	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Utility / balcony 3 -	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Other												
12	Other												
Remarks		Note:- In M. Bed hole packing to be done.											

Quality Control Check Report. Stage: After Plumbing & Electrical (Apartments)

Flat No.	C-103	Other	Sl. No.	37499
Company	MPL	Project	Phase	-
Prepared by	T. Vinod Kumar	Sign	Date	14/04/21
Project Manager	Subba Reddy	Sign	Date	14/04/21
Previous stage report no.	36089	Report filed and signed by PM?	☒ Yes ☐ No	
Additions & alterations sheet date	Vacant Flat	All pages signed by engineer & customer?	☐ Yes ☐ No	
Checked By MD on	MD Sign	For filling	☐ Yes ☐ No	

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- after cleaning the apartment.
- before starting painting, tiling & flooring.
- electrical conduct, waterproofing & plumbing work is completed (for stage II only).
- additions & alterations is finalized and signed. In case there are no additions and alterations printout of email by PM to CR confirming the same must be filed.
- additions & alterations sheets to be transferred to QC file. QC to check if A&A are made as per request.

Confirmed that all corrections mentioned in the QC report have been completed. Work can proceed to next stage.

After Plumbing & Electrical Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. Location of CPVC & PVC fittings must be checked as per measurements given in circular. Tolerance 1".
6. Location, height and spirit level of electrical points must be checked as per measurements given in circular & plan. Tolerance 1".
7. Civil work near pipes in balcony & utility must be neat and mortar should be removed from the pipes.
8. Water proofing must cover all pipes & check height above SFL.
9. Fasteners must be used as specified in circular. Especially check fixing of PVC pipes.
10. Height of DB box must be 6" below false ceiling level or 12" below slab level.
11. In case of many changes in civil work, electrical work and plumbing work, a new drawing must be prepared at HO and approved by MD.

Project in-charge	Sign	Date
<i>[Signature]</i>		17 Jul 2021

Quality Control Check Report. Stage: After Plumbing & Electrical (Apartments)

S No	Room	Civil work near pipes in balcony & utility ⁷ (✓ or ✕)	CPVC & PVC Check ⁵ (✓ or ✕)	Electrical points check ⁶ (✓ or ✕)	Water proofing check ⁸ (✓ or ✕)	Proper use of fasteners check ⁹ (✓ or ✕)	Placement of DB ¹⁰ (✓ or ✕)	Placement of Generator changeover (✓ or ✕)
1	Bedroom 1 M. Bed	-	-	✓	-	-	-	-
2	Toilet 1 M. Toi	-	✓	✓	✓	-	-	-
3	Bedroom 2 C. Bed	-	-	✓	-	-	-	-
4	Toilet 2 C. Toi	-	✓	✓	✓	-	-	-
5	Bedroom 3 C. Bed	-	-	✓	-	-	-	-
6	Toilet 3	-	-	✓	-	-	-	✓
7	Drawing	-	-	✓	-	-	✓	-
8	Dining	-	-	✓	-	-	-	-
9	Lobby 1	-	-	-	-	-	-	-
10	Utility / balcony 1	✓	-	✓	-	✓	-	-
11	Utility / balcony 2	✓	✓	✓	✓	✓	-	-
12	Utility / balcony 3	-	-	-	-	-	-	-
13	Kitchen	-	-	✕	-	-	-	-
14	Other							
15	Other							
Remarks								

Remarks on additions & alteration sheet: *vacant flat*

Signed by engineer,	☐ Yes ☐ No	Signed by customer,	☐ Yes ☐ No
Revised drawing required from HO	☐ Yes ☐ No	Approved revised drawing attached	☐ Yes ☐ No


Quality Control Check Repot. Stage: After Plumbing & Electrical (Apartments)

Miscellaneous check

Screeding done on walls upto 12" outside bathroom/utility	☒ Yes	☐ No
Bathroom /utility filled with 4" water for water proof check	☒ Yes	☐ No
Hole packing done around all pipes in ceiling and internal walls	☒ Yes	☐ No
Remarks:		


ELECTRICAL LEGEND		
SYMBOL	DESCRIPTION	MOUNTING HT.
	5 amp outlet with switch on raw power	3'-6" from FFL
	Outlet Point	5'-3" from FFL
	1/8 amp outlet with switch on raw power (for floor)	below counter
	1/8 amp light	9'-6" from FFL
	Ceiling fan	ceiling ht.
	TV point	3'-6" from FFL
	Telephone point	3'-6" from FFL
	LAN / Ethernet	3'-6" from FFL
	Ceiling light	ceiling ht.
	Switch board	4'-0" from FFL
	Bed Side Switch board	2'-0" from FFL
	Distribution board	8'-0" from FFL
	Exhaust point	7'-6" from FFL
	AC Point	9'-0" from FFL
	AC Unit	as per standard
	Ceiling bell switch	4'-0" from FFL
	Ceiling bell	9'-0" from FFL
	Exhaust	7'-0" from FFL

APPROVED
02 DEC 2019
SOHAM MODI
MANAGING DIRECTOR

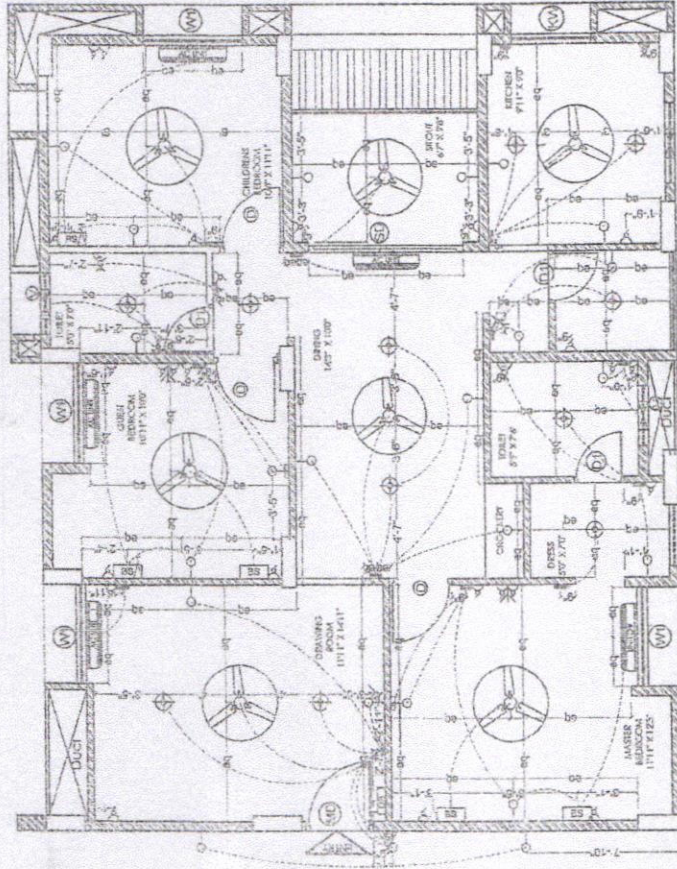

C-103 Elect

Description		Direction	Owners & Developers :	Date :	Promoted by
QUALITY CONTROL ELECTRICAL CHECK PLAN OF BLOCK-A TYPE-A2 & A3			BNC Estates	02.12.2019	Modi Properties & Investments Pvt. Ltd.
			Project Name & Phase :	Prepared By :	Phone: +91-40-60335551
			Mayflower-Grande platinum	Approved By : Soham Modi	
				Scale :	
					N.T.S

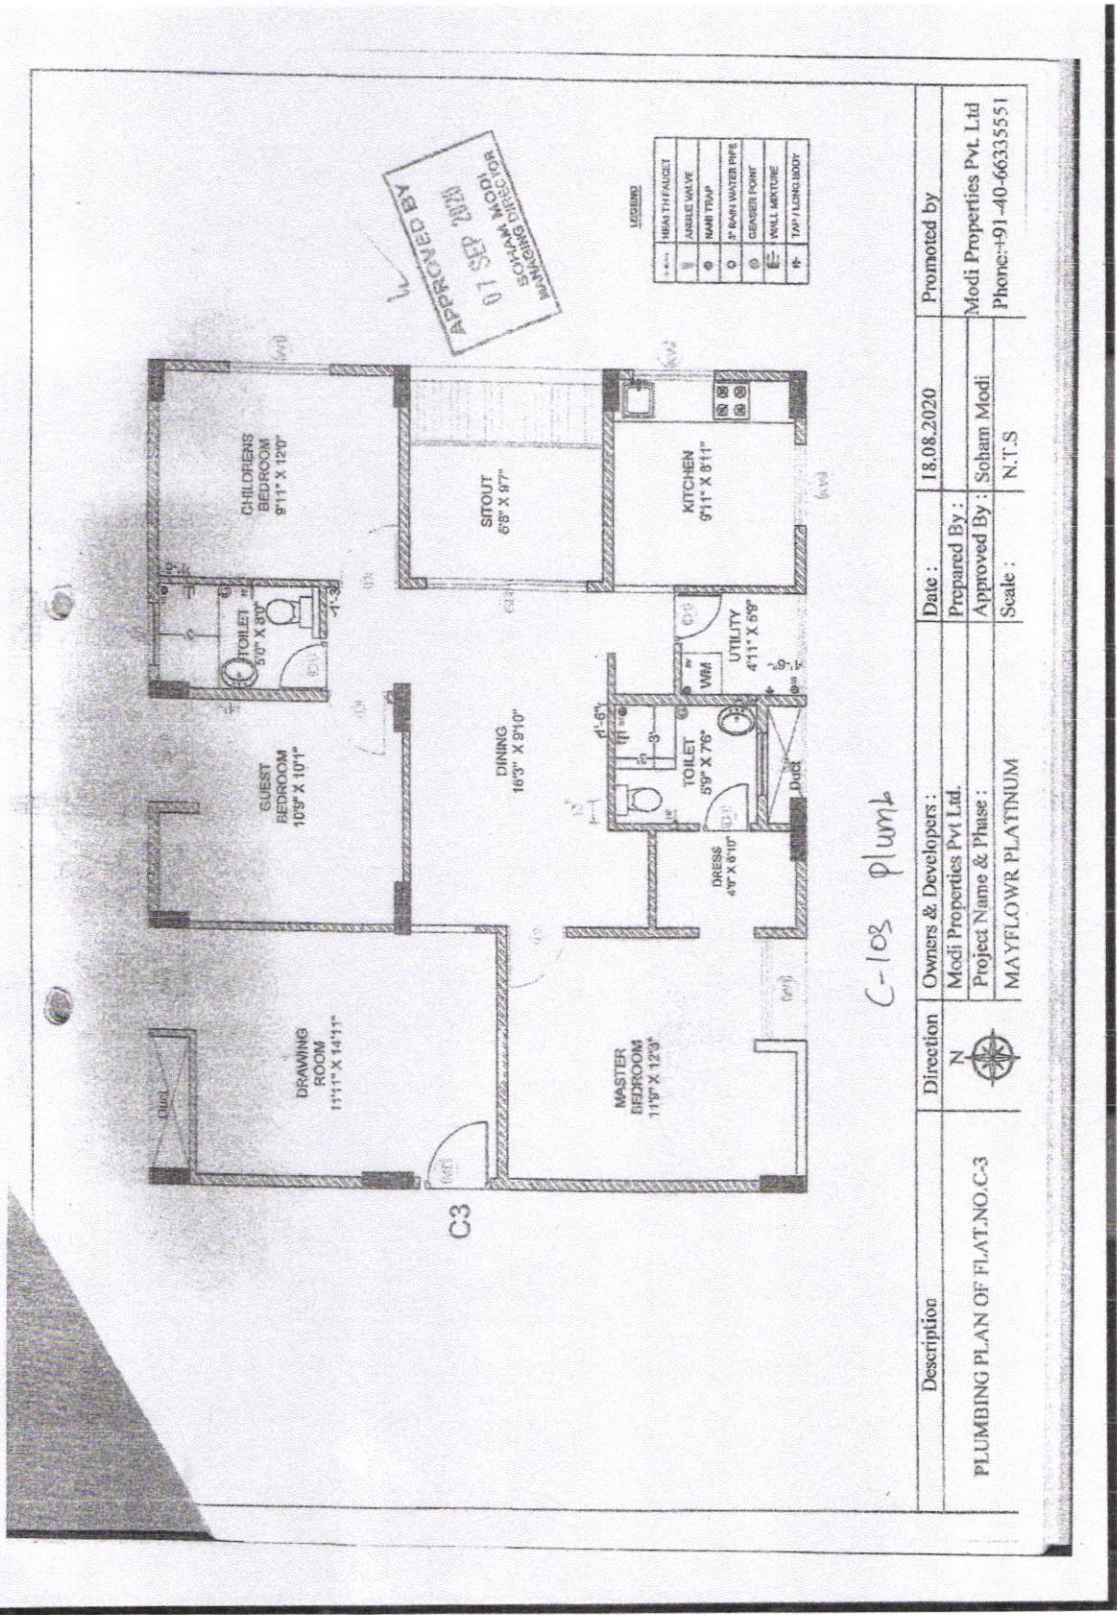

Quality Control Check Report

Flat No.	C-103	Other		SL. No.	3	6089
Company	MFP	Project		Phase		
Prepared by	S. RAJESH	Sign		Date	20/09/20	
Project Manager	S. Rajesh Reddy	Sign		Date	20/09/20	
Previous stage report no.	359	Re		Report filed and signed by PM?	☒	Yes ☐ No ☐
Checked By MD on	MD Sign			For filling	☐	Yes ☐ No ☐
Recommendation:	Submit ATR on QC report to QC team. Proceed only after recheck by QC. Proceed with work after submitting ATR on QC report to QC team. Work only after making corrections pointed out in the QC report. ATR not required. Work. ATR not required.					
☐ Stop further work. Stop further work. Proceed with further work. Proceed with further work.						

Inspection should be done after plastering is completed. After plastering is completed, the work should be checked for any defects. If any defects are found, the work should be stopped and the defects should be rectified before proceeding with the work.

Plastering Check

1. Mark ✓ for correct or minor mistake.
2. Mark ✗ for major mistake.
3. Mark ✗✗ for major mistake.
4. Mark ✗✗✗ for major mistake.
5. 9" unplastered area from window.
6. Windows must be checked for plastering.
7. Provision of tiles in bathroom, kitchen & wash areas (rough plastering).
8. Check size of sink bowl. Hole should be 1" to 2" larger. (Tolerance: 1")
9. All doors frames should be checked for plastering.
10. Sill top must be of uniform thickness, correct height, at one level & without broken edges.

Certified that all corrections mentioned in the QC report have been completed. Work can proceed to next stage.

Project in-charge	Sign	Date
S.V.S. Rajesh	20/09/20	20/09/20

Quality Control Check Report. Stage: After Plastering (Apartments)

S No	Room	Skirting Provision (✓ or X)	Finishing around door frame (✓ or X)	Beams & columns finishing (✓ or X)	Finishing of lofts (✓ or X)	Electrical junctions finishing (✓ or X)	Window check ⁶	(✓ or X)	Tiles provision (✓ or X)	Sink provision & size (✓ or X)	Grooves for door frames (✓ or X)	Balcony & terrace sill top finishing (✓ or X)	Screeding in bathroom & utility (✓ or X)	Screeding in 6" above FFL? (✓ or X)
1	Bedroom 1 M.B	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M.T	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 K.B	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 K.T	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 G.B	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Utility 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other													
15	Other													
Remarks														

Quality Control Check Report. Stage: After Brickwork (Apartments)

Flat No.	C-103	Others	Sl. No.	35956
Company	MPL	Project	Phase	-
Prepared by	V. Sanketh	Sign	Date	01/09/2020
Project Manager	SubbaReddy	Sign	Date	01/09/2020
Previous stage report no.	35813	Report filed and signed by PM?	☒ Yes ☐ No	
Apartment No		Other		
Checked By MD on	MD Sign	For filling	☐ Yes ☐ No	

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- brickwork is completed
- chicken mesh fixed
- after cleaning the apartment
- electrical conducting work is completed

Brickwork Check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark X for minor mistake that requires minor correction.
3. Mark X X for major mistake that requires correction by replacement or re-fixing.
4. Mark X X X for major mistake that cannot be corrected.
5. Wall thickness should be as per plan. Use of 4", 6" & 8" blocks must be checked.
6. All walls should have 2 beds of about 2" to 3" thickness with one no. 6 mm or 8 mm rod with M15 CC.
7. Chicken mesh should be used in each and every joint between RCC & Brickwork.
8. Joint between brickwork & beam on external side must be filled.
9. Check room dimensions with working plan. (Tolerance: 1")
10. Diagonals of each room shall be equal. (Tolerance: 2")
11. Balcony sill level should be 3" from SFL. (Tolerance: 1")
12. Check room height with specified height. (Tolerance: 1")
13. Check plumb of walls where ever it appears to be out of plumb. (Tolerance: 1/2")
14. Specify the No. of beams which are not aligned by more than 1" in a room.
15. Door frames must have black Japan coating and wood primer / pellambar - at cost of painter.

Certified that all corrections mentioned in the QC report have been completed. Work can proceed to next stage.

Project in-charge	Sign	Date
S.V.S. Reddy	[Signature]	21/9/2020

Quality Control Check Report, Stage 1 After Brickwork (Apartments)

S.No	Room	Wall thickness (✓ or X)	Rods in walls (✓ or X)	Chimney masonry (✓ or X)	External brickwork & beam join (✓ or X)	Room Dimensions (✓ or X)	Room Dimensions (✓ or X)	Difference in inches	Diagonal (✓ or X)	Difference in inches	Balcony sill level (✓ or X)	Room Height (✓ or X)	Plumb of walls (Good Avg. Bad)	Alignment of beams and walls - Not
1	Bedroom 1 MB	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 MB	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 MB	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 MB	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 MB	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3 MB	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other													
15	Other													

Remarks: NOT AT Couple of places Electrical metal boxes are flushed into the walls.

Quality Control Check Report. Slabs After Brickwork (Apartments)

Quality of edges and corners in all rooms?	☐ Good ☒ Avg. ☐ Bad
Specify rooms that need correction:	—

Miss Checks

Was 3/5 CFT preparation form provided?	☒ Yes ☐ No
Continuity of preparation form?	☒ Good ☐ Avg. ☐ Bad
Was this Apartment cleaned before starting brick work?	☐ Yes ☐ No ☒ Can't say
Is this Apartment cleaned for plastering?	☒ Yes ☐ No
Wastage?	☐ High ☐ Medium ☒ Low
Storage of building material like bricks sand and cement.	☒ Good ☐ Avg. ☐ Bad
Iron (20%) is provided for curing in each flat?	☐ Yes ☐ No —
Remarks	

Door Frames & Windows check

Notes

1. Mark ✓ for correct or minor mistakes which does not require correction
2. Mark ✗ for minor mistake that requires minor correction
3. Mark ✗✗ for major mistakes that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistakes that cannot be corrected
5. Window roughness depth should be between 2 to 2 1/2" after plastering.
6. Lintel is set should be 1" from SFL & 7" from FFL. (Tolerances 1")
7. Lintel should be at a height of 7'6", 7'3" from FFL. Kitchens flat from should be at a height of 32" or 33" from FFL and 35" or 36" from SPL. (Tolerances 1")
8. Slopes of lintel and kitchen platforms to be checked by using 12" spirit level and check height from floor from 2 or 3 points.
9. Thickness of platforms & lintel should be between 2 & 2.5"
10. Provide single layer table brick at bottom of each door frame without threshold.

Quality Control Check Report. Stage: After Brickwork (Apartments)

S No	Room	Door size, face and position (✓ or X)	Brick at bottom of door frame (✓ or X)	Door lintel level (✓ or X)	Door diagonal check (✓ or X)	Door Plumb - two sides (✓ or X)	Door frame black Japan/wood primer/Pecelambar check (✓ or X)	Windows lintel & sill level (✓ or X)	Windows size (✓ or X)	Windows - template depth & diagonal (✓ or X)	Windows - template powder coated (✓ or X)	Loft & Kitchen platform required? (Yes or No)	Loft & Kitchen platform provided (✓ or X or NA)	Loft & Kitchen platform slope (✓ or X)
1	Bedroom 1 MB	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 P-Tal	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 MB	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 C-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 MB	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3-	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby J	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility/balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility/balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
15	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓

Remarks: NOTE: Instead of Bricks, C.C Beds are using at Bottom of all internal door frames.

MAYFLOWER PLATINUM

Survey no. 82/1, Mallapur, Hyderabad – 500 076.
Owned & Developed by: M/s. Modi Properties Pvt. Ltd.
Head office; 5-4-187/3&4 M G Road Secunderabad.

Details of Additions & Alterations

Flat No	103	Block	'C'
Flat Area	1500 sft	Type	Deluxe / Luxury
Buyer Name	GADEPOKA BHASKAR VINAY		
Phone No.	8918486149	Email	Vin.Vinaygb@gmail.com.

I hereby confirm that I have given the details of the minor additions and alterations that are required in the above referred flat in the pages attached herein. Please complete the changes suggested by me. I agree to pay the charges, if any, for the additions and alterations that I have asked you to make, as per the rates suggested by you. I shall deliver all the materials that are required to be provided by me at the site on or before _____. In case I fail to deliver these items to the site by the specified date, you may complete the works in the flat as per the standard items provided by you.

Buyers sign	GB-vinay	Engg. Sign	B. Nandini
Date:	21/4/21	Date	21/4/21

Note:

1. Colour shades of paints may vary from batch to batch & company to company. The Builder will not take responsibility of quality of work for dark shades especially green & blue.
2. Shade / colour of natural material like marble and granite can't be guaranteed and may vary from lot to lot. Cracks like appearance in marble is a natural feature and Builder shall not be responsible for repairs or replacement.
3. Availability of bathroom or flooring tiles of the same type /colour/make can not be guaranteed and closest possible type/colour/make may be used in its place.
4. No further change shall be permitted from this day.
5. Please sign on all pages.

Buyers sign:

Engg. Sign:

Date: 21/4/21

Choice of colours:

No changes same as model flat A105

Changes in flooring:

Yet to be decide.

1). Tiles same as default 2'x2' verified tiles except
Dyers area.

⇒ Dyers area to be default tiles (Mentioned in whatsapp).

B. N. D. S.
08/06/21

Buyers sign:

Engg. Sign:

Date: 21/4/21

Changes in electrical points: (mark on plan)

- 1) Tr point to be given in CBR as marked.
- 2) Every room with internet connection to be given. Ep Tublight to be given.
- 3) SA point to dining to be shifted to opp wall.

Choice of Bathroom tiles, CP fittings & Sanitary ware:

No changes to be done.

Buyers Sign: 

Engg. Sign: 

Date: 21/4/21


Changes in kitchen platform: (mark on plan)

No changes to be done.


Other Changes:

- 1) Wall in dining area to be removed as marked.
- 2) 'L' Shape Left to be provided in kitchen.

Buyers sign: 

Engg. Sign: 

Date: 21/4/21

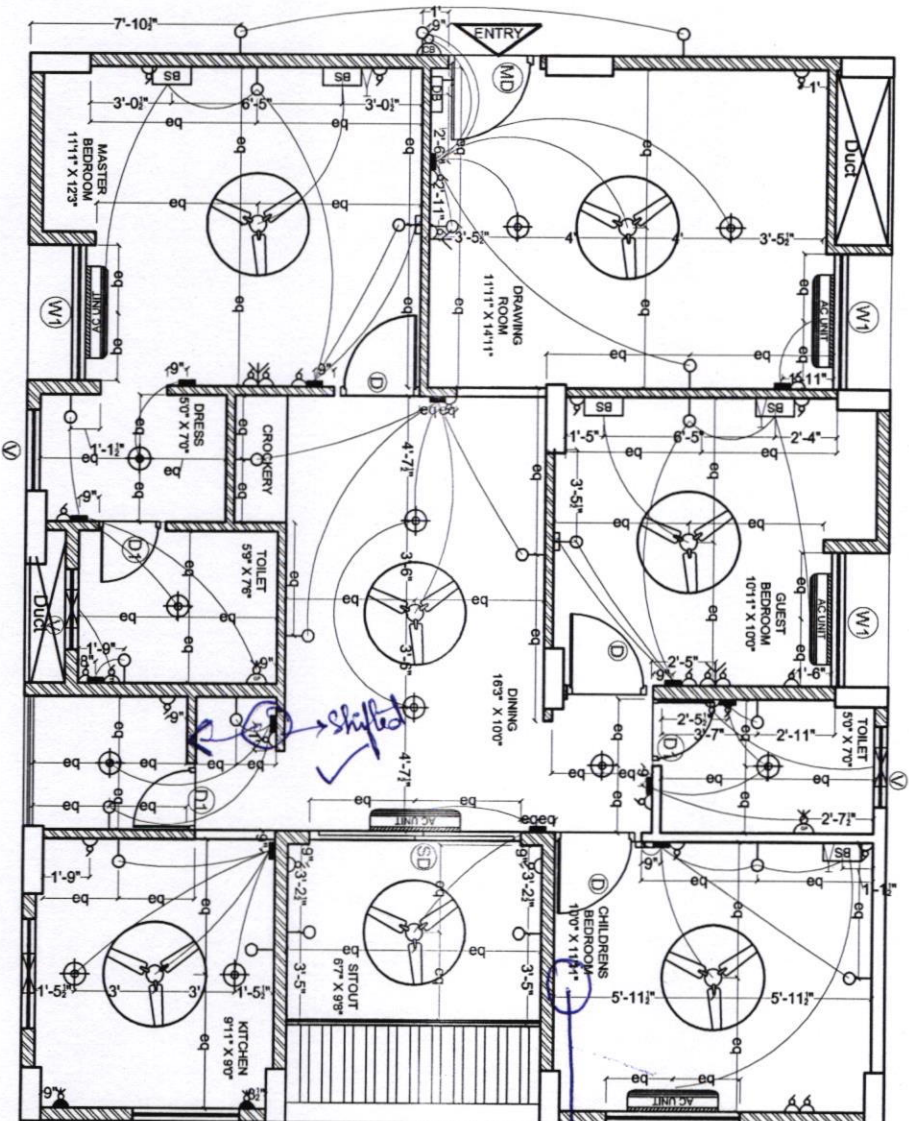

ELECTRICAL LEGEND		
SYMBOL	DESCRIPTION	MOUNTING HT.
	5 amp outlet with switch on raw power	3'-6" from FFL
	Geyser Point	8'-3" from FFL
	15 amp outlet with switch on raw power (for fridge)	below counter
	Wall light	6'-6" from FFL
	Ceiling fan	ceiling ht
	TV point	3'-6" from FFL
	Telephone point	3'-6" from FFL
	LAN / Ethernet	3'-6" from FFL
	Ceiling light	ceiling ht
	Switch board	4'-6" from FFL
	Bed Side Switch board	2'-0" from FFL
	Distribution board	5'-6" from FFL
	Exhaust point	7'-6" from FFL
	AC Point	8'-0" from FFL
	AC Unit	as per standard
	Calling bell switch	4'-6" from FFL
	Calling bell	8'-0" from FFL
	Exhaust	7'-0" from FFL

Description

Direction

Owners & Developers :

Date :

Promoted by

ELECTRICAL PLAN OF FLAT-C3

BNC Estates

Prepared By :

Modi Properties & Investments Pvt. Ltd.

Project Name & Phase :

Approved By :

Phone: +91-40-66335551




Mayflower Grande

Scale :

N.T.S

BNC
12/6/20

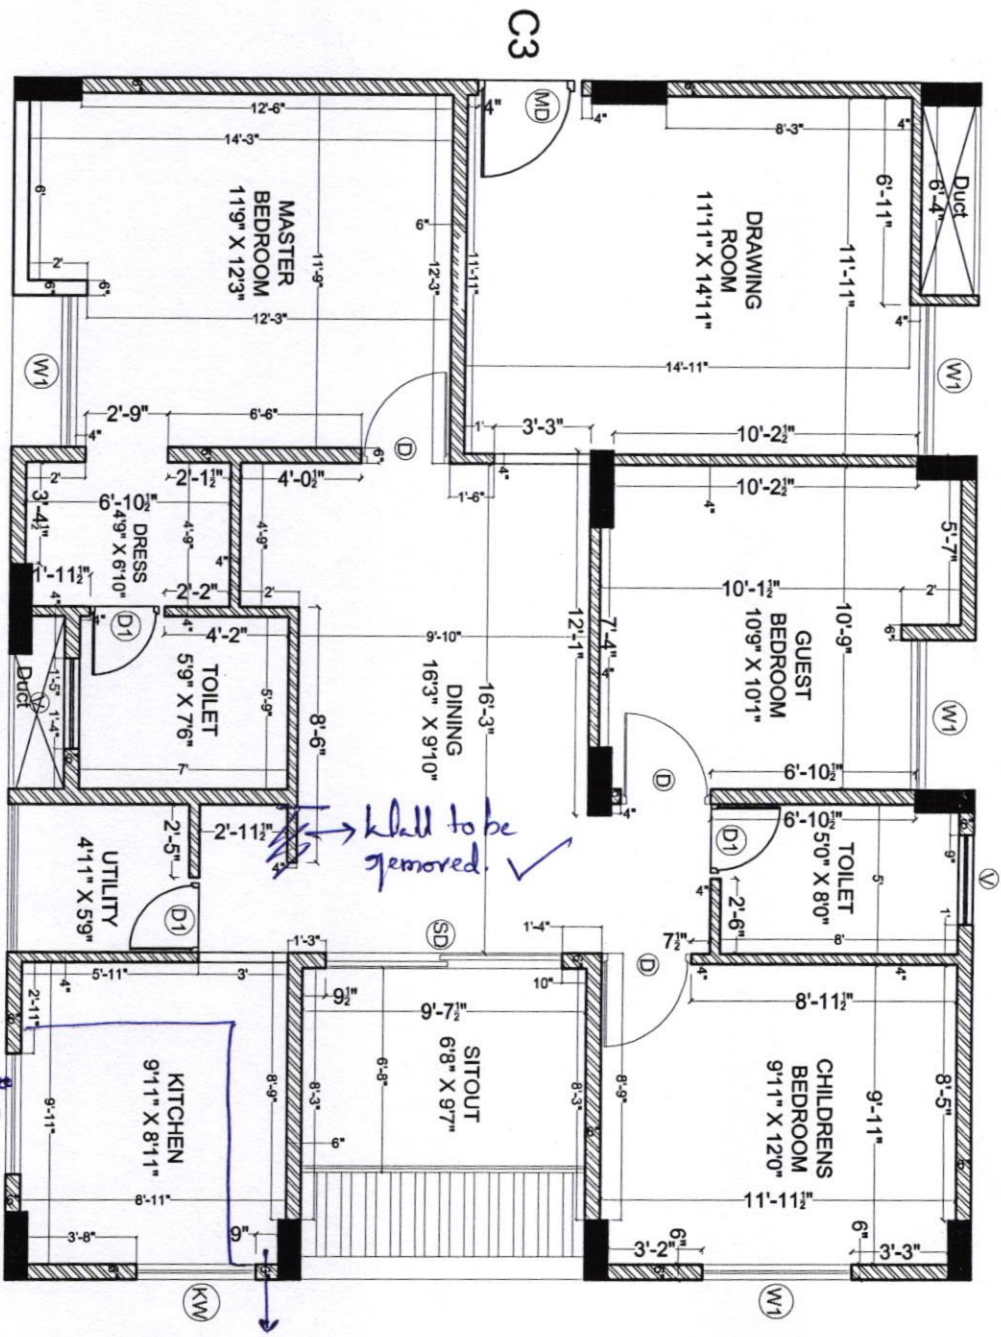


C3

Description		Direction	Owners & Developers :		Date :	Promoted by	
WORKING DRAWING OF FLAT.NO.C-3		N	Modi Properties Pvt Ltd.		18.08.2020	Modi Properties Pvt. Ltd	
			Project Name & Phase :		Prepared By :	Phone: +91-40-66335551	
			MAYFLOWR PLATINUM		Approved By : Soham Modi		
					Signature :		
					N.T.S		

off. sec

B. Nandini
12/8/20

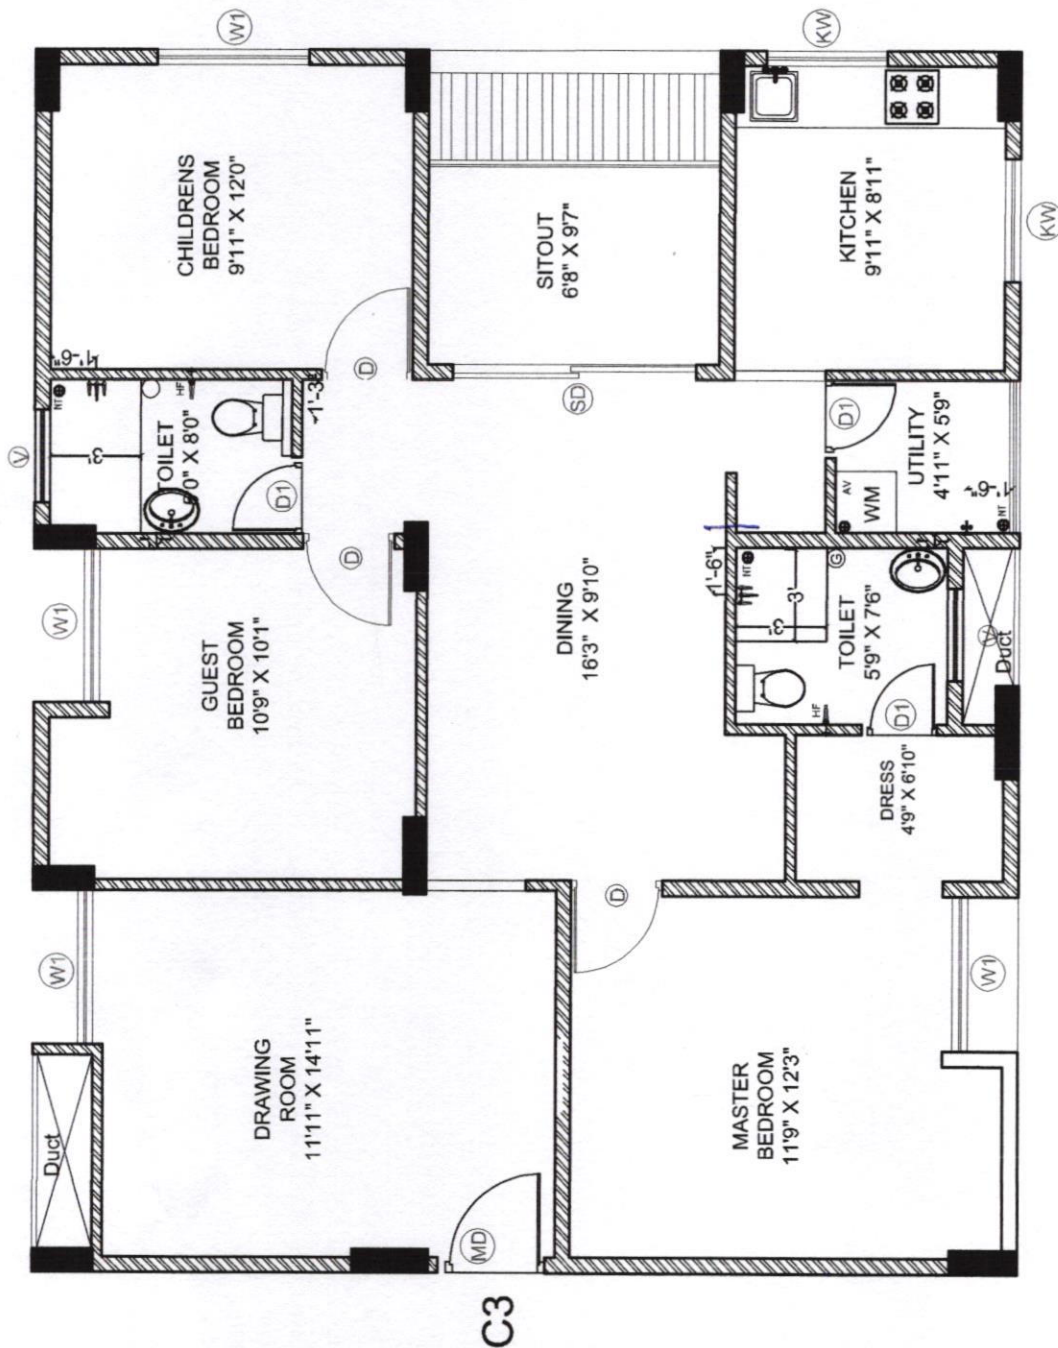

C3

Handwritten signature

*B. Nandlal
21/4/21*

Description	Direction	Owners & Developers :	Date :	Promoted by
PLUMBING PLAN OF FLAT.NO.C-3	N	Modi Properties Pvt Ltd.	18.08.2020	
		Project Name & Phase :	Prepared By :	Modi Properties Pvt. Ltd
		MAYFLOWR PLATINUM	Approved By : Soham Modi	Phone:+91-40-66335551
			Scale :	N.T.S
