

Internal memo no. 903/35/A
Annexure - B
RMC pour report

Company/ firm:	Modi Reality Mallapur LLP	Block No.:	Driveway
Project:	Gulmohar Residency	Flat / Villa no.:	Driveway slab a b/n I of C&E Block purpose
Supplier:	KN INFRA	Slab no.:	-
Requisition nos.:	20240610008	A. Estimated quantity:	40M3(M20)
PO nos.:	20240610027	B. Requisition quantity:	40M3
	Sign of Admin	C. Actual quantity poured	35M3
	Sign of Project Manger	D. Difference (C-A)	5M3

Details of RMC pour

Sl.	Date	Time of dispatch from RMC plant	Time of receipt at site	Time of pour	Quantity poured	Dc No. / Batch no.	Specified wt @2400 kgs/m3	Measured weight (kgs)	Short fall in weight in kgs	Deduction for shortfall in Rs.	7 day cube test strength in kN/m2	28 days cube test strength in kN/m2
1.	13.06.24	19:08	21:07	21:15	8	0197	19200	19350	+150			
2.	13.06.24	19:20	22:07	22:15	8	0198	19200	19060	-140			
3.	13.06.24	22:51	00:00	00:20	8	0201	19200	19150	-50			
4.	13.06.24	23:11	02:25	02:35	8	0202	19200	19140	-60			
5.	13.06.24	01:16	02:57	03:00	3	0203	7200	7260	+60			
6.												
7.												
8.												
Total:					35 M3		84000	83960	-40			
Remarks	Po to be closed.											

Note: 1. Report to be sent on a daily basis to purchase@modiproperties.com and report-audit@modiproperties.com. 2. Report must be prepared during pour and not later. 3. Report must be sent within one working day. 4. Multiple report can be sent for one PO. 5. Weigh all vehicles. 6. 6 cubic meters vehicle should have a net weight of 14,110 kgs @ 2,400kgs/ m3. If the shortfall is more than 50 kgs per load purchase to debit supplier shortfall amount on pro-rata basis. 7. Site to calculate shortfall. 8. Maintain original report + weightment slips + pour reports + test reports + photographs at sit

RA
No: 294, Ramapally (V), Keesara(M)
Tel Dist - 501 301


mail : kninfra1@gmail.com
a. No: 9100999994/9100755567

20240615027

GLOBAL RMC
ENGINEER'S CONCRETE

DELIVERY CHALLAN

Customer Name: GULMOHAR RESIDENCY		D.C. No: 0197	Date: 13-06-2024		
Delivery Site: MALLAPUR		Truck No: TS08UG4352	Mode: PUMP		
S.No:	Description	Qty	Units	Cum. Qty	Remarks
12	M 20 RMC	8	Cum	96	-
Other Documents Enclosed:					
1) 2)					
Note: No alterations will be accepted without supplier & Customer Signatures alongwith reasons.					
Received above material in good condition					
Customer Signature					
for K N INFRA					
Authorized Signatory					

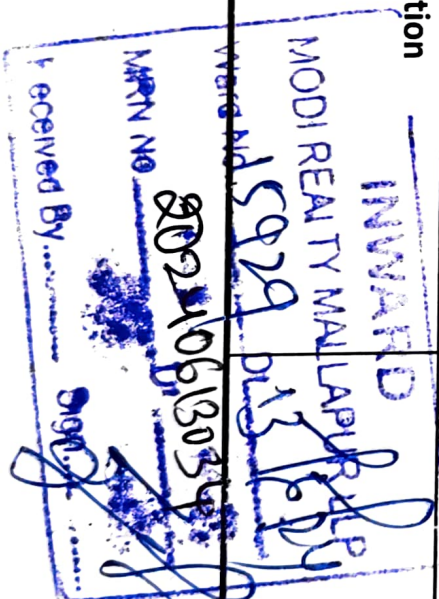

Survey No: 294, Ramapilly (V), Keesara(M)
Medchel Dist - 501 301

Email : kninfra1@gmail.com

Ph. No: 9100999994/9100755567

GLOBAL RMC
ENGINEER'S CONCRETE

DELIVERY CHALLAN

Customer Name: **GULMOHAR RESIDENCY**

D.C. No: **0198** Date: **13-06-2024**

Delivery Site: **MALLAPUR**

S.No: Description Qty Units Truck No: **TS08UG4350** Mode: **PUMP**

S.No:	Description	Qty	Units	Cum. Qty	Remarks
13	M 20 RMC	8	Cum	104	

Other Documents Enclosed:

- 1)
- 2)

For Office use only

Driver Name: **NARENDER**

Signature:

Note: No alterations will be accepted without supplier & Customer Signatures along with consistency MALLAPUR

Received above material in good condition

Customer Signature

for KN INFRA
Authorised Signatory

Survey No: 294, Ramapally (V), Keesara(M)
Medchel Dist - 501 301



Email : kninfra1@gmail.com

Ph. No: 9100999994/9100755567

DELIVERY CHALLAN

Customer Name: GULMOHAR RESIDENCY			D.C. No: 0201		Date: 13-06-2024
Delivery Site: MALLAPUR			Truck No: TS08UG5054		Mode: PUMP
S.No:	Description	Qty	Units	Cum. Qty	Remarks
14	M 20 RMC	8	Cum	112	-
Other Documents Enclosed: 1) 2)			For Office use only		
Note: No alterations will be accepted without supplier & Customer Signatures along with reasons. Received above material in good condition 2024/06/13/24 MARTIN NO. 15431012/13/24 INWARD MOD REALTY MALLAPUR LLP for KN INFRA			Driver Name: RAJU KUMAR		
			Signature:		
Customer Signature			Authorised Signatory		

kninfra1@gmail.com
9100999994/9100755567



DELIVERY CHALLAN

Customer Name: **GULMOHAR RESIDENCY**

D.C. No: 0203

Date: **14-06-2024**

Delivery Site: **MALLAPUR**

S.No:	Description	Qty
-------	-------------	-----

16

M 20 RMC

3

Truck No: TS08UG4351

Units

Cum. Qty

Mode: PUMP

Remarks

Cum

123

Other Documents Enclosed:

1)

2)

Note: No alterations will be accepted without supplier & Customer Signatures along with reasons.

Received above material in good condition.

Customer Signature

For Office use only

Driver Name:

PRABHAKAR

Signature:

for KN INFRA

Authorised Signatory

TOTAL

Act	0.0	2405.0	1200.0	2010.0	0.0	0.0	750.0	240.0	0.0	0.0	0.0	514.0	0.0	0.0	0.0	6.0	0.0	0.0
Tar	0.0	2400.0	1200.0	2010.0	0.0	0.0	750.0	240.0	0.0	0.0	0.0	514.0	0.0	0.0	0.0	6.0	0.0	0.0
