


Internal memo no. 903/35/A
Annexure - B
RMC pour report

Company/ firm:	Modi Reality Mallapur LLP	Block No.:	E-Block
Project:	Gulmohar Residency	Flat / Villa no.:	Towards e block column 6 concreting use purpose
Supplier:	KN Infra	Slab no.:	-
Requisition nos.:	20240719030	A. Estimated quantity:	60M3(M25)
PO nos.:	20240719034	B. Requisition quantity:	60M3
	Sign of Admin	C. Actual quantity poured	50M3
		D. Difference (C-A)	10M3
	Sign of Project Manager		
			

Details of RMC pour

Sl.	Date	Time of dispatch h from RMC plant	Time of receipt at site	Time of pour	Quantity poured	Batch no.	Specified wt @2400 kgs/m ³	Measured weight (kgs)	Short fall in weight in kgs	Deduction for shortfall in Rs.	7 day cube test strength in kN/m ²	28 days cube test strength in kN/m ²
1.	29.07.24	07:37	10:13	10:30	8	0384	19200	19290	+90			
2.	29.07.24	08:26	12:12	12:30	8	0385	19200	19210	+10			
3.	29.07.24	10:37	14:48	14:58	5	0386	12000	12600	+600			
4.	03.08.24	10:40	12:34	12:45	8	0029	19200	19000	-200			
5.	03.08.24	11:53	14:03	14:20	8	0032	19200	18710	-490			
6.	03.08.24	13:08	16:19	16:35	8	0035	19200	18750	-450			
7.	03.08.24	14:35	18:11	18:25	5	0037	12000	11960	-40			
Total:					50 M3		120000	119520	-480			
Remarks	Po to be closed.											

Note: 1. Report to be sent on a daily basis to purchase@modiproperties.com and report-audit@modiproperties.com. 2. Report must be prepared during pour and not later. 3. Report must be sent within one working day. 4. Multiple report can be sent for one PO. 5. Weight all vehicles. 6. 6 cubic meters vehicle should have a net weight of 14,110 kgs @ 2,400kgs/ m³. If the shortfall is more than 50 kgs per load purchase to debit supplier shortfall amount on pro-rata basis. 7. Site to calculate shortfall. 8. Maintain original report + weightment slips + pour reports + test reports + photographs at site

KA

No: 294, Ramapally (V), Keesara(M)
nel Dist - 501 301


GLOBAL RMC
ENGINEER'S CONCRETE

ail : kninfra1@gmail.com

h. No: 9100999994/9100755567

DELIVERY CHALLAN

Customer Name: GULMOHAR RESIDENCY		D.C. No: 0029		Date: 03-08-2024	
Delivery Site: MALLAPUR		Truck No: TS08UG4353		Mode: PUMP	
S.No:	Description	Qty	Units	Cum. Qty	Remarks
1	M 25 RMC	8	Cum	8	-
Other Documents Enclosed:					
1) Driver Name:					
2) Signature:					
Note: No alterations will be accepted without supplier & Customer Signatures alongwith reasons.					
Received above material in good condition					
Customer Signature					
fo K N INFRA					
Authorized Signatory					

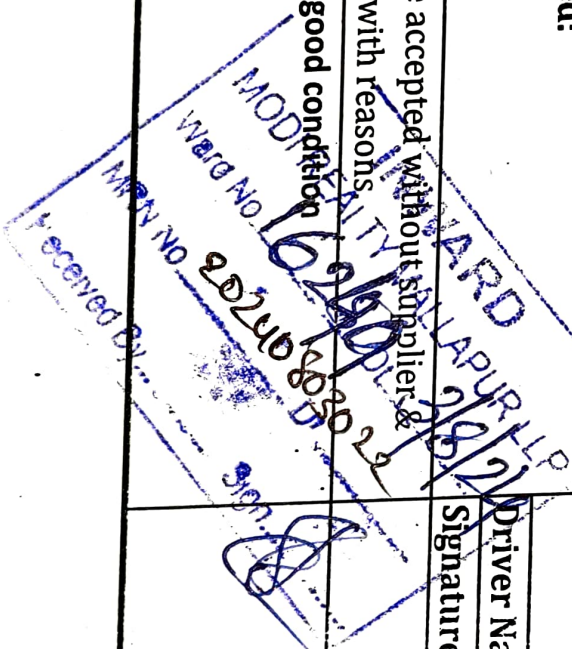

Y No: 294, Ramapally (V), Keesara(M)
chel Dist - 501 301

mail : krinfra1@gmail.com

Ph. No: 9100999994/9100755567

DELIVERY CHALLAN

Customer Name: GULMOHAR RESIDENCY		D.C. No: 0032		Date: 03-08-2024	
Delivery Site: MALLAPUR		Truck No: TS08UG4352		Mode: PUMP	
S.No:	Description	Qty	Units	Cum. Qty	Remarks
2	M 25 RMC	8	Cum	16	
Other Documents Enclosed:					
1)					
2)					
Note: No alterations will be accepted without supplier & Customer Signatures alongwith reasons.					
Received above material in good condition					
fo K N INFRA					
Customer Signature					
Authorized Signatory					

INWARD
MODI REALITY MALLAPUR
Ward No **202**
MRN No **202400303025**
Entered By...
Sign...

Y No: 294, Ramapally (V), Keesara(M)
chel Dist - 501 301

mail : kninfra1@gmail.com

ph. No: 9100999994/9100755567

DELIVERY CHALLAN

Customer Name: GULMOHAR RESIDENCY		D.C. No: 0035		Date: 03-08-2024	
Delivery Site: MALLAPUR		Truck No: TS08UG5055		Mode: PUMP	
S.No:	Description	Qty	Units	Cum. Qty	Remarks
3	M 25 RMC	8	Cum	24	-
Other Documents Enclosed:					
1)					
2) Note: No alterations will be accepted without supplier's Customer Signatures alongwith reasons.					
Received above material in good condition					
Customer Signature					
Authorised Signatory					

GNINRA
Survey No: 294, Ramapally (V), Keesara(M)
Medchel Dist - 501 301
Email : kninfrat1@gmail.com
Ph. No: 9100999994/9100755567

DELIVERY CHALLAN

Customer Name: **GULMOHAR RESIDENCY**

Delivery Site: **MALLAPUR**

Truck No: **TS08UG4354** Mode: **PUMP**

S.No:	Description	Qty	Units	Cum. Qty	Remarks
-------	-------------	-----	-------	----------	---------

4	M 25 RMC	5	Cum	29	-
---	----------	---	-----	----	---

Other Documents Enclosed:

1) Driver Name: _____
2) Signature: _____

Note: No alterations will be accepted without supplier & Customer Signatures alongwith reasons.

Received above material in good condition

Customer Signature

Authorised Signatory

GLOBAL RMC
ENGINEER'S CONCRETE
