

Name:	MRMLLP	Site	Gulmohar Residency
e customer	Sreenivasa Meenokshi Sundaram		
No.	D-508-		
Description	Amount		
Total extra Charges	Nil.		
Total refundable amount	18,440/-		
Net amount to be charges (if any)	-		
Net amount to be refunded (if any)	18,440/-		
ed by Project Manager	Approved by Design Team		Approved by MD
26/6/2023 	Date		Date
	Sign:		Sign:

1. Enclose measurement & estimate sheet. 2. Send scanned copy by email to plans@modiproperties.com & CR. 3.
 4. Keep originals in A&A of customers at site.

ESTIMATE SHEET														
Company Name:		MRMLLP			Approved by:									
Project:		Gulmohar Residency			Sign:									
Work Description:		Extra Specs												
F no :-		Sreenivasa Meenakshi Sundaram D-508												
Prepared By		B.Meenakshi												
Date:		26-06-2023												
S No.		Item Head			Quantity		Units		Rate		Amount		Item Head Total	
Refund charges														
1 Kitchen		Sink With drain board			1.00		Nos		5420.00		5,420.00			
2 Tiles		Country Chocolet			34.00		Sft		30.00		1,020.00			
3 Bathroom		Bathroom Tiles Common,Master			400.00		Sft		30.00		12,000.00			
											Total Amount :-A		18,440.00	
Extra charges														
1 Null		Null			Null		Null		Null		Null		Null	
Amount in words:- Eighteen Thousand Four Hundred Forty Rupees only														

4

SUREMENT SHEET											
Party Name:		MRMLLP			Approved by:						
ct:		Gulmohar Residency			Sign:						
Description:		Extra Specs									
		Sreenivasa Meenakshi Sundaram D-508									
red By		B.Meenakshi									
		26-06-2023									
No.	Item Head	Item Description			Length	Width	Height	Nos.	Quantity	Units	Item Head Total
id charges											
1	Kitchen	Sink With drain board			1.00	1.00	1.00	1.00	1.00	Nos	
2	Tiles	Country Chocolet			17.00	0.00	2.00	1.00	34.00	Sft	
3	Bathroom	Bathroom Tiles Common,Master			200.00	1.00	1.00	2.00	400.00	Sft	
Charges											
1	Nil	Nil			Nil	Nil	Nil	Nil	Nil	Nil	


GULMOHAR RESIDENCY

Sy. No. 19, Mallapur Village, Uppal, Hyderabad.
Owned & Developed by: M/s. Modi Realty Mallapur LLP.
Head office; 5-4-187/3&4 M G Road Secunderabad.

Details of Additions & Alterations

Flat No	508	Block no.	' D ' ✓
Flat Area	1660 sft	Type	Deluxe / Luxury
Buyer Name	SREENIVAS MEENAKSHI SUNDARAM		
Phone No.	9849935880 6309396875	Email	

I hereby confirm that I have given the details of the minor additions and alterations that are required in the above referred flat in the pages attached herein. Please complete the changes suggested by me. I agree to pay the charges, if any, for the additions and alterations that I have asked you to make, as per the rates suggested by you. I shall deliver all the materials that are required to be provided by me at the site on or before _____. In case I fail to deliver these items to the site by the specified date, you may complete the works in the flat as per the standard items provided by you.

Buyers sign		Engg. Sign	
Date:	26/2/2022	Date	

Note:

1. Colour shades of paints may vary from batch to batch & company to company. The Builder will not take responsibility of quality of work for dark shades especially green & blue.
2. Shade / colour of natural material like marble and granite can't be guaranteed and may vary from lot to lot. Cracks like appearance in marble is a natural feature and Builder shall not be responsible for repairs or replacement.
3. Availability of bathroom or flooring tiles of the same type /colour/make can not be guaranteed and closest possible type/colour/make may be used in its place.
4. No further change shall be permitted from this day.
5. Please sign on all pages.

Buyers sign:

Engg. Sign:

Date: 26/2/2022

Choice of colours:

Changes in flooring:

- 1) Hall & Dining - Regal Beige
- 2) master Bed - Urban wood Dark
- 3) Childrens bedroom - Urban wood Natural
- 4) Guest Bedroom - Urban wood Dark
- 5) Balcony floor - Country cafee
- 6) Kitchen floor - Country Almond
- 7) Utility wall - Country Almond
- 8) Utility floor - Country Rosso

Buyers sign:

Engg. Sign:

Date:

Changes in electrical points: (mark on plan)

- 1) Electrical ~~Panel~~ Switch Board Refund to customers
- 2) Providing Switch Boards by customers.

[Signature]
12/03/22

Choice of Bathroom tiles, CP fittings & Sanitary ware:

- 1) Common toilet -

Buyers sign:

Engg. Sign:

Date:


Changes in kitchen platform: (mark on plan)

1) need Full platform in kitchen

2)

Other Changes:


1) Brick work changes as per Drawing.



Buyers sign:

Engg. Sign:

Date:

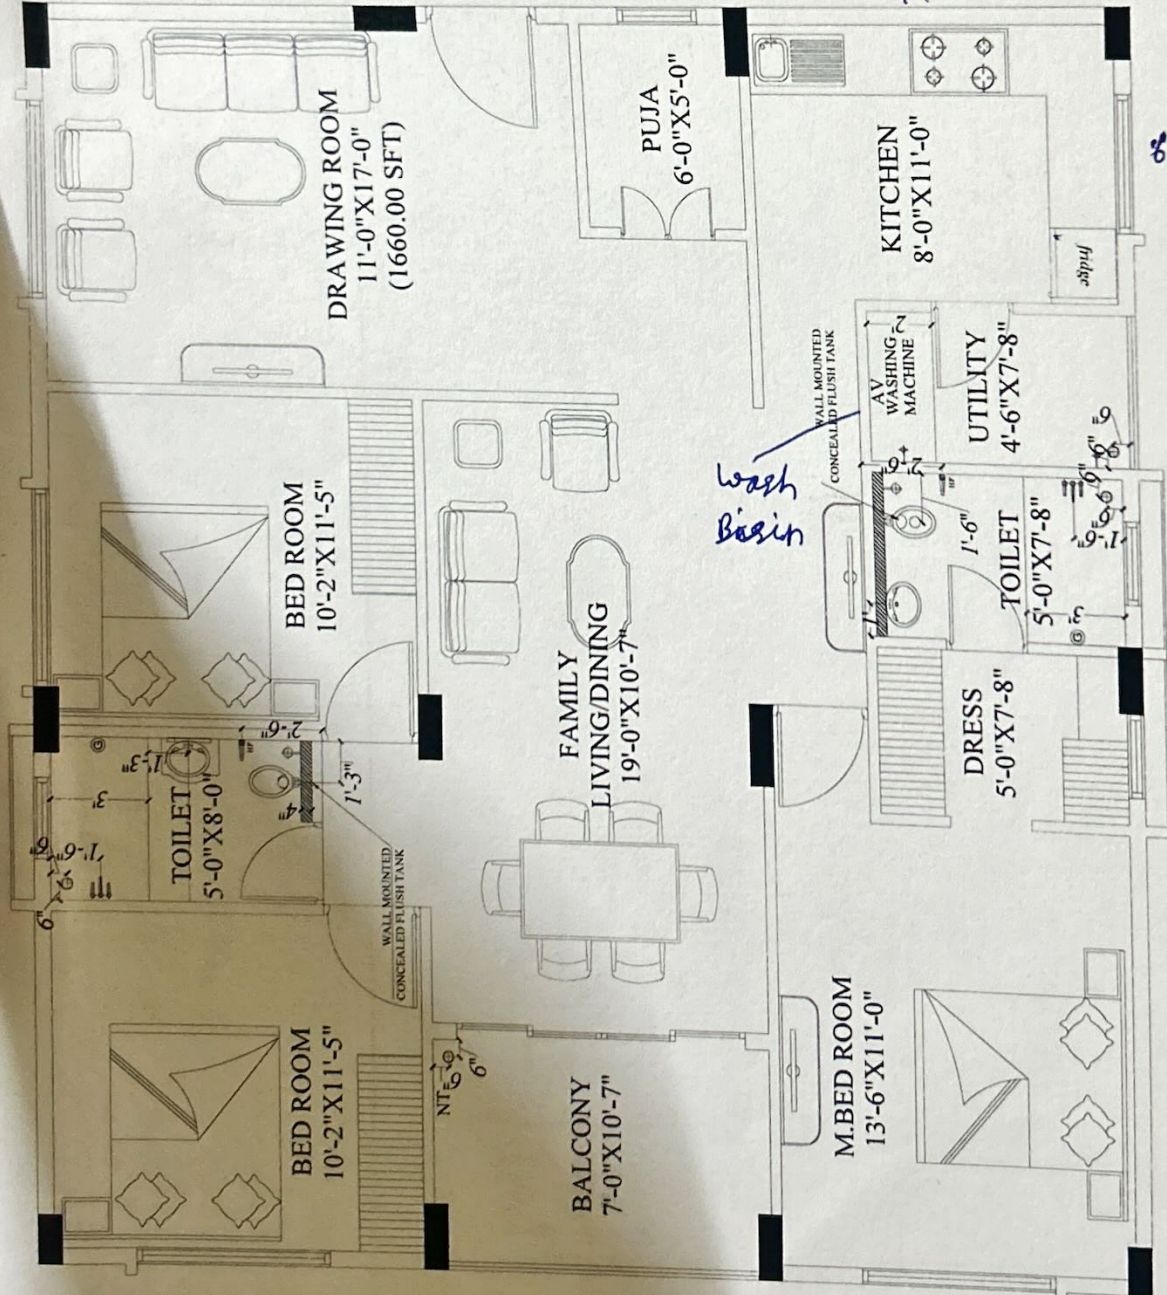

Description	Direction	Owners & Developers :	Date :	Promoted by
PLUMBING PLAN-1660 Sft (B1-TYPE)	N	Modi Reality Mallapur LLP	04.09.20	Modi Properties Pvt Ltd
		Project Name & Phase :	Prepared By :	
		Gulmohar Residency	Approved By :	
			Scale :	Phone: +91-40-66335551

26/02/22

Quality Control Check Report. Stage: After Plumbing & Electrical (Apartments)

Flat No.	D - 508	Other	SI. No.	40295
Company	MRM-UP	Project	Phase	-
Prepared by	K. Sneha	Sign	Date	01/08/2022
Project Manager	Ram Prasad	Sign	Date	01/08/2022
Previous stage report no.			Report filed and signed by PM?	☐ Yes ☒ No
Additions & alterations sheet date	26/02/2022		All pages signed by engineer & customer?	☐ Yes ☒ No
Checked By MD on		MD Sign	For filling	☐ Yes ☒ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- after cleaning the apartment.
- before starting painting, tiling & flooring.
- electrical conduct, waterproofing & plumbing work is completed (for stage II only)
- additions & alterations is finalized and signed. In case there are no additions and alterations printout of email by PM to CR confirming the same must be filed.
- additions & alterations sheets to be transferred to QC file. QC to check if A&A are made as per request.

After Plumbing & Electrical Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. Location of CPVC & PVC fittings must be checked as per measurements given in circular. Tolerance 1".
6. Location, height and spirit level of electrical points must be checked as per measurements given in circular & plan. Tolerance 1".
7. Civil work near pipes in balcony & utility must be neat and mortar should be removed from the pipes.
8. Water proofing must cover all pipes & check height above SFL.
9. Fasteners must be used as specified in circular. Especially check fixing of PVC pipes.
10. Height of DB box must be 6" below false ceiling level or 12" below slab level.
11. In case of many changes in civil work, electrical work and plumbing work, a new drawing must be prepared at HO and approved by MD.

Certified that all corrections mentioned in the QC Report have been completed.
 Project In-charge _____
 Sign _____ Date 10-8-22
 Work can proceed to next stage.

Quality Control Check Report. Stage: After Plumbing & Electrical (Apartments)

S No	Room	Civil work near pipes in balcony & utility ⁷ (✓ or ✕)	CPVC & PVC Check ⁵ (✓ or ✕)	Electrical points check ⁶ (✓ or ✕)	Water proofing check ⁸ (✓ or ✕)	Proper use of fasteners check ⁹ (✓ or ✕)	Placement of DB ¹⁰ (✓ or ✕)	Placement of Generator changeover (✓ or ✕)
1	Bedroom 1 M. Bed	-	-	✓	-	-	-	-
2	Toilet 1 M. Toi	-	✓	✓	✕	✓	-	-
3	Bedroom 2 G. Bed	-	-	✓	-	-	-	-
4	Toilet 2 G. Toi	-	✓	✓	✕	✓	-	-
5	Bedroom 3 K. Bed	-	-	✓	-	-	-	-
6	Toilet 3	-	-	-	-	-	-	-
7	Drawing	-	-	✓	-	-	-	-
8	Dining	-	-	✓	-	-	✓	-
9	Lobby-1 pooja	-	-	✓	-	-	-	-
10	Utility / balcony 1	✕	✕	✓	-	✕	-	-
11	Utility / balcony-2	✓	✓	✓	✕	✓	-	-
12	Utility / balcony-3	-	-	-	-	-	-	-
13	Kitchen	-	✓	✓	-	-	-	-
14	Other							
15	Other							

Remarks Note: 1. Level marking was not done. 2. Without stage-I qc check filing

Work started. 3. Lappam work was pending in dining

Remarks on additions & alteration sheet:

Signed by engineer,	☐ Yes ☒ No	Signed by customer,	☒ Yes ☐ No
Revised drawing required from HO	☐ Yes ☐ No -	Approved revised drawing attached	☐ Yes ☐ No -

Quality Control Check Report, Stage: After Plumbing & Electrical (Apartments)

Miscellaneous check

Screeding done on walls upto 12" outside bathroom/utility	☒ Yes	☐ No
Bathroom /utility filled with 4" water for water proof check	☐ Yes	☒ No
Hole packing done around all pipes in ceiling and internal walls	☒ Yes	☐ No
Remarks:		

Quality Control Check Report. Stage: After Brickwork (Apartments/ Lab Spaces)

Flat No.	D-508	Others	Sl. No.	39846.
Company	MRM (LIP)	Project	Phase	
Prepared by	S. Sundar Kumar	Sign	Date	06/5/82
Project Manager	Rampasobad	Sign	Date	06/5/82
Previous Stage report no.	38593.	Report filed and signed by PM?	Yes ☐ No ☐	
Apartment No.	Other	other	For filling	Yes ☐ No ☐
Checked By MD on	MD Sign			

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- brickwork is completed
- chicken mesh fixed
- after cleaning the apartment
- electrical conducting work is completed

Brickwork Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. Wall thickness should be as per plan. Use of 4", 6" & 8" blocks must be checked.
6. All walls should have 2 beds of about 2" to 3" thickness with one no. 6 mm or 8 mm rod with M15 CC.
7. Chicken mesh should be used in each and every joint between RCC & Brickwork.
8. Joint between brickwork & beam on external side must be filled.
9. Check room dimensions with working plan. (Tolerance: 1")
10. Check room dimensions with working plan. (Tolerance: 2")
11. Diagonals of each room shall be equal. (Tolerance: 1")
12. Balcony sill level should be 3"3" from SFL. (Tolerance: 1")
13. Check room height with specified height. (Tolerance: 1")
14. Check plumb of walls wherever it appears to be out of plumb. (Tolerance: 1/2")
15. Specify the No. of beams which are not aligned by more than 1" in a room.
16. Door frames must have black Japan coating and wood primer /pellambar - at cost of painter.

Certified that all corrections mentioned in the QC Report have been completed. Work can Proceed to next Stage.

Project In-charge	Sign	Date
[Signature]	[Signature]	15/5/22

S No	Room	Wall thickness (✓ or X)	Beds in walls (✓ or X)	Chicken mesh (✓ or X)	External brickwork & beam joint (✓ or X)	Room Dimensions (✓ or X)	Room Dimensions (✓ or X)	Diagonal Difference in inches (✓ or X)	Diagonal Difference in inches (✓ or X)	Balcony sill level (✓ or X)	Room Height (✓ or X)	Plumb of walls (Good/Avg./Bad)	Alignment of beams and walls - Nos.
1	Bedroom 1 M.Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M.Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 K.Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 C.Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 G.Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility/balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Utility/balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility/balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other- Pooja	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
15	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
Remarks ① Internal walls are changed as per customer request													

Specify rooms that need correction:

☐ Good ☒ Avg. ☐ Bad

Misc. Checks.

Was 3.75 CFT proportion box provided?

Condition of proportion box?

Was the Apartment cleaned before starting brick work?

Is the Apartment cleaned for plastering?

Wastage?

Storage of building material like bricks sand and cement.

Drum (200 ltrs) provided for curing in each flat?

Remarks:

Door Frames & Windows check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. Window template depth should be between 2 to 2 1/2" after plastering.
6. Lintel level should be 7'3" from SFL & 7' from FFL. (Tolerance 1"). Lintel should be as per standard design.
7. Lints should be at a height of 7' to 7'3" from FFL. Kitchen plat form thickness should be 2" SFL to bottom 31" (Tolerance 1")
8. Slopes of lofts and kitchen platforms to be checked by using 12" spirit level and check height from floor from 2 or 3 points.
9. Thickness of platforms & lofts should be between 2 & 2.5".
10. Provide single layer table brick at bottom of each door frame without threshold.
11. Check Z angle template size (Z angle for bathroom ventilators not required in new projects).
12. Window opening must be checked with MS square pipe templates of 2 sizes for inner and outer openings.
13. Z angle template must be 1" from brick wall surface from the inner side.

S No	Room	Door size, face and position (✓ or X)	Brick at bottom of door frame (✓ or X)	Door frame hold fast provision and fasteners. (✓ or X)	Door lintel design & level (✓ or X)	Door diagonal check (✓ or X)	Door Plumb - two sides (✓ or X)	Windows lintel design & level, Sill level (✓ or X)	Windows size (✓ or X)	Windows - template depth & diagonal (✓ or X)	Windows - template red oxide painting (✓ or X)	Loft & Kitchen platform height (✓ or X)	Loft & Kitchen platform slope (✓ or X)	Door size, face and position (✓ or X)
1	Bedroom 1 M.Bed	✓	XX	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 K.Bed	✓	XX	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 C-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3	✓	XX	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other- Pooja	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
15	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓

Remarks: ① Kilt platform not casted.

② Over positions are charged as per customer request.

ATR on Quality Control Check Report. (Apartments)

Flat No	D-508.	QC report stage	Plastering	Sl. No.	39983
Company	MRMCL	Project	GMB	Phase	-
Prepared by	Munath	Sign	<i>[Signature]</i>	Date	16/12/23
Project Manager	K. Narendar.	Sign	<i>[Signature]</i>	Date	18/12/23.
Receipt by QC date		Sign		Other	
Receipt at HO date		Sign		Other	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No
Recommendation that was made by QC: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team.					

Notes:

1. Attach a copy of the QC report to this sheet.
2. Circle each correction with a red pen - tick (✓) each circle for work completed and cross (X) each circle where work has not been completed.
3. Give remarks for each case where work has not completed on this sheet.
4. Make 2 copied of the ATR - send one to MD and other to QC.
5. Enclose required photographs - hard copy.

Remarks:

works completed.

Quality Control Check Report. Stage: After Plastering (Apartments)			
Flat No.			
Company	D-508	Other	Sl. No.
Prepared by	MRM-CLLP)	Project	Phase
Project Manager	P. Bhaxath	Sign	Date
Previous stage report no.	Rampdasad	Sign	Date
Checked By MD on	39846	Report filed and signed by PM?	02-06-22
Recommendation:	MD Sign	For filling	02-06-22
☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☐ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.			

Inspection should be done after:

- brickwork & 2 coats plastering is completed
- after cleaning the villa.
- Water proofing, screeding in bathrooms is completed.
- before starting painting, tiling & flooring.

Certified that all corrections mentioned in the QC Report have been completed. Work can Proceed to next Stage.

Project In-charge	Sign	Date

Plastering Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. 9" unplastered area from SFL should be left including in common areas and terraces.
6. Windows must be checked with templates. Plastering must be 3mm margin for luppum work. Tolerance 1/4"
7. Provision of tiles in bathrooms, kitchen & wash areas (rough plastering).
8. Check size of sink bowl. Hole should be 1" to 2" larger. (Tolerance: 1")
9. All doors frames should have 1/2" grooves.
10. Sill top must me of uniform thickness, correct height, at one level & without broken edges.

Control Check Report. Stage: After Plastering (Apartments)

S No	Room	Skirting Provision (✓ or X)	Furnishing around door frame (✓ or X)	Beams & columns finishing (✓ or X)	Finishing of lofts (✓ or X)	Electricity junctions finishing (✓ or X)	Windows check (✓ or X)	Tiles provision (✓ or X)	Sink provision & size (✓ or X)	Grooves for door frames (✓ or X)	Balcony & terrace sill top finishing (✓ or X)	Screeding in bathroom & utility (✓ or X)	Screeding in 6" above FFL? (✓ or X)
1	Bedroom-1 M-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom-2 K-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 C-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom-3 Gr-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Bedroom 4	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Toilet 4	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Lobby 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Balcony	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Utility	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
15	Portico	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
16	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
17	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓

✓ Screeding works were poor in the flat.

✓ plastering near DB Box was not done.

Remarks
