

Construction Division
Additions & Alteration Charges Approval Form

Company Name:	MRMLLP	Site	Gulmohar Residency
Name of the customer	Mr. Sanjay Majumdar F-302		
Villa/ Flat No.			
Sl.No	Description	Amount	
1	Total extra Charges	20,428	
2	Total refundable amount	1080	
3	Net amount to be charges (if any)	19,348	
4	Net amount to be refunded (if any)	-	
Remarks :			
Approved by Project Manager		Approved by Design Team	
Date		Date	
Sign:		Sign:	

Note: 1. Enclose measurement & estimate sheet. 2. Send scanned copy by email to plans@modiproperties.com & CR. 3. Maintain originals in A&A of customers at site.

MEASUREMENT SHEET

Company Name:		MRMLLP		Approved by:		Ramprasad		
Project:		Gulmohar Residency		Sign:				
Work Description:		Extra Specs						
Contractor Name:		F-302(Mr.Sanjay Majumder)						
Prepared By		G.Rajesh						
Date:		26.12.2022						
		A	B	C	D	E=AxBxCxD	F	
S No.	Item Head	Item Description	Length	Width	Height	Nos.	Quantity	Units
1	Crema Marfil -4'x2'	Living Room	23	1	11	1	253	sft
2		passage 1	10	1	3	1	30	sft
3		passage 2	5	1	3	1	15	sft
4	Urban Wood natural -4'X8"	C.BedRoom	11	1	13	1	143	sft
5		Skirting 18%	1	1	1	1	79.38	Rft
6	Extra Wash Basin point	Wash Basin point	1	1	1	1	1	No's
Refund								
1	Kitchen Dado	Kitchen Dado	18	1	2	1	36	sft

Value

1.00

17.00

3.00

1.00

11.00

21.00

17.00

2.70

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

7.00

ESTIMATE SHEET						
Company Name:		MRMLIP		Approved by:		Ram Prasad
Project:		Gulmohar Residency		Sign:		
Work Description:		Extra Specs				
Contractor Name:		F-302(Mr.Sanjay Majumder)				
Prepared By		G.Rajesh				
Date:		26.12.2022				
S No.	Item Head	Item Description	Quantity	Units	Rate	Amount
1	Crema Marfil -4'x2'	Living Room passage 1	253	sft	35	8855
2		passage 2	30	sft	35	1050
3		passage 2	15	sft	35	525
4	Urban Wood natural -4'X8"	C.BedRoom Skirting 18%	143	sft	40	5720
5			79.38	Rft	35	2778.3
6	Extra Wash Basin point	Wash Basin point	1	No's	1500	1500
					Total	20428.3
	Refund					
1	Kitchen Dado	Kitchen Dado	36	sft	30	1080
					Total	1080



GULMOHAR RESIDENCY

Sy. No. 19, Mallapur Village, Uppal, Hyderabad.
Owned & Developed by: M/s. Modi Realty Mallapur LLP.
Head office; 5-4-187/3&4 M G Road Secunderabad.

Details of Additions & Alterations

Flat No	302	Block no.	' F '
Flat Area	1360 sft	Type	Deluxe / Luxury
Buyer Name	Sanjay Majumder		
Phone No.	9581004400	Email	


I hereby confirm that I have given the details of the minor additions and alterations that are required in the above referred flat in the pages attached herein. Please complete the changes suggested by me. I agree to pay the charges, if any, for the additions and alterations that I have asked you to make, as per the rates suggested by you. I shall deliver all the materials that are required to be provided by me at the site on or before _____ . In case I fail to deliver these items to the site by the specified date, you may complete the works in the flat as per the standard items provided by you.

Buyers sign		Engg. Sign	
Date:	19/03/22	Date	19/03/22


Note:

1. Colour shades of paints may vary from batch to batch & company to company. The Builder will not take responsibility of quality of work for dark shades especially green & blue.
2. Shade / colour of natural material like marble and granite can't be guaranteed and may vary from lot to lot. Cracks like appearance in marble is a natural feature and Builder shall not be responsible for repairs or replacement.
3. Availability of bathroom or flooring tiles of the same type /colour/make can not be guaranteed and closest possible type/colour/make may be used in its place.
4. No further change shall be permitted from this day.
5. Please sign on all pages.

Buyers sign:



Engg. Sign:



Date: 19/03/22

Choice of colours:

Changes in flooring:

1) Living/Dinning. Creama Mafill.

2) M. Bed Room & G. Bed Room. Super glossy. & C-Bed Urban Wood Natural

3) M. Bed Toilet Malaysia.

4) C. M Toilet Luna.

Buyers sign:

Engg. Sign:

Date: 19/03/22.

Changes in electrical points: (mark on plan)

Choice of Bathroom tiles, CP fittings & Sanitary ware:

Buyers sign:

Engg. Sign:

Date:

Changes in kitchen platform: (mark on plan)

→ Granite not required



→ 4" skirting required on kitchen platform

Other Changes:

Buyers sign:

Engg. Sign:

Date:

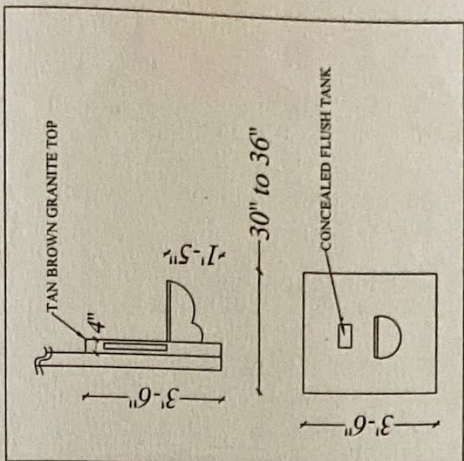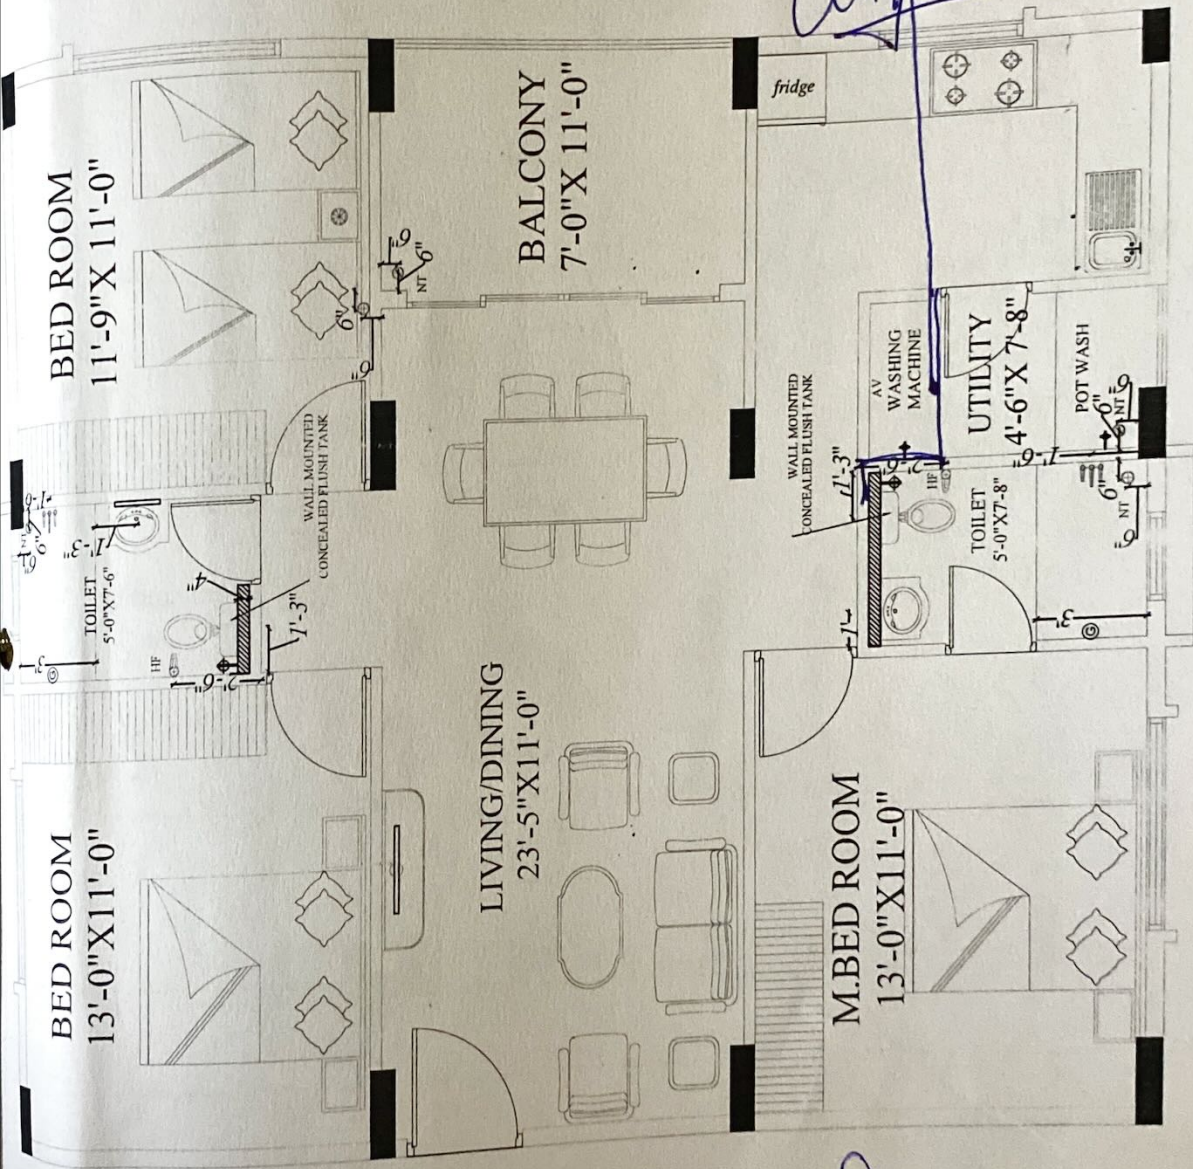


LEGEND

+	HEALTH FAUCET
⌋	ANGLE VALVE
⊙	NANI TRAP
○	3" RAIN WATER PIPE
⊙	GEASER POINT
⌋	WALL MIXTURE
+	TAP / LONG BODY

Handwritten signature and date: 19/03/2022

Description	Direction	Owners & Developers :		Date :	Promoted by	
		Modi Reality Mallapur LLP		16.09.20	Jayapradha	
		Project Name & Phase :		Prepared By :	Soham Modi	
		Gulmohar Dacidanov		Approved By :	Soham Modi	
		PLUMBING PLAN-1360 Sft (A2-TYPE)		Scale :	N T D	

Phone: +91 90 66225551

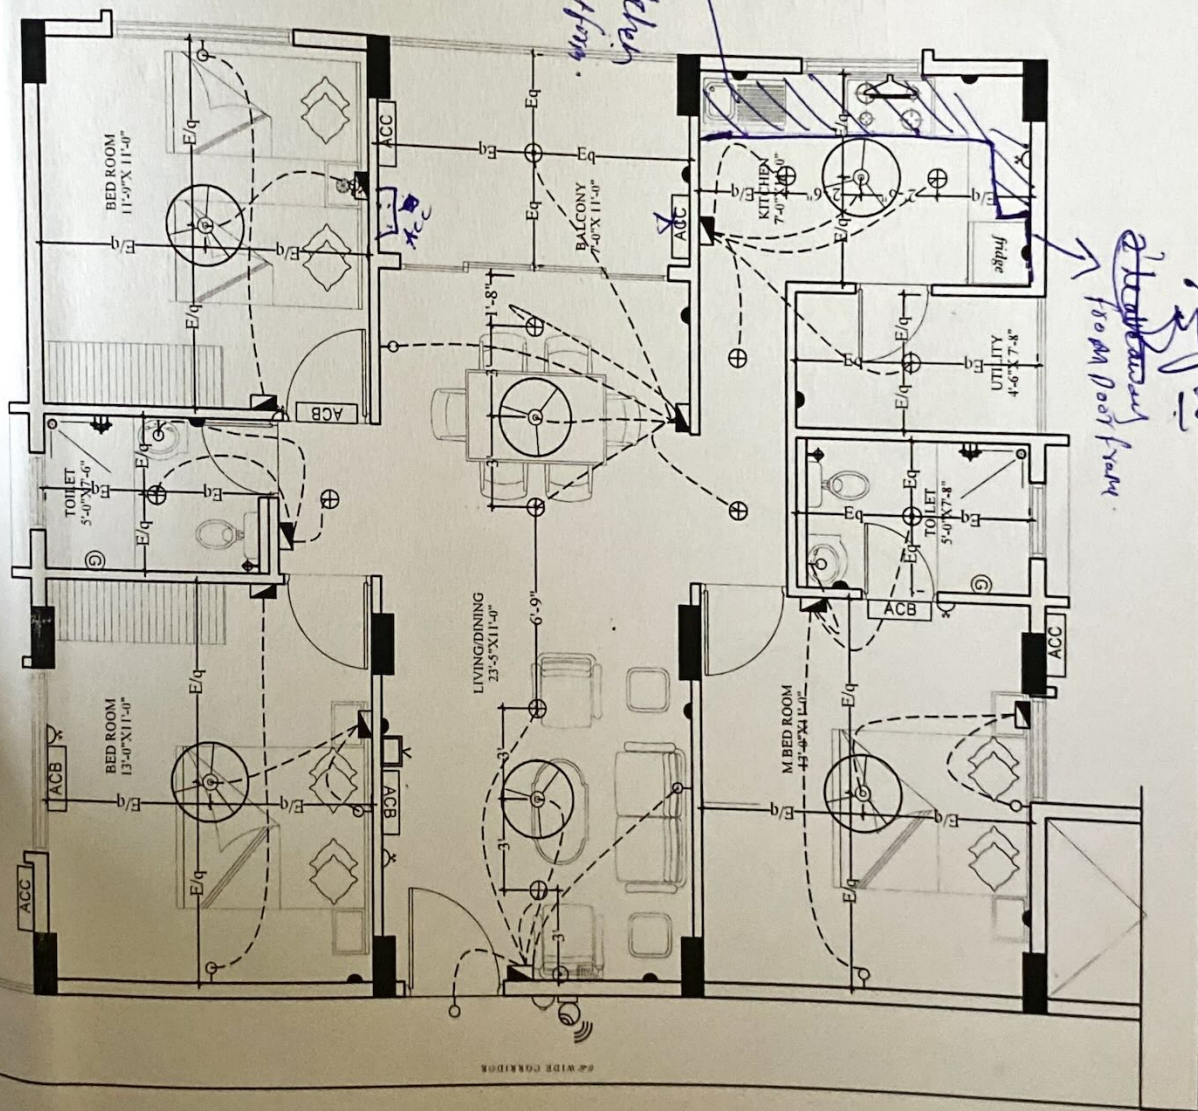

LEGEND:-

S.NO	ITEM	SYMBOL	HEIGHTS from FFL
1.	Distribution Board & Change over		7' TO 7'6"
2.	Switch board		4 OR 4'6"
3.	Wall pendant/track light		7'3" TO 7'6"
4.	5 amp plug point		2'
5.	Ceiling fan		6'6" OR 7'6"
6.	Exhaust fan		7'3"
7.	10 amp plug point		2' OR 3'6" OR 7'6"
8.	Television point		3'
9.	Telephone point		2'
10.	Ceiling Bell		4'6"
11.	Bed Push		6'
12.	Ceiling light		7'6"
13.	W8 Camera		7' TO 7'6"
14.	AC Compressor		7' TO 7'6"
15.	AC Blower		7' TO 7'6"
16.	Switch board with SA socket		4' TO 4'6"

Note - Switch boards next to bed side must be @ 35" from center of bed.

Description	Direction	Owners & Developers	Date	Promoted by
ELECTRICAL PLAN - 1360 sq ft FLATS-A2 TYPE	N	Modi Realty Multi pur LLP	21.09.2020	Modi Properties Pvt Ltd
		Project Name & Phase	Prepared By	
			Approved By	
				Soham Modi

Complaints And Suggestions from Gulmohar Residency

From: Gulmohar Residency (info@modiproperties.com)

To: cr@modiproperties.com; feedback@modiproperties.com; kprasad@modiproperties.com;
gbrambabu@modiproperties.com; gmr-const@modiproperties.in; sanjay217@gmail.com

Date: Monday, August 7, 2023 at 07:39 PM GMT+5:30

Complaint Id : 624574

Project Name : Gulmohar Residency

Block No / Phase : Block F

Flat No/Villa :302

Nature of complaint :Day to Day Maintenance

Customer Name : Sanjay Majumder

Email : sanjay217@gmail.com

Complaints :

1. Garbage is not collected every day. We have wet waste all non veg since 3 days no one collected , Plus dog comes and dismantle it with bad smell all over .

Note:

1. Please allow atleast two weeks for us to attend your complaint.
2. In general written response / reply to complaints shall not be given.
3. In case the complaint is not attended to for over two weeks customers are requested to send a reminder using the form given.

ACTION TAKEN REPORT (FOR COMPLAINTS)

Flat / bungalow No.	F-302	ATR Date	13-09-2023
Project	GMR	Complaint Date	19-08-2023
Customer Name	Sanjay	Com.ID.no:	13928
Prepared By	B.Meenakshi		
Project Manager's Sign	K.Narender	Admin Officer's Sign	Meenakshi

Note: Original ATR should be sent to CR & a copy to MD. CR to file original in customer's file.

[illegible]

Note: 1. Keep the report brief. 2. Do not repeat the complaint. 3. Use terms like "Work completed", "Changes not permitted – work not taken up", "Kept pending at customer's request", "Beyond our scope of work", etc

Quality Control Check Report for ATR on Complaints.

Flat / bungalow No.	F-302	ATR Date	13-09-2023
Project	GMR	Complaint Date	19-08-2023
Customer Name	Sanjay		
Prepared by	Saikiran	Date	25-09-2023
Project Manager	Narendar	Date	25-09-2023
HO receipt date		Sign	
Checked by MD on		MD Sign	
MD's Remarks:			
CR to send letter to customer	☐ Yes ☐ No	For filling	☐ Yes ☐ No

Note: CR will send a copy of ATR and complaint to QC immediately after the receipt of the ATR. QC will send their report on the ATR to the MD within 3 working days. Aruna to file to file it in MDs pending complaints file.

Complaint S No.	Quality of action taken by Site Engg on complaint?	If action on the complaint was not taken then, was the reason for not taking action justified?
1.	Avg	☐ Yes ☐ No
2.	☐ Good ☐ Avg. ☐ Bad	☐ Yes ☐ No
3.	☐ Good ☐ Avg. ☐ Bad	☐ Yes ☐ No
4.	☐ Good ☐ Avg. ☐ Bad	☐ Yes ☐ No
5.	☐ Good ☐ Avg. ☐ Bad	☐ Yes ☐ No
6.	☐ Good ☐ Avg. ☐ Bad	☐ Yes ☐ No
7.	☐ Good ☐ Avg. ☐ Bad	☐ Yes ☐ No
8.	☐ Good ☐ Avg. ☐ Bad	☐ Yes ☐ No
9.	☐ Good ☐ Avg. ☐ Bad	☐ Yes ☐ No
10.	☐ Good ☐ Avg. ☐ Bad	☐ Yes ☐ No
11.	☐ Good ☐ Avg. ☐ Bad	☐ Yes ☐ No
12.	☐ Good ☐ Avg. ☐ Bad	☐ Yes ☐ No
Remarks:		

ATR on Quality Control Check Repot. (Apartments)

Flat No	F-302	QC report stage	After stage - II	SL No.	40741
Company	MRMLP	Project	GMR	Phase	
Prepared by	Nagendar	Sign	<i>[Signature]</i>	Date	7/1/22
Project Manager		Sign	<i>[Signature]</i>	Date	7/1/22
Receipt by QC date		Sign		Other	
Receipt at HO date		Sign		Other	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation that was made by QC:

☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.

☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team.

Notes:

1. Attach a copy of the QC report to this sheet.
2. Circle each correction with a red pen – tick (✓) each circle for work completed and cross (X) each circle where work has not been completed.
3. Give remarks for each case where work has not completed on this sheet.
4. Make 2 copied of the ATR – send one to MD and other to QC.
5. Enclose required photographs – hard copy.

Remarks:

Quality Control Check Report. Stage: After Finishing Stage III (Apartments)

Flat No	F-302	Other	Project	SI. No.	40741
Company	MRM- (LIP)	Sign	GMR	Phase	
Prepared by	P. Bhaxath	Sign	PB	Date	28-10-22
Project Manager	Ramprasad	Sign		Date	28-10-22
Previous stage report no.				Report filed and signed by PM	☒ Yes ☐ No
Checked By MD on	40320	MD Sign			☐ Yes ☐ No
Recommendation:				For filling	

☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.

☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team.

☐ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.


☐ Proceed with further work. ATR not required.

Inspection should be done after :

- Completing stage II works.
- Complete works like doors, windows, grills, electrical wiring, switches, french door glass, etc.
- In case of modular kitchen provide platform, granite and dado and modular kitchen in this stage.
- Provide video door phone in this stage.
- Possession for wood work cannot be given until QC check for stage III is completed and all corrections mentioned in the report are made.

Miscellaneous check:

Modular kitchen to be provided	☐ Yes ☐ No	Modular kitchen provided	☐ Yes ☐ No
Modular kitchen workman ship	☐ Good ☐ Avg ☐ Poor	Modular kitchen granite & dado workman ship & finishing	☐ Good ☐ Avg ☐ Poor
Video door phone /wifi cam to be provided	☒ Yes ☐ No	Video door phone/wifi cam provided	☐ Yes ☒ No
Painting marks and drops are cleaned from floor, windows, walls.	☐ Good ☐ Avg ☒ Poor		

Project In-charge

 10/11/22

Quality Control Check Report. Stage: After Finishing Stage III (Apartments)

Rate the quality of (Good ✓, Avg. X, Poor – needs correction XX, NA)													
S No	Room	Door, door knob & door stopper fitting	Door, door knob & door stopper cleaning	Window grills & quality	Window grills fitting & finishing	Windows quality	Window fitting & finishing	Balcony railing quality & finishing	French door quality & fitting	CP jali quality and fitting	Edge building	Switch boards fitting & covering with plastic covers	Junction box covers painting
1	Bedroom-1 M-Bed	✓	✓	✓	XX	✓	✓	✓	✓	✓	✓	✓	✓
2	Bedroom-2 K-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom-3 G-Bed	✓	✓	✓	XX	✓	✓	✓	✓	✓	XX	XX	✓
4	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	XX	✓	✓
5	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Lobby-1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	XX	✓	✓	✓
8	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Utility / balcony-3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Toilet-1 M-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Toilet-2 C-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Toilet-3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
15	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
Remarks		1) For Main door stopper not provided 2) G-Bed Sengage started											
3)		Finishing under kitchen platform not done, skirting piece not provided in											
5)		For utility grill not provided.											

Quality Control Check Report. Stage: After Finishing Stage III (Apartments)

Rate the quality of (Good ✓, Avg. X, Poor - needs correction XX, NA)													
S No	Room	Door, door knob & door stopper fitting	Door, door knob & door stopper cleaning	Window grills & quality	Window grills fitting & finishing	Windows quality	Window fitting & finishing	Balcony railing quality & finishing	French door quality & fitting	CP jali quality and fitting	Edge building	Switch boards fitting & covering with plastic covers	Junction box covers painting
1	Bedroom 1 M. Bed	✓	✓	✓	XX	✓	✓				✓	✓	✓
2	Bedroom 2 K. Bed	✓	✓	✓	✓	✓	✓				✓	✓	✓
3	Bedroom 3 Gr Bed	✓	✓	✓	XX	✓	✓				✓	✓	✓
4	Drawing	✓	✓	✓	✓	✓	✓				✓	✓	✓
5	Dining	✓	✓	✓	✓	✓	✓				✓	✓	✓
6	Lobby 1	✓	✓	✓	✓	✓	✓				✓	✓	✓
7	Utility / balcony 1	✓	✓	✓	✓	✓	✓				✓	✓	✓
8	Utility / balcony 2	✓	✓	✓	✓	✓	✓	XX	✓	✓	✓	✓	✓
9	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Toilet 1 M-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Toilet 2 C-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
15	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
Remarks		1) For main door stopper not provided 2) Gr Bed sewage stated											
3)		Finishing under kitchen platform not done, skirting piece not provided in											
5)		For utility grill not provided.											

ATR on Quality Control Check Report. (Apartments)

Flat No	F-302	QC report stage	stage - 2	Sl. No.	40320
Company	MRMLLP	Project	G.M.R	Phase	
Prepared by	D. Srikanth	Sign	D. Srikanth	Date	21/9/2022
Project Manager	M. Ramprasad	Sign	M. Ramprasad	Date	21/9/2022
Receipt by QC date		Sign		Other	
Receipt at HO date		Sign		Other	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No
Recommendation that was made by QC: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team.					

Notes:

1. Attach a copy of the QC report to this sheet.
2. Circle each correction with a red pen - tick (✓) each circle for work completed and cross (X) each circle where work has not been completed.
3. Give remarks for each case where work has not completed on this sheet.
4. Make 2 copied of the ATR - send one to MD and other to QC.
5. Enclose required photographs - hard copy.

Remarks:

1) All works completed

F-203
 Prepared by: **BM (LLP)**
 Project Manager: **S. Sundar**
 Previous stage report no: **39733**
 Checked By: MD on **39733**
 Recommendation: **For Pass**
 Other: **40380**
 Project: **GMR**
 Sign: **[Signature]**
 Date: **05/02/22**
 Date: **05/02/22**
 Report filed and signed by PM: **[Signature]**
 For filing: ☐ Yes ☐ No

Certified that all corrections mentioned in the QC Report have been completed.
 Work can proceed to next Stage.

Project In-charge Sign Date
[Signature]

- Inspection should be done after:
- Completion of flooring, bathroom/utility tiles, first coat of paint.
 - Completion of doors, windows, grills, electrical wiring, switches must be done in next stage.
 - False ceiling must be completed before flooring.
 - Kitchen platform, granite and dado must be completed where modular kitchen is not provided.
 - Provide granite soffit for main door and balconies in this stage.

Miscellaneous check

Main door fixed with lock & stopper	☒ Yes ☐ No	Granite soffit for balcony provided	☒ Yes ☐ No
Granite soffit for balcony required	☒ Yes ☐ No	Balcony granite soffit edge polishing	☒ Good ☐ Avg ☐ Poor
Balcony granite soffit workmanship	☒ Good ☐ Avg ☐ Poor	Granite soffit for main door provided	☒ Yes ☐ No
Granite soffit for main door required	☒ Yes ☐ No	Main door granite soffit edge polishing	☒ Good ☐ Avg ☐ Poor
Main door granite soffit workmanship	☒ Good ☐ Avg ☐ Poor		

Tiling & granite work		Rate the quality of (Good ✓, Avg. X, Poor - needs correction XX, NA)													
S No	Room	Workmanship of tiling	White cement filling around PVC lines	corners finishing	finishing near doors	finishing on top of tiles	finishing near ventilators	Step at bathroom entrance / utility	Step for shower / pool wash	Tile joint grouting	Granite platform finishing and edge polishing	Granite platform slope	Granite platform height	Finishing under granite platform	
1	Toilet 1 M. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
2	Toilet 2 C. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
3	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
4	Toilet 4	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
5	Wash basin in dining area	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
6	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
7	Utility	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
8	Other														
9	Other														
Remarks		① Provision for Modular Kitchen.													

Rate the quality of (Good $\circ$ Avg. $\times$ Poor $\times$ needs correction $\times$ X, N.A.)

S No	Room	Floor tiles	Footing workman ship & grouting	Skirting size (3")	Skirting workmanship	Plastering above skirting	Plastering & finishing of walls	Crack filling	Left Finishing	Windows check	General quality of painting & finishing	Door & frame painting quality	Door beading, lipjam and painting quality	Ledge banding
1	Bedroom 1 M.Bed	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$
2	Bedroom 2 K.Bed	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$
3	Bedroom 3 G.Bed	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$
4	Drawing	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$
5	Dining	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$
6	Lobby	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$
7	Utility balcony 1	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$
8	Utility balcony 2	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$
9	Utility balcony 3	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$
10	Kitchen	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$
11	Other	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$
12	Other	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$	$\times$

Remarks: In M.Bed (4 no) Tile Broken. In Balcony. Toilets, in kitchen-
(1 no) of wall painting was not done. In C-Toi Tile piece broken-
near Switch board. For Ocean Side painting was not done.
Given all painting and clearing quality was very poor.

Quality Control Check Report. Stage: After Plumbing & Electrical (Apartments)

Flat No.	F-302	Other		Sl. No.	39733
Company	MRM(L2P)	Project	GMR	Phase	
Prepared by	S. S. Vaidyanathan	Sign		Date	14/4/22
Project Manager	R. R. S. S. S.	Sign		Date	14/4/22
Previous stage report no.				Report filed and signed by PM?	☒ Yes ☐ No
Additions & alterations sheet date				All pages signed by engineer & customer?	☐ Yes ☐ No
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- after cleaning the apartment.
- before starting painting, tiling & flooring.
- electrical conduct, waterproofing & plumbing work is completed (for stage II only).
- additions & alterations is finalized and signed. In case there are no additions and alterations printout of email by PM to CR confirming the same must be stage.
- additions & alterations sheets to be transferred to QC file. QC to check if A&A are made as per request.

After Plumbing & Electrical Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. Location of CPVC & PVC fittings must be checked as per measurements given in circular. Tolerance 1".
6. Location, height and spirit level of electrical points must be checked as per measurements given in circular & plan. Tolerance 1".
7. Civil work near pipes in balcony & utility must be neat and mortar should be removed from the pipes.
8. Water proofing must cover all pipes & check height above SFL.
9. Fasteners must be used as specified in circular. Especially check fixing of PVC pipes.
10. Height of DB box must be 6" below false ceiling level or 12" below slab level.
11. In case of many changes in civil work, electrical work and plumbing work, a new drawing must be prepared at HO and approved by MD.

all corrections mentioned
in the QC report must be stage.
Work can proceed only after
Project in-charge Sign Date
14/4/22

Quality Control Check Report. Stage: After Plumbing & Electrical (Apartments)

Flat No.	F-302	Other	Sl. No.	39733
Company	MRM(122P)	Project	Phase	
Prepared by	S. S. W. S. W. S. W.	Sign	Date	14/4/22
Project Manager	S. S. W. S. W. S. W.	Sign	Date	14/4/22
Previous stage report no.	39322	Report filed and signed by PM?	Yes ☒ No ☐	
Additions & alterations sheet date	19/3/22	All pages signed by engineer & customer?	Yes ☒ No ☐	
Checked By MD on	MD Sign	For filling	Yes ☐ No ☐	

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- after cleaning the apartment.
- before starting painting, tiling & flooring.
- electrical conduct, waterproofing & plumbing work is completed (for stage II only).
- additions & alterations is finalized and signed. In case there are no additions and alterations printout of email by PM to CR confirming the same must be Stage.
- additions & alterations sheets to be transferred to QC file. QC to check if A&A are made as per request.

After Plumbing & Electrical Check.

Notes:

1. Mark ☒ for correct or minor mistake which does not require correction
2. Mark ☒ for minor mistake that requires minor correction.
3. Mark ☒ for major mistake that requires correction by replacement or re-fixing.
4. Mark ☒ for major mistake that cannot be corrected.
5. Location of CPVC & PVC fittings must be checked as per measurements given in circular. Tolerance 1".
6. Location, height and spirit level of electrical points must be checked as per measurements given in circular & plan. Tolerance 1".
7. Civil work near pipes in balcony & utility must be neat and mortar should be removed from the pipes.
8. Water proofing must cover all pipes & check height above SFL.
9. Fasteners must be used as specified in circular. Especially check fixing of PVC pipes.
10. Height of DB box must be 6" below false ceiling level or 12" below slab level.
11. In case of many changes in civil work, electrical work and plumbing work, a new drawing must be prepared at HO and approved by MD.

all corrections mentioned.
 Certified by the QC Reduced to the Stage.
 Work can proceed to the next stage.
 Project in-charge Sign Date
 19/3/22 14/22

S No	Room	Civil work near pipes in balcony & utility (✓ or ✗)	CPVC & PVC Check ⁵ (✓ or ✗)	Electrical points check ⁶ (✓ or ✗)	Water proofing check ⁸ (✓ or ✗)	Proper use of fasteners check ⁹ (✓ or ✗)	Placement of DB ¹⁰ (✓ or ✗)	Placement of Generator changeover (✓ or ✗)
1	Bedroom 1 M-Bed	—	—	✓	—	—	—	—
2	Toilet 1 M-Toilet	—	—	✓	✓	—	—	—
3	Bedroom 2 K-Bed	—	✓	✓	✓	—	—	—
4	Toilet 2 C-Toilet	—	—	✓	✓	—	—	—
5	Bedroom 3 G-Bed	—	—	✓	—	—	—	—
6	Toilet 3	—	—	✓	—	—	—	—
7	Drawing	—	—	—	—	—	—	—
8	Dining	—	—	✓	—	—	✓	—
9	Lobby 1	—	—	—	—	—	—	—
10	Utility / balcony 1	✓	—	—	—	—	—	—
11	Utility / balcony 2	✓	—	✓	—	✓	—	—
12	Utility / balcony 3	—	✗	✓	—	✓	—	—
13	Kitchen	—	✓	—	—	—	—	—
14	Other	—	—	✓	—	—	—	—
15	Other	—	—	—	—	—	—	—
Remarks		① A light points are missing. ② In utility a pot wash point is not as per specifications.						
Signed by engineer,		☒ Yes ☐ No		Signed by customer,		☐ Yes ☒ No		
Revised drawing required from HO		☐ Yes ☒ No		Approved revised drawing attached		☐ Yes ☐ No		

Miscellaneous check

Screeding done on walls upto 12" outside bathroom/utility	☒ Yes	☐ No
Bathroom /utility filled with 4" water for water proof check	☒ Yes	☐ No
Hole packing done around all pipes in ceiling and internal walls	☒ Yes	☐ No
Remarks:		

Quality Control Check Report. Stage: After Plastering (Apartments)

Flat No.	F-302	Other	Sl. No.	39322
Company	MRMA (UP)	Project	Phase	
Prepared by	T. Vinod Kumar	Sign	Date	14-02-22
Project Manager	Ram Prasad	Sign	Date	14-02-22
Previous stage report no.		Report filed ad signed by PM?		NO
Checked By MD on		MD Sign	For filling	☐ Yes ☐ No
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.				


Inspection should be done after:

- brickwork & 2 coats plastering is completed
- after cleaning the villa.
- Water proofing, screeding in bathrooms is completed.
- before starting painting, tiling & flooring.

Plastering Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark X for minor mistake that requires minor correction.
3. Mark X X for major mistake that requires correction by replacement or re-fixing.
4. Mark X X X for major mistake that cannot be corrected.
5. 9" unplastered area from SFL should be left including in common areas and terraces.
6. Windows must be checked with templates. Plastering must be 3mm margin for luppum work. Tolerance 1/4".
7. Provision of tiles in bathrooms, kitchen & wash areas (rough plastering).
8. Check size of sink bowl. Hole should be 1" to 2" larger. (Tolerance: 1")
9. All doors frames should have 1/2" grooves.
10. Sill top must me of uniform thickness, correct height, at one level & without broken edges.

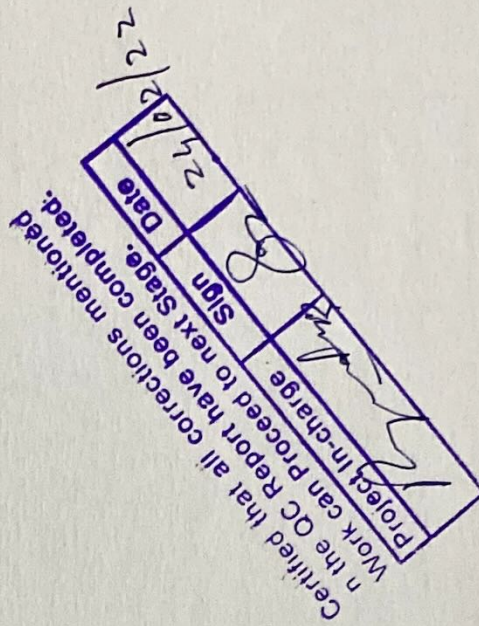

Quality Control Check Report. Stage: After Plastering (Apartments)

S No	Room	Skirting Provision (✓ or X)	Furnishing around door frame (✓ or X)	Beams & columns finishing (✓ or X)	Finishing of lofts (✓ or X)	Electricity junctions finishing (✓ or X)	Windows check (✓ or X)	Tiles provision (✓ or X)	Sink provision & size (✓ or X)	Grooves for door frames (✓ or X)	Balcony & terrace sill top finishing (✓ or X)	Screeding in bathroom & utility (✓ or X)	Screeding in 6" above FFL? (✓ or X)
1	Bedroom 1 M. Bed	✓	✓	✓	✓	✓	X	✓	✓	✓	✓	✓	✓
2	Toilet 1 M. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 C. Bed	✓	✓	✓	✓	✓	X	✓	✓	✓	✓	✓	✓
4	Toilet 2 C. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 G. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Bedroom 4	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Toilet 4	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Drawing	✓	✓	✓	✓	✓	X	✓	✓	✓	✓	✓	✓
10	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Lobby 2 Utility	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Terrace/ balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Terrace/ balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
15	Terrace/ balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
16	Portico	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
17	Kitchen	✓	✓	✓	✓	✓	X	✓	✓	✓	✓	✓	✓
18	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
Remarks		Note:- In both toilets Screeding work to be improve.											

ATR on Quality Control Check Repot. (Apartments)

Quantity Control Check Report. (Apartments)						
Flat No	Company	QC report stage	Sl. No.			
	F-302	Project				38448
Prepared by	MRM (LLP)	Sign	Phase			-
Project Manager	G. Srikanth	Sign	Date			27/10/2024
Receipt by QC date	Rampasab	Sign	Date			
Receipt at HO date		Sign	Other			
Checked By MD on		MD Sign	Other			
Recommendation that was made by QC:				For filling		☐ Yes ☐ No
☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team.						

Notes:

1. Attach a copy of the QC report to this sheet.
2. Circle each correction with a red pen – tick (✓) each circle for work completed and cross (X) each circle where work has not been completed.
3. Give remarks for each case where work has not been completed on this sheet.
4. Make 2 copied of the ATR – send one to MD and other to QC.
5. Enclose required photographs – hard copy.

Remarks:

Remarks:

1) All works completed.

Quality Control Check Repot:

Annual Check Repot.

Stage: After Brickwork (Apartments)

Flat No.	Quality Control Check Repol.			Stage: After Brickwork (Apartments)		
Company	Others	Project	Sl. No.	Phase		
F-302						38148
Prepared by	MRM(11P)	Project		GMR		
Project Manager	S. Sundar Kumar	Sign				
Previous Stage report no.	PMR 02802	Sign				23/9/21
Apartment No.		37819				23/9/21
Checked By MD on		Other		Report filed and signed by PM?		
Recommendation:		MD Sign		other		
						For filling
						☐ Yes ☐ No

☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
☐ Proceed with further work only after making corrections pointed out in the QC report.
☐ Proceed with further work.

Inspection should be done after:

- brickwork is completed
- chicken mesh fixed
- after cleaning the apartment
- electrical conducting work

Brickwork Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✕ for minor mistake that requires minor correction.
3. Mark ✕ ✕ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✕ ✕ ✕ for major mistake that cannot be corrected.
5. Wall thickness should be as per plan. Use of 4", 6" & 8" blocks must be checked.
6. All walls should have 2 beds of about 2" to 3" thickness with one no. 6 mm or 8 mm rod with M15 CC.
7. Chicken mesh should be used in each and every joint between RCC & Brickwork.
8. Joint between brickwork & beam on external side must be filled.
9. Check room dimensions with working plan. (Tolerance: 1")
10. Diagonals of each room shall be equal. (Tolerance: 2")
11. Balcony sill level should be 3'3" from SFL. (Tolerance: 1")
12. Check room height with specified height. (Tolerance: 1")
13. Check plumb of walls wherever it appears to be out of plumb. (Tolerance: 1/2")
14. Specify the No. of beams which are not aligned by more than 1" in a room.
15. Door frames must have black Japan coating and wood primer /pellambar – at cost of painter.

draft brickwork check report for Apts dt 14-0-2021 ver6

Quality Control Check Report. Stage: After Brickwork (Apartments)

S No	Room	Wall thickness (✓ or X)	Beds in walls (✓ or X)	Chicken mesh (✓ or X)	External brickwork & beam joint (✓ or X)	Room Dimensions (✓ or X)	Room Dimensions (✓ or X)	Difference in inches	Diagonal (✓ or X)	Diagonal Difference in inches	Balcony sill level (✓ or X)	Room Height (✓ or X)	Plumb of walls (Good/Avg/Bad)	Alignment of beams and walls - Nos.
1	Bedroom 1 M.Bed	✓	✓	✓	✓	✓	✓	1	✓	1	1	✓	Avg	✓
2	Toilet 1 M.Toi	✓	✓	✓	✓	✓	✓	1	✓	1	1	✓	✓	✓
3	Bedroom 2 K.Bed	✓	✓	✓	✓	✓	✓	1	✓	1	1	✓	✓	✓
4	Toilet 2 C.Toi	✓	✓	✓	✓	✓	✓	1	✓	1	1	✓	✓	✓
5	Bedroom 3 (M.Bed)	✓	✓	✓	✓	✓	✓	1	✓	1	1	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	1	✓	1	1	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	1	✓	1	1	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	1	✓	1	1	✓	✓	✓
9	Lobby	✓	✓	✓	✓	✓	✓	1	✓	1	1	✓	✓	✓
10	Utility/balcony 1	✓	✓	✓	✓	✓	✓	1	✓	1	1	✓	✓	✓
11	Utility/balcony 2	✓	✓	✓	✓	✓	✓	1	✓	1	1	✓	✓	✓
12	Utility/balcony 3	✓	✓	✓	✓	✓	✓	1	✓	1	1	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	1	✓	1	1	✓	✓	✓
14	Other	✓	✓	✓	✓	✓	✓	1	✓	1	1	✓	✓	✓
15	Other	✓	✓	✓	✓	✓	✓	1	✓	1	1	✓	✓	✓
Remarks		1) Balcony Sill level wall not constructed. 2) Utility Sill level wall not constructed as per specification. 3) the Supervision (Engineer) not happening. 4) Hacking work also not so good.												

Quality Control Check Report. Stage: After Brickwork (Apartments)

Quality of edges and corners in all rooms?

☐ Good ☒ Avg. ☐ Bad

Specify rooms that need correction:

Misc. Checks.

Was 3.75 CFT proportion box provided?

☐ Yes ☒ No

Condition of proportion box?

☐ Good ☐ Avg. ☐ Bad

Was the Apartment cleaned before starting brick work?

☐ Yes ☐ No ☒ Cant' say

Is the Apartment cleaned for plastering?

☒ Yes ☐ No

Wastage?

☐ High ☒ Medium ☐ Low

Storage of building material like bricks sand and cement.

☐ Good ☒ Avg. ☐ Bad

Drum (200 ltrs) provided for curing in each flat?

☒ Yes ☐ No

Remarks:

Door Frames & Windows check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark X for minor mistake that requires minor correction.
3. Mark X X for major mistake that requires correction by replacement or re-fixing.
4. Mark X X X for major mistake that cannot be corrected.
5. Window template depth should be between 2 to 2 1/2" after plastering.
6. Lintel level should be 7'3" from SFL & 7' from FFL. (Tolerance 1"). Lintel should be as per standard design.
7. Slopes of lofts and kitchen platforms to be checked by using 12" spirit level and check height from floor from 2 or 3 points. (Tolerance 1")
8. Thickness of platforms & lofts should be between 2 & 2.5".
9. Provide single layer table brick at bottom of each door frame without threshold.
10. Check Z angle template size (Z angle for bathroom ventilators not required in new projects).
11. Window opening must be checked with MS square pipe templates of 2 sizes for inner and outer openings.
12. Z angle template must be 1" from brick wall surface from the inner side.

Quality Control Check Report.

Stage: After Brickwork (Apartments)

S No	Room	Door size, face and position (✓ or X)	Brick at bottom of door frame (✓ or X)	Door lintel design & level (✓ or X)	Door diagonal check (✓ or X)	Door Plumb - two sides (✓ or X)	Windows lintel design & level, sill level (✓ or X)	Windows size (✓ or X)	Windows - template depth & diagonal (✓ or X)	Windows - template red oxide painting (✓ or X)	Loft & Kitchen platform height (✓ or X)	Loft & Kitchen platform slope (✓ or X)	Door size, face and position (✓ or X)
1	Bedroom 1 M. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M. Tol	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 K. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 C. Tol	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 M. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
15	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
Remarks:		① M. Bed of M. Tol should be removed & Re-fix properly. ② All window sill level installed (3'-3") - 1st, they provided (3'-6"). ③ Kit. Platform not casted											

Quality Control Check Report. Stage: After Brickwork (Apartments)

Flat No.	F-302	Others	Sl. No.	138148
Company	MRM (12P)	Project	Phase	
Prepared by	S. Sundar Kumar	Sign	Date	23/9/21
Project Manager	Ram Prasad	Sign	Date	23/9/21
Previous Stage report no.	37819	Report filed and signed by PM?		
Apartment No.		other		
Checked By MD on	MD Sign	For filling		
Recommendation:				

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
☐ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
☐ Proceed with further work. ATR not required.

Inspection should be done after:

- brickwork is completed
- chicken mesh fixed
- after cleaning the apartment
- electrical conducting work is completed

Brickwork Check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. Wall thickness should be as per plan. Use of 4", 6" & 8" blocks must be checked.
6. All walls should have 2 beds of about 2" to 3" thickness with one no. 6 mm or 8 mm rod with M15 CC.
7. Chicken mesh should be used in each and every joint between RCC & Brickwork.
8. Joint between brickwork & beam on external side must be filled.
9. Check room dimensions with working plan. (Tolerance: 1")
10. Diagonals of each room shall be equal. (Tolerance: 2")
11. Balcony sill level should be 3'3" from SFL. (Tolerance: 1")
12. Check room height with specified height. (Tolerance: 1")
13. Check plumb of walls wherever it appears to be out of plumb. (Tolerance: 1/2")
14. Specify the No. of beams which are not aligned by more than 1" in a room.
15. Door frames must have black Japan coating and wood primer / pellambar - at cost of painter.

Certified that all corrections mentioned in the QC Report have been completed. Date: 22/10/21

S No	Room	Wall thickness (✓ or X)	Beds in walls (✓ or X)	Chicken mesh (✓ or X)	External brickwork & beam joint (✓ or X)	Room Dimensions (✓ or X)	Room Dimensions (✓ or X)	Difference in inches	Diagonal (✓ or X)	Diagonal in inches	Balcony sill level (✓ or X)	Room Height (✓ or X)	Plumb of walls (Good/Avg/Bad)	Alignment of beams and walls - Nos.
1	Bedroom 1 M. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 K. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 C. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 G. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3-	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby 1-	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
15	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
Remarks														
① Balcony Sill level wall not constructed.														
② Utility Sill level wall not constructed as per Specification.														
③ Supervision (Engineer) not happening.														
④ Hacking work also not so good.														

Quality Control Check Report. Stage: After Brickwork (Apartments)

Quality of edges and corners in all rooms?	☐ Good ☒ Avg. ☐ Bad
Specify rooms that need correction:	

Misc. Checks.

Was 3.75 CFT proportion box provided?	☐ Yes ☒ No
Condition of proportion box?	☐ Good ☐ Avg. ☐ Bad
Was the Apartment cleaned before starting brick work?	☐ Yes ☐ No ☒ Cant' say
Is the Apartment cleaned for plastering?	☒ Yes ☐ No
Wastage?	☐ High ☒ Medium ☐ Low
Storage of building material like bricks sand and cement.	☐ Good ☒ Avg. ☐ Bad
Drum (200 ltrs) provided for curing in each flat?	☒ Yes ☐ No
Remarks:	

Door Frames & Windows check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark X for minor mistake that requires minor correction.
3. Mark X X for major mistake that requires correction by replacement or re-fixing.
4. Mark X X X for major mistake that cannot be corrected.
5. Window template depth should be between 2 to 2 ½" after plastering.
6. Lintel level should be 7'3" from SFL & 7' from FFL. (Tolerance 1"). Lintel should be as per standard design.
7. Slopes of lofts and kitchen platforms to be checked by using 12" spirit level and check height from floor from 2 or 3 points. (Tolerance 1")
8. Thickness of platforms & lofts should be between 2 & 2.5".
9. Provide single layer table brick at bottom of each door frame without threshold.
10. Check Z angle template size (Z angle for bathroom ventilators not required in new projects).
11. Window opening must be checked with MS square pipe templates of 2 sizes for inner and outer openings.
12. Z angle template must be 1" from brick wall surface from the inner side.

Quality Control Check Report. Stage: After Brickwork (Apartments)

S No	Room	Door size, face and position (✓ or X)	Brick at bottom of door frame (✓ or X)	Door lintel design & level (✓ or X)	Door diagonal check (✓ or X)	Door Plumb - two sides (✓ or X)	Windows lintel design & level, Sill level (✓ or X)	Windows size (✓ or X)	Windows - template depth & diagonal? (✓ or X)	Windows - template red oxide painting (✓ or X)	Loft & Kitchen platform height (✓ or X)	Loft & Kitchen platform slope (✓ or X)	Door size, face and position (✓ or X)
1	Bedroom 1 M-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 K-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 C-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 G-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
15	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
Remarks: ① M-Bed & M-Toi Should be removed & Refix Properly. ② All window sill level instead of (3'3") - it, they provided (3'6"). ③ Kit-platform not casted													

Flat No	F-302	QC report stage	Sl. No.	38448
Company	MRM (LLP)	Project	Phase	-
Prepared by	P. Sribanthi	Sign	Date	27/10/2024
Project Manager	Rampasada	Sign	Date	
Receipt by QC date		Sign	Other	
Receipt at HO date		Sign	Other	
Checked By MD on		MD Sign	For filling	☐ Yes ☐ No
Recommendation that was made by QC: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team.				

Notes:

1. Attach a copy of the QC report to this sheet.
2. Circle each correction with a red pen - tick (✓) each circle for work completed and cross (X) each circle where work has not been completed.
3. Give remarks for each case where work has not completed on this sheet.
4. Make 2 copied of the ATR - send one to MD and other to QC.
5. Enclose required photographs - hard copy.

Remarks:

1) All works completed.
