

Company Name:	MRMLLP	Site	Gulmohar Residency
Name of the customer			
Villa/ Flat No.	Mrs. Rahul Gadharelli		
	F 2-1		

Sl No	Description	Amount
1	Total extra Charges	—
2	Total refundable amount	—
3	Net amount to be charges (if any)	—
4	Net amount to be refunded (if any)	—

Will

Approved by Project Manager	Approved by Design Team	Approved by MD
Date	Date	Date
Sign: 	Sign:	Sign:
		

Note: 1. Enclose measurement & estimate sheet. 2. Send scanned copy by email to plans@modiproperties.com & CR. 3. Maintain originals in A & A of customers at site.

M. RAM PRASAD. (G.M.R.)
Project Manager

Quality Control Check Report. Stage: After Finishing Stage III (Apartments)

Flat No	F-304	Other	—	Sl. No.	40742
Company	MRM-CLIP	Project	GMR	Phase	—
Prepared by	P. Bhargava	Sign	<i>P. Bhargava</i>	Date	28-10-22
Project Manager	Rampasud	Sign	<i>Rampasud</i>	Date	28-10-22
Previous stage report no.			40322	Report filed and signed by PM	☐ Yes ☐ No
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after :

- Completing stage II works.
- Complete works like doors, windows, grills, electrical wiring, switches, french door glass, etc.
- In case of modular kitchen provide platform, granite and dado and modular kitchen in this stage.
- Provide video door phone in this stage.
- Possession for wood work cannot be given until QC check for stage III is completed and all corrections mentioned in the report are made.

Certified that all corrections mentioned in the QC Report have been completed. Work can Proceed to next Stage.

Project In-charge	Sign	Date
<i>[Signature]</i>	<i>[Signature]</i>	4/11/22

Miscellaneous check:

Modular kitchen to be provided	☐ Yes ☐ No	Modular kitchen provided	☐ Yes ☐ No
Modular kitchen workman ship	☐ Good ☐ Avg ☐ Poor	Modular kitchen granite & dado workman ship & finishing	☐ Good ☐ Avg ☐ Poor
Video door phone /wifi cam to be provided	☒ Yes ☐ No	Video door phone/wifi cam provided	☐ Yes ☒ No
Painting marks and drops are cleaned from floor, windows, walls.	☐ Good ☐ Avg ☒ Poor		

Quality Control Check Report. Stage: After Finishing Stage III (Apartments)

Rate the quality of (Good ✓, Avg. X, Poor - needs correction XX, NA)													
S No	Room	Door, door knob & door stopper fitting	Door, door knob & door stopper cleaning	Window grills & quality	Window grills fitting & finishing	Windows quality	Window fitting & finishing	Balcony railing quality & finishing	French door quality & fitting	CP jali quality and fitting	Edge building	Switch boards fitting & covering with plastic covers	Junction box covers painting
1	Bedroom 1 M. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Bedroom 2 K. Bed	✓	✓	✓	XX	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 3 Gr. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Toilet 1 M. Toi	✓	✓	✓	XX	✓	✓	✓	✓	✓	✓	✓	✓
12	Toilet 2 C. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
15	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
Remarks		1) Utility grill, At coupe patchworks painting not done											
		2) In Bedn Toilets false ceiling work not done											

ATR on Quality Control Check Report. (Apartments)

Flat No	F-304	QC report stage	Stage-2	Sl. No.	40320
Company	MRLLP	Project	G.M.R	Phase	
Prepared by	K. Srikanth	Sign	K. Srikanth	Date	7/9/2022
Project Manager	M. Ramprasad	Sign	R. V. S.	Date	7/9/2022
Receipt by QC date		Sign		Other	
Receipt at HO date		Sign		Other	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No
Recommendation that was made by QC: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team.					

Notes:

1. Attach a copy of the QC report to this sheet.
2. Circle each correction with a red pen – tick (✓) each circle for work completed and cross (X) each circle where work has not been completed.
3. Give remarks for each case where work has not completed on this sheet.
4. Make 2 copied of the ATR – send one to MD and other to QC.
5. Enclose required photographs – hard copy.

Remarks:

1) All works completed

Quality Control Check Report, Stage: After Finishing Stage II (Apartments)

Flat No	F-304	Other		Sl. No.	40382
Company	MM(LTD)	Project	GMR	Phase	
Prepared by	S. Sundkumar	Sign	<i>[Signature]</i>	Date	05/08/88
Project Manager	Ranprasad	Sign	<i>[Signature]</i>	Date	05/08/88
Previous stage report no.				Report filed and signed by PM	☒ Yes ☐ No
Checked By MD on	39736	MD Sign		For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☐ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- Completion of flooring, bathroom /utility tiles, first coat of paint.
- Completion of doors, windows, grills, electrical wiring, switches must be done in next stage
- False ceiling must be completed before flooring.
- Kitchen platform, granite and dado must be completed where modular kitchen is not provided.
- Provide granite soffit for main door and balconies in this stage.

Miscellaneous check:

Main door fixed with lock & stopper	☒ Yes ☐ No	Granite soffit for balcony provided	☒ Yes ☐ No
Granite soffit for balcony required	☒ Yes ☐ No	Balcony granite soffit edge polishing	☐ Good ☒ Avg ☐ Poor
Balcony granite soffit workmanship	☐ Good ☒ Avg ☐ Poor	Granite soffit for main door provided	☒ Yes ☐ No
Granite soffit for main door required	☒ Yes ☐ No	Main door granite soffit edge polishing	☐ Good ☒ Avg ☐ Poor
Main door granite soffit workmanship	☐ Good ☒ Avg ☐ Poor		

Quality Control Check Report

Stage: After Finishing Stage II (Apartments)

S No	Room	Tiling & granite work	Rate the quality of (Good ✓, Avg. X, Poor - needs correction XX, NA)													Remarks
			Workmanship of tiling	White cement filling around CPVC lines	Corners finishing	Finishing near doors	Finishing on top of tiles	Finishing near ventilators	Step at bathroom entrance / utility	Step for shower / pot wash	Tile joint grouting	Granite platform finishing and edge polishing	Granite platform slope	Granite platform height	Finishing under granite platform	
1	Toilet 1	M.Tol	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
2	Toilet 2	C.Tol	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
3	Toilet 3		✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
4	Toilet 4		✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
5	Wash basin in dining area		✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
6	Kitchen		✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
7	Utility		✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
8	Other		✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
9	Other		✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
			(1) Provision for Modular kitchen. (2) M.Tol and C.Tol doors are jacked.													

Ramp/road

Quality Control Check Report

Stage: After Finishing Stage II (Apartments)

Flooring & painting		Rate the quality of (Good ✓, Avg. X, Poor - needs correction XX, NA)												
S No	Room	Color variation of floor tiles	Flooring workman ship & grouting	Skirting size (3")	Skirting workmanship	Plastering above skirting	Plastering & finishing of walls	Crack filling	Loft Finishing	Windows check	General quality of painting & finishing	Door & frame painting quality	Door beading, hupam and painting quality.	Edge building
1	Bedroom 1 M.Bed	<	<	<	<	<	<	<	<	<	<	<	<	<
2	Bedroom 2 K.Bed	<	<	<	<	<	<	<	<	<	<	<	<	<
3	Bedroom 3 Gr.Bed	<	<	<	<	<	<	<	<	<	<	<	<	<
4	Drawing	<	<	<	<	<	<	<	<	<	<	<	<	<
5	Dining	<	<	<	<	<	<	<	<	<	<	<	<	<
6	Lobby	<	<	<	<	<	<	<	<	<	<	<	<	<
7	Utility balcony 1	<	<	<	<	<	<	<	<	<	<	<	<	<
8	Utility balcony 2	<	<	<	<	<	<	<	<	<	<	<	<	<
9	Utility balcony 3	<	<	<	<	<	<	<	<	<	<	<	<	<
10	Kitchen	<	<	<	<	<	<	<	<	<	<	<	<	<
11	Other	<	<	<	<	<	<	<	<	<	<	<	<	<
12	Other	<	<	<	<	<	<	<	<	<	<	<	<	<
Remarks		① In balcony and utility 1st coat of painting not done. ② (2 nos) Toilets are locked. ③ In Previous Report some points mentioned, that points also not Rectified.												

Quality Control Check Report. Stage: After Plumbing & Electrical (Apartments)

Flat No.	F-304	Other	SI. No.	39736
Company	MRM(22P)	Project	Phase	
Prepared by	S. Sundar	Sign	Date	14/4/22
Project Manager	Ram Prasad	Sign	Date	14/4/22
Previous stage report no.	39604	Report filed and signed by PM?	Yes ☐ No ☐	
Additions & alterations sheet date		All pages signed by engineer & customer?	Yes ☐ No ☐	
Checked By MD on		For filling	Yes ☐ No ☐	

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- after cleaning the apartment.
- before starting painting, tiling & flooring.
- electrical conduct, waterproofing & plumbing work is completed (for stage II only).
- additions & alterations is finalized and signed. In case there are no additions and alterations printout of email by PM to CR confirming the same must be filed.
- additions & alterations sheets to be transferred to QC file. QC to check if A&A are made as per request.

After Plumbing & Electrical Check.

Notes:

1. Mark ☒ for correct or minor mistake which does not require correction
2. Mark ☒ for minor mistake that requires minor correction.
3. Mark ☒ for major mistake that requires correction by replacement or re-fixing.
4. Mark ☒ for major mistake that cannot be corrected.
5. Location of CPVC & PVC fittings must be checked as per measurements given in circular. Tolerance 1".
6. Location, height and spirit level of electrical points must be checked as per measurements given in circular & plan. Tolerance 1".
7. Civil work near pipes in balcony & utility must be neat and mortar should be removed from the pipes.
8. Water proofing must cover all pipes & check height above SFL.
9. Fasteners must be used as specified in circular. Especially check fixing of PVC pipes.
10. Height of DB box must be 6" below false ceiling level or 12" below slab level.
11. In case of many changes in civil work, electrical work and plumbing work, a new drawing must be prepared at HO and approved by MD.

Confirmed all corrections mentioned in the report have been completed.
 Signature: *[Signature]*
 Date: 25/4/22
 Name: *[Name]*

		Civil work near pipes in balcony & utility ⁷ (✓ or ✗)	CPVC & PVC Check ⁵ (✓ or ✗)	Electrical points check ⁶ (✓ or ✗)	Water proofing check ⁸ (✓ or ✗)	Proper use of fasteners check ⁹ (✓ or ✗)	Placement of DB ¹⁰ (✓ or ✗)	Placement of Generator changeover (✓ or ✗)
1	Bedroom 1 M.Bed	—	—	✓	—	—	—	—
2	Toilet 1 M.Toi	—	—	✓	✓	—	—	—
3	Bedroom 2 K.Bed	—	✗	✓	—	—	—	—
4	Toilet 2 C.Toi	—	—	✓	✓	—	—	—
5	Bedroom 3 G.Bed	—	✗	✓	—	—	—	—
6	Toilet 3-	—	—	✓	—	—	—	—
7	Drawing	—	—	—	—	—	—	—
8	Dining	—	—	✓	—	—	—	—
9	Lobby +	—	—	—	—	—	—	—
10	Utility / balcony 1	✓	—	—	—	—	—	—
11	Utility / balcony 2-	✓	—	✓	—	—	—	—
12	Utility / balcony 3	—	✗	✓	✓	—	—	—
13	Kitchen	—	—	—	—	—	—	—
14	Other	—	—	✓	—	—	—	—
15	Other	—	—	—	—	—	—	—

Remarks 1 In bath toilet Greyson point hd is not as per specified
2 In utility a Pak wash point hd is not as per specified.

Signed by engineer,	☐ Yes ☒ No	Signed by customer,	☐ Yes ☒ No
Revised drawing required from HO	☐ Yes ☒ No	Approved revised drawing attached	☐ Yes ☐ No

Miscellaneous check

Screeding done on walls upto 12" outside bathroom/utility	☒ Yes	☐ No
Bathroom /utility filled with 4" water for water proof check	☐ Yes	☒ No
Hole packing done around all pipes in ceiling and internal walls	☒ Yes	☐ No
Remarks:		

Quality Control Check Report. Stage: After Plastering (Apartments)

Flat No.	F-304	Other	Sl. No.	39604
Company	MRM-CLLP	Project	Phase	
Prepared by	P. Bhargava	Sign	Date	24-03-22
Project Manager	Rampasada	Sign	Date	24-03-22
Previous stage report no.	39320	Report filed and signed by PM?	Yes	
Checked By MD on	MD Sign	For filling	Yes	No
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.				


Inspection should be done after:

- brickwork & 2 coats plastering is completed
- after cleaning the villa.
- Water proofing, screeding in bathrooms is completed.
- before starting painting, tiling & flooring.

Plastering Check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. 9" unplastered area from SFL should be left including in common areas and terraces.
6. Windows must be checked with templates. Plastering must be 3mm margin for luppum work. Tolerance 1/4"
7. Provision of tiles in bathrooms, kitchen & wash areas (rough plastering).
8. Check size of sink bowl. Hole should be 1" to 2" larger. (Tolerance: 1")
9. All doors frames should have 1/2" grooves.
10. Sill top must me of uniform thickness, correct height, at one level & without broken edges.



Quality Control Check Report. Stage: After Plastering (Apartments)

S No	Room	Skirting Provision (✓ or X)	Furnishing around door frame (✓ or X)	Beams & columns finishing (✓ or X)	Finishing of lofts (✓ or X)	Electricity junctions finishing (✓ or X)	Windows check (✓ or X)	Tiles provision (✓ or X)	Sink provision & size (✓ or X)	Grooves for door frames (✓ or X)	Balcony & terrace sill top finishing (✓ or X)	Screeding in bathroom & utility (✓ or X)	Screeding in 6" above FFL? (✓ or X)
1	Bedroom 1 M. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 K. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 C. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 G. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Bedroom 4	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Toilet 4	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Lobby 2 Utility	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Terrace/ balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Terrace / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
15	Terrace / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
16	Portico	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
17	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
18	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
Remarks													

Quality Control Check Report. Stage: After Brickwork (Apartments)

Flat No.	F-304	Others	Sl. No.	39320
Company	MR MALU	Project	Phase	-
Prepared by	T. Vinod Kumar	Sign	Date	14-02-22
Project Manager	Ram Prasad	Sign	Date	14-02-22
Previous Stage report no.	28397	Report filed and signed by PM?	Yes	
Apartment No.		Other	For filling	☐ Yes ☐ No
Checked By MD on		MD Sign		
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.				

Inspection should be done after:

- brickwork is completed
- chicken mesh fixed
- after cleaning the apartment
- electrical conducting work is completed

Brickwork Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. Wall thickness should be as per plan. Use of 4", 6" & 8" blocks must be checked.
6. All walls should have 2 beds of about 2" to 3" thickness with one no. 6 mm or 8 mm rod with M15 CC.
7. Chicken mesh should be used in each and every joint between RCC & Brickwork.
8. Joint between brickwork & beam on external side must be filled.
9. Check room dimensions with working plan. (Tolerance: 1")
10. Diagonals of each room shall be equal. (Tolerance: 2")
11. Balcony sill level should be 3" from SFL. (Tolerance: 1")
12. Check room height with specified height. (Tolerance: 1")
13. Check plumb of walls wherever it appears to be out of plumb. (Tolerance: 1/2")
14. Specify the No. of beams which are not aligned by more than 1" in a room.
15. Door frames must have black Japan coating and wood primer /pellambar - at cost of painter.

Certified that all corrections mentioned in the QC Report have been completed. Work can proceed to next Stage.

Project Manager	Sign	Date

S No	Room	Wall thickness (✓ or X)	Beds in walls (✓ or X)	Chicken mesh (✓ or X)	External brickwork & beam joint (✓ or X)	Room Dimensions (✓ or X)	Room Dimensions Difference in inches	Diagonal (✓ or X)	Diagonal Difference in inches	Balcony sill level (✓ or X)	Room Height (✓ or X)	Plumb of walls (Good/Avg/Bad)	Alignment of beams and walls - Nos.
1	Bedroom 1 M. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 C. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 C. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 G. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other												
15	Other												
Remarks													

Quality of edges and corners in all rooms?	☐ Good ☒ Avg. ☐ Bad
Specify rooms that need correction:	

Misc. Checks.

Was 3.75 CFT proportion box provided?	☒ Yes ☐ No
Condition of proportion box?	☐ Good ☒ Avg. ☐ Bad
Was the Apartment cleaned before starting brick work?	☐ Yes ☐ No ☒ Cant' say
Is the Apartment cleaned for plastering?	☒ Yes ☐ No
Wastage?	☐ High ☒ Medium ☐ Low
Storage of building material like bricks sand and cement.	☐ Good ☒ Avg. ☐ Bad
Drum (200 ltrs) provided for curing in each flat?	☐ Yes ☒ No
Remarks:	

Door Frames & Windows check

Notes:

- 1. Mark ✓ for correct or minor mistake which does not require correction
- 2. Mark ✗ for minor mistake that requires minor correction.
- 3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
- 4. Mark ✗✗✗ for major mistake that cannot be corrected.
- 5. Window template depth should be between 2 to 2 1/2" after plastering.
- 6. Lintel level should be 7'3" from SFL & 7' from FFL. (Tolerance 1")
- 7. Lofis should be at a height of 7' to 7'3" from FFL. Kitchen plat form thickness should be 2", SFL to bottom 31" .. (Tolerance 1")
- 8. Slopes of lofts and kitchen platforms to be checked by using 12" spirit level and check height from floor from 2 or 3 points.
- 9. Thickness of platforms & lofts should be between 2 & 2.5".
- 10. Provide single layer table brick at bottom of each door frame without threshold.
- 11. Check Z angle template size.
- 12. Window opening must be checked with MS square pipe templates of 2 sizes for inner and outer openings.
- 13. Z angle template must be 1" from brick wall surface from the inner side.

S No	Room	Door size, face and position (✓ or X)	Brick at bottom of door frame (✓ or X)	Door lintel level (✓ or X)	Door diagonal check (✓ or X)	Door Plumb - two sides (✓ or X)	Windows lintel & sill level (✓ or X)	Windows size (✓ or X)	Windows - template depth & diagonal (✓ or X)	Windows - template red oxide painting (✓ or X)	Loft & Kitchen platform height (✓ or X)	Loft & Kitchen platform slope (✓ or X)	Door size, face and position (✓ or X)
1	Bedroom 1- M. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1- M. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2- C. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2- C. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3- C. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
15	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
Remarks:		Note:- For 2 no. of doors E-angle not provided.											



GULMOHAR RESIDENCY

Sy. No. 19, Mallapur Village, Uppal, Hyderabad.
Owned & Developed by: M/s. Modi Realty Mallapur LLP.
Head office: 5-4-187/3&4 M G Road Secunderabad.

Details of Additions & Alterations

Flat No	304	Block no.	' F ' ☒
Flat Area	1360 sft	Type	Deluxe / Luxury ☒
Buyer Name	Mr. Rahul Gaddameddi		
Phone No.	8885569886	Email	

I hereby confirm that I have given the details of the minor additions and alterations that are required in the above referred flat in the pages attached herein. Please complete the changes suggested by me. I agree to pay the charges, if any, for the additions and alterations that I have asked you to make, as per the rates suggested by you. I shall deliver all the materials that are required to be provided by me at the site on or before _____. In case I fail to deliver these items to the site by the specified date, you may complete the works in the flat as per the standard items provided by you.

Buyers sign		Engg. Sign	
Date:	15/4/22	Date	15/4/2022



Note:

1. Colour shades of paints may vary from batch to batch & company to company. The Builder will not take responsibility of quality of work for dark shades especially green & blue.
2. Shade / colour of natural material like marble and granite can't be guaranteed and may vary from lot to lot. Cracks like appearance in marble is a natural feature and Builder shall not be responsible for repairs or replacement.
3. Availability of bathroom or flooring tiles of the same type /colour/make can not be guaranteed and closest possible type/colour/make may be used in its place.
4. No further change shall be permitted from this day.
5. Please sign on all pages.

Buyers sign:

Engg. Sign:

Date:



15/4/22

Choice of colours:


Changes in flooring:

M.T: ultra sprinkle


C.T: Malaysian Brown

flooring: vertified tiles including kitchen

Kitchen: Contry chocolate



Buyers sign:

Engg. Sign: 

Date: 15/4/22

Changes in electrical points: (mark on plan)

Choice of Bathroom tiles, CP fittings & Sanitary ware:


glass. partition in two bathrooms.

Buyers sign:


Engg. Sign:

Date:

15/4/22

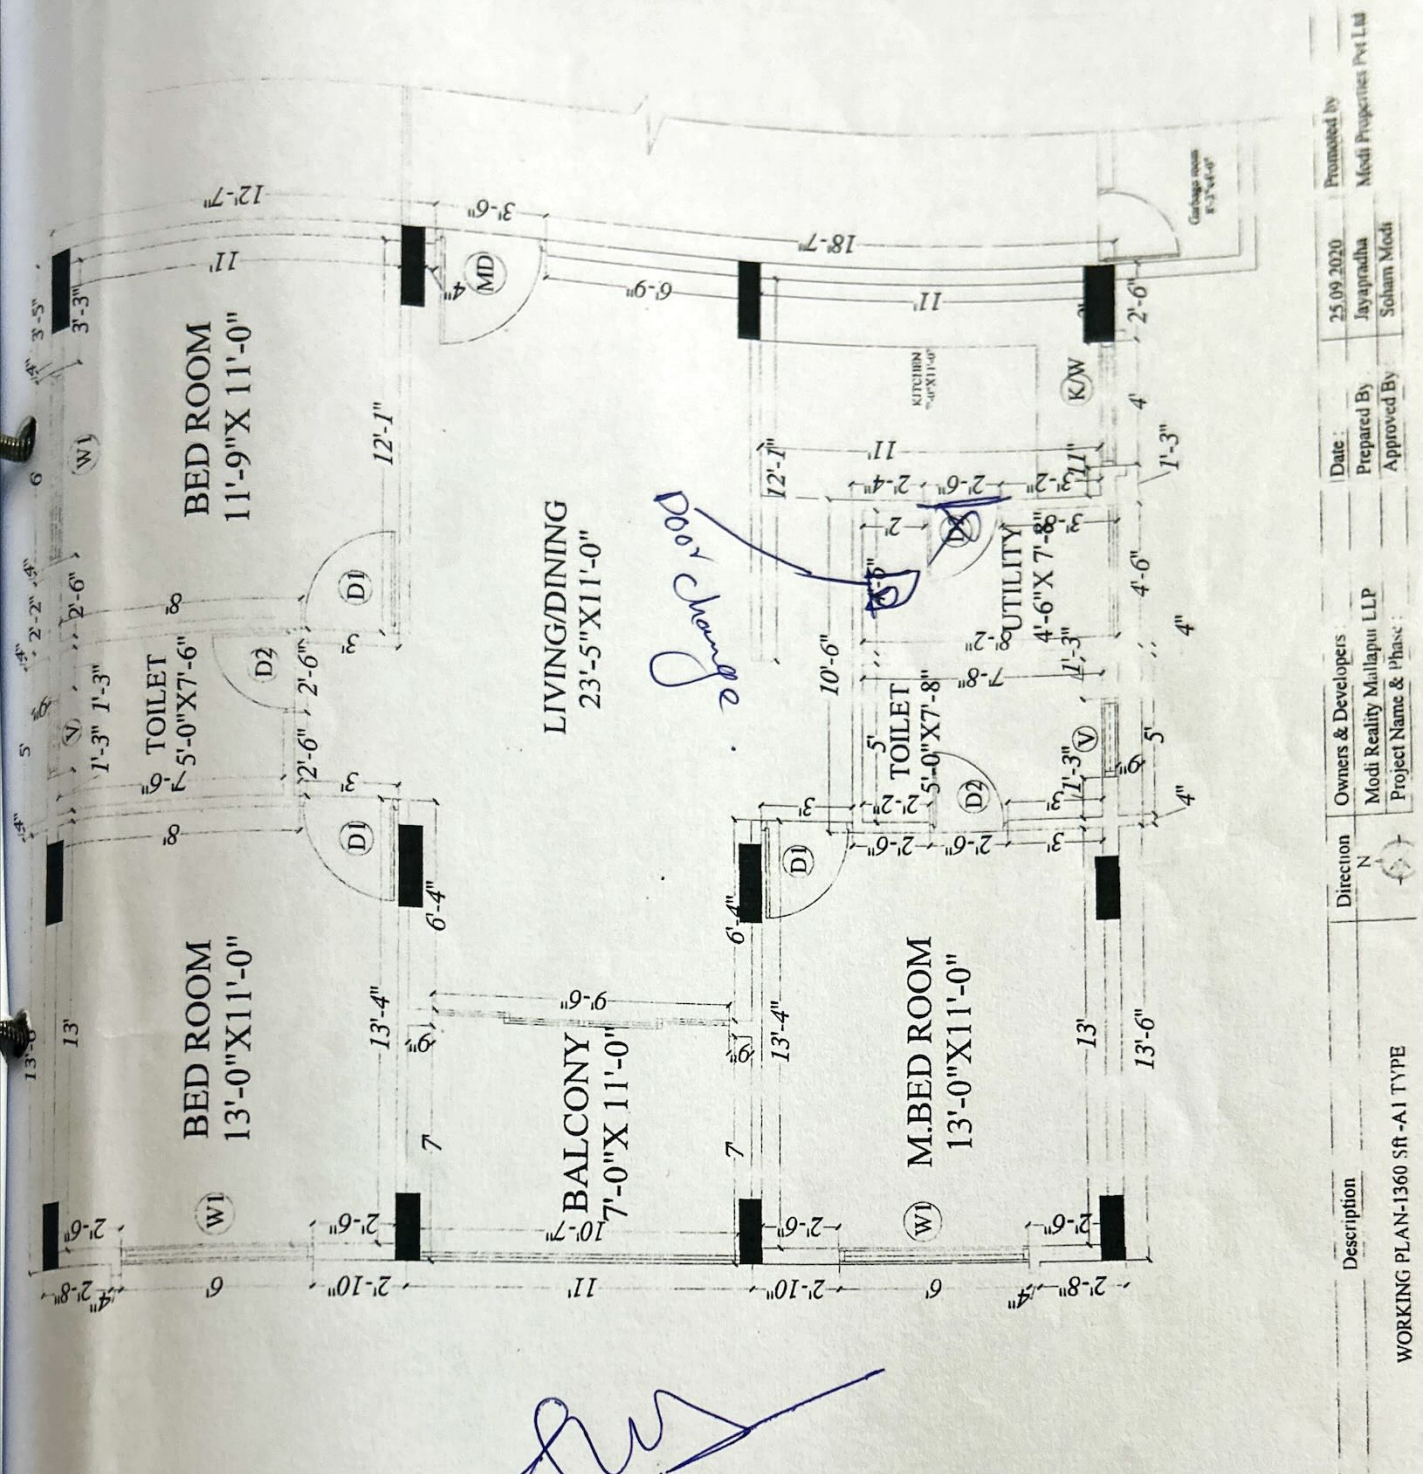

For

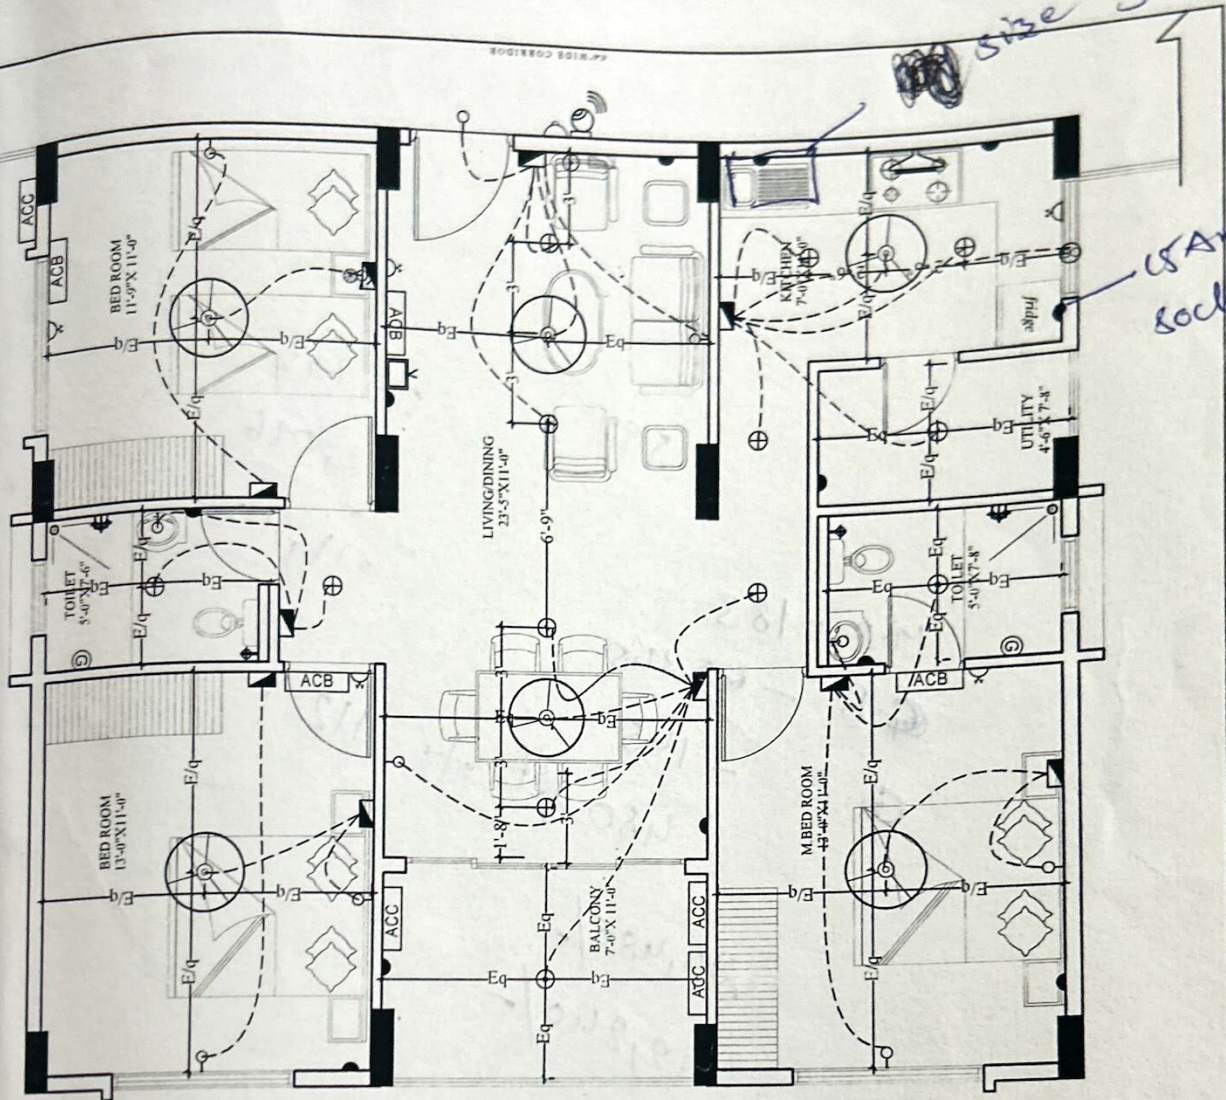

LEGEND:-

S.NO	ITEM	SYMBOL	HEIGHTS
1.	Distribution Board A	DB	7' TO 7'6"
2.	Change over	CO	4' TO 4'6"
3.	Switch board	SB	7' TO 7'6"
4.	Wall point/switch light	WPL	7' TO 7'6"
5.	8 amps plug point	8AP	7'
6.	Ceiling fan	CF	7' TO 7'6"
7.	Daycare point-1/2A	DP-1/2A	7' TO 7'6"
8.	Exhaust fan	EF	7' TO 7'6"
9.	15 amps plug point	15AP	7' TO 7'6"
10.	Telephone point	TP	7'
11.	Television point	TV	7'
12.	Ceiling light	CL	7'
13.	Bed light	BL	7'
14.	W/C Current	WC	7'
15.	AC Compressor	AC	7' TO 7'6"
16.	AC Blower	AB	7' TO 7'6"
17.	Switch board with SA	SB-SA	4' TO 4'6"

Note:- Switch board/point to and from must be @ 15' from center of wall.

Description	Direction	Owners & Developers	Date	Promoted by
		Modi Reality Mallapur LLP	Prepared By	Modi Properties Pvt Ltd
		Project Name & Phase	Approved By	
		Scale		
		ELECTRICAL PLAN -1360 sq ft FLATS-A1 TYPE		
