

Check report by Sales + CR after finishing stage IV (Apartments)

Flat No	206	Other		Sl. No.	43064
Company	MRCV LLP	Project	BRGV	Phase	
Prepared by	Venkat Reddy	Sign	<i>[Signature]</i>	Date	6/8/24
Project Manager	Sorwar	Sign	<i>[Signature]</i>	Date	06-08-24
Stage II report no.					
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No
Recommendation: ☒ Work is satisfactorily completed. Possession may be handed over. ☐ Minor corrections given herein to be completed before handing over possession. ☐ Major corrections required. Do not handover possession. Request for recheck after completion of works. ☐ Works incomplete. Check report cannot be prepared. Request for recheck after completion of works.					

Notes:

- Site to make request for stage IV inspection on M-codex. QC to forward request by email to Sales/CR manager with SI No. generated by M-codex.
- Inspection to be carried out with one member of sales team and CR team + site engineer within 3 days of request.
- Site engineer shall ensure that all works are completed and the flat is thoroughly cleaned in all respects before requesting for inspection.
- Possession cannot be handed over to customer without this inspection.
- Report to be made on same day. Scanned copy to be sent to CR for uploading. Original to be sent to Ashaiya.
- Mark green tick if work is completed. Red 'x' if minor corrections are required. Red 'xx' if work not completed/needs major corrections. Mark 'NA' if not applicable.

[Signature] Niranjana

Check report by Sales + CR after finishing stage IV (Apartments)

Miscellaneous check (check for quality & completion):

Modular kitchen	N/A	Security camera provided	x
Main door soffit quality	✓	False ceiling provided by developer	N/A
No material is stored in flat	✓	Properly labelled keys – 3 sets	✓
Loft tank installed in utility	✓	Kitchen granite platform and dado	✓
Loft provided	✓	Loft finishing	✓
Water supply	✓	Electricity supply	✓
Generator backup (auto)	✓	Car parking provided	✓
Flat label	✓	Car parking label	✓
Provision of lift	✓	Cleanliness of corridors + staircase	✓
Remarks:			

Check report by Sales + CR after finishing stage IV (Apartments)

S No	Room/ quality check	Floor & wall tiles	Painting	Doors + hardware + door beading	Windows/ventilator + grill + hardware	Electricals – switches, switch boards, points	CP & sanitary fittings	Ratings	Painting of exposed pipes + hole packing	Air cracks are treated and painted	Seepages (Nil)	Cleanliness /removal of paint spots
1	Bedroom 1	✓	✓	✓	✓	✓	-	-	✓	✓	✓	✓
2	Bedroom 2	✓	✓	✓	✓	✓	-	-	✓	✓	✓	✓
3	Bedroom 3											
4	Drawing	✓	✓	✓	✓	✓	-	-	✓	✓	✓	✓
5	Dining	✓	✓	✓	✓	✓	-	-	✓	✓	✓	✓
6	Lobby 1											
7	Utility / balcony 1	✓	✓	✓	✓	✓	-	-	✓	✓	✓	✓
8	Utility / balcony 2	✓	✓	✓	✓	-	-	-	✓	✓	✓	✓
9	Utility / balcony 3											
10	Kitchen	✓	✓	-	✓	✓	✓	-	✓	✓	✓	✓
11	Toilet 1	✓	✓	✓	✓	✓	✓	-	✓	✓	✓	✓
12	Toilet 2	✓	✓		✓	✓	✓	-	✓	✓	✓	✓
13	Toilet 3											
14	Other:											
15	Other:											

Quality Control Check Report. Stage: After Finishing Stage III (Apartments)

Flat No	206	Other	—	Sl. No.	42453
Company	MRGV	Project	BRGV	Phase	—
Prepared by	SATKIRAN	Sign	<i>[Signature]</i>	Date	10-10-2023
Project Manager	SARWAR	Sign	<i>[Signature]</i>	Date	10-10-2023
Previous stage report no.		41942	Report filed and signed by PM		☒ Yes ☐ No
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.					

Inspection should be done after :

- Completing stage II works.
- Complete works like doors, windows, grills, electrical wiring, switches, french door glass, etc.
- In case of modular kitchen provide platform, granite and dado and modular kitchen in this stage.
- Provide video door phone in this stage.
- Possession for wood work cannot be given until QC check for stage III is completed and all corrections mentioned in the report are made.

Miscellaneous check:

Modular kitchen to be provided	☐ Yes ☒ No	Modular kitchen provided	☐ Yes ☐ No —
Modular kitchen workman ship	☐ Good ☐ Avg ☐ Poor	Modular kitchen granite & dado workman ship & finishing	☐ Good ☐ Avg ☐ Poor
Video door phone /wifi cam to be provided	☒ Yes ☐ No	Video door phone/wifi cam provided	☐ Yes ☒ No
Painting marks and drops are cleaned from floor, windows, walls.		☐ Good ☒ Avg ☐ Poor	

Quality Control Check Report. Stage: After Finishing Stage III (Apartments)

		Rate the quality of (Good ✓, Avg. ✕, Poor – needs correction ✕✕, NA)											
S No	Room	Door, door knob & door stopper fitting	Door, door knob & door stopper cleaning	Window grills & quality	Window grills fitting & finishing	Windows quality	Window fitting & finishing	Balcony railing quality & finishing	French door quality & fitting	CP jali quality and fitting	Edge building	Switch boards fitting & covering with plastic covers	Junction box covers painting
1	Bedroom 1 M. Bed	✓	✓	✕	✕	✓	✓	✓	✓	✓	✕	✓	✓
2	Bedroom 2 G. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕	✓	✓
3	Bedroom 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕	✓	✓
8	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕	✓	✓
9	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕	✓	✓
10	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Toilet 1 M. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Toilet 2 C. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other												
15	Other												
Remarks		NOTE :- 1) Quality of window grill in M. Bed to be improved. 2) In utility, finishing near PVC pipes & patch painting work to be done.											

Quality Control Check Report.

Stage: After Finishing Stage II (Apartments)

Flat No	A-206	Other	-	Sl. No.	41942
Company	MRGV	Project	BRGV	Phase	-
Prepared by	P. Bhaskar	Sign	Buss	Date	09-06-23
Project Manager	Srinivas	Sign	Srinivas	Date	09-06-23
Previous stage report no.	411404	Report filed and signed by PM	☒ Yes ☐ No		
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☐ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- Completion of flooring, bathroom /utility tiles, first coat of paint.
- Completion of doors, windows, grills, electrical wiring, switches must be done in next stage
- False ceiling must be completed before flooring.
- Kitchen platform, granite and dado must be completed where modular kitchen is not provided.
- Provide granite soffit for main door and balconies in this stage.

Miscellaneous check:

Main door fixed with lock & stopper	☒ Yes ☐ No		
Granite soffit for balcony required	☐ Yes ☒ No	Granite soffit for balcony provided	☐ Yes ☐ No -
Balcony granite soffit workmanship	☐ Good ☐ Avg ☐ Poor	Balcony granite soffit edge polishing	☐ Good ☐ Avg ☐ Poor
Granite soffit for main door required	☐ Yes ☒ No	Granite soffit for main door provided	☐ Yes ☐ No -
Main door granite soffit workmanship	☐ Good ☐ Avg ☐ Poor	Main door granite soffit edge polishing	☐ Good ☐ Avg ☐ Poor

Quality Control Check Repot. Stage: After Finishing Stage II (Apartments)

Tiling & granite work		Rate the quality of (Good ✓, Avg. ✗, Poor – needs correction ✗✗, NA)												
S No	Room	Workmanship of tiling	White cement filling around CPVC lines	Corners finishing	Finishing near doors	Finishing on top of tiles	Finishing near ventilators	Step at bathroom entrance / utility	Step for shower / pot wash	Tile joint grouting	Granite platform finishing and edge polishing	Granite platform slope	Granite platform height	Finishing under granite platform
1	Toilet 1 <i>M-Toi</i>	✓	✓	✗	✗	✗	✗	✓	✓	✗	✓	✓	✓	✓
2	Toilet 2 <i>(-Toi)</i>	✓	✓	✗	✗	✗	✗	✓	✓	✓	✓	✓	✓	✓
3	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 4	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Wash basin in dining area	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Kitchen	✓	✓	✗	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility	✓	✗	✗	✗	✓	✓	✓	✓	✗	✓	✓	✓	✓
8	Other													
9	Other													
Remarks		<i>1) Kitchen platform was not provided 2) In both Toilets, Balcony and utility painting works was not done.</i>												

Flooring & painting		Rate the quality of (Good ✓, Avg. ✕, Poor – needs correction ✕✕, NA)												
S No	Room	Color variation of floor tiles	Flooring workmanship & grouting	Skirting size (3")	Skirting workmanship	Plastering above skirting	Plastering & finishing of walls	Crack filling	Loft Finishing	Windows check	General quality of painting & finishing	Door & frame painting quality	Door beading, luppam and painting quality.	Edge building
1	Bedroom 1 M-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Bedroom 2 K-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✕✕	✓	✓	✓	✕
3	Bedroom 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕✕
5	Dining	✓	✓	✓	✓	✓	✓	✕	✓	✓	✓	✓	✓	✓
6	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕	✓	✓	✕✕
8	Utility / balcony 2	✓	✓	✓	✓	✕✕	✓	✓	✓	✓	✕	✓	✓	✓
9	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Kitchen	✓	✓	✓	✓	✓	✓	✓	✕✕	✕	✓	✓	✓	✕
11	Other													
12	Other													
Remarks		1) In K-Bed, G-Bed finishing near door to be done, Gaps between door frame and beading to be filled. 2) For all doors stoppers not provided. 3) Near lock hole was formed near main 4) one tile to be fixed properly in dining.												

Quality Control Check Report.

Stage: After Finishing Stage II (Apartments)

Flat No	A-206	Other	-	Sl. No.	41942
Company	MRGV	Project	BRGV	Phase	-
Prepared by	P. Bhaskar	Sign	Buss	Date	09-06-23
Project Manager	Srinivas	Sign	Srinivas	Date	09-06-23
Previous stage report no.	411404	Report filed and signed by PM	☒ Yes ☐ No		
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☐ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- Completion of flooring, bathroom /utility tiles, first coat of paint.
- Completion of doors, windows, grills, electrical wiring, switches must be done in next stage
- False ceiling must be completed before flooring.
- Kitchen platform, granite and dado must be completed where modular kitchen is not provided.
- Provide granite soffit for main door and balconies in this stage.

Miscellaneous check:

Main door fixed with lock & stopper	☒ Yes ☐ No		
Granite soffit for balcony required	☐ Yes ☒ No	Granite soffit for balcony provided	☐ Yes ☐ No -
Balcony granite soffit workmanship	☐ Good ☐ Avg ☐ Poor	Balcony granite soffit edge polishing	☐ Good ☐ Avg ☐ Poor
Granite soffit for main door required	☐ Yes ☒ No	Granite soffit for main door provided	☐ Yes ☐ No -
Main door granite soffit workmanship	☐ Good ☐ Avg ☐ Poor	Main door granite soffit edge polishing	☐ Good ☐ Avg ☐ Poor

Quality Control Check Repot. Stage: After Finishing Stage II (Apartments)

Tiling & granite work		Rate the quality of (Good ✓, Avg. ✗, Poor – needs correction ✗✗, NA)												
S No	Room	Workmanship of tiling	White cement filling around CPVC lines	Corners finishing	Finishing near doors	Finishing on top of tiles	Finishing near ventilators	Step at bathroom entrance / utility	Step for shower / pot wash	Tile joint grouting	Granite platform finishing and edge polishing	Granite platform slope	Granite platform height	Finishing under granite platform
1	Toilet 1 <i>M-Toi</i>	✓	✓	✗	✗	✗	✗	✓	✓	✗	✓	✓	✓	✓
2	Toilet 2 <i>(-Toi)</i>	✓	✓	✗	✗	✗	✗	✓	✓	✓	✓	✓	✓	✓
3	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 4	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Wash basin in dining area	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Kitchen	✓	✓	✗	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility	✓	✗	✗	✗	✓	✓	✓	✓	✗	✓	✓	✓	✓
8	Other													
9	Other													
Remarks		<i>1) Kitchen platform was not provided 2) In both Toilets, Balcony and utility painting works was not done.</i>												

Flooring & painting		Rate the quality of (Good ✓, Avg. ✗, Poor – needs correction ✗✗, NA)												
S No	Room	Color variation of floor tiles	Flooring workmanship & grouting	Skirting size (3")	Skirting workmanship	Plastering above skirting	Plastering & finishing of walls	Crack filling	Loft Finishing	Windows check	General quality of painting & finishing	Door & frame painting quality	Door beading, luppam and painting quality.	Edge building
1	Bedroom 1 M-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Bedroom 2 K-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✗✗	✓	✓	✓	✗
3	Bedroom 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✗✗
5	Dining	✓	✓	✓	✓	✓	✓	✗	✓	✓	✓	✓	✓	✓
6	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✗	✓	✓	✗✗
8	Utility / balcony 2	✓	✓	✓	✓	✗✗	✓	✓	✓	✓	✗	✓	✓	✓
9	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Kitchen	✓	✓	✓	✓	✓	✓	✓	✗✗	✗	✓	✓	✓	✗
11	Other													
12	Other													
Remarks		1) In K-Bed, G-Bed finishing near door to be done, Gaps between door frame and beading to be filled. 2) For all doors stoppers not provided. 3) Near lock hole was formed near main 4) one tile to be fixed properly in dining.												

Quality Control Check Report. Stage: After Plumbing & Electrical (Apartments)

Flat No.	A-206	Other	-	SI. No.	41404
Company	MRGV	Project	BRGV	Phase	-
Prepared by	K. Snela	Sign	<i>[Signature]</i>	Date	27-02-2023
Project Manager	Saxwar	Sign	<i>[Signature]</i>	Date	27-02-2023
Previous stage report no.	41185	Report filed and signed by PM?		☒ Yes ☐ No	
Additions & alterations sheet date	19/03/2022	All pages signed by engineer & customer?		☐ Yes ☒ No	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- after cleaning the apartment.
- before starting painting, tiling & flooring.
- electrical conduct, waterproofing & plumbing work is completed (for stage II only).
- additions & alterations is finalized and signed. In case there are no additions and alterations printout of email by PM to CR confirming the same must be filed.
- additions & alterations sheets to be transferred to QC file. QC to check if A&A are made as per request.

After Plumbing & Electrical Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. Location of CPVC & PVC fittings must be checked as per measurements given in circular. Tolerance 1".
6. Location, height and spirit level of electrical points must be checked as per measurements given in circular & plan. Tolerance 1".
7. Civil work near pipes in balcony & utility must be neat and mortar should be removed from the pipes.
8. Water proofing must cover all pipes & check height above SFL.
9. Fasteners must be used as specified in circular. Especially check fixing of PVC pipes.
10. Height of DB box must be 6" below false ceiling level or 12" below slab level.
11. In case of many changes in civil work, electrical work and plumbing work, a new drawing must be prepared at HO and approved by MD.

Quality Control Check Report. Stage: After Plumbing & Electrical (Apartments)

S No	Room	Civil work near pipes in balcony & utility ⁷ (✓ or ✗)	CPVC & PVC Check ⁵ (✓ or ✗)	Electrical points check ⁶ (✓ or ✗)	Water proofing check ⁸ (✓ or ✗)	Proper use of fasteners check ⁹ (✓ or ✗)	Placement of DB ¹⁰ (✓ or ✗)	Placement of Generator changeover (✓ or ✗)
1	Bedroom 1 M. bed	—	—	✓	—	—	—	—
2	Toilet 1 M. Toi	—	✓	✓	✓	✓	—	—
3	Bedroom 2 K. bed	—	—	✓	—	—	—	—
4	Toilet 2 C. Toi	—	✓	✓	✓	✓	—	—
5	Bedroom 3	—	—	—	—	—	—	—
6	Toilet 3	—	—	—	—	—	—	—
7	Drawing	—	—	✓	—	—	✓	—
8	Dining	—	—	✓	—	—	—	—
9	Lobby 1	—	—	—	—	—	—	—
10	Utility / balcony 1	✓	✓	—	—	✓	—	—
11	Utility / balcony 2	✓	✓	✓	✓	✓	—	—
12	Utility / balcony 3	—	—	—	—	—	—	—
13	Kitchen	—	✓	✓	—	—	—	—
14	Other							
15	Other							

Remarks *Note: 1. Level marking was not done. 2. In Maindoor entrance light point was missing. 3. In M. Toi Geyser point height^{was} not providing as per specifications.*

Remarks on additions & alteration sheet:

Signed by engineer,	☒ Yes ☐ No	Signed by customer,	☒ Yes ☐ No
Revised drawing required from HO	☐ Yes ☐ No	Approved revised drawing attached	☐ Yes ☐ No

4. In utility & balcony first coat of lappum work was not done.

Quality Control Check Repot. **Stage: After Plumbing & Electrical (Apartments)**

Miscellaneous check

Screeding done on walls upto 12" outside bathroom/utility	☐ Yes ☒ No
Bathroom /utility filled with 4" water for water proof check	☐ Yes ☒ No
Hole packing done around all pipes in ceiling and internal walls	☒ Yes ☐ No
Remarks:	

Quality Control Check Report.**Stage: After Brickwork (Apartments/ Lab Spaces)**

Flat No.	A - 206	Others	-	Sl. No.	40778
Company	MRGV	Project	BRGV	Phase	-
Prepared by	K. Sneha	Sign	Sneha	Date	04-11-2022
Project Manager	B. Mallikarjun	Sign	Mallikarjun	Date	04-11-2022
Previous Stage report no.		38156	Report filed and signed by PM?		☒ Yes ☐ No
Apartment No.		Other		other	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- brickwork is completed
- chicken mesh fixed
- after cleaning the apartment
- electrical conducting work is completed

Brickwork Check.**Notes:**

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✕ for minor mistake that requires minor correction.
3. Mark ✕✕ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✕✕✕ for major mistake that cannot be corrected.
5. Wall thickness should be as per plan. Use of 4", 6" & 8" blocks must be checked.
6. All walls should have 2 beds of about 2" to 3" thickness with one no 6 mm or 8 mm rod with M15 CC.
7. Chicken mesh should be used in each and every joint between RCC & Brickwork.
8. Joint between brickwork & beam on external side must be filled.
9. Check room dimensions with working plan. (Tolerance: 1")
10. Diagonals of each room shall be equal (Tolerance: 2")
11. Balcony sill level should be 3'3" from SFL. (Tolerance: 1")
12. Check room height with specified height. (Tolerance: 1")
13. Check plumb of walls wherever it appears to be out of plumb. (Tolerance: 1/2")
14. Specify the No. of beams which are not aligned by more than 1" in a room.
15. Door frames must have black Japan coating and wood primer / pellambar – at cost of painter.

Quality Control Check Repot. Stage: After Brickwork (Apartments/ Lab Spaces)

S No	Room	Wall thickness (✓ or ✕)	Beds in walls (✓ or ✕)	Chicken mesh (✓ or ✕)	External brickwork & beam joint (✓ or ✕)	Room Dimensions (✓ or ✕)	Room Dimensions Difference in inches	Diagonal (✓ or ✕)	Diagonal Difference in inches	Balcony sill level (✓ or ✕)	Room Height (✓ or ✕)	Plumb of walls (Good/Avg./Bad)	Alignment of beams and walls - Nos.
1	Bedroom-1 M. Bed	✓	✓	✓	✓	✓	-	✓	-	-	✓	Avg	✓
2	Toilet 1 m. Toi	✓	✓	✓	✓	✓	-	✓	-	-	✓	"	✓
3	Bedroom 2 K. Bed	✓	✓	✓	✓	✓	-	✓	-	-	✓	"	✓
4	Toilet 2 c. Toi	✓	✓	✓	✓	✓	-	✓	-	-	✓	"	✓
5	Bedroom 3	-	-	-	-	-	-	-	-	-	-	-	-
6	Toilet 3	-	-	-	-	-	-	-	-	-	-	-	-
7	Drawing	✓	✓	✓	✓	✓	-	✓	-	-	✓	Avg	✓
8	Dining	✓	✓	✓	✓	✓	-	✓	-	-	✓	"	✓
9	Lobby 1	-	-	-	-	-	-	-	-	-	-	-	-
10	Utility / balcony 1	✓	✓	✓	✓	✓	-	✓	-	✓	✓	Avg	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	-	✓	-	-	✓	"	✓
12	Utility / balcony 3	-	-	-	-	-	-	-	-	-	-	-	-
13	Kitchen	✓	✓	✓	✓	✓	-	✓	-	-	✓	Avg	✓
14	Other												
15	Other												
Remarks		Note: 1. In m-Toi, c-Toi & utility the lintel wall not constructed as per specification. [ventilation position].											

Quality Control Check Repot. Stage: After Brickwork (Apartments/ Lab Spaces)

Quality of edges and corners in all rooms?	☐ Good ☒ Avg. ☐ Bad
Specify rooms that need correction:	

Misc. Checks.

Was 3.75 CFT proportion box provided?	☒ Yes ☐ No
Condition of proportion box?	☐ Good ☒ Avg. ☐ Bad
Was the Apartment cleaned before starting brick work?	☐ Yes ☐ No ☒ Cant' say
Is the Apartment cleaned for plastering?	☒ Yes ☐ No
Wastage?	☐ High ☒ Medium ☐ Low
Storage of building material like bricks sand and cement.	☐ Good ☒ Avg. ☐ Bad
Drum (200 ltrs) provided for curing in each flat?	☒ Yes ☐ No
Remarks:	

Door Frames & Windows check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✕ for minor mistake that requires minor correction.
3. Mark ✕✕ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✕✕✕ for major mistake that cannot be corrected.
5. Window template depth should be between 2 to 2 ½" after plastering.
6. Lentil level should be 7'3" from SFL & 7' from FFL. (Tolerance 1"). Lentil should be as per standard design.
7. Lofts should be at a height of 7' to 7'3" from FFL. Kitchen platform thickness should be 2", SFL to bottom 31" .. (Tolerance 1")
8. Slopes of lofts and kitchen platforms to be checked by using 12" spirit level and check height from floor from 2 or 3 points.
9. Thickness of platforms & lofts should be between 2 & 2.5".
10. Provide single layer table brick at bottom of each door frame without threshold.
11. Check Z angle template size (Z angle for bathroom ventilators not required in new projects).
12. Window opening must be checked with MS square pipe templates of 2 sizes for inner and outer openings.
13. Z angle template must be 1" from brick wall surface from the inner side.

Quality Control Check Repot.

Stage: After Brickwork (Apartments/ Lab Spaces)

S No	Room	Door size, face and position (✓ or ✗)	Brick at bottom of door frame (✓ or ✗)	Door frame hold fast provision and fasteners. (✓ or ✗)	Door lenthil design & level (✓ or ✗)	Door diagonal check (✓ or ✗)	Door Plumb - two sides (✓ or ✗)	Windows lenthil design & level. Sill level (✓ or ✗)	Windows size (✓ or ✗)	Windows - template depth & diagonal ^s (✓ or ✗)	Windows - template red oxide painting (✓ or ✗)	Loft & Kitchen platform height (✓ or ✗)	Loft & Kitchen platform slope (✓ or ✗)	Door size, face and position (✓ or ✗)
1	Bedroom 1 <i>m. Bed</i>	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 <i>m. Toi</i>	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 <i>k. Bed</i>	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 <i>c. Toi</i>	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3	-	-	-	-	-	-	-	-	-	-	-	-	-
6	Toilet 3	-	-	-	-	-	-	-	-	-	-	-	-	-
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	-	-	-	-	-	-	-	-	-	-	-	-	-
9	Lobby-1	-	-	-	-	-	-	-	-	-	-	-	-	-
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	-	-	-	-	-	-	-
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	-	-	-	-	-	-	-
12	Utility / balcony 3	-	-	-	-	-	-	-	-	-	-	-	-	-
13	Kitchen	-	✓	-	✓	-	-	✓	✓	✓	✓	✓	✓	-
14	Other													
15	Other													
	Remarks: <i>Note: 1. Kitchen platform was not casted.</i>													
	<i>2. Loft hacking was not done.</i>													

100

100

Details of the following operations

Book No.	Book Name	No.	Type	Deluxe / Semi Deluxe
		206		
		Vajjala Lakshmi		
		7182436703	Enrol	Vajjala Lakshmi

I hereby agree that I have given the details of the minor additions and alterations that are required in the above mentioned work to the person(s) named below. I agree to pay the cost of such additions and alterations that I have asked you to make, as per the rates suggested by you. I shall deliver all the materials that are required to be provided by me at the site on or before _____.

In case I fail to deliver these items to the site by the specified date, you may complete the works in the place for the standard items provided by you.

Engg. Sign	80	Engg. Sign	8
Date	8/3/22	Date	19/3/22

Notes

1. Colour shades of paints may vary from batch to batch & company to company. The Builder will not take responsibility of quality of work for dark shades especially green & blue.
2. Shade / colour of natural material like marble and granite can't be guaranteed and may vary from lot to lot. Cracks like appearance in marble is a natural feature and Builder shall not be responsible for repairs or replacement.
3. Availability of bathroom or flooring tiles of the same type /colour/make can not be guaranteed and closest possible type/colour/make may be used in its place.
4. No further change shall be permitted from this day.
5. Please sign on all pages.

Choice of colours:

① no charge as per Company.

Changes in flooring:

① no charge as per Company.

12

PR

Changes in electrical points (mark on plan)

- (i) No change in electrical points.
- (ii) No change in electrical points.

Change of bathroom tiles, CP fittings & sanitary ware

- (i) No change in bathroom tiles, CP fittings & sanitary ware.

Changes in kitchen platform: (mark on plan)

- (i) No change in kitchen platform.

Extra work should be added during
the plan for the work.

Signature


Signature

State of New York

Other Charges:

~~11/11/11~~
11/11/11

[Handwritten signature]

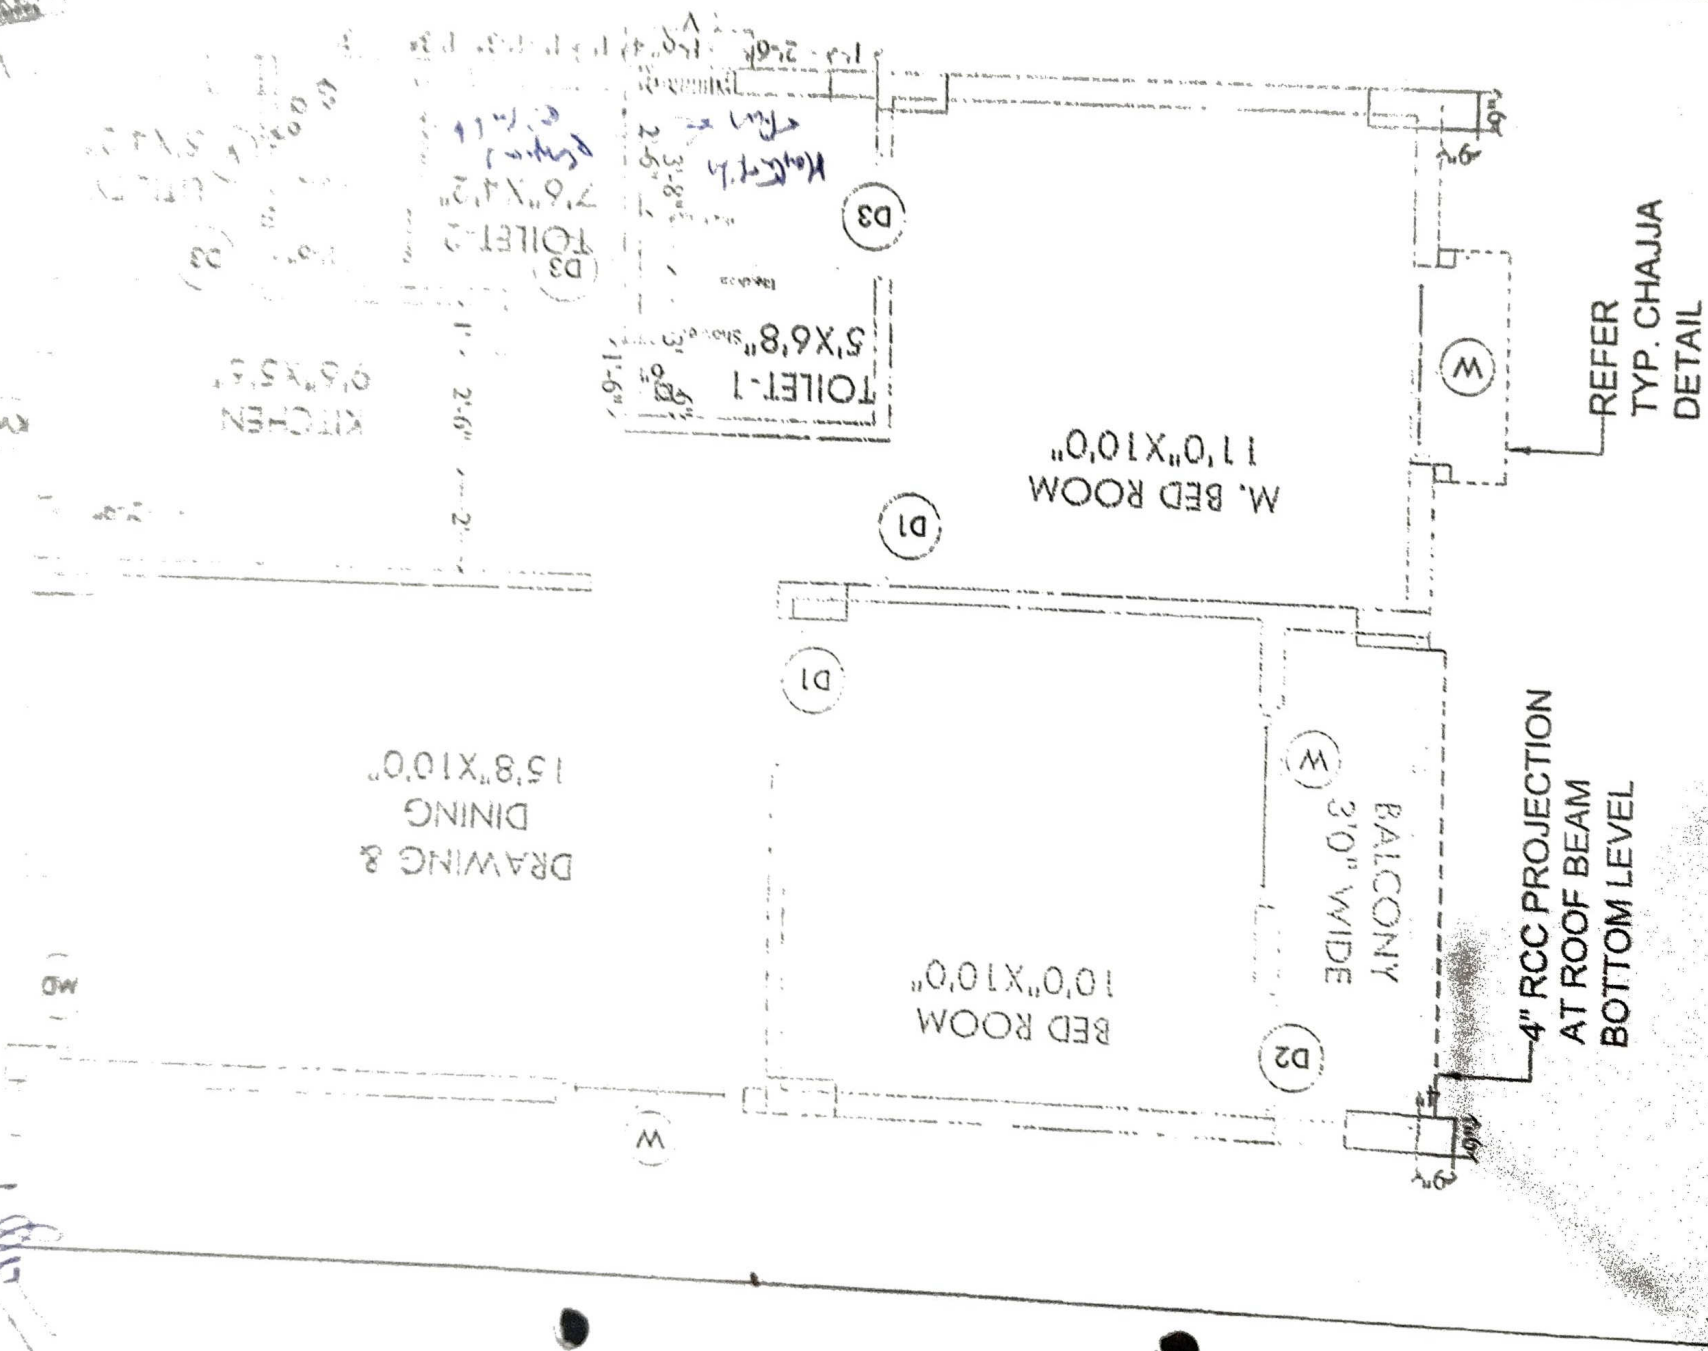

[Handwritten notes and stamps]

Description	Plumbing plan East Facing
-------------	------------------------------

Direction	N
-----------	---

Owners & Developers :	Modi Realty Genome Valley LLP
Project Name & Phase :	BRGIV

Date :	24.09.2021
Prepared By :	Sahani Mohd
Approved By :	N.T.S

Modi Properties Pvt. Ltd.	Project No. 27/2021/100
---------------------------	-------------------------

FLAT NOS. 101, 103, 105, 107, 109 & 111

ELECTRICAL PLAN



Direction

Owners & Developers :

Modi Realty Genome Valley LLP

Prepared By :

Saham Modi

Scale :


M.T.S

Prepared By :

Modi Properties Pvt. Ltd.


Phone: +91-40-0011111


Notes : 1. Switches should be provided near the door.
2. 5 ampere socket should be provided near the door.
3. Switches should be provided near the door.
4. 5 ampere socket should be provided near the door.
5. 5 ampere socket should be provided near the door.

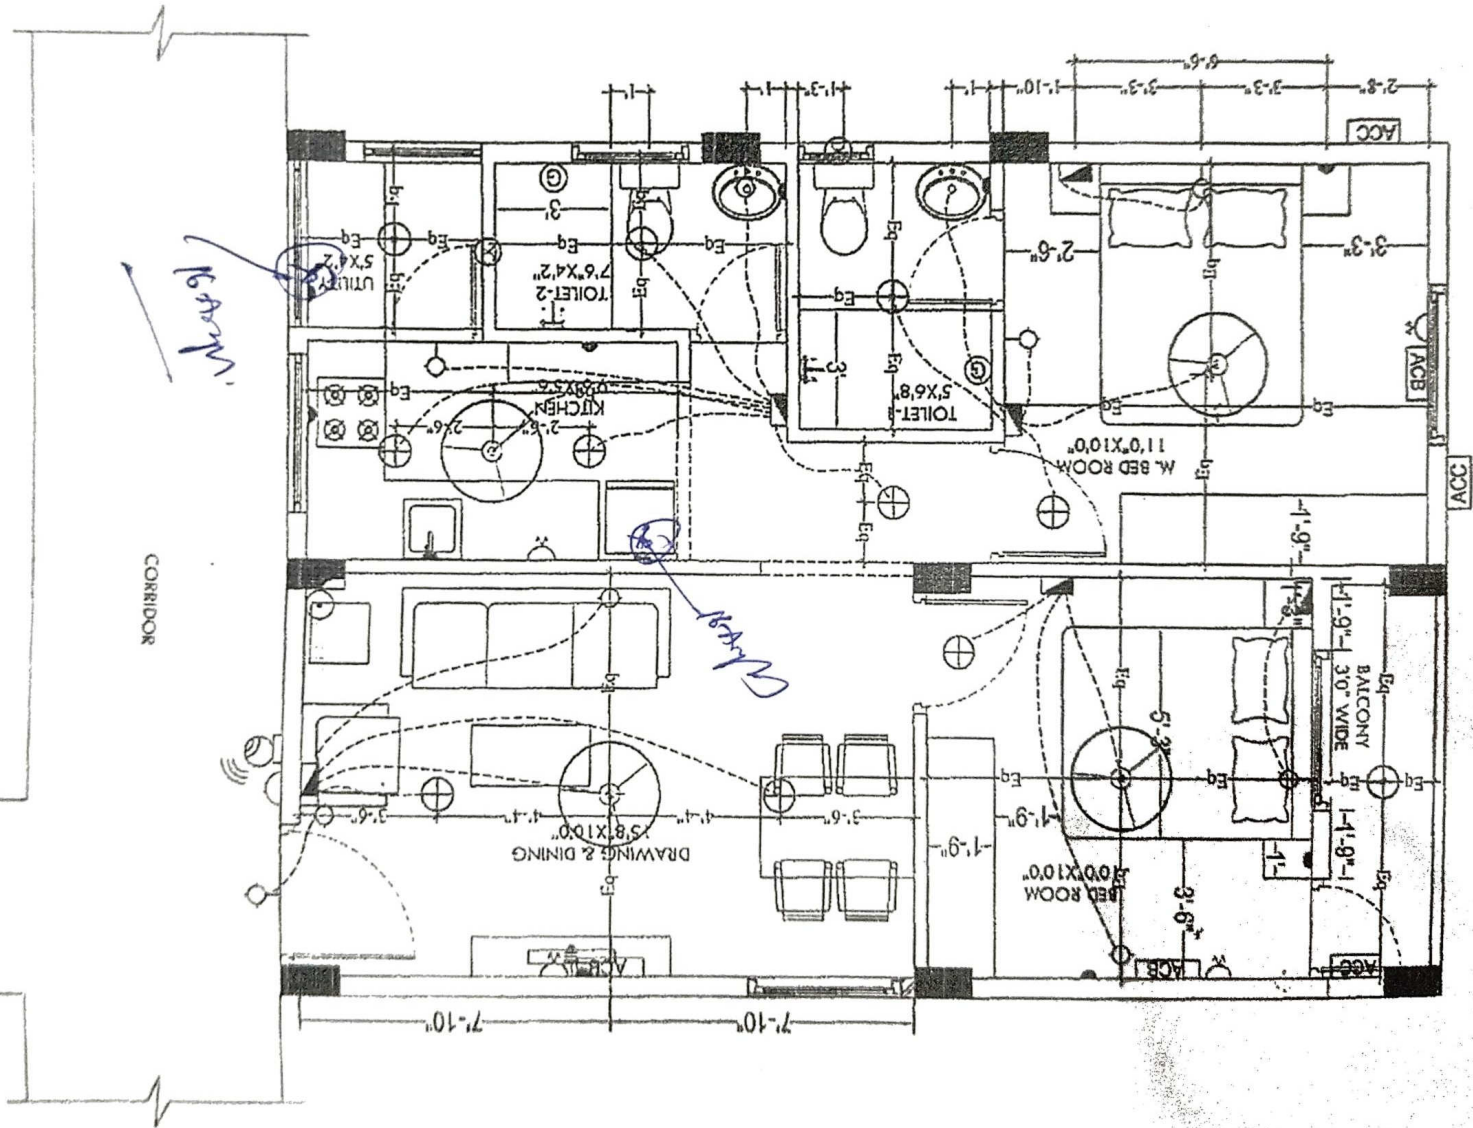

S. NO.	ITEM	QTY	UNIT
1	Switch board	1	nos
2	Switch board	1	nos
3	Switch board	1	nos
4	Switch board	1	nos
5	Switch board	1	nos
6	Switch board	1	nos
7	Switch board	1	nos
8	Switch board	1	nos
9	Switch board	1	nos
10	Switch board	1	nos
11	Switch board	1	nos
12	Switch board	1	nos
13	Switch board	1	nos
14	Switch board	1	nos
15	Switch board	1	nos
16	Switch board	1	nos
17	Switch board	1	nos
18	Switch board	1	nos
19	Switch board	1	nos
20	Switch board	1	nos

LEGEND



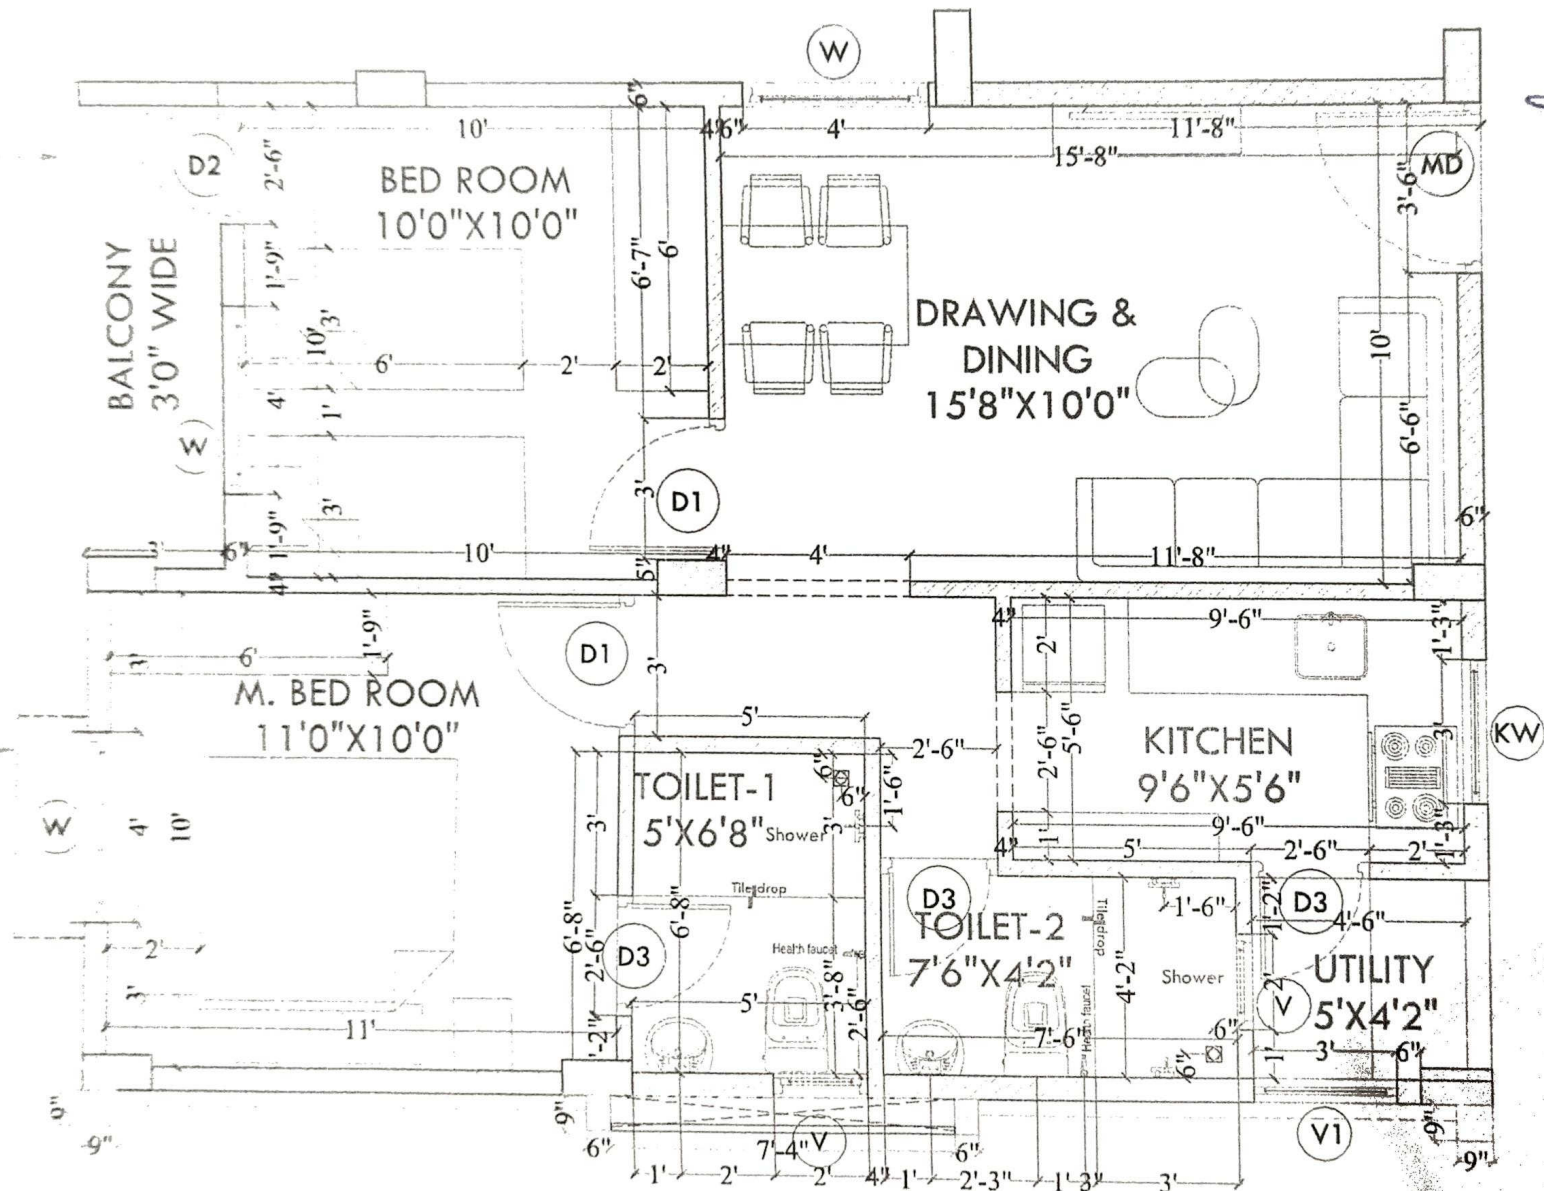

Description	Direction	Owners & Developers :	Date :	08.03.2022	Promoted by
Typical Flat - 201		Modi Realty Genome Valley LLP	Prepared By :	Imran	Modi Properties Pvt Ltd
		Project Name & Phase :	Approved By :	Soham Modi	
		BRGV	Scale :	N.T.S	
					Phone:+91-40-66335551
