

Quality Control Check Report. Stage: After Finishing Stage III (Apartments)

Flat No	118	Other	-	Sl. No.	42532
Company	MRGV	Project	BRGV	Phase	-
Prepared by	Saikiran	Sign	<i>Saikiran</i>	Date	02-11-2023
Project Manager	Sarwan	Sign	<i>Sarwan</i>	Date	02-11-2023
Previous stage report no.		41970	Report filed and signed by PM		☒ Yes ☐ No
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.					

Inspection should be done after :

- Completing stage II works.
- Complete works like doors, windows, grills, electrical wiring, switches, french door glass, etc.
- In case of modular kitchen provide platform, granite and dado and modular kitchen in this stage.
- Provide video door phone in this stage.
- Possession for wood work cannot be given until QC check for stage III is completed and all corrections mentioned in the report are made.

Miscellaneous check:

Modular kitchen to be provided	☐ Yes ☒ No	Modular kitchen provided	☐ Yes ☒ No
Modular kitchen workman ship	☐ Good ☒ Avg ☐ Poor	Modular kitchen granite & dado workman ship & finishing	☐ Good ☒ Avg ☐ Poor
Video door phone /wifi cam to be provided	☒ Yes ☐ No	Video door phone/wifi cam provided	☐ Yes ☒ No
Painting marks and drops are cleaned from floor, windows, walls.		☐ Good ☒ Avg ☐ Poor	

Quality Control Check Repot. Stage: After Finishing Stage III (Apartments)

		Rate the quality of (Good ✓, Avg. ✕, Poor – needs correction ✕✕, NA)											
S No	Room	Door, door knob & door stopper fitting	Door, door knob & door stopper cleaning	Window grills & quality	Window grills fitting & finishing	Windows quality	Window fitting & finishing	Balcony railing quality & finishing	French door quality & fitting	CP jali quality and fitting	Edge building	Switch boards fitting & covering with plastic covers	Junction box covers painting
1	Bedroom 1 M-Red	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕	✓	✓
2	Bedroom 2 C-Red	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕	✓	✕
5	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✕✕	✓	✓	✕
8	Utility / balcony 2	✓	✓	✓	✕	✓	✓	✓	✓	✓	✕	✓	✕
9	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕	✓	✓
11	Toilet-1 M-toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Toilet-2 C-toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other												
15	Other												
Remarks		NOTE :- 1) In Balcony, cp jali was not placed.											

Quality Control Check Report. Stage: After Finishing Stage II (Apartments)

Flat No	A-118		Other		SL. No.	41970
Company	MRGV		Project	BRGv	Phase	
Prepared by	P. Bhargava		Sign	Bhargava	Date	20-06-23
Project Manager	Sawar		Sign	Singh	Date	20-06-23
Previous stage report no.	41390		Report filed and signed by PM		Yes ☒ No ☐	
Checked By MD on			MD Sign		For filling	Yes ☐ No ☐
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☐ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.						

Inspection should be done after:

- Completion of flooring, bathroom/utility tiles, first coat of paint.
- Completion of doors, windows, grills, electrical wiring, switches must be done in next stage
- False ceiling must be completed before flooring.
- Kitchen platform, granite and dado must be completed where modular kitchen is not provided.
- Provide granite soffit for main door and balconies in this stage.

Miscellaneous check:

Main door fixed with lock & stopper	Yes ☒ No ☐		
Granite soffit for balcony required	Yes ☒ No ☐	Granite soffit for balcony provided	Yes ☐ No ☒
Balcony granite soffit workmanship	Good ☐ Avg ☒ Poor ☐	Balcony granite soffit edge polishing	Good ☐ Avg ☐ Poor ☐
Granite soffit for main door required	Yes ☒ No ☐	Granite soffit for main door provided	Yes ☐ No ☒
Main door granite soffit workmanship	Good ☐ Avg ☒ Poor ☐	Main door granite soffit edge polishing	Good ☐ Avg ☐ Poor ☐

Tiling & granite work	Rate the quality of (Good ✓, Avg. X, Poor – needs correction XX, NA)									
S No	Room	1	2	3	4	5	6	7	8	9
		Toilet-1	Toilet-2	Toilet-3	Toilet-4	Wash-basin in dining area	Kitchen	Utility	Other	Other
		M-Toi	C-Toi							
	Workmanship of tiling	✓	✓	✓	✓	✓	✓	✓		
	White cement filling around CPVC lines	X	✓	✓	✓	✓	✓	✓		
	Corners finishing	✓	✓	✓	✓	✓	✓	X		
	Finishing near doors	XX	XX	✓	✓	✓	✓	✓		
	Finishing on top of tiles	X	X	✓	✓	✓	✓	✓		
	Finishing near ventilators	X	X	✓	✓	✓	✓	✓		
	Step at bathroom entrance / utility	✓	✓	✓	✓	✓	✓	✓		
	Step for shower / pot wash	✓	✓	✓	✓	✓	✓	✓		
	Tile joint grouting	XX	XX	✓	✓	✓	✓	✓		
	Granite platform finishing and edge polishing	✓	✓	✓	✓	✓	✓	✓		
	Granite platform slope	✓	✓	✓	✓	✓	✓	✓		
	Granite platform height	✓	✓	✓	✓	✓	✓	✓		
	Finishing under granite platform	✓	✓	✓	✓	✓	✓	✓		
Remarks		1) In Kitchen platform was not casted. 2) In Bath Toilets Grouting work was poor. 3) Finishing near C-Toi door was poor.								

	Flooring & painting	Rate the quality of (Good ✓, Avg. ✗, Poor – needs correction ✗✗, NA)											
S No	Room	Bedroom 1 M-Bed	Bedroom 2 K-Bed	Bedroom 3	Drawing	Dining	Lobby 1	Utility / balcony 1	Utility / balcony 2	Utility / balcony 3	Kitchen	11 Other	12 Other
1	Bedroom 1 M-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Bedroom 2 K-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
		Remarks											
		1) IN Drawing and M-Bed seepage started, 2) IN Balcony Tiles work was pending and finishing above skirting was pending.											

Quality Control Check Report. Stage: After Plumbing & Electrical (Apartments)

Flat No.	A - 118	Other	-	SI. No.	41390
Company	MRGV	Project	BRGV	Phase	-
Prepared by	K. Sneha	Sign	<i>Sneha</i>	Date	24-02-2023
Project Manager	Sarwar	Sign	<i>Sarwar</i>	Date	24-02-2023
Previous stage report no.	41103	Report filed and signed by PM?		☐ Yes ☒ No	
Additions & alterations sheet date	15/06/2022	All pages signed by engineer & customer?		☐ Yes ☒ No	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- after cleaning the apartment.
- before starting painting, tiling & flooring.
- electrical conduct, waterproofing & plumbing work is completed (for stage II only).
- additions & alterations is finalized and signed. In case there are no additions and alterations printout of email by PM to CR confirming the same must be filed.
- additions & alterations sheets to be transferred to QC file. QC to check if A&A are made as per request.

After Plumbing & Electrical Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. Location of CPVC & PVC fittings must be checked as per measurements given in circular. Tolerance 1".
6. Location, height and spirit level of electrical points must be checked as per measurements given in circular & plan. Tolerance 1".
7. Civil work near pipes in balcony & utility must be neat and mortar should be removed from the pipes.
8. Water proofing must cover all pipes & check height above SFL.
9. Fasteners must be used as specified in circular. Especially check fixing of PVC pipes.
10. Height of DB box must be 6" below false ceiling level or 12" below slab level.
11. In case of many changes in civil work, electrical work and plumbing work, a new drawing must be prepared at HO and approved by MD.

Quality Control Check Report. Stage: After Plumbing & Electrical (Apartments)

S No	Room	Civil work near pipes in balcony & utility ⁷ (✓ or ✕)	CPVC & PVC Check ⁵ (✓ or ✕)	Electrical points check ⁶ (✓ or ✕)	Water proofing check ⁸ (✓ or ✕)	Proper use of fasteners check ⁹ (✓ or ✕)	Placement of DB ¹⁰ (✓ or ✕)	Placement of Generator changeover (✓ or ✕)
1	Bedroom 1 m.bed	—	—	✕	—	—	—	—
2	Toilet 1 m.Toi	—	✓	✓	✓	✓	—	—
3	Bedroom 2 K.bed	—	—	✓	—	—	—	—
4	Toilet 2 c.Toi	—	✓	✓	✓	✓	—	—
5	Bedroom 3	—	—	—	—	—	—	—
6	Toilet 3	—	—	—	—	—	—	—
7	Drawing	—	—	✓	—	—	✓	—
8	Dining	—	—	✓	—	—	—	—
9	Lobby 1	—	—	—	—	—	—	—
10	Utility / balcony 1	✕	✕✕	✓	—	✕	—	—
11	Utility / balcony 2	✓	✓	✓	✓	✓	—	—
12	Utility / balcony 3	—	—	—	—	—	—	—
13	Kitchen	—	✓	✓	—	—	—	—
14	Other							
15	Other							

Remarks

Note: 1. In m.bed AC point was not provided. 2. In m.Toid c.Toi Shower points & Geyser point's height's were not providing as per specification's.

Remarks on additions & alteration sheet:

Signed by engineer,	☒ Yes ☐ No	Signed by customer,	☒ Yes ☐ No
Revised drawing required from HO	☐ Yes ☐ No	Approved revised drawing attached	☐ Yes ☐ No

Quality Control Check Repot. **Stage: After Plumbing & Electrical (Apartments)**

Miscellaneous check

Screeding done on walls upto 12" outside bathroom/utility	☒ Yes ☐ No
Bathroom /utility filled with 4" water for water proof check	☐ Yes ☒ No
Hole packing done around all pipes in ceiling and internal walls	☐ Yes ☒ No
Remarks:	

Quality Control Check Report. Stage: After Plastering (Apartments)

Flat No.	A-118	Other		Sl. No.	41103
Company	MRCV	Project	BRGV	Phase	-
Prepared by	S. Sund Kumar	Sign		Date	21/123
Project Manager	Sarwan.	Sign	<i>[Signature]</i>	Date	21/123
Previous stage report no.		40776	Report filed and signed by PM?	☒ Yes ☐ No	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☐ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.					

Inspection should be done after:

- brickwork & 2 coats plastering is completed
- after cleaning the villa.
- Water proofing, screeding in bathrooms is completed.
- before starting painting, tiling & flooring.

Plastering Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. 9" unplastered area from SFL should be left including in common areas and terraces.
6. Windows must be checked with templates. Plastering must be 3mm margin for luppum work. Tolerance ¼".
7. Provision of tiles in bathrooms, kitchen & wash areas (rough plastering).
8. Check size of sink bowl. Hole should be 1" to 2" larger. (Tolerance: 1")
9. All doors frames should have ½" grooves.
10. Sill top must be of uniform thickness, correct height, at one level & without broken edges.

Quality Control Check Report. Stage: After Plastering (Apartments)

S No	Room	Skirting Provision (✓ or ✗)	Furnishing around door frame (✓ or ✗)	Beams & columns finishing (✓ or ✗)	Finishing of lofts (✓ or ✗)	Electricity junctions finishing (✓ or ✗)	Windows check (✓ or ✗)	Tiles provision (✓ or ✗)	Sink provision & size (✓ or ✗)	Grooves for door frames (✓ or ✗)	Balcony & terrace sill top finishing (✓ or ✗)	Screeding in bathroom & utility (✓ or ✗)	Screeding in 6" above FFL? (✓ or ✗)
1	Bedroom 1 M-Bed	✗	✗	✓	—	✓	✗	—	—	✗	—	—	—
2	Toilet 1 M-Toi	—	✗	✗	—	✗	✗	—	—	✗	—	—	—
3	Bedroom 2 G-Bed	✗	—	✓	—	✗	✗	✗	—	✗	—	✗	✗
4	Toilet 2 C-Toi	—	✗	✗	—	✗	✗	✗	—	✗	—	✗	✗
5	Bedroom 3	—	—	—	—	—	—	—	—	—	—	—	—
6	Toilet 3	—	—	—	—	—	—	—	—	—	—	—	—
7	Bedroom 4	—	—	—	—	—	—	—	—	—	—	—	—
8	Toilet 4	—	—	—	—	—	—	—	—	—	—	—	—
9	Drawing	✗	✓	✓	—	✓	✗	—	—	✗	—	—	—
10	Dining	—	—	—	—	—	—	—	—	—	—	—	—
11	Lobby 1	—	—	—	—	—	—	—	—	—	—	—	—
12	Lobby 2	—	—	—	—	—	—	—	—	—	—	—	—
13	Balcony	—	—	—	—	—	—	—	—	—	—	—	—
14	Utility	—	✗	✓	—	✗	—	✗	—	✗	—	✗	✗
15	Portico	—	—	—	—	—	—	—	—	—	—	—	—
16	Kitchen	✗	—	✓	✓	✓	✗	✗	—	—	—	—	—
17	Other	—	—	—	—	—	—	—	—	—	—	—	—

Remarks: ① G-Bed room & Balcony doors frames not provided. ② In Balcony plastering work not done. ③ Plastering quality was very poor.

④ Engineer's Supervision was not happening at site. ⑤ Grooves-work to be improved.

Quality Control Check Report. Stage: After Brickwork (Apartments/ Lab Spaces)

Flat No.	A-118	Others	-	Sl. No.	40776
Company	MRGV	Project	BRGV	Phase	-
Prepared by	K. Sneha	Sign	Sneha	Date	04-11-2022
Project Manager	B. Mallikarjun	Sign	Mallikarjun	Date	04-11-2022
Previous Stage report no.	39327	Report filed and signed by PM?		☒ Yes ☐ No	
Apartment No.		Other		other	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- brickwork is completed
- chicken mesh fixed
- after cleaning the apartment
- electrical conducting work is completed

Brickwork Check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. Wall thickness should be as per plan. Use of 4", 6" & 8" blocks must be checked.
6. All walls should have 2 beds of about 2" to 3" thickness with one no. 6 mm or 8 mm rod with M15 CC.
7. Chicken mesh should be used in each and every joint between RCC & Brickwork.
8. Joint between brickwork & beam on external side must be filled.
9. Check room dimensions with working plan. (Tolerance: 1")
10. Diagonals of each room shall be equal. (Tolerance: 2")
11. Balcony sill level should be 3'3" from SFL. (Tolerance: 1")
12. Check room height with specified height. (Tolerance: 1")
13. Check plumb of walls wherever it appears to be out of plumb. (Tolerance: 1/2")
14. Specify the No. of beams which are not aligned by more than 1" in a room.
15. Door frames must have black Japan coating and wood primer /pellambar – at cost of painter.

Quality Control Check Repot. Stage: After Brickwork (Apartments/ Lab Spaces)

S No	Room	Wall thickness (✓ or ✗)	Beds in walls (✓ or ✗)	Chicken mesh (✓ or ✗)	External brickwork & beam joint (✓ or ✗)	Room Dimensions (✓ or ✗)	Room Dimensions Difference in inches	Diagonal (✓ or ✗)	Diagonal Difference in inches	Balcony sill level (✓ or ✗)	Room Height (✓ or ✗)	Plumb of walls (Good/Avg./Bad)	Alignment of beams and walls - Nos.
1	Bedroom 1 M. Red	✓	✓	✓	✓	✓	-	✓	-	-	✓	Avg	✓
2	Toilet 1 M. Toi	✓	✓	✓	✓	✓	-	✓	-	-	✓	"	✓
3	Bedroom 2 K. Red	✓	✓	✓	✓	✓	-	✓	-	-	✓	"	✓
4	Toilet 2 C. Toi	✓	✓	✓	✓	✓	-	✓	-	-	✓	"	✓
5	Bedroom 3	-	-	-	-	-	-	-	-	-	-	-	-
6	Toilet 3	-	-	-	-	-	-	-	-	-	-	-	-
7	Drawing	✓	✓	✓	✓	✓	-	✓	-	-	✓	Avg	✓
8	Dining	✓	✓	✓	✓	✓	-	✓	-	-	✓	"	✓
9	Lobby 1	-	-	-	-	-	-	-	-	-	-	-	-
10	Utility / balcony 1	✓	✓	✓	✓	✓	-	✓	-	✓	✓	Avg	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	-	✓	-	-	✓	"	✓
12	Utility / balcony 3	-	-	-	-	-	-	-	-	-	-	-	-
13	Kitchen	✓	✓	✓	✓	✓	-	✓	-	-	✓	Avg	✓
14	Other												
15	Other												
Remarks Note: 1. In m-Toi, c-Toi & Utility the lintel wall are not constructed as per specification [ventilation provision]													

Quality Control Check Repot. Stage: After Brickwork (Apartments/ Lab Spaces)

Quality of edges and corners in all rooms?	☐ Good ☒ Avg. ☐ Bad
Specify rooms that need correction:	

Misc. Checks.

Was 3.75 CFT proportion box provided?	☒ Yes ☐ No
Condition of proportion box?	☐ Good ☒ Avg. ☐ Bad
Was the Apartment cleaned before starting brick work?	☐ Yes ☐ No ☒ Cant' say
Is the Apartment cleaned for plastering?	☒ Yes ☐ No
Wastage?	☐ High ☒ Medium ☐ Low
Storage of building material like bricks sand and cement.	☐ Good ☒ Avg. ☐ Bad
Drum (200 ltrs) provided for curing in each flat?	☒ Yes ☐ No
Remarks:	

Door Frames & Windows check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✕ for minor mistake that requires minor correction.
3. Mark ✕✕ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✕✕✕ for major mistake that cannot be corrected.
5. Window template depth should be between 2 to 2 ½" after plastering.
6. Lentil level should be 7'3" from SFL & 7' from FFL. (Tolerance 1"). Lentil should be as per standard design.
7. Lofts should be at a height of 7' to 7'3" from FFL. Kitchen platform thickness should be 2", SFL to bottom 31" (Tolerance 1")
8. Slopes of lofts and kitchen platforms to be checked by using 12" spirit level and check height from floor from 2 or 3 points.
9. Thickness of platforms & lofts should be between 2 & 2 5".
10. Provide single layer table brick at bottom of each door frame without threshold.
11. Check Z angle template size (Z angle for bathroom ventilators not required in new projects).
12. Window opening must be checked with MS square pipe templates of 2 sizes for inner and outer openings.
13. Z angle template must be 1" from brick wall surface from the inner side.

Quality Control Check Report. Stage: After Brickwork (Apartments/ Lab Spaces)

S No	Room	Door size, face and position (✓ or ✗)	Brick at bottom of door frame (✓ or ✗)	Door frame hold fast provision and fasteners (✓ or ✗)	Door lintel design & level (✓ or ✗)	Door diagonal check (✓ or ✗)	Door Plumb - two sides (✓ or ✗)	Windows lintel design & level Still level (✓ or ✗)	Windows size (✓ or ✗)	Windows - template depth & diagonal (✓ or ✗)	Windows - template red oxide painting (✓ or ✗)	Loft & Kitchen platform height (✓ or ✗)	Loft & Kitchen platform slope (✓ or ✗)	Door size, face and position (✓ or ✗)
1	Bedroom 1 M. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 K. Bed	✗	-	-	-	-	-	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 S. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3	-	-	-	-	-	-	-	-	-	-	-	-	-
6	Toilet 3	-	-	-	-	-	-	-	-	-	-	-	-	-
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	-	-	-	-	-	-	-	-	-	-	-	-	-
9	Lobby 1	-	-	-	-	-	-	-	-	-	-	-	-	-
10	Utility / balcony 1	✗	-	-	-	-	-	-	-	-	-	-	-	-
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	-	-	-	-	-	-	-
12	Utility / balcony 3	-	-	-	-	-	-	-	-	-	-	-	-	-
13	Kitchen	-	-	-	-	-	-	✓	✓	✓	✓	✓	✓	✓
14	Other													
15	Other													
Remarks:		Note: 1 In K. Bed & Balcony Door frame was not fixed because material shifting purpose. 2 Kitchen platform was not casted. 3 Loft hacking was not done. 4 In M-Toi ventilation position was not provided as per drawing.												

100

[Faint vertical text or bleed-through from the reverse side of the page]

[illegible]

卷之四

卷之三

卷之五

THE UNIVERSITY OF CHICAGO

Manager Customer Relations | +91 98866 90150 | kprasad@modiproperties.com
Modi Properties Pvt. Ltd. | www.modiproperties.com

www.realtyproperties.com

Don't miss the 2004 MG Road, Secunderabad - 03 | 91 40 6635551

Just buy a flat or villa! Buy a great lifestyle!

we build affordable flats & villas in gated communities.

out:blank

BLOOMDALE

Residency @ Genome Valley

Shamirpet, Hyderabad

Sale Office : S. No. 31 & 32, Muraharipally,

Medchal Mandal, Hyderabad - 500 078

☎ : +91-91210-21717 ☎ : bvgv@modiproperties.com

Developed by : M/s. Bloomdale Residency Genome Valley LLP.



Head Office: 5-4-18/3&4, II Floor, M. G. Road,

Secunderabad - 500 003 ☎ +91 4066135551,

✉ info@modiproperties.com www.modiproperties.com

Details of Additions & Alterations

Flat No	117 + 118	Type	Deluxe / Semi-Deluxe
Buyer Name	Ch. Nagababinda. / ch. Ravichandra.		
Phone No.	9000862602	Email	banchharg@gmail.com

I hereby confirm that I have given the details of the minor additions and alterations that are required in the above referred flat in the pages attached herein. Please complete the changes suggested by me. I agree to pay the charges, if any, for the additions and alterations that I have asked you to make, as per the rates suggested by you. I shall deliver all the materials that are required to be provided by me at the site on or before _____ . In case I fail to deliver these items to the site by the specified date, you may complete the works in the flat as per the standard items provided by you.

Buyers sign	R. Nagababinda	Engg. Sign	P. Palatho
Date:	15/06/2022	Date	

Note:

1. Colour shades of paints may vary from batch to batch & company to company. The Builder will not take responsibility of quality of work for dark shades especially green & blue.
2. Shade / colour of natural material like marble and granite can't be guaranteed and may vary from lot to lot. Cracks like appearance in marble is a natural feature and Builder shall not be responsible for repairs or replacement.
3. Availability of bathroom or flooring tiles of the same type /colour/make can not be guaranteed and closest possible type/colour/make may be used in its place.
4. No further change shall be permitted from this day.
5. Please sign on all pages.

Changes in flooring:

- 1) Flooring tiles should be Dyna in two flats.
- 2) Kitchen side walls should be Ultra-sprinkle Dk.

R. Neeta Bhandal

Choice of Bathroom tiles, CP fittings & Sanitary ware:

1) Bathroom Tiles should be Ultraspinkle-DK
in four Bathrooms.

Changes in kitchen platform: (mark on plan)

No changes

Details of solar water heater:

- No change.

Other Changes:

- 1) Main entrance of 117 flat should be close.
- 2) In 117 flat, Second Bedroom Balcony railing partially close with small gate.
- 3) In 118 flat, Entrance has to N-E corner.
- 4) NO kitchen in 117 flat.
- 5) Door should be on Common wall of 117 & 118 flat.

R. Naga Bunder

BLOOMDALE

Residency @ Genome Valley

Hyderabad

Sale Office: No. 31 & 32, Mubashirpally,

Mechhal Mandal, Hyderabad - 500 078

Tel: 01210 21717 - 333 bgrv@modiproperties.com

Developed by: M/s. Bloomdale Residency Genome Valley LLP



Head Office: 31 & 32, Mubashirpally, Mechhal Mandal,

Hyderabad - 500 078 Tel: 01210 21717

333 bgrv@modiproperties.com

Date: 17.05.2022

To,

Mrs. Chiruvolu Naga Brunda,
W/o Mr. Chiruvolu Ravi Shankar,
H. No: 1-8-22/71/202, S.V.Nivas,
Shashikanth Nagar, North Kamala Nagar,
Kapra, Secunderabad -500062

Dear Customer,

If you wish to make any minor additions or alterations to the flat that you have booked, we request you to visit the site during office hours between 18.05.2022 & 22.05.2022. We also request you to finalize details like color of walls, etc., during your visit to the site. Our site engineers will make note of these details.

For your convenience we request you to take prior appointment so that our engineers can give you their undivided attention. You may contact Mr. G. Sarwar (Project in-charge) on +91-9100036740 or Ms. Puspaltha (Asst. Engineer) on +91-9848942990 or by email at bgrv_const@modiproperties.com

In case you fail to contact us during the above mentioned period, we shall assume that no changes are required, and your flat will be completed as per the standard specifications shown in the model flat.

Thank You.

Yours Sincerely,

For Modi Realty Genome Valley LLP.



Authorised Signatory.

Please refer to the notes attached herein.

Working drawings submitted along with planning drawings for your flat have been enclosed for your reference.

Based upon the fact that the elevator is provided like this, which is the better, which one must be taken into account in our site plan & work of completion is to be done and the material provided.

Changes in structural appearance and colour shall not be permitted. Changes in colour of

work shall be done in accordance with the approved plan and be determined. Change in colour of

work shall be done in accordance with the approved plan and be determined.

Changes in colour of work shall not be permitted. Changes in colour of

work shall be done in accordance with the approved plan and be determined. Change in colour of

work shall be done in accordance with the approved plan and be determined.

Additional changes & work shall not be permitted.

Changes in colour of work shall not be permitted.

No charge for

1. Choice of two floor colours for walls.
2. Choice of two floor combinations for bathroom tiles.

No material items to be supplied by the owner & installed free of cost.

1. Hardware.
2. CP & Sanitaryware.
3. Flooring tiles.
4. Kitchen platform - granite marble.
5. Bathroom tiles.

Extra charges shall be payable for


1. Extra electrical points, switch boards, sockets, switches.
2. Additional kitchen platform with granite & marble.
3. Raising / polishing of granite platform.
4. Exhaust hole in bathroom kitchen.

Refund charges for upgrade or downgrade or substitutions shall be applicable for

1. Kitchen & bathroom tiles.
2. Flooring tiles.
3. CP fittings.
4. Sanitaryware & bathroom.
5. Doors & hardware.
6. Kitchen sink.
7. Civil work.
8. Electrical switches.
9. Kitchen platform.

No refunds shall be made for

1. Kitchen platform.
2. Civil work.



R. Nagar Boud

DRAWING &
DINING
15'8"X10'0"

BED ROOM
10'0"X10'0"

BALCONY
3'0" WIDE

M. BED ROOM
11'0"X10'0"

KITCHEN
9'6"X5'6"

TOILET-1
5'X6'8"

TOILET-2
7'6"X4'2"

UTILITY
5'X4'2"

4" RCC PROJECTION
AT ROOF BEAM
BOTTOM LEVEL

REFER
TYP. CHAJJA
DETAIL


1st option

1st option 1st floor

Direction 	Owner & Developer : Modi Realty Genome Valley LLP Project Name & Phase : HRV IV	Date : 08.03.2022 Prepared By : Imran Approved By : Soham Modi Scale : 1:100	Promoted by Modi Properties Pvt Ltd
--	---	--	---

K. Nagar Boud

APPROVED FOR CONSTRUCTION
73 JUL 2021
SOHAM MODI
MANAGING DIRECTOR

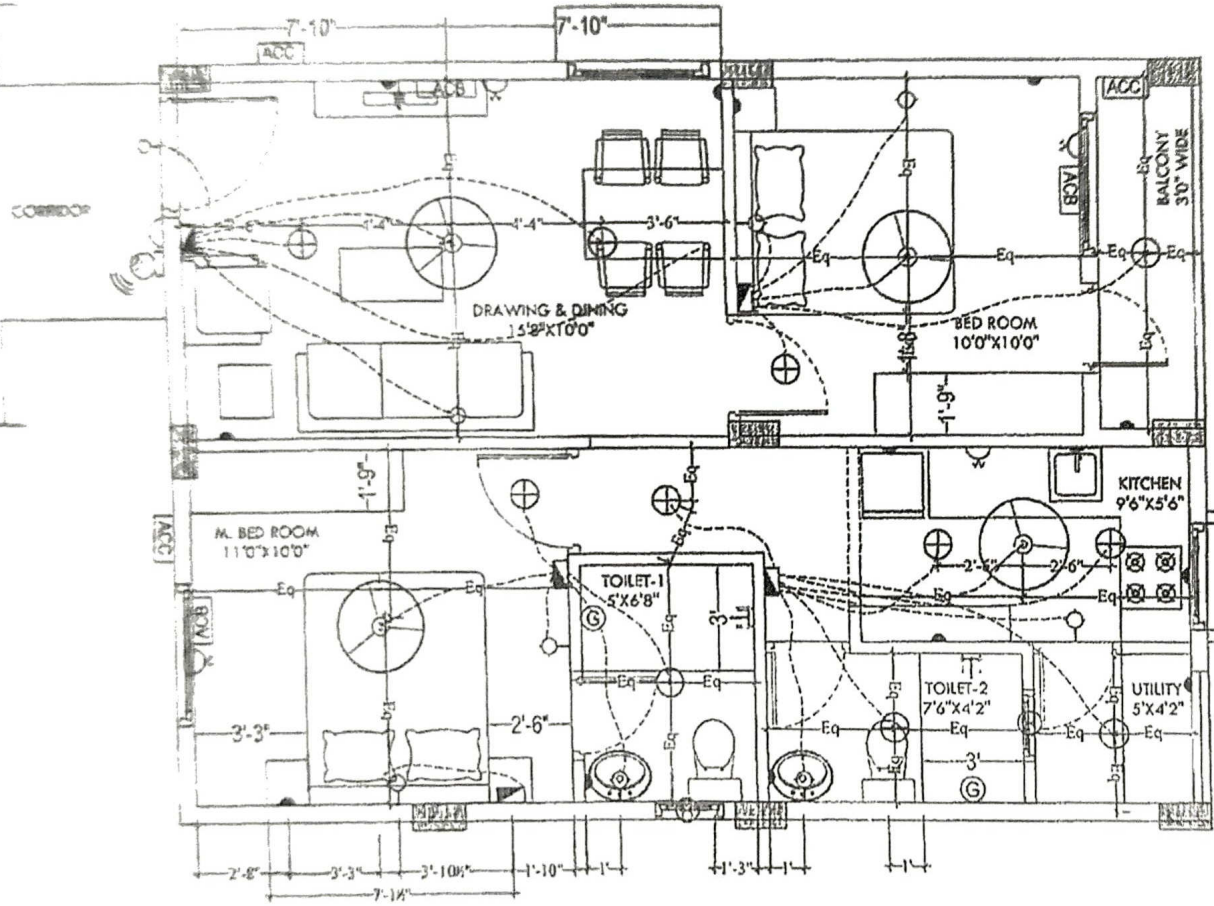


LEGEND:-

S.NO	ITEM	SYMBOL	HEIGHT bottom switch
1	Distribution Board & Change over		7 TO 71
2	Switch board		4' OR 4"
3	Wall point/Bracket light		7'3" TO
4	5 amps plug point		2'
5	Ceiling fan		
6	Geyser point-15A		6'6" OR "
7	Exhaust fan		7'3"
8	15 amps plug point		12" above height 7'
9	Television point		3'
10	Calling Bell		Below 1'
11	Bell Push		4' to 4'6"
12	Calling light		
13	Wall Camera		7'6"
14	AC Compressor		7' TO 7'
15	AC Blower		7' TO 7'
16	Switch board with SA bracket		4' TO 4'

- Notes :-
1. Switch boards c/c behind bed must be 6'6"
 2. 5 amps socket behind fridge must be at the height
 3. Switch boards & Sockets must be 12" above pl
 4. 5 amps socket for chimneys must be at 6' height
 5. 5 amps socket for water filter must be at 6' height

Description	Direction	Owners & Developers :	Date :	23.07.2021	Promoted by
ELECTRICAL PLAN FLAT NOS. 112, 114, 116, 118, 120 & 122		Modi Realty Genome Valley LLP	Prepared By :		Modi Properties Pvt Ltd Phone: +91-40-6633555
		Project Name & Phase :	Approved By :	Soham Modi	
		BRGV	Scale :	N.T.S	

R. Nagaraj

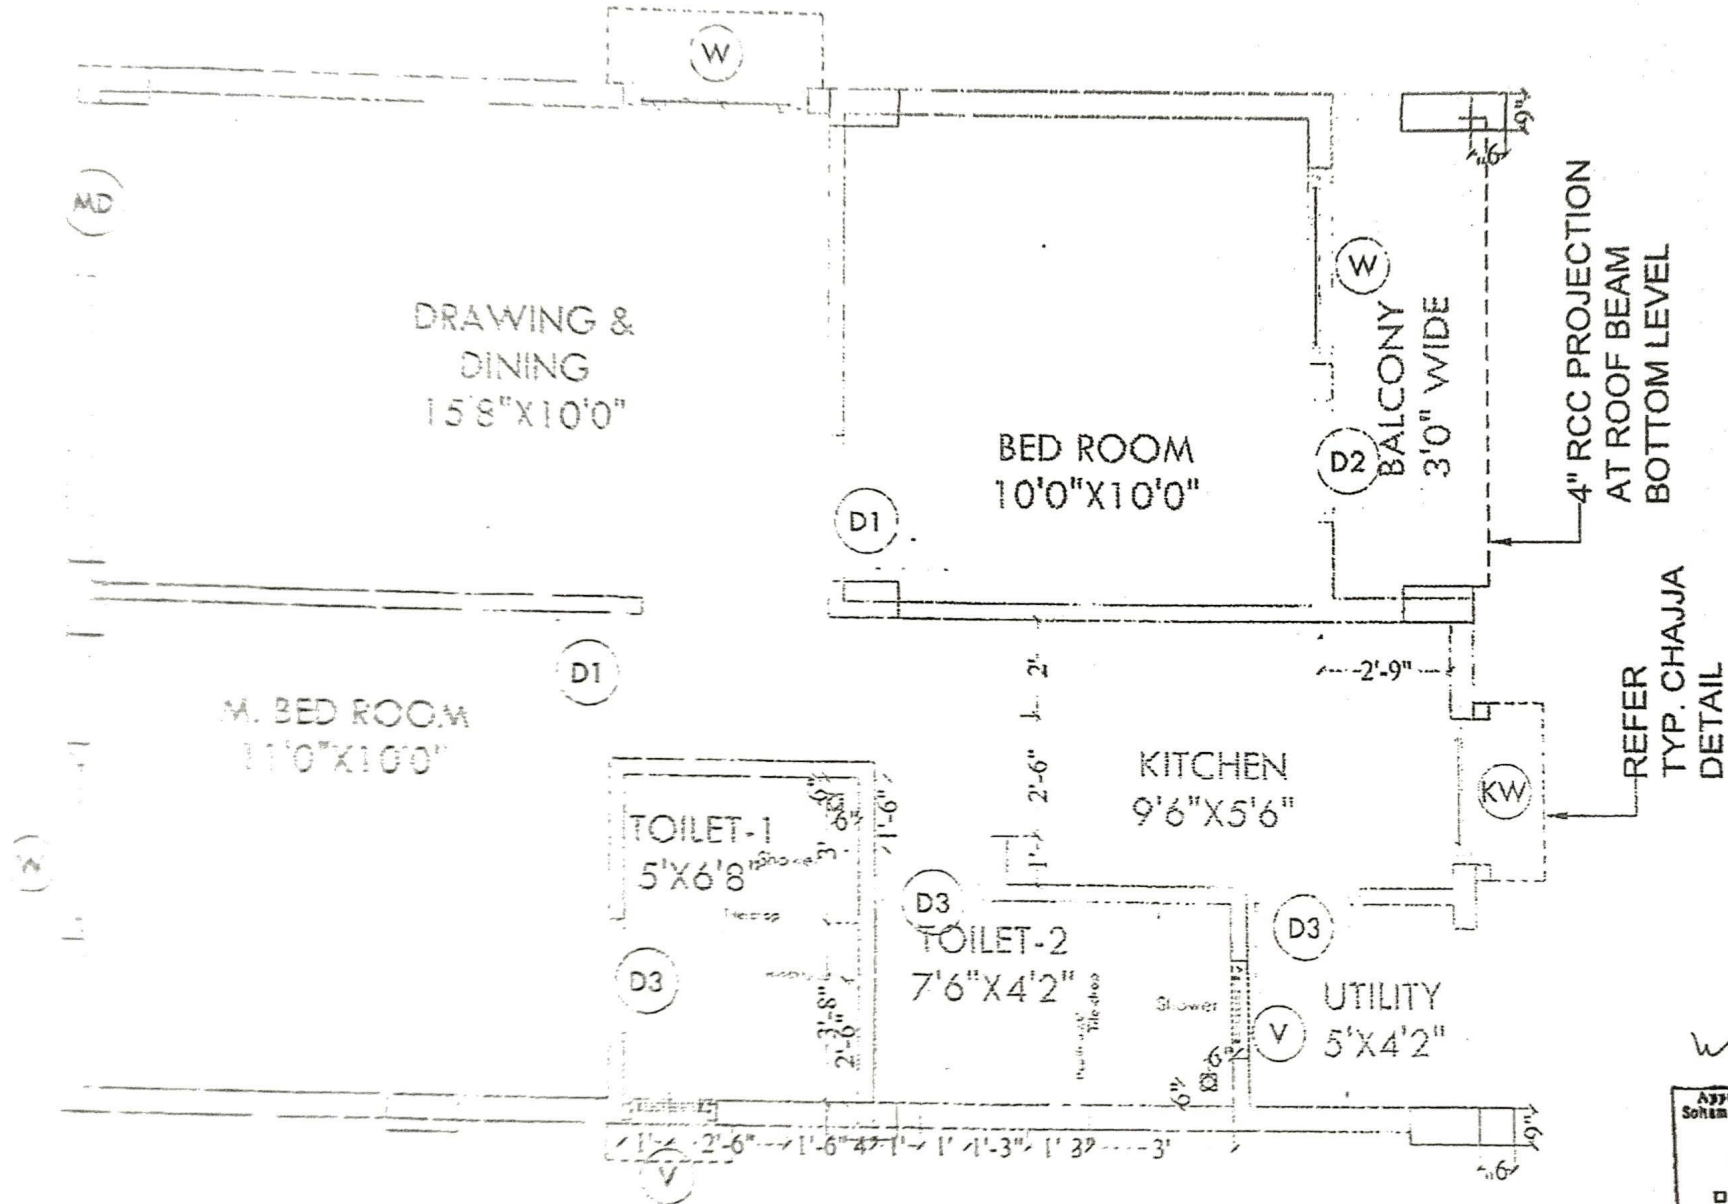

Approved for Construction
Soham Modi, Managing Direct

24 SEP 2021

☐ Original ☐ Copy

Plan ID No:

Description	Direction	Owners & Developers :	Date :	24.09.2021	Promoted by
Planning & Design	N	Modi Realty Genome Valley LLP	Prepared By :	Imran	Modi Properties Pvt Ltd
		Project Name & Phase :	Approved By :	Soham Modi	
		BRGV	Scale :	NTS	Phone: +91-40-66335551
