

Quality Control Check Report. Stage: After Finishing Stage III (Apartments)

Flat No	518	Other	←	Sl. No.	42584
Company	MRGV	Project	BRGV	Phase	←
Prepared by	Saikin	Sign	<i>[Signature]</i>	Date	14-11-2023
Project Manager	Sarwan	Sign	<i>[Signature]</i>	Date	14-11-2023
Previous stage report no.		42107	Report filed and signed by PM		☒ Yes ☐ No
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
☐ Proceed with further work. ATR not required.

Inspection should be done after :

- Completing stage II works.
- Complete works like doors, windows, grills, electrical wiring, switches, french door glass, etc.
- In case of modular kitchen provide platform, granite and dado and modular kitchen in this stage.
- Provide video door phone in this stage.
- Possession for wood work cannot be given until QC check for stage III is completed and all corrections mentioned in the report are made.

Miscellaneous check:

Modular kitchen to be provided	☐ Yes ☒ No	Modular kitchen provided	☐ Yes ☒ No
Modular kitchen workman ship	☐ Good ☐ Avg ☐ Poor	Modular kitchen granite & dado workman ship & finishing	☐ Good ☐ Avg ☐ Poor
Video door phone /wifi cam to be provided	☒ Yes ☐ No	Video door phone/wifi cam provided	☐ Yes ☒ No
Painting marks and drops are cleaned from floor, windows, walls.		☐ Good ☒ Avg ☐ Poor	

Quality Control Check Report. Stage: After Finishing Stage III (Apartments)

		Rate the quality of (Good ✓, Avg. ✗, Poor – needs correction ✗✗, NA)											
S No	Room	Door, door knob & door stopper fitting	Door, door knob & door stopper cleaning	Window grills & quality	Window grills fitting & finishing	Windows quality	Window fitting & finishing	Balcony railing quality & finishing	French door quality & fitting	CP jali quality and fitting	Edge building	Switch boards fitting & covering with plastic covers	Junction box covers painting
1	Bedroom 1 M.Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Bedroom 2 C.Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✗	✓	✗
5	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Utility / balcony 2	✓	✓	✓	✗	✓	✓	✓	✓	✓	✗	✓	✗
9	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Kitchen	✓	✓	✓	✗	✓	✓	✓	✓	✓	✗	✓	✓
11	Toilet 1 M-toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✗	✓
12	Toilet 2 C-toi	✓	✓	✓	✓	✓	✗	✓	✓	✓	✓	✓	✓
13	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other												
15	Other												
Remarks		NOTE :- 1) In M-toi, S.Band to be placed. (keyser) 2) flat to be clean.											

Quality Control Check Report.**Stage: After Plumbing & Electrical (Apartments)**

Flat No.	A-518	Other	—	Sl. No.	41865
Company	MRGV	Project	BRGV	Phase	—
Prepared by	P. Bhasath	Sign	P. Bhasath	Date	29/05/23
Project Manager	Saxena	Sign	Saxena	Date	29/05/23
Previous stage report no.	41839	Report filed and signed by PM?			☒ Yes ☐ No
Additions & alterations sheet date	19/3/22	All pages signed by engineer & customer?			☒ Yes ☐ No
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.					

Inspection should be done after:

- after cleaning the apartment.
- before starting painting, tiling & flooring.
- electrical conduct, waterproofing & plumbing work is completed (for stage II only).
- additions & alterations is finalized and signed. In case there are no additions and alterations printout of email by PM to CR confirming the same must be filed.
- additions & alterations sheets to be transferred to QC file. QC to check if A&A are made as per request.

After Plumbing & Electrical Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. Location of CPVC & PVC fittings must be checked as per measurements given in circular. Tolerance 1".
6. Location, height and spirit level of electrical points must be checked as per measurements given in circular & plan. Tolerance 1".
7. Civil work near pipes in balcony & utility must be neat and mortar should be removed from the pipes.
8. Water proofing must cover all pipes & check height above SFL.
9. Fasteners must be used as specified in circular. Especially check fixing of PVC pipes.
10. Height of DB box must be 6" below false ceiling level or 12" below slab level.
11. In case of many changes in civil work, electrical work and plumbing work, a new drawing must be prepared at HO and approved by MD.

Quality Control Check Repot. Stage: After Plumbing & Electrical (Apartments)

S No	Room	Civil work near pipes in balcony & utility ⁷ (✓ or ✕)	CPVC & PVC Check ⁵ (✓ or ✕)	Electrical points check ⁶ (✓ or ✕)	Water proofing check ⁸ (✓ or ✕)	Proper use of fasteners check ⁹ (✓ or ✕)	Placement of DB ¹⁰ (✓ or ✕)	Placement of Generator changeover (✓ or ✕)
1	Bedroom 1 <i>M-Bed</i>	—	—	✓	—	—	—	—
2	Toilet 1 <i>M-Toi</i>	—	✓	✓	✓	✓	—	—
3	Bedroom 2 <i>K-Bed</i>	—	—	✓	—	—	—	—
4	Toilet 2 <i>C-Toi</i>	—	✓	✓	✓	—	—	—
5	Bedroom 3	—	—	—	—	—	—	—
6	Toilet 3	—	—	—	—	—	—	—
7	Drawing	—	—	✓	—	—	✓	—
8	Dining	—	—	✓	—	—	—	—
9	Lobby 1	—	—	—	—	—	—	—
10	Utility / balcony 1	✓	✓	✓	✓	✓	—	—
11	Utility / balcony 2	✕	✓	✓	—	✓	—	—
12	Utility / balcony 3	—	—	—	—	—	—	—
13	Kitchen	—	✓	✓	—	—	—	—
14	Other							
15	Other							
Remarks								
Remarks on additions & alteration sheet:								
Signed by engineer,			☐ Yes ☒ No		Signed by customer,		☒ Yes ☐ No	
Revised drawing required from HO			☐ Yes ☒ No		Approved revised drawing attached		☐ Yes ☒ No	

Quality Control Check Repot. **Stage: After Plumbing & Electrical (Apartments)**

Miscellaneous check

Screeding done on walls upto 12" outside bathroom/utility	☒ Yes ☐ No
Bathroom /utility filled with 4" water for water proof check	☐ Yes ☒ No
Hole packing done around all pipes in ceiling and internal walls	☒ Yes ☐ No
Remarks:	

Quality Control Check Report. Stage: After Plastering (Apartments)

Flat No.	A-518	Other	—	Sl. No.	41839
Company	MRGV	Project	BRGV	Phase	—
Prepared by	SAIKIRAN	Sign	Sul	Date	23-05-2023
Project Manager	SARWAR	Sign	Sul	Date	23-05-2023
Previous stage report no.		41611	Report filed and signed by PM?		☒ Yes ☐ No
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.					

Inspection should be done after:

- brickwork & 2 coats plastering is completed
- after cleaning the villa.
- Water proofing, screeding in bathrooms is completed.
- before starting painting, tiling & flooring.

Plastering Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✕ for minor mistake that requires minor correction.
3. Mark ✕✕ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✕✕✕ for major mistake that cannot be corrected.
5. 9" unplastered area from SFL should be left including in common areas and terraces.
6. Windows must be checked with templates. Plastering must be 3mm margin for luppum work. Tolerance ¼".
7. Provision of tiles in bathrooms, kitchen & wash areas (rough plastering).
8. Check size of sink bowl. Hole should be 1" to 2" larger. (Tolerance: 1")
9. All doors frames should have ½" grooves.
10. Sill top must be of uniform thickness, correct height, at one level & without broken edges.

Quality Control Check Report. Stage: After Plastering (Apartments)

S No	Room	Skirting Provision (✓ or ✗)	Furnishing around door frame (✓ or ✗)	Beams & columns finishing (✓ or ✗)	Finishing of lofts (✓ or ✗)	Electricity junctions finishing (✓ or ✗)	Windows check (✓ or ✗)	Tiles provision (✓ or ✗)	Sink provision & size (✓ or ✗)	Grooves for door frames (✓ or ✗)	Balcony & terrace sill top finishing (✓ or ✗)	Screeding in bathroom & utility (✓ or ✗)	Screeding in 6" above FFL? (✓ or ✗)
1	Bedroom 1 M-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✗	✓	✓	✓
2	Toilet 1 M-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 G-Bed	✓	✓	✓	✓	✓	✗	✓	✓	✓	✓	✓	✓
4	Toilet 2 C-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✗	✓	✓	✓
5	Bedroom 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Bedroom 4	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Toilet 4	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Drawing	✓	✓	✓	✓	✓	✗	✓	✓	✗	✓	✓	✓
10	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Lobby 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Balcony	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Utility	✓	✓	✓	✓	✓	✓	✓	✓	✗	✓	✓	✓
15	Portico	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
16	Kitchen	✓	✓	✓	✓	✓	✗	✓	✓	✓	✓	✓	✓
17	Other												
Remarks		NOTE:-1) Grooves for door frames, work to be pro improved.											

Quality Control Check Report. Stage: After Brickwork (Apartments/ Lab Spaces)

Flat No.	A-518	Others	—	Sl. No.	41611
Company	MRGV	Project	BRGV	Phase	—
Prepared by	SAIKIRAN	Sign	<i>Saikiran</i>	Date	30-03-2023
Project Manager	SARKAR	Sign	<i>Sarkar</i>	Date	30-03-2023
Previous Stage report no.		40595	Report filed and signed by PM?		☒ Yes ☐ No
Apartment No.		Other		other	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☐ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.					

Inspection should be done after:

- brickwork is completed
- chicken mesh fixed
- after cleaning the apartment
- electrical conducting work is completed

Brickwork Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction.
2. Mark ✕ for minor mistake that requires minor correction.
3. Mark ✕✕ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✕✕✕ for major mistake that cannot be corrected.
5. Wall thickness should be as per plan. Use of 4", 6" & 8" blocks must be checked.
6. All walls should have 2 beds of about 2" to 3" thickness with one no. 6 mm or 8 mm rod with M15 CC.
7. Chicken mesh should be used in each and every joint between RCC & Brickwork.
8. Joint between brickwork & beam on external side must be filled.
9. Check room dimensions with working plan. (Tolerance: 1")
10. Diagonals of each room shall be equal. (Tolerance: 2")
11. Balcony sill level should be 3'3" from SFL. (Tolerance: 1")
12. Check room height with specified height. (Tolerance: 1")
13. Check plumb of walls wherever it appears to be out of plumb. (Tolerance: 1/2")
14. Specify the No. of beams which are not aligned by more than 1" in a room.
15. Door frames must have black Japan coating and wood primer /pellambar – at cost of painter.

Quality Control Check Repot.
Stage: After Brickwork (Apartments/ Lab Spaces)

S No	Room	Wall thickness (✓ or ✗)	Beds in walls (✓ or ✗)	Chicken mesh (✓ or ✗)	External brickwork & beam joint (✓ or ✗)	Room Dimensions (✓ or ✗)	Room Dimensions Difference in inches	Diagonal (✓ or ✗)	Diagonal Difference in inches	Balcony sill level (✓ or ✗)	Room Height (✓ or ✗)	Plumb of walls (Good/Avg./Bad)	Alignment of beams and walls - Nos.
1	Bedroom 1 M. Bed	✓	✓	✓	✗	✓	1	✓	1	1	✓	Avg	✓
2	Toilet 1 M. toi	✓	✓	✓	✗	✓	1	✓	1	1	✓	✓	✗
3	Bedroom 2 G. Bed	✓	✗	✓	✗	✓	1	✓	1	1	✓	✓	✓
4	Toilet 2 G. wi	✓	✓	✓	✗	✓	1	✓	1	1	✓	✓	✗
5	Bedroom 3	1	1	1	1	1	1	1	1	1	1	1	1
6	Toilet 3	1	1	1	1	1	1	1	1	1	1	1	1
7	Drawing	✓	✓	✓	✗	✓	1	✓	1	1	✓	Avg	✓
8	Dining	1	1	1	1	1	1	1	1	1	1	1	1
9	Lobby 1	1	1	1	1	1	1	1	1	1	1	1	1
10	Utility / balcony 1	✓	✓	✓	✗	✓	1	✓	1	1	✓	Avg	✓
11	Utility / balcony 2	✓	✓	✓	✗	✓	1	✓	1	1	✓	✓	✗
12	Utility / balcony 3	1	1	1	1	1	1	1	1	1	1	1	1
13	Kitchen	✓	✗	✓	✗	✓	1	✓	1	1	✓	✗	✗
14	Other												
15	Other												
Remarks NOTE :- (1) Workmanship of Brickwork & joint is to be improved.													
(2) Sil' level beds was not providing as per specification.													

Quality Control Check Repot. Stage: After Brickwork (Apartments/ Lab Spaces)

Quality of edges and corners in all rooms?	☐ Good ☒ Avg. ☐ Bad
Specify rooms that need correction:	

Misc. Checks.

Was 3.75 CFT proportion box provided?	☒ Yes ☐ No
Condition of proportion box?	☐ Good ☒ Avg. ☐ Bad
Was the Apartment cleaned before starting brick work?	☐ Yes ☐ No ☒ Cant' say
Is the Apartment cleaned for plastering?	☒ Yes ☐ No
Wastage?	☐ High ☒ Medium ☐ Low
Storage of building material like bricks sand and cement.	☐ Good ☒ Avg. ☐ Bad
Drum (200 ltrs) provided for curing in each flat?	☒ Yes ☐ No
Remarks:	

Door Frames & Windows check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✕ for minor mistake that requires minor correction.
3. Mark ✕✕ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✕✕✕ for major mistake that cannot be corrected.
5. Window template depth should be between 2 to 2 ½" after plastering.
6. Lintel level should be 7'3" from SFL & 7' from FFL. (Tolerance 1"). Lintel should be as per standard design.
7. Lofts should be at a height of 7' to 7'3" from FFL. Kitchen platform thickness should be 2", SFL to bottom 31".. (Tolerance 1")
8. Slopes of lofts and kitchen platforms to be checked by using 12" spirit level and check height from floor from 2 or 3 points.
9. Thickness of platforms & lofts should be between 2 & 2.5".
10. Provide single layer table brick at bottom of each door frame without threshold.
11. Check Z angle template size (Z angle for bathroom ventilators not required in new projects).
12. Window opening must be checked with MS square pipe templates of 2 sizes for inner and outer openings.
13. Z angle template must be 1" from brick wall surface from the inner side.

Quality Control Check Repot.

Stage: After Brickwork (Apartments/ Lab Spaces)

S No	Room	Door size, face and position (✓ or ✕)	Brick at bottom of door frame 10 (✓ or ✕)	Door frame hold fast provision and fasteners. (✓ or ✕)	Door lenthil design & level (✓ or ✕)	Door diagonal check (✓ or ✕)	Door Plumb - two sides (✓ or ✕)	Windows lenthil design & level. Sill level (✓ or ✕)	Windows size (✓ or ✕)	Windows - template depth & diagonal ^s (✓ or ✕)	Windows - template red oxide painting (✓ or ✕)	Loft & Kitchen platform height (✓ or ✕)	Loft & Kitchen platform slope (✓ or ✕)	Door size, face and position (✓ or ✕)
1	Bedroom 1 M.Red	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M-toi	✓	✕	✓	✕	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 K.Red	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 C-toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2	✓	✕	✓	✕	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✕	✓	✓	✓	✓	✓	✓
14	Other													
15	Other													
Remarks:		NOTE:-1) In K.Red & Balcony, Door frames are not provided due to a material lifting purpose.												
		(2) Kitchen platform was not casted.												
		(3) Door lenthil are also was improved.												
		(4) Loft hacking was not done.												

Quality Control Check Report. Stage: After Finishing Stage II (Apartments)

Flat No	A-518	Other	-	Sl. No.	42107
Company	MRGV	Project	BRGV	Phase	-
Prepared by	P. Bhaskar	Sign	Buss	Date	27-07-23
Project Manager	Sorawar	Sign	Sorawar	Date	27-07-23
Previous stage report no.	41865	Report filed and signed by PM		☒ Yes ☐ No	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- Completion of flooring, bathroom /utility tiles, first coat of paint.
- Completion of doors, windows, grills, electrical wiring, switches must be done in next stage
- False ceiling must be completed before flooring.
- Kitchen platform, granite and dado must be completed where modular kitchen is not provided.
- Provide granite soffit for main door and balconies in this stage.

Miscellaneous check:

Main door fixed with lock & stopper	☒ Yes ☐ No		
Granite soffit for balcony required	☐ Yes ☒ No	Granite soffit for balcony provided	☐ Yes ☐ No
Balcony granite soffit workmanship	☐ Good ☒ Avg ☐ Poor	Balcony granite soffit edge polishing	☐ Good ☐ Avg ☐ Poor
Granite soffit for main door required	☐ Yes ☒ No	Granite soffit for main door provided	☐ Yes ☐ No
Main door granite soffit workmanship	☐ Good ☐ Avg ☐ Poor	Main door granite soffit edge polishing	☐ Good ☐ Avg ☐ Poor

Quality Control Check Repot. Stage: After Finishing Stage II (Apartments)

Tiling & granite work		Rate the quality of (Good ✓, Avg. ✕, Poor – needs correction ✕✕, NA)												
S No	Room	Workmanship of tiling	White cement filling around CPVC lines	Corners finishing	Finishing near doors	Finishing on top of tiles	Finishing near ventilators	Step at bathroom entrance / utility	Step for shower / pot wash	Tile joint grouting	Granite platform finishing and edge polishing	Granite platform slope	Granite platform height	Finishing under granite platform
1	Toilet 1 M-Toi	✓	✕✕	✓	✕	✕	✕✕	✓	✓	✕	-	-	-	-
2	Toilet 2 C-Toi	✓	✕✕	✓	✓	✕	✕✕	✓	✓	✕	-	-	-	-
3	Toilet 3	-	-	-	-	-	-	-	-	-	-	-	-	-
4	Toilet 4	-	-	-	-	-	-	-	-	-	-	-	-	-
5	Wash basin in dining area	-	-	-	-	-	-	-	-	-	-	-	-	-
6	Kitchen	✓	✕✕	✓	-	✓	-	✕	-	✓	✓	✓	✓	-
7	Utility	✓	✕✕	✓	✓	✕	-	-	-	✓	-	-	-	✕
8	Other									✓	-	-	-	-
9	Other													
Remarks		1) Some tiles were hollow sound was observed in the floor.												

Quality Control Check Repot. Stage: After Finishing Stage II (Apartments)

Flooring & painting		Rate the quality of (Good ✓, Avg. ✗, Poor – needs correction ✗✗, NA)												
S No	Room	Color variation of floor tiles	Flooring workmanship & grouting	Skirting size (3")	Skirting workmanship	Plastering above skirting	Plastering & finishing of walls	Crack filling	Loft Finishing	Windows check	General quality of painting & finishing	Door & frame painting quality	Door beading, luppam and painting quality.	Edge building
1	Bedroom 1 <i>M-Bed</i>	✓	✓	✓	✓	✓	✓	✓	—	✗	✓	✓	✓	✗
2	Bedroom 2 <i>K-Bed</i>	✓	✓	✓	✓	✓	✓	✓	—	✗	✓	✓	✓	✗
3	Bedroom 3	—	—	—	—	—	—	—	—	—	—	—	—	—
4	Drawing	✓	✓	✓	✓	✓	✓	✓	—	✓	✓	✓	✓	✓
5	Dining	✓	✓	✓	✓	✓	✓	✓	—	—	✓	✓	✓	✗
6	Lobby 1	—	—	—	—	—	—	—	—	—	—	—	—	—
7	Utility / balcony 1	✓	✓	—	—	—	✓	✓	—	—	✓	✓	✓	✗
8	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	—	—	✓	✓	✓	✗
9	Utility / balcony 3	—	—	—	—	—	—	—	—	—	—	—	—	—
10	Kitchen	✓	✓	✓	✓	✓	✓	✓	✗	✗	✓	✓	✓	✗
11	Other													
12	Other													
Remarks		1) As per M.D sir's instruction's stage-II QC check was done without false -ceiling.												

BLOOMDALE

Residency @ Genome Valley

Shamshad, Hyderabad

Sale Office : S/o. No. 31 & 32, Muradnagar,
Mehdial Mandal, Hyderabad - 500 078

Ph: 01-91210 21717 Fax: 01-91210 21717
E-mailed by : M/s Bloomdale Residency Genome Valley LLP



Head Office : A-4, H.No. 16 & 17, II Floor, M. G. Road,

Secunderabad - 500 001 Ph: 4066345251

E-mail: modiproperties.com & www.modiproperties.com

Details of Additions & Alterations

Flat No	Type	Deluxe / Semi Deluxe
5/8		
Buyer Name	J. M. Sharada Reddy	
Phone No.	9008882867	Email: Sharada.070@gmail.com

I hereby confirm that I have given the details of the minor additions and alterations that are required in the above referred flat in the pages attached herein. Please complete the changes suggested by me, I agree to pay the charges, if any, for the additions and alterations that I have asked you to make, as per the rates suggested by you. I shall deliver all the materials that are required to be provided by me at the site on or before _____.

In case I fail to deliver these items to the site by the specified date, you may complete the works in the flat as per the standard items provided by you.

Buyers sign	Sharada	Engg. Sign	AS
Date:	19/3/22	Date	19/3/22

Note:

1. Colour shades of paints may vary from batch to batch & company to company. The Builder will not take responsibility of quality of work for dark shades especially green & blue.
2. Shade / colour of natural material like marble and granite can't be guaranteed and may vary from lot to lot. Cracks like appearance in marble is a natural feature and Builder shall not be responsible for repairs or replacement.
3. Availability of bathroom or flooring tiles of the same type /colour/make can not be guaranteed and closest possible type/colour/make may be used in its place.
4. No further change shall be permitted from this day.
5. Please sign on all pages.

Changes in electrical points: (mark on plan)

- ① 16 amp Extn for kitchen
- ② 16 amp Extn utility.
- ③ Extn pit for T.V. subs.

Choice of Bathroom tiles, CP fittings & Sanitary ware:

- ① no chgs.

Changes in kitchen platform: (mark on plan)

- ① no chgs.

Shanaka

Details of solar water heater:

Other Changes:

Alameda

To,

Date: 04.03.2022

Mr. Kola Sampath Reddy,
S/o Mr. Kola Malla Reddy,
H. No. 5-5-100, Old Bazar,
Kapuwada, Karimnagar-505001.

Dear Sir,

If you wish to make any minor additions or alterations to the flat that you have booked, we request you to visit the site during office hours between 05-03-2022 & 03-04-2022. We also request you to finalize details like color of walls, etc., during your visit to the site. Our site engineers will make note of these details.

For your convenience we request you to take prior appointment so that our engineers can give you their undivided attention. You may contact Mr. G. Sarwar (Project in-charge) on +91-9100036740 or Ms. Pusalatha (Asst. Engineer) on +91-9848942990 or by email at brgv_const@modiproperties.com

In case you fail to contact us during the above mentioned period, we shall assume that no changes are required, and your flat will be completed as per the standard specifications shown in the model flat.

Thank You.

Yours Sincerely,

For Modi Realty Genome Valley LLP.



Authorised Signatory.

Please refer to the notes attached herein.

Notes:

1. Working drawings, electrical layout & plumbing drawing for your flat have been enclosed for your reference.
2. Select materials that you may choose to provide like tiles, sinks, CP and sanitary ware, etc. must be handed over at our site within 4 weeks of completion of brickwork and internal plastering.
3. Changes to external appearance and colour shall not be permitted. Changes to colour of doors/door frames in balcony/main entrance shall not be permitted. Change in colour of balcony walls shall not be permitted.
4. Fixing of grills & gates to the main door / balcony shall not be permitted.
5. Changes in walls, door positions or other structural changes shall not be permitted.
6. You may provide your own flooring tiles, bathroom tiles, CP & sanitary fittings and they shall be installed by us.
7. Additional shelves & lofts shall not be permitted.
8. Charges & refunds will be as follows:

No charge for:

1. Choice of two free colors for walls;
2. Choice of two/three combinations for bathroom tiles.

Non standard items to be supplied by the buyer & installed free of cost:

1. Hardware.
2. CP & Sanitaryware.
3. Flooring tiles
4. Kitchen platform - granite / marble.
5. Bathroom tiles.

Extra charges shall be payable for:

1. Extra electrical points / switch boards / sockets / switches.
2. Additional kitchen platform with granite & dado.
3. Rounding / polishing of granite & dado.
4. Exhaust hole in bathroom/kitchen.


Refund / charges for upgrade or downgrade or substitutions shall be applicable for:

1. Kitchen & bathroom tiles.
2. Flooring tiles.
3. CP fittings.
4. Sanitaryware & bathtubs.
5. Doors & hardware.
6. Kitchen sink.
7. Civil work.
8. Electrical switches.
9. Kitchen platform

No refunds shall be made for:

1. Kitchen platform.
2. Civil work.

Shinde

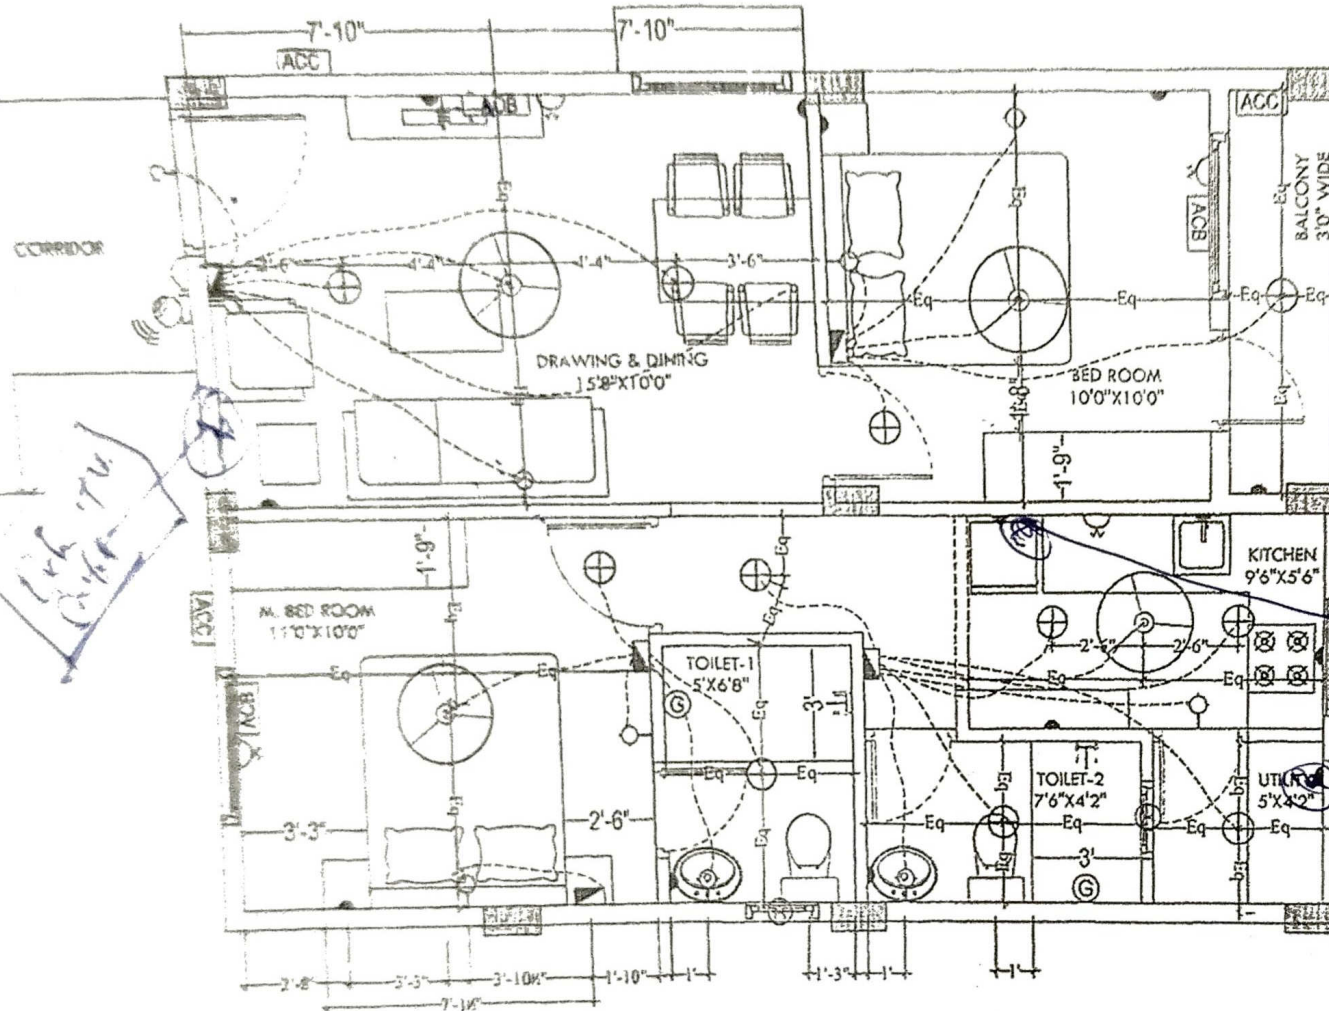

LEGEND:-

S.NO	ITEM	SYMBOL	HEIG bolt switc
1.	Distribution Board & Change over		7' TO
2.	Switch board		4' OR
3.	Wall point/Bracket light		7'3" T
4.	5 amps plug point		2'
5.	Ceiling fan		-
6.	Geyser point-15A		6'6" OF
7.	Exhaust fan		7'3"
8.	15 amps plug point		12" ab height
9.	Television point		3'
10.	Ceiling Bell		Below
11.	Bell Push		4' to 4'
12.	Ceiling light		-
13.	Wifi Camera		7'5"
14.	AC Compressor		7' TC
15.	AC Blower		7' TC
16.	Switch board with 5A socket		4' TC

- Notes :-
1. Switch boards c/c behind bed must be 6'6"
 2. 5 amps socket behind fridge must be at the height
 3. Switch boards & Sockets must be 12" above p
 4. 5 amps socket for chimneys must be at 5' height
 5. 5 amps socket for water filter must be at 5' height

Description

ELECTRICAL PLAN

118, 120 & 122

Direction



Owners & Developers :

Modi Realty Genome Valley LLP

Project Name & Phase :

BRGV

Date :

23.07.2021

Prepared By :

Approved By :

S :

Soham Modi


N.T.S

Promoted by

Modi Properties Pvt L


Phone:+91-40-663355

Sharda

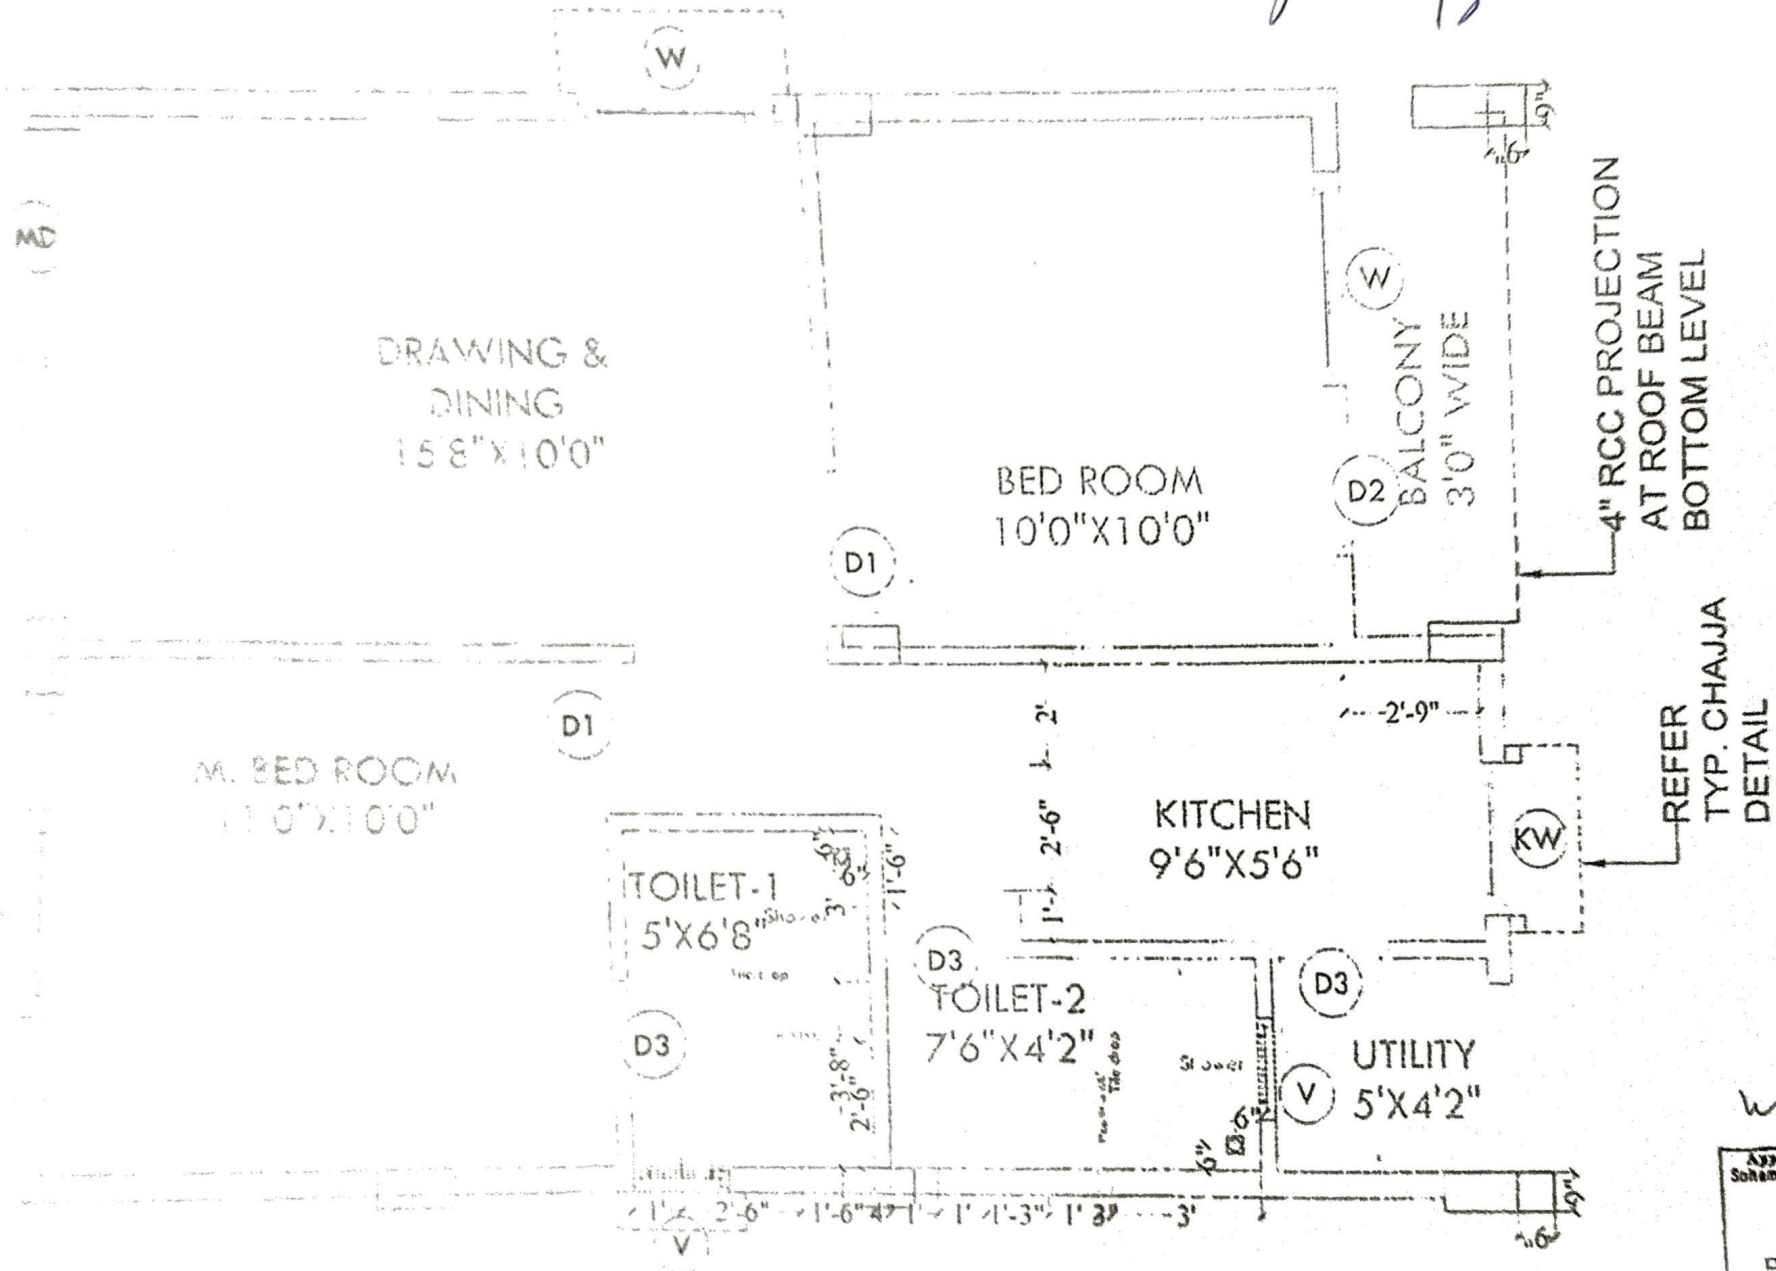

Approved for Construction
Soham Modi, Managing Director
24 SEP 2021
☐ Original ☐ Copy
Plan ID No:

Direction	Owners & Developers :	Date :	24.09.2021	Promoted by
	Modi Realty Genome Valley LLP	Prepared By :	Imran	Modi Properties Pvt Ltd
	Project Name & Phase	Approved By :	Soham Modi	
	BRGV	Scale :	N T S	
				Phone +91-40-66335551

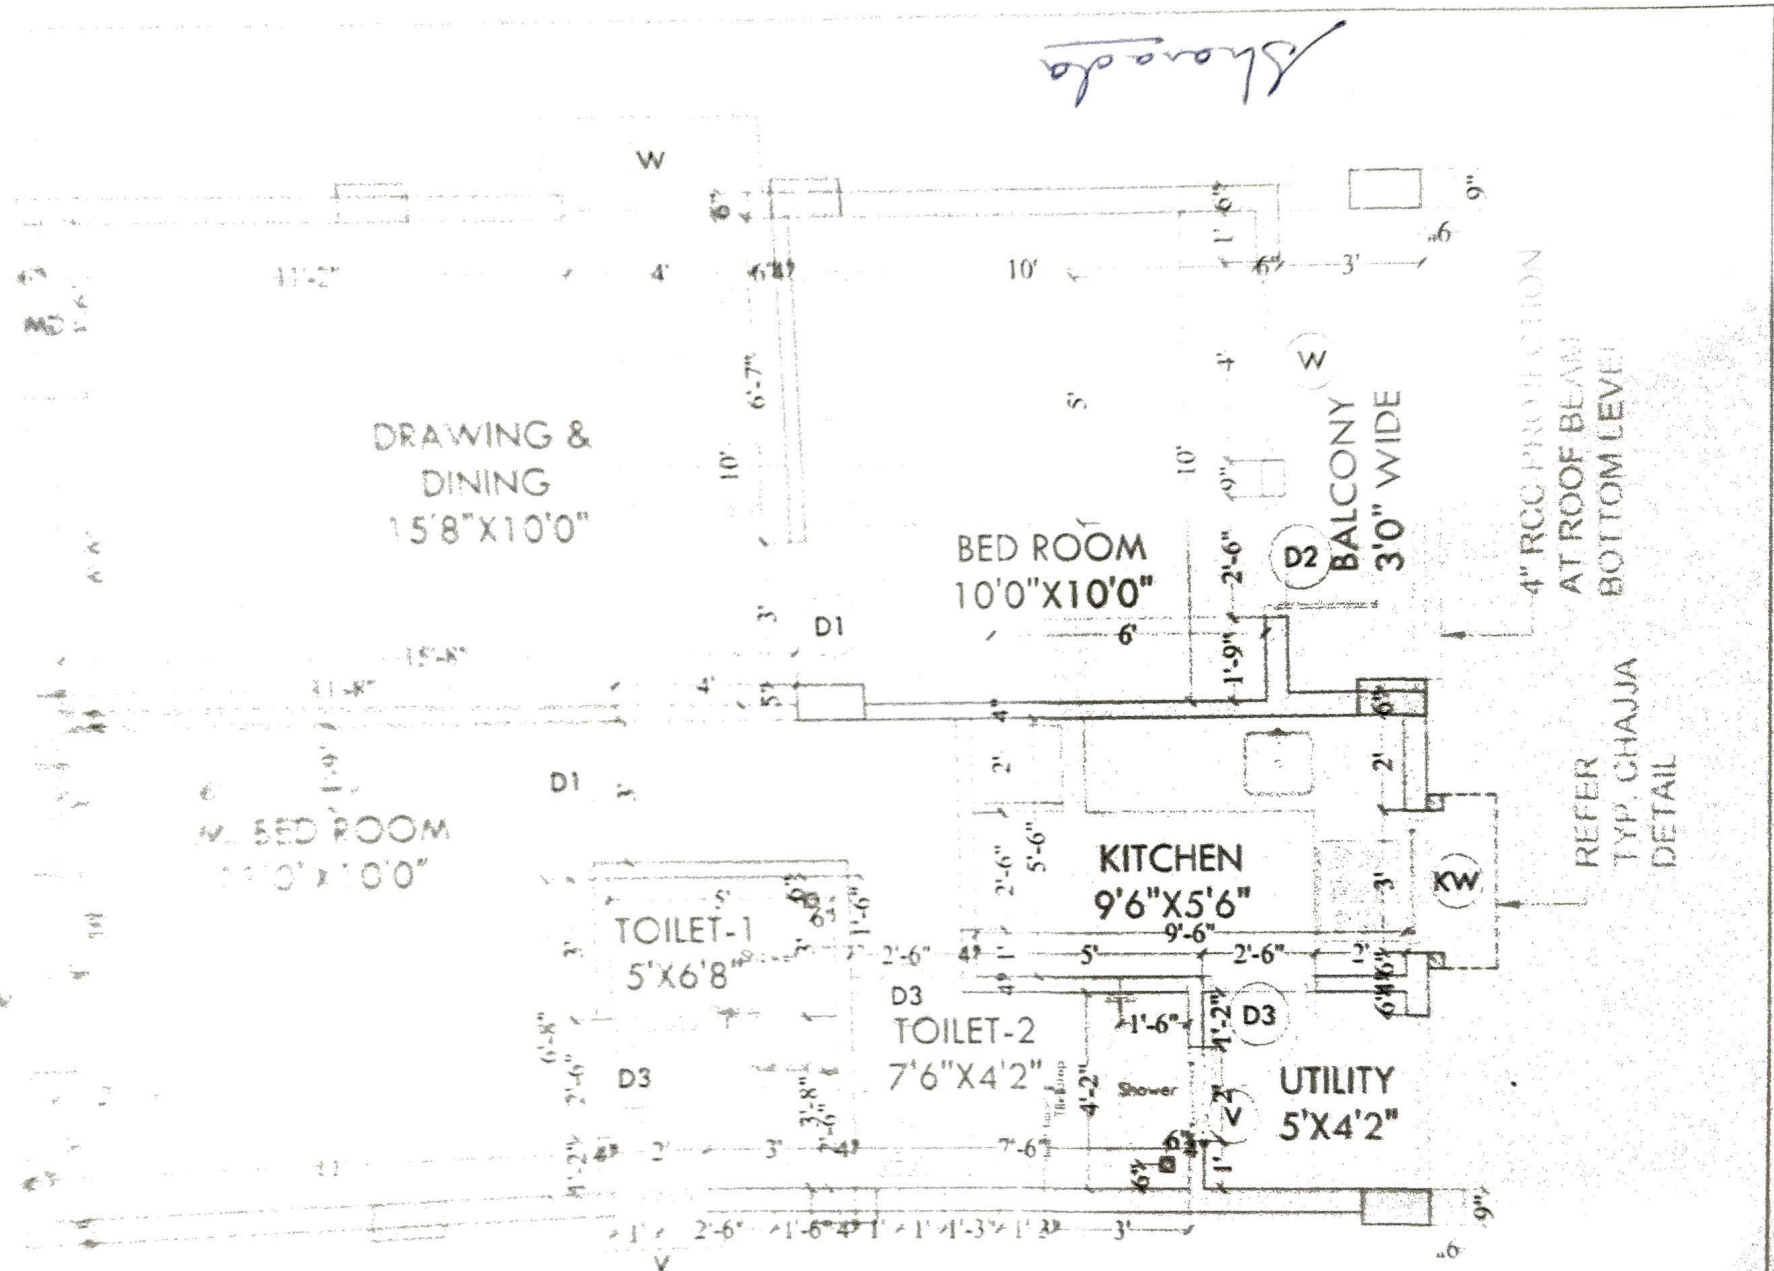

Direction	Owners & Developers	Date	06.09.2021	Promoted by
N	Modi Realty Genome Valley LLP	Prepared By	Imran	Modi Properties Pvt Ltd
	Project Name & Phase	Approved By	Soham Modi	Phone: +91-40-66335551
	BRGV	Scale	N.T.S	
