


Check report by Sales + CR after finishing stage IV (Apartments)

Flat No	322	Other		Sl. No.	43206
Company	MRCV	Project		Phase	
Prepared by	Venkatesh Reddy	Sign	BRCV	Date	5/11/24
Project Manager	Sarwan	Sign		Date	5-11-2024
Stage II report no.					
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No
Recommendation: ☒ Work is satisfactorily completed. Possession may be handed over. ☐ Minor corrections given herein to be completed before handing over possession. ☐ Major corrections required. Do not handover possession. Request for recheck after completion of works. ☐ Works incomplete. Check report cannot be prepared. Request for recheck after completion of works.					

Notes:

- Site to make request for stage IV inspection on M-codex. QC to forward request by email to Sales/CR manager with Sl No. generated by M-codex.
- Inspection to be carried out with one member of sales team and CR team + site engineer within 3 days of request.
- Site engineer shall ensure that all works are completed and the flat is thoroughly cleaned in all respects before requesting for inspection.
- Possession cannot be handed over to customer without this inspection.
- Report to be made on same day. Scanned copy to be sent to CR for uploading. Original to be sent to Ashaiya.
- Mark green tick if work is completed. Red 'x' if minor corrections are required. Red 'xx' if work not completed/needs major corrections. Mark 'NA' if not applicable.



Check report by Sales + CR after finishing stage IV (Apartments)

Miscellaneous check (check for quality & completion):

Modular kitchen	N/A	Security camera provided	
Main door soffit quality	✓	False ceiling provided by developer	N/A
No material is stored in flat	✓	Properly labelled keys – 3 sets	✓
Loft tank installed in utility	✓	Kitchen granite platform and dado	✓
Loft provided	✓	Loft finishing	✓
Water supply	✓	Electricity supply	✓
Generator backup (auto)	✓	Car parking provided	✓
Flat label	✓	Car parking label	✓
Provision of lift	✓	Cleanliness of corridors + staircase	✓
Remarks:			

Check report by Sales + CR after finishing stage IV (Apartments)

S No	Room/ quality check	Floor & wall tiles	Painting	Doors + hardware + door beading	Windows/ventilator + grill + hardware	Electricals – switches, switch boards, points	CP & sanitary fittings	Ratings	Painting of exposed pipes + hole packing	Air cracks are treated and painted	Seepages (Nil)	Cleanliness /removal of paint spots
1	Bedroom 1	✓	✓	✓	✓	✓			✓	✓	✓	✓
2	Bedroom 2	✓	✓	✓	✓	✓			✓	✓	✓	✓
3	Bedroom 3								✓	✓	✓	✓
4	Drawing	✓	✓	✓	✓	✓						
5	Dining	✓	✓	✓	✓	✓			✓	✓	✓	✓
6	Lobby 1					✓			✓	✓	✓	✓
7	Utility / balcony 1	✓	✓	✓	✓	✓	✓		✓	✓	✓	✓
8	Utility / balcony 2											
9	Utility / balcony 3	✓	✓	✓	✓	✓						
10	Kitchen	✓	✓	✓	✓	✓	✓		✓	✓	✓	✓
11	Toilet 1	✓	✓	✓	✓	✓	✓		✓	✓	✓	✓
12	Toilet 2	✓	✓	✓	✓	✓	✓		✓	✓	✓	✓
13	Toilet 3								✓	✓	✓	✓
14	Other:											
15	Other:											

Quality Control Check Report. Stage: After Finishing Stage III (Apartments)

Flat No	A-322	Other	-	Sl. No.	42005
Company	MRGV	Project	BRGV	Phase	-
Prepared by	P. Bhaskar	Sign	Bhaskar	Date	28-06-23
Project Manager	Sowar	Sign	Syligh Sam	Date	28-06-23
Previous stage report no.	41541	Report filed and signed by PM	☒ Yes ☐ No		
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☐ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after :

- Completing stage II works.
- Complete works like doors, windows, grills, electrical wiring, switches, french door glass, etc.
- In case of modular kitchen provide platform, granite and dado and modular kitchen in this stage.
- Provide video door phone in this stage.
- Possession for wood work cannot be given until QC check for stage III is completed and all corrections mentioned in the report are made.

Miscellaneous check:

Modular kitchen to be provided	☐ Yes ☒ No	Modular kitchen provided	☐ Yes ☒ No
Modular kitchen workman ship	☐ Good ☒ Avg ☐ Poor	Modular kitchen granite & dado workman ship & finishing	☐ Good ☒ Avg ☐ Poor
Video door phone /wifi cam to be provided	☒ Yes ☐ No	Video door phone/wifi cam provided	☐ Yes ☒ No
Painting marks and drops are cleaned from floor, windows, walls.		☐ Good ☐ Avg ☒ Poor	

Quality Control Check Report. Stage: After Finishing Stage III (Apartments)

		Rate the quality of (Good ✓, Avg. ✕, Poor – needs correction ✕✕, NA)											
S No	Room	Door, door knob & door stopper fitting	Door, door knob & door stopper cleaning	Window grills & quality	Window grills fitting & finishing	Windows quality	Window fitting & finishing	Balcony railing quality & finishing	French door quality & fitting	CP jali quality and fitting	Edge building	Switch boards fitting & covering with plastic covers	Junction box covers painting
1	Bedroom 1 <i>M-Red</i>	✓	✓	✓	✕	✓	✓	✓	✓	✓	✓	✓	✓
2	Bedroom 2 <i>K-Red</i>	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕	✓	✓
3	Bedroom 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕	✓	✓
5	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕
6	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕	✓	✓
8	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕	✓	✓
9	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Toilet 1 <i>M-Toi</i>	✓	✓	✓	✕	✓	✓	✓	✓	✓	✕	✓	✓
12	Toilet 2 <i>C-Toi</i>	✓	✓	✓	✕	✓	✓	✓	✓	✓	✓	✕	✓
13	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other												
15	Other												

Remarks

1) Utility door was not fixed properly 2) Main door was slightly damaged 3) Balcony grill painting was poor 4) In Both Toilets white enamel was not provided, which was mentioned in previous Report 5) In M-Toi Tile was broken. 6) Finishing near M-Toi door to be improved.

Quality Control Check Report. Stage: After Finishing Stage III (Apartments)

Flat No	A-322	Other	-	Sl. No.	42005
Company	MRGV	Project	BRGV	Phase	-
Prepared by	P. Bhaskar	Sign	Bhaskar	Date	28-06-23
Project Manager	Sowar	Sign	Sydney Sam	Date	28-06-23
Previous stage report no.	41541	Report filed and signed by PM	☒ Yes ☐ No		
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☐ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after :

- Completing stage II works.
- Complete works like doors, windows, grills, electrical wiring, switches, french door glass, etc.
- In case of modular kitchen provide platform, granite and dado and modular kitchen in this stage.
- Provide video door phone in this stage.
- Possession for wood work cannot be given until QC check for stage III is completed and all corrections mentioned in the report are made.

Miscellaneous check:

Modular kitchen to be provided	☐ Yes ☒ No	Modular kitchen provided	☐ Yes ☒ No
Modular kitchen workman ship	☐ Good ☒ Avg ☐ Poor	Modular kitchen granite & dado workman ship & finishing	☐ Good ☒ Avg ☐ Poor
Video door phone /wifi cam to be provided	☒ Yes ☐ No	Video door phone/wifi cam provided	☐ Yes ☒ No
Painting marks and drops are cleaned from floor, windows, walls.		☐ Good ☐ Avg ☒ Poor	

Quality Control Check Report. Stage: After Finishing Stage III (Apartments)

		Rate the quality of (Good ✓, Avg. ✕, Poor – needs correction ✕✕, NA)											
S No	Room	Door, door knob & door stopper fitting	Door, door knob & door stopper cleaning	Window grills & quality	Window grills fitting & finishing	Windows quality	Window fitting & finishing	Balcony railing quality & finishing	French door quality & fitting	CP jali quality and fitting	Edge building	Switch boards fitting & covering with plastic covers	Junction box covers painting
1	Bedroom 1 <i>M-Red</i>	✓	✓	✓	✕	✓	✓	✓	✓	✓	✓	✓	✓
2	Bedroom 2 <i>K-Red</i>	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕	✓	✓
3	Bedroom 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕	✓	✓
5	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕
6	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕	✓	✓
8	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕	✓	✓
9	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Toilet 1 <i>M-Toi</i>	✓	✓	✓	✕	✓	✓	✓	✓	✓	✕	✓	✓
12	Toilet 2 <i>C-Toi</i>	✓	✓	✓	✕	✓	✓	✓	✓	✓	✓	✕	✓
13	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other												
15	Other												

Remarks

1) Utility door was not fixed properly 2) Main door was slightly damaged 3) Balcony grill painting was poor 4) In Both Toilets white enamel was not provided, which was mentioned in previous Report 5) In M-Toi Tile was broken. 6) Finishing near M-Toi door to be improved.

ATR on Quality Control Check Repot. (Apartments)

Flat No	A-322	QC report stage	After finishing stage - III	Sl. No.	42005
Company	MRGV	Project	BRGV	Phase	-
Prepared by	Tejwana	Sign	Tul	Date	30/6/2023
Project Manager	Sarwan	Sign	Spry E	Date	30/6/2023
Receipt by QC date		Sign		Other	
Receipt at HO date		Sign		Other	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation that was made by QC:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team.

Notes:

1. Attach a copy of the QC report to this sheet.
2. Circle each correction with a red pen – tick (✓) each circle for work completed and cross (X) each circle where work has not been completed.
3. Give remarks for each case where work has not completed on this sheet.
4. Make 2 copied of the ATR – send one to MD and other to QC.
5. Enclose required photographs – hard copy.

Remarks:

All remarks were corrected.

Quality Control Check Report. Stage: After Finishing Stage III (Apartments)

Flat No	A-322	Other	-	Sl. No.	42005
Company	M R G v	Project	BR G v	Phase	-
Prepared by	P-Bhaxath	Sign	Buay	Date	28-06-23
Project Manager	Sarwar	Sign	Syulgh Sam	Date	28-06-23
Previous stage report no.	41541	Report filed and signed by PM		☒ Yes ☐ No	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☐ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after :

- Completing stage II works.
- Complete works like doors, windows, grills, electrical wiring, switches, french door glass, etc.
- In case of modular kitchen provide platform, granite and dado and modular kitchen in this stage.
- Provide video door phone in this stage.
- Possession for wood work cannot be given until QC check for stage III is completed and all corrections mentioned in the report are made.

Miscellaneous check:

Modular kitchen to be provided	☐ Yes ☒ No	Modular kitchen provided	☐ Yes ☒ No
Modular kitchen workman ship	☐ Good ☐ Avg ☐ Poor	Modular kitchen granite & dado workman ship & finishing	☐ Good ☐ Avg ☐ Poor
Video door phone /wifi cam to be provided	☒ Yes ☐ No	Video door phone/wifi cam provided	☐ Yes ☒ No
Painting marks and drops are cleaned from floor, windows, walls.		☐ Good ☐ Avg ☒ Poor	

Quality Control Check Repot. Stage: After Finishing Stage III (Apartments)

		Rate the quality of (Good ✓, Avg. ✕, Poor – needs correction ✕✕, NA)											
S No	Room	Door, door knob & door stopper fitting	Door, door knob & door stopper cleaning	Window grills & quality	Window grills fitting & finishing	Windows quality	Window fitting & finishing	Balcony railing quality & finishing	French door quality & fitting	CP jali quality and fitting	Edge building	Switch boards fitting & covering with plastic covers	Junction box covers painting
1	Bedroom 1 <i>M-Red</i>	✓	✓	✓	✕	✓	✓	)	)	)	✓	✓	✓
2	Bedroom 2 <i>K-Red</i>	✓	✓	✓	✓	✓	✓	)	)	)	✕	✓	✓
3	Bedroom 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Drawing	✓	✓	✓	✓	✓	✓	)	)	)	✕	✓	✓
5	Dining	✓	✓	✓	✓	✓	✓	)	)	)	✓	✓	✕
6	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕	✓	✓
8	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕	✓	✓
9	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Kitchen	✓	✓	✓	✓	✓	✓	)	)	)	✓	✓	✓
11	Toilet 1 <i>M-Toi</i>	✓	✓	✓	✕	✓	✓	)	)	✓	✕	✓	✓
12	Toilet 2 <i>C-Toi</i>	✓	✓	✓	✕	✓	✓	)	)	✓	✓	✕	✓
13	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other												
15	Other												

Remarks

1) utility door was not fixed properly 2) main door was slightly damaged 3) Balcony grill painting was poor 4) In Both Toilets white cement was not provided, which was mentioned in previous Report. 5) In M-Toi Tile was Broken. 6) Finishing near M-Toi door to be improved.

Quality Control Check Report. Stage: After Finishing Stage II (Apartments)

Flat No	A-322	Other	-	Sl. No.	41541
Company	MARGY	Project	BARGY	Phase	-
Prepared by	P. Bhosath	Sign	P.B	Date	23-03-23
Project Manager	Saxwax	Sign	Saxwax	Date	23-03-23
Previous stage report no.		40840	Report filed and signed by PM		☒ Yes ☐ No
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- Completion of flooring, bathroom /utility tiles, first coat of paint.
- Completion of doors, windows, grills, electrical wiring, switches must be done in next stage
- False ceiling must be completed before flooring.
- Kitchen platform, granite and dado must be completed where modular kitchen is not provided.
- Provide granite soffit for main door and balconies in this stage.

Miscellaneous check:

Main door fixed with lock & stopper	☒ Yes ☐ No		
Granite soffit for balcony required	☐ Yes ☐ No	Granite soffit for balcony provided	☐ Yes ☐ No
Balcony granite soffit workmanship	☐ Good ☐ Avg ☐ Poor	Balcony granite soffit edge polishing	☐ Good ☐ Avg ☐ Poor
Granite soffit for main door required	☐ Yes ☐ No	Granite soffit for main door provided	☐ Yes ☐ No
Main door granite soffit workmanship	☐ Good ☐ Avg ☐ Poor	Main door granite soffit edge polishing	☐ Good ☐ Avg ☐ Poor

Quality Control Check Repot. Stage: After Finishing Stage II (Apartments)

Tiling & granite work		Rate the quality of (Good ✓, Avg. ✗, Poor – needs correction ✗✗, NA)												
S No	Room	Workmanship of tiling	White cement filling around CPVC lines	Corners finishing	Finishing near doors	Finishing on top of tiles	Finishing near ventilators	Step at bathroom entrance / utility	Step for shower / pot wash	Tile joint grouting	Granite platform finishing and edge polishing	Granite platform slope	Granite platform height	Finishing under granite platform
1	Toilet 1 <i>M-Toi</i>	✓	✗✗	✓	✓	✓	✓	✓	✓	✓	-	-	-	-
2	Toilet 2 <i>C-Toi</i>	✓	✗✗	✓	✓	✗	✓	✓	✓	✓	-	-	-	-
3	Toilet 3	-	-	-	-	-	-	-	-	-	-	-	-	-
4	Toilet 4	-	-	-	-	-	-	-	-	-	-	-	-	-
5	Wash basin in dining area	-	-	-	-	-	-	-	-	-	-	-	-	-
6	Kitchen	✓	-	✓	-	✓	-	-	-	✓	-	-	-	-
7	Utility	✓	✗	✗	✓	✓	-	-	-	✗	-	-	-	-
8	Other													
9	Other													
Remarks		<i>1) kitchen platform was not provided, utility cleaning work was poor.</i>												

Quality Control Check Report. Stage: After Finishing Stage II (Apartments)

Flooring & painting		Rate the quality of (Good ✓, Avg. ✗, Poor – needs correction ✗✗, NA)												
S No	Room	Color variation of floor tiles	Flooring workmanship & grouting	Skirting size (3")	Skirting workmanship	Plastering above skirting	Plastering & finishing of walls	Crack filling	Loft Finishing	Windows check	General quality of painting & finishing	Door & frame painting quality	Door beading, luppam and painting quality.	Edge building
1	Bedroom 1 M. Bed	✓	✓	✓	✓	✓	✓	✓	-	✗	✓	✓	✓	✗
2	Bedroom 2 K. Bed	✓	✓	✓	✓	✓	✓	✓	-	✓	✓	✓	✓	✓
3	Bedroom 3	-	-	-	-	-	-	-	-	-	-	-	-	-
4	Drawing	✓	✓	✓	✓	✓	✓	✓	-	✓	✓	✓	✓	✓
5	Dining	✓	✓	✓	✓	✓	✓	✓	-	-	✓	-	-	✗
6	Lobby 1	-	-	-	-	-	-	-	-	-	-	-	-	-
7	Utility / balcony 1	✓	✓	-	-	-	✓	✓	-	-	✓	✓	✓	✗
8	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	-	-	✓	✓	✓	✗
9	Utility / balcony 3	-	-	-	-	-	-	-	-	-	-	-	-	-
10	Kitchen	✓	✓	✓	✓	✓	✓	✓	✗	✗	✓	-	-	✗
11	Other													
12	Other													
Remarks		1) Utility lock was provided in Reverse position												

Quality Control Check Report. Stage: After Finishing Stage II (Apartments)

Flat No	D-322	Other	-	Sl. No.	41541
Company	MRGV	Project	BAGV	Phase	-
Prepared by	P. Bhargava	Sign	P.B.	Date	23-03-23
Project Manager	Saxwax	Sign	Saxwax	Date	23-03-23
Previous stage report no.	40840	Report filed and signed by PM			☒ Yes ☐ No
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- Completion of flooring, bathroom /utility tiles, first coat of paint.
- Completion of doors, windows, grills, electrical wiring, switches must be done in next stage
- False ceiling must be completed before flooring.
- Kitchen platform, granite and dado must be completed where modular kitchen is not provided.
- Provide granite soffit for main door and balconies in this stage.

Miscellaneous check:

Main door fixed with lock & stopper	☒ Yes ☐ No		
Granite soffit for balcony required	☐ Yes ☐ No	Granite soffit for balcony provided	☐ Yes ☐ No
Balcony granite soffit workmanship	☐ Good ☐ Avg ☐ Poor	Balcony granite soffit edge polishing	☐ Good ☐ Avg ☐ Poor
Granite soffit for main door required	☐ Yes ☐ No	Granite soffit for main door provided	☐ Yes ☐ No
Main door granite soffit workmanship	☐ Good ☐ Avg ☐ Poor	Main door granite soffit edge polishing	☐ Good ☐ Avg ☐ Poor

Quality Control Check Repot. Stage: After Finishing Stage II (Apartments)

Tiling & granite work		Rate the quality of (Good ✓, Avg. ✗, Poor – needs correction ✗✗, NA)												
S No	Room	Workmanship of tiling	White cement filling around CPVC lines	Corners finishing	Finishing near doors	Finishing on top of tiles	Finishing near ventilators	Step at bathroom entrance / utility	Step for shower / pot wash	Tile joint grouting	Granite platform finishing and edge polishing	Granite platform slope	Granite platform height	Finishing under granite platform
1	Toilet 1 <i>M-Toi</i>	✓	✗✗	✓	✓	✓	✓	✓	✓	✓	-	-	-	-
2	Toilet 2 <i>C-Toi</i>	✓	✗✗	✓	✓	✗	✓	✓	✓	✓	-	-	-	-
3	Toilet 3	-	-	-	-	-	-	-	-	-	-	-	-	-
4	Toilet 4	-	-	-	-	-	-	-	-	-	-	-	-	-
5	Wash basin in dining area	-	-	-	-	-	-	-	-	-	-	-	-	-
6	Kitchen	✓	-	✓	-	-	-	-	-	-	-	-	-	-
7	Utility	✓	✗	✗	✓	✓	-	-	-	✗	-	-	-	-
8	Other													
9	Other													
Remarks		1) kitchen platform was not provided, utility cleaning work was poor.												

Quality Control Check Repot. Stage: After Finishing Stage II (Apartments)

Flooring & painting		Rate the quality of (Good ✓, Avg. ✗, Poor – needs correction ✗✗, NA)												
S No	Room	Color variation of floor tiles	Flooring workmanship & grouting	Skirting size (3")	Skirting workmanship	Plastering above skirting	Plastering & finishing of walls	Crack filling	Loft Finishing	Windows check	General quality of painting & finishing	Door & frame painting quality	Door beading, luppam and painting quality.	Edge building
1	Bedroom 1 M. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✗	✓	✓	✓	✗
2	Bedroom 2 K. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 3	-	-	-	-	-	-	-	-	-	-	-	-	-
4	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Dining	✓	✓	✓	✓	✓	✓	✓	✓	-	✓	-	-	✗
6	Lobby-1	-	-	-	-	-	-	-	-	-	-	-	-	-
7	Utility / balcony 1	✓	✓	-	-	-	✓	✓	-	-	✓	✓	✓	✗
8	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	-	-	✓	✓	✓	✗✗
9	Utility / balcony 3	-	-	-	-	-	-	-	-	-	-	-	-	-
10	Kitchen	✓	✓	✓	✓	✓	✓	✓	✗	✗	✓	-	-	✗✗
11	Other													
12	Other													
Remarks		1) Utility lock was provided in Reverse position												

Quality Control Check Report. Stage: After Plumbing & Electrical (Apartments)

Flat No.	A-322	Other	—	Sl. No.	40840
Company	MRGV	Project	BRGV	Phase	—
Prepared by	R.S. SAIKIRAN	Sign	R.S. Saikiran	Date	18-11-2022
Project Manager	MALLIKARJUN	Sign	Mallikarjun	Date	18-11-2022
Previous stage report no.	40721	Report filed and signed by PM?		☒ Yes ☐ No	
Additions & alterations sheet date	10-03-2022	All pages signed by engineer & customer?		☒ Yes ☐ No	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.					

Inspection should be done after:

- after cleaning the apartment.
- before starting painting, tiling & flooring.
- electrical conduct, waterproofing & plumbing work is completed (for stage II only).
- additions & alterations is finalized and signed. In case there are no additions and alterations printout of email by PM to CR confirming the same must be filed.
- additions & alterations sheets to be transferred to QC file. QC to check if A&A are made as per request.

After Plumbing & Electrical Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. Location of CPVC & PVC fittings must be checked as per measurements given in circular. Tolerance 1".
6. Location, height and spirit level of electrical points must be checked as per measurements given in circular & plan. Tolerance 1".
7. Civil work near pipes in balcony & utility must be neat and mortar should be removed from the pipes.
8. Water proofing must cover all pipes & check height above SFL.
9. Fasteners must be used as specified in circular. Especially check fixing of PVC pipes.
10. Height of DB box must be 6" below false ceiling level or 12" below slab level.
11. In case of many changes in civil work, electrical work and plumbing work, a new drawing must be prepared at HO and approved by MD.

Quality Control Check Report. Stage: After Plumbing & Electrical (Apartments)

S No	Room	Civil work near pipes in balcony & utility ⁷ (✓ or ✕)	CPVC & PVC Check ⁵ (✓ or ✕)	Electrical points check ⁶ (✓ or ✕)	Water proofing check ⁸ (✓ or ✕)	Proper use of fasteners check ⁹ (✓ or ✕)	Placement of DB ¹⁰ (✓ or ✕)	Placement of Generator changeover (✓ or ✕)
1	Bedroom 1 M. Bed	—	—	✓	—	—	—	—
2	Toilet 1 M. Toi	—	✓	✓	✓	—	—	—
3	Bedroom 2 G. Bed	—	—	✓	—	—	—	—
4	Toilet 2 C. Toi	—	✓	✓	✓	—	—	—
5	Bedroom 3	—	—	—	—	—	—	—
6	Toilet 3	—	—	—	—	—	—	—
7	Drawing	—	—	✓	—	—	✓	—
8	Dining	—	—	—	—	—	—	—
9	Lobby 1	—	—	—	—	—	—	—
10	Utility / balcony 1	✕	✓	✓	—	✕	—	—
11	Utility / balcony 2	✓	✓	✓	✓	✕	—	—
12	Utility / balcony 3	—	—	—	—	—	—	—
13	Kitchen	—	✓	✓	—	—	—	—
14	Other							
15	Other							
Remarks NOTE:- (1) level marking was not done.								
(2) In Drawing, The light point was missed.								
Remarks on additions & alteration sheet:								
Signed by engineer,		☒ Yes ☐ No		Signed by customer,		☒ Yes ☐ No		
Revised drawing required from HO		☐ Yes ☐ No —		Approved revised drawing attached		☐ Yes ☐ No —		

Quality Control Check Repot. Stage: After Plumbing & Electrical (Apartments)

Miscellaneous check

Screeding done on walls upto 12" outside bathroom/utility	☒ Yes ☐ No
Bathroom /utility filled with 4" water for water proof check	☒ Yes ☐ No
Hole packing done around all pipes in ceiling and internal walls	☐ Yes ☒ No
Remarks:	

Quality Control Check Report. Stage: After Plumbing & Electrical (Apartments)

Flat No.	A-322	Other	—	Sl. No.	40840
Company	MRGV	Project	BRGV	Phase	—
Prepared by	R.S. SAIKIRAN	Sign	R.S. Saikiran	Date	18-11-2022
Project Manager	MALLIKARJUN	Sign	Mallikarjun	Date	18-11-2022
Previous stage report no.	40721	Report filed and signed by PM?		☒ Yes ☐ No	
Additions & alterations sheet date	10-03-2022	All pages signed by engineer & customer?		☒ Yes ☐ No	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.					

Inspection should be done after:

- after cleaning the apartment.
- before starting painting, tiling & flooring.
- electrical conduct, waterproofing & plumbing work is completed (for stage II only).
- additions & alterations is finalized and signed. In case there are no additions and alterations printout of email by PM to CR confirming the same must be filed.
- additions & alterations sheets to be transferred to QC file. QC to check if A&A are made as per request.

After Plumbing & Electrical Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. Location of CPVC & PVC fittings must be checked as per measurements given in circular. Tolerance 1".
6. Location, height and spirit level of electrical points must be checked as per measurements given in circular & plan. Tolerance 1".
7. Civil work near pipes in balcony & utility must be neat and mortar should be removed from the pipes.
8. Water proofing must cover all pipes & check height above SFL.
9. Fasteners must be used as specified in circular. Especially check fixing of PVC pipes.
10. Height of DB box must be 6" below false ceiling level or 12" below slab level.
11. In case of many changes in civil work, electrical work and plumbing work, a new drawing must be prepared at HO and approved by MD.

Quality Control Check Report. Stage: After Plumbing & Electrical (Apartments)

S No	Room	Civil work near pipes in balcony & utility ⁷ (✓ or ✕)	CPVC & PVC Check ⁵ (✓ or ✕)	Electrical points check ⁶ (✓ or ✕)	Water proofing check ⁸ (✓ or ✕)	Proper use of fasteners check ⁹ (✓ or ✕)	Placement of DB ¹⁰ (✓ or ✕)	Placement of Generator changeover (✓ or ✕)
1	Bedroom 1 M. Bed	—	—	✓	—	—	—	—
2	Toilet 1 M. Toi	—	✓	✓	✓	—	—	—
3	Bedroom 2 G. Bed	—	—	✓	—	—	—	—
4	Toilet 2 C. Toi	—	✓	✓	✓	—	—	—
5	Bedroom 3	—	—	—	—	—	—	—
6	Toilet 3	—	—	—	—	—	—	—
7	Drawing	—	—	✓	—	—	✓	—
8	Dining	—	—	—	—	—	—	—
9	Lobby 1	—	—	—	—	—	—	—
10	Utility / balcony 1	✕	✓	✓	—	✕	—	—
11	Utility / balcony 2	✓	✓	✓	✓	✕	—	—
12	Utility / balcony 3	—	—	—	—	—	—	—
13	Kitchen	—	✓	✓	—	—	—	—
14	Other							
15	Other							
Remarks NOTE:- (1) level marking was not done.								
(2) In Drawing, The light point was missed.								
Remarks on additions & alteration sheet:								
Signed by engineer,		☒ Yes ☐ No		Signed by customer,		☒ Yes ☐ No		
Revised drawing required from HO		☐ Yes ☐ No —		Approved revised drawing attached		☐ Yes ☐ No —		

Quality Control Check Repot. Stage: After Plumbing & Electrical (Apartments)

Miscellaneous check

Screeding done on walls upto 12" outside bathroom/utility	☒ Yes ☐ No
Bathroom /utility filled with 4" water for water proof check	☒ Yes ☐ No
Hole packing done around all pipes in ceiling and internal walls	☐ Yes ☒ No
Remarks:	

Quality Control Check Report. Stage: After Plumbing & Electrical (Apartments)

Flat No.	A-322	Other	—	Sl. No.	40840
Company	MRGV	Project	BRGV	Phase	—
Prepared by	R.S. SAIKIRAN	Sign	R.S. Saikiran	Date	18-11-2022
Project Manager	MALLIKARJUN	Sign	Mallikarjun	Date	18-11-2022
Previous stage report no.	40721	Report filed and signed by PM?		☒ Yes ☐ No	
Additions & alterations sheet date	10-03-2022	All pages signed by engineer & customer?		☒ Yes ☐ No	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.					

Inspection should be done after:

- after cleaning the apartment.
- before starting painting, tiling & flooring.
- electrical conduct, waterproofing & plumbing work is completed (for stage II only).
- additions & alterations is finalized and signed. In case there are no additions and alterations printout of email by PM to CR confirming the same must be filed.
- additions & alterations sheets to be transferred to QC file. QC to check if A&A are made as per request.

After Plumbing & Electrical Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. Location of CPVC & PVC fittings must be checked as per measurements given in circular. Tolerance 1".
6. Location, height and spirit level of electrical points must be checked as per measurements given in circular & plan. Tolerance 1".
7. Civil work near pipes in balcony & utility must be neat and mortar should be removed from the pipes.
8. Water proofing must cover all pipes & check height above SFL.
9. Fasteners must be used as specified in circular. Especially check fixing of PVC pipes.
10. Height of DB box must be 6" below false ceiling level or 12" below slab level.
11. In case of many changes in civil work, electrical work and plumbing work, a new drawing must be prepared at HO and approved by MD.

Quality Control Check Report. Stage: After Plumbing & Electrical (Apartments)

S No	Room	Civil work near pipes in balcony & utility ⁷ (✓ or ✕)	CPVC & PVC Check ⁵ (✓ or ✕)	Electrical points check ⁶ (✓ or ✕)	Water proofing check ⁸ (✓ or ✕)	Proper use of fasteners check ⁹ (✓ or ✕)	Placement of DB ¹⁰ (✓ or ✕)	Placement of Generator changeover (✓ or ✕)
1	Bedroom 1 M. Bed	—	—	✓	—	—	—	—
2	Toilet 1 M. Toi	—	✓	✓	✓	—	—	—
3	Bedroom 2 G. Bed	—	—	✓	—	—	—	—
4	Toilet 2 C. Toi	—	✓	✓	✓	—	—	—
5	Bedroom 3	—	—	—	—	—	—	—
6	Toilet 3	—	—	—	—	—	—	—
7	Drawing	—	—	✓	—	—	✓	—
8	Dining	—	—	—	—	—	—	—
9	Lobby 1	—	—	—	—	—	—	—
10	Utility / balcony 1	✕	✓	✓	—	✕	—	—
11	Utility / balcony 2	✓	✓	✓	✓	✕	—	—
12	Utility / balcony 3	—	—	—	—	—	—	—
13	Kitchen	—	✓	✓	—	—	—	—
14	Other							
15	Other							
Remarks NOTE:- (1) level marking was not done.								
(2) In Drawing, The light point was missed.								
Remarks on additions & alteration sheet:								
Signed by engineer,		☒ Yes ☐ No		Signed by customer,		☒ Yes ☐ No		
Revised drawing required from HO		☐ Yes ☐ No —		Approved revised drawing attached		☐ Yes ☐ No —		

Quality Control Check Repot. Stage: After Plumbing & Electrical (Apartments)

Miscellaneous check

Screeding done on walls upto 12" outside bathroom/utility	☒ Yes ☐ No
Bathroom /utility filled with 4" water for water proof check	☒ Yes ☐ No
Hole packing done around all pipes in ceiling and internal walls	☐ Yes ☒ No
Remarks:	

Quality Control Check Repot. Stage: After Brickwork (Apartments/ Lab Spaces)

Flat No.	A - 322	Others		Sl. No.	40107
Company	MRGV	Project	BRGV	Phase	-
Prepared by	K. Sneha	Sign	Sneha	Date	24/06/22
Project Manager	Sarwar	Sign	Sarwar	Date	24/06/22
Previous Stage report no.		38156	Report filed and signed by PM?		☒ Yes ☐ No
Apartment No.		Other		other	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.					

Inspection should be done after:

- brickwork is completed
- chicken mesh fixed
- after cleaning the apartment
- electrical conducting work is completed

Brickwork Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✕ for minor mistake that requires minor correction.
3. Mark ✕✕ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✕✕✕ for major mistake that cannot be corrected.
5. Wall thickness should be as per plan. Use of 4", 6" & 8" blocks must be checked.
6. All walls should have 2 beds of about 2" to 3" thickness with one no. 6 mm or 8 mm rod with M15 CC.
7. Chicken mesh should be used in each and every joint between RCC & Brickwork.
8. Joint between brickwork & beam on external side must be filled.
9. Check room dimensions with working plan. (Tolerance: 1")
10. Diagonals of each room shall be equal. (Tolerance: 2")
11. Balcony sill level should be 3'3" from SFL. (Tolerance: 1")
12. Check room height with specified height. (Tolerance: 1")
13. Check plumb of walls wherever it appears to be out of plumb. (Tolerance: 1/2")
14. Specify the No. of beams which are not aligned by more than 1" in a room.
15. Door frames must have black Japan coating and wood primer /pellambar – at cost of painter.

Quality Control Check Report.

Stage: After Brickwork (Apartments/ Lab Spaces)

S No	Room	Wall thickness (✓ or ✗)	Beds in walls (✓ or ✗)	Chicken mesh (✓ or ✗)	External brickwork & beam joint (✓ or ✗)	Room Dimensions (✓ or ✗)	Room Dimensions Difference in inches	Diagonal (✓ or ✗)	Diagonal Difference in inches	Balcony sill level (✓ or ✗)	Room Height (✓ or ✗)	Plumb of walls (Good/Avg./Bad)	Alignment of beams and walls - Nos.
1	Bedroom 1 m. Bed	✓	✗✗	✓	✓	✓	-	✓	-	-	✓	Avg	✓
2	Toilet 1 m. Toi	✓	✓	✓	✓	✓	-	✓	-	-	✓	"	✓
3	Bedroom 2 r. Bed	✓	✓	✓	✓	✓	-	✓	-	-	✓	"	✓
4	Toilet 2 c. Toi	✓	✓	✓	✓	✓	-	✓	-	-	✓	"	✓
5	Bedroom 3	-	-	-	-	-	-	-	-	-	-	-	-
6	Toilet 3	-	-	-	-	-	-	-	-	-	-	-	-
7	Drawing	✓	✓	✓	✓	✓	-	✓	-	-	✓	"	✓
8	Dining	-	-	-	-	-	-	-	-	-	-	-	-
9	Lobby 1	-	-	-	-	-	-	-	-	-	-	-	-
10	Utility / balcony 1	✓	✓	✓	✓	✓	-	✓	-	✓	✓	Avg	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	-	✓	-	-	✓	"	✓
12	Utility / balcony 3	-	-	-	-	-	-	-	-	-	-	"	-
13	Kitchen	✓	✓	✓	✓	✓	-	✓	-	-	✓	-	✓
14	Other												
15	Other												
Remarks													
Note: 1. In Master toilet, Z-Angle template was not provided													
As per drawing.													

Quality of edges and corners in all rooms?	☐ Good ☒ Avg. ☐ Bad
Specify rooms that need correction: -	

Misc. Checks.

Was 3.75 CFT proportion box provided?	☒ Yes ☐ No
Condition of proportion box?	☐ Good ☒ Avg. ☐ Bad
Was the Apartment cleaned before starting brick work?	☐ Yes ☐ No ☒ Cant' say
Is the Apartment cleaned for plastering?	☒ Yes ☐ No
Wastage?	☐ High ☒ Medium ☐ Low
Storage of building material like bricks sand and cement.	☐ Good ☒ Avg. ☐ Bad
Drum (200 ltrs) provided for curing in each flat?	☒ Yes ☐ No
Remarks:	

Door Frames & Windows check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✕ for minor mistake that requires minor correction.
3. Mark ✕✕ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✕✕✕ for major mistake that cannot be corrected.
5. Window template depth should be between 2 to 2 ½" after plastering.
6. Lintel level should be 7'3" from SFL & 7' from FFL. (Tolerance 1"). Lintel should be as per standard design.
7. Lofts should be at a height of 7' to 7'3" from FFL. Kitchen platform thickness should be 2", SFL to bottom 31".. (Tolerance 1")
8. Slopes of lofts and kitchen platforms to be checked by using 12" spirit level and check height from floor from 2 or 3 points.
9. Thickness of platforms & lofts should be between 2 & 2.5".
10. Provide single layer table brick at bottom of each door frame without threshold.
11. Check Z angle template size (Z angle for bathroom ventilators not required in new projects).
12. Window opening must be checked with MS square pipe templates of 2 sizes for inner and outer openings.
13. Z angle template must be 1" from brick wall surface from the inner side.

Quality Control Check Report.

Stage: After Brickwork (Apartments/ Lab Spaces)

S No	Room	Door size, face and position (✓ or ✗)	Brick at bottom of door frame 10 (✓ or ✗)	Door frame hold fast provision and fasteners. (✓ or ✗)	Door lintel design & level (✓ or ✗)	Door diagonal check (✓ or ✗)	Door Plumb - two sides (✓ or ✗)	Windows lintel design & level. Sill level (✓ or ✗)	Windows size (✓ or ✗)	Windows - template depth & diagonal (✓ or ✗)	Windows - template red oxide painting (✓ or ✗)	Loft & Kitchen platform height (✓ or ✗)	Loft & Kitchen platform slope (✓ or ✗)	Door size, face and position (✓ or ✗)
1	Bedroom 1 m. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 m. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 k. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 c. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3	-	-	-	-	-	-	-	-	-	-	-	-	-
6	Toilet 3	-	-	-	-	-	-	-	-	-	-	-	-	-
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	-	-	-	-	-	-	-	-	-	-	-	-	-
9	Lobby 1	-	-	-	-	-	-	-	-	-	-	-	-	-
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	-	-	-	-	-	-	-
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	-	-	-	-	-	-	-
12	Utility / balcony 3	-	-	-	-	-	-	-	-	-	-	-	-	-
13	Kitchen	-	-	-	-	-	-	✓	✓	✓	✓	✓	-	-
14	Other													
15	Other													
	Remarks: Note: 1. Loft hatching was not done.													
	2. Kitchen platform were not casted.													


**Construction division
Additions & Alteration Charges Approval Form**

Company Name		MIRGV	Site	MIRGV
Name of Customer		Stanley Perera		
Villa Plot No		322		
S/ No	Description			Amount
1	Total extra charges			3,850
2	Total refundable amount			Nil
3	Net amount to be charges (if any)			3,850
4	Net amount to be refunded (if any)			Nil

Remarks

Approved by Project Manager	Approved by Design Team	Approved by M.D.
Date	Date:	Date:
Sign	Sign:	Sign:

Notes: 1. The above mentioned amount is an estimate sheet. 2. Send scanned copy by email to plans@modiproperties.com & CR. 3. Maintain a proper file of customers at site.



ESTIMATE SHEET

Company Name

Project

Work Description

1 no

Prepared By

Date

S No Item Head

Refund charges

MARKET
HIGLY
Extra Spec
Sample Permit-122
Sawari
11-10-2024

Item Description

Extra charges

Flooring(8" x4')

Specialty Tile

1
2
3
4
5

Amount in words:- Seven Thousand Three Hundred fifty Rupees only

Grand Total Extra charges(B-A)

Total Amount -B

Total Amount -A

SFT

110.00

35.00

3.850

3.850

3.850

Approved by
Nign

Amount Item Head Total

TABLE 1

Inventory
Work Description
no
Inspected by
Date

TABLE
BROV
Lead Spots
Steady Picking 122
Survey
11.10.2024

Item Head
No

Item & Qty

Account No

MASIR BIRAJ (M) PVT. LTD.

Approved by		Length	Width	Height	Nos	Quantity	Units	Item Head Code
		11.00	10.00	1.00	1.00	110.00	SFT	

31/03/2023, 16:36

Yahoo Mail - RCC kitchen platform

RCC kitchen platform

From: stanly pereira (stanleypereira@hotmail.com)

To: jeevana@modiproperties.com

Date: Tuesday, March 14, 2023 at 01:20 PM GMT +5:30

Hi

This is in regards to my flat no 322 at Bloomdale residency.
Please construct kitchen as per standard fitment.

Regards
Stanly Pereira

BIOMODAL

Real Estate & Property

Modi Realty Pvt. Ltd.

Modi Realty Pvt. Ltd. 25, Phosun Road,

Chennai 600 006, India

Modi Realty Pvt. Ltd. 25, Phosun Road,

Chennai 600 006, India

MODI
PROPERTIES

Modi Realty Pvt. Ltd. 25, Phosun Road,

Chennai 600 006, India

Modi Realty Pvt. Ltd. 25, Phosun Road,

To,

Mt. Stanley Perera,

S/o Mr. Subramanian Perera,

14 No 302, Silver Oak Bangalore,

Phase 3, Chertepally, Hyderabad

Dear Sir/Madam,

If you wish to make any minor additions or alterations to the flat that you have purchased, we request you to visit the site during office hours between 09.00 AM to 05.00 PM. We also request you to finalize details like color of walls, etc., during your visit to the site. Our engineers will make note of these details.

For your convenience we request you to take prior appointment so that our engineers can give you their undivided attention. You may contact Mr. C. Subham Babu (Asst. Project Manager) on +91-9100036740 or Mr. Puspala (Asst. Engineer) on +91-984942924 by email at bigv_const@modiproperties.com

In case you fail to contact us during the above mentioned period, we shall assume that no changes are required, and your flat will be completed as per the standard specifications shown on the model flat.

Thank You.

Yours Sincerely,

For Modi Realty Genome Valley LLP.



Please refer to the notes attached herein.

Notes

1. Working drawings, electrical layout & plumbing drawing for your flat have been enclosed for your reference.
2. Select materials that you may choose to provide like tiles, sinks, CP and sanitary ware, etc. must be handled over at our site within 4 weeks of completion of brickwork and internal plastering.
3. Changes to external appearance and colour shall not be permitted. Changes to colour of doors/dorm frames in balcony/main entrance shall not be permitted. Change in colour of balcony walls shall not be permitted.
4. Fixing of grills & gates to the main door / balcony shall not be permitted.
5. Changes in walls, door positions or other structural changes shall not be permitted.
6. You may provide your own flooring tiles, bathroom tiles, CP & sanitary fittings and they shall be installed by us.
7. Additional shelves & lofts shall not be permitted.
8. Charges & refunds will be as follows:

No charge for:

1. Choice of two free colors for walls;
2. Choice of two/three combinations for bathroom tiles.

Non standard items to be supplied by the buyer & installed free of cost:

1. Hardware.
2. CP & Sanitaryware.
3. Flooring tiles
4. Kitchen platform - granite / marble.
5. Bathroom tiles.

Extra charges shall be payable for:

1. Extra electrical points / switch boards / sockets / switches.
2. Additional kitchen platform with granite & dado.
3. Rounding / polishing of granite platform.
4. Exhaust hole in bathroom/kitchen.

Refund / charges for upgrade or downgrade or substitutions shall be applicable for:

1. Kitchen & bathroom tiles.
2. Flooring tiles.
3. CP fittings.
4. Sanitaryware & bathtubs.
5. Doors & hardware.
6. Kitchen sink.
7. Civil work.
8. Electrical switches.
9. Kitchen platform

No refunds shall be made for:

1. Kitchen platform.
2. Civil work.

**MODI
PROPERTIES**

1. The first part of the document is a list of names and addresses, which appears to be a directory or a list of contacts. The names are written in a cursive script, and the addresses are listed below them.

1870-1871. The first year of the war. The first year of the war. The first year of the war.

1870

[Faint vertical text or markings]

卷之四
 四
 五
 六
 七
 八
 九
 十
 十一
 十二
 十三
 十四
 十五
 十六
 十七
 十八
 十九
 二十
 二十一
 二十二
 二十三
 二十四
 二十五
 二十六
 二十七
 二十八
 二十九
 三十
 三十一
 三十二
 三十三
 三十四
 三十五
 三十六
 三十七
 三十八
 三十九
 四十
 四十一
 四十二
 四十三
 四十四
 四十五
 四十六
 四十七
 四十八
 四十九
 五十
 五十一
 五十二
 五十三
 五十四
 五十五
 五十六
 五十七
 五十八
 五十九
 六十
 六十一
 六十二
 六十三
 六十四
 六十五
 六十六
 六十七
 六十八
 六十九
 七十
 七十一
 七十二
 七十三
 七十四
 七十五
 七十六
 七十七
 七十八
 七十九
 八十
 八十一
 八十二
 八十三
 八十四
 八十五
 八十六
 八十七
 八十八
 八十九
 九十
 九十一
 九十二
 九十三
 九十四
 九十五
 九十六
 九十七
 九十八
 九十九
 一百

Flial No	322	Type	Deluxe / Semi-Deluxe
Buyer Name	Mr. Stanley Pereira.	Email	Stanley Pereira C
Phone No.	9866654420		

Buyers sign	Engg. Sign	
Date:	Date	

1. Colour shades of paints may vary from batch to batch & company to company. The Builder will not take responsibility of quality of work for dark shades especially green & blue.
2. Shade / colour of natural material like marble and granite can't be guaranteed and may vary from lot to lot. Cracks like appearance in marble is a natural feature and Builder shall not be responsible for repairs or replacement.
3. Availability of bathroom or flooring tiles of the same type /colour/make can not be guaranteed and closest possible type/colour/make may be used in its place.
4. No further change shall be permitted from this day.
5. Please sign on all pages.

① Same as Corp

Changes in flooring:

- ① H. Red Room Cuban wood. 4th only (natural)
(next as per company) 2' x 2'
Kitchen - country almond

/

Holmes

Dir 10/3/22

① kitchen (2m x 2m x 2m)

② 1m x 1m x 1m

③ 1m x 1m x 1m

④ 1m x 1m x 1m

⑤ 1m x 1m x 1m

⑥

Choice of Bathroom tiles, CP fittings & Sanitary ware:

① ~~1m x 1m x 1m~~ 1m x 1m x 1m

② C.T. 1m x 1m x 1m

③ In Master Toilet flooring tiles should be 800 x 800 mm

④ C Toilet and M. toilet → both are ultra sprinkle tiles.

Changes in kitchen platform: (mark on plan)

① no change.

22/10/22

22/10/22

22/3/01

Atuluck

(Miles / hours)

Typical Plan - P-1



Direction

Description


(Number & Description)

Small Details (Number & Description)

Reference to


Section

Notes

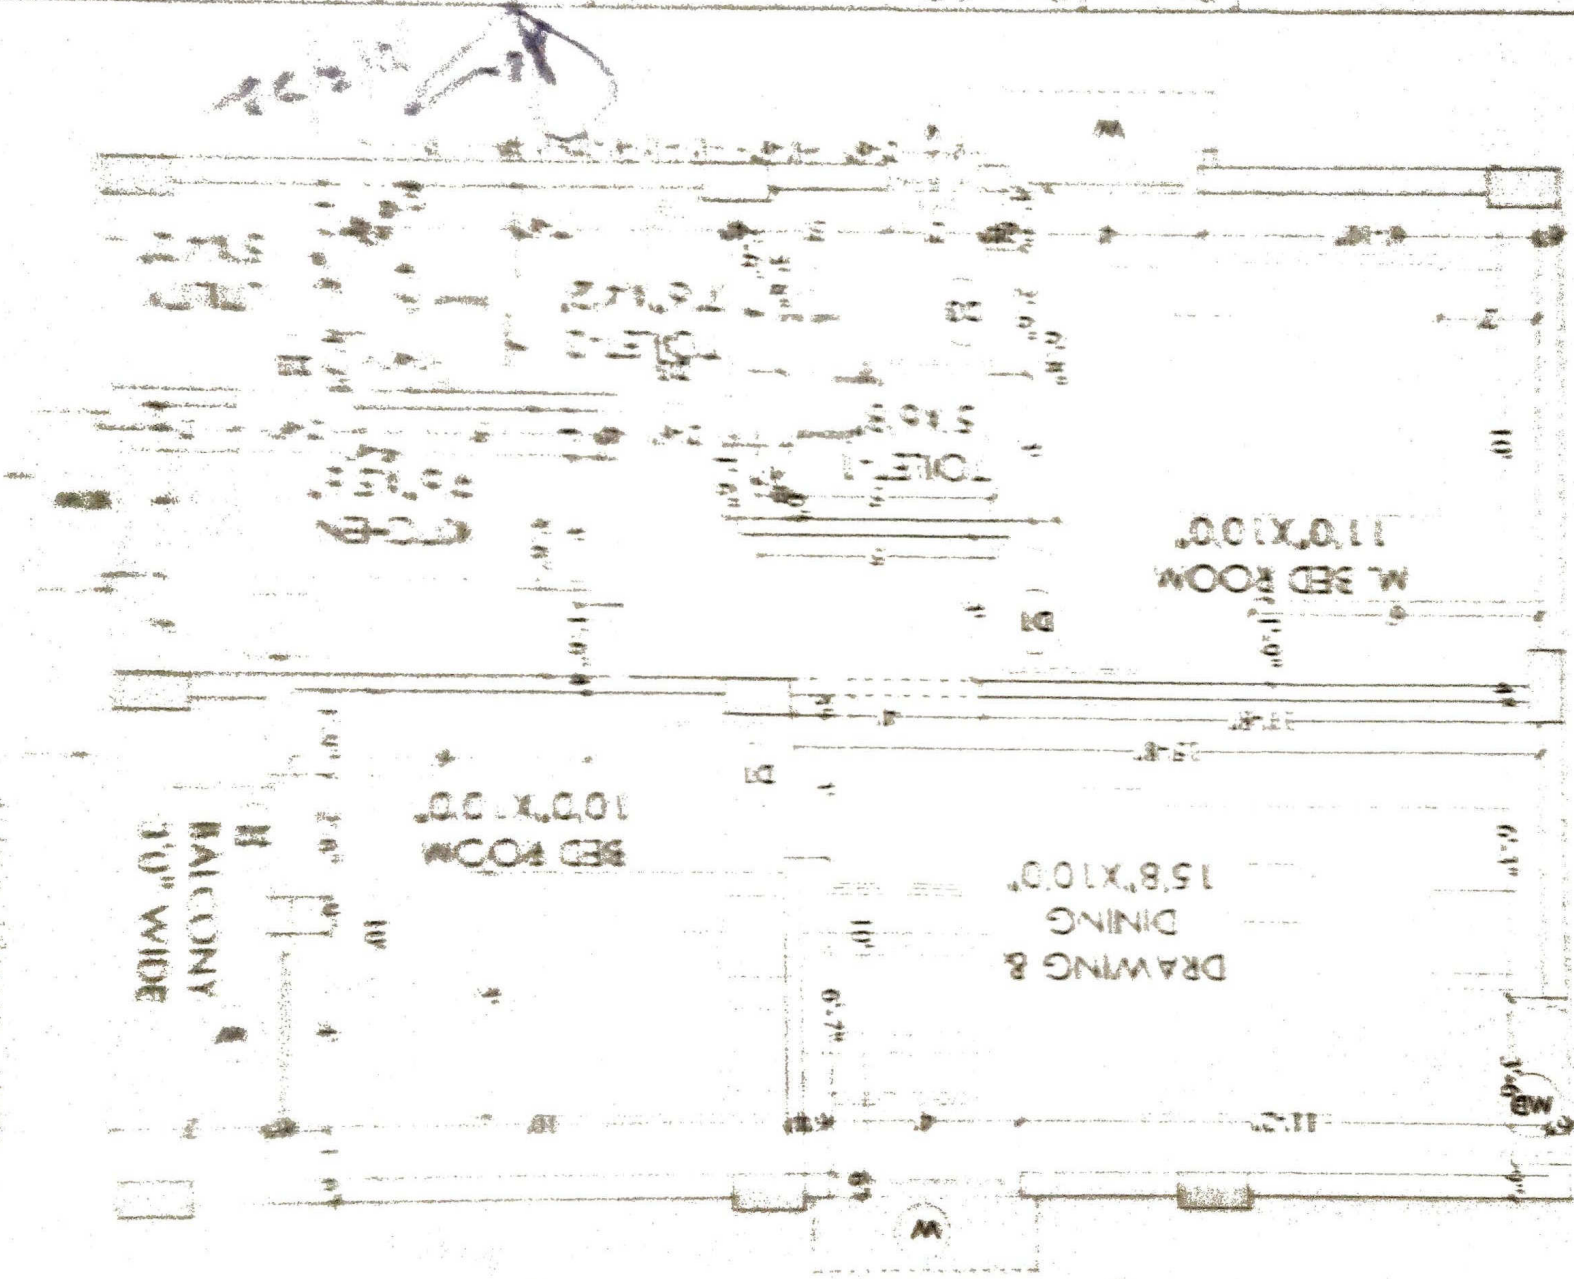

1. Living Room (15'0" x 10'0")
2. Dining Room (15'8" x 10'0")
3. Kitchen (11'0" x 10'0")
4. Bedroom (10'0" x 10'0")
5. Bathroom (6'0" x 6'0")
6. Balcony (10'0" wide)
7. Front Porch (6'0" x 10'0")

Description		Direction	Owners & Developers :			
Plumbing plan		N	Modi Realty Genome Valley LLP			
West Facing			Project Name & Phase :			
			BRGV			
			Scale :			
			Approved By : Soham Modi			
			Prepared By : Imran			
			Date : 24.09.2021			
			Promoted by			
			Modi Properties Pvt Ltd			
			N.T.S			
			Phone+91-40-66335551			

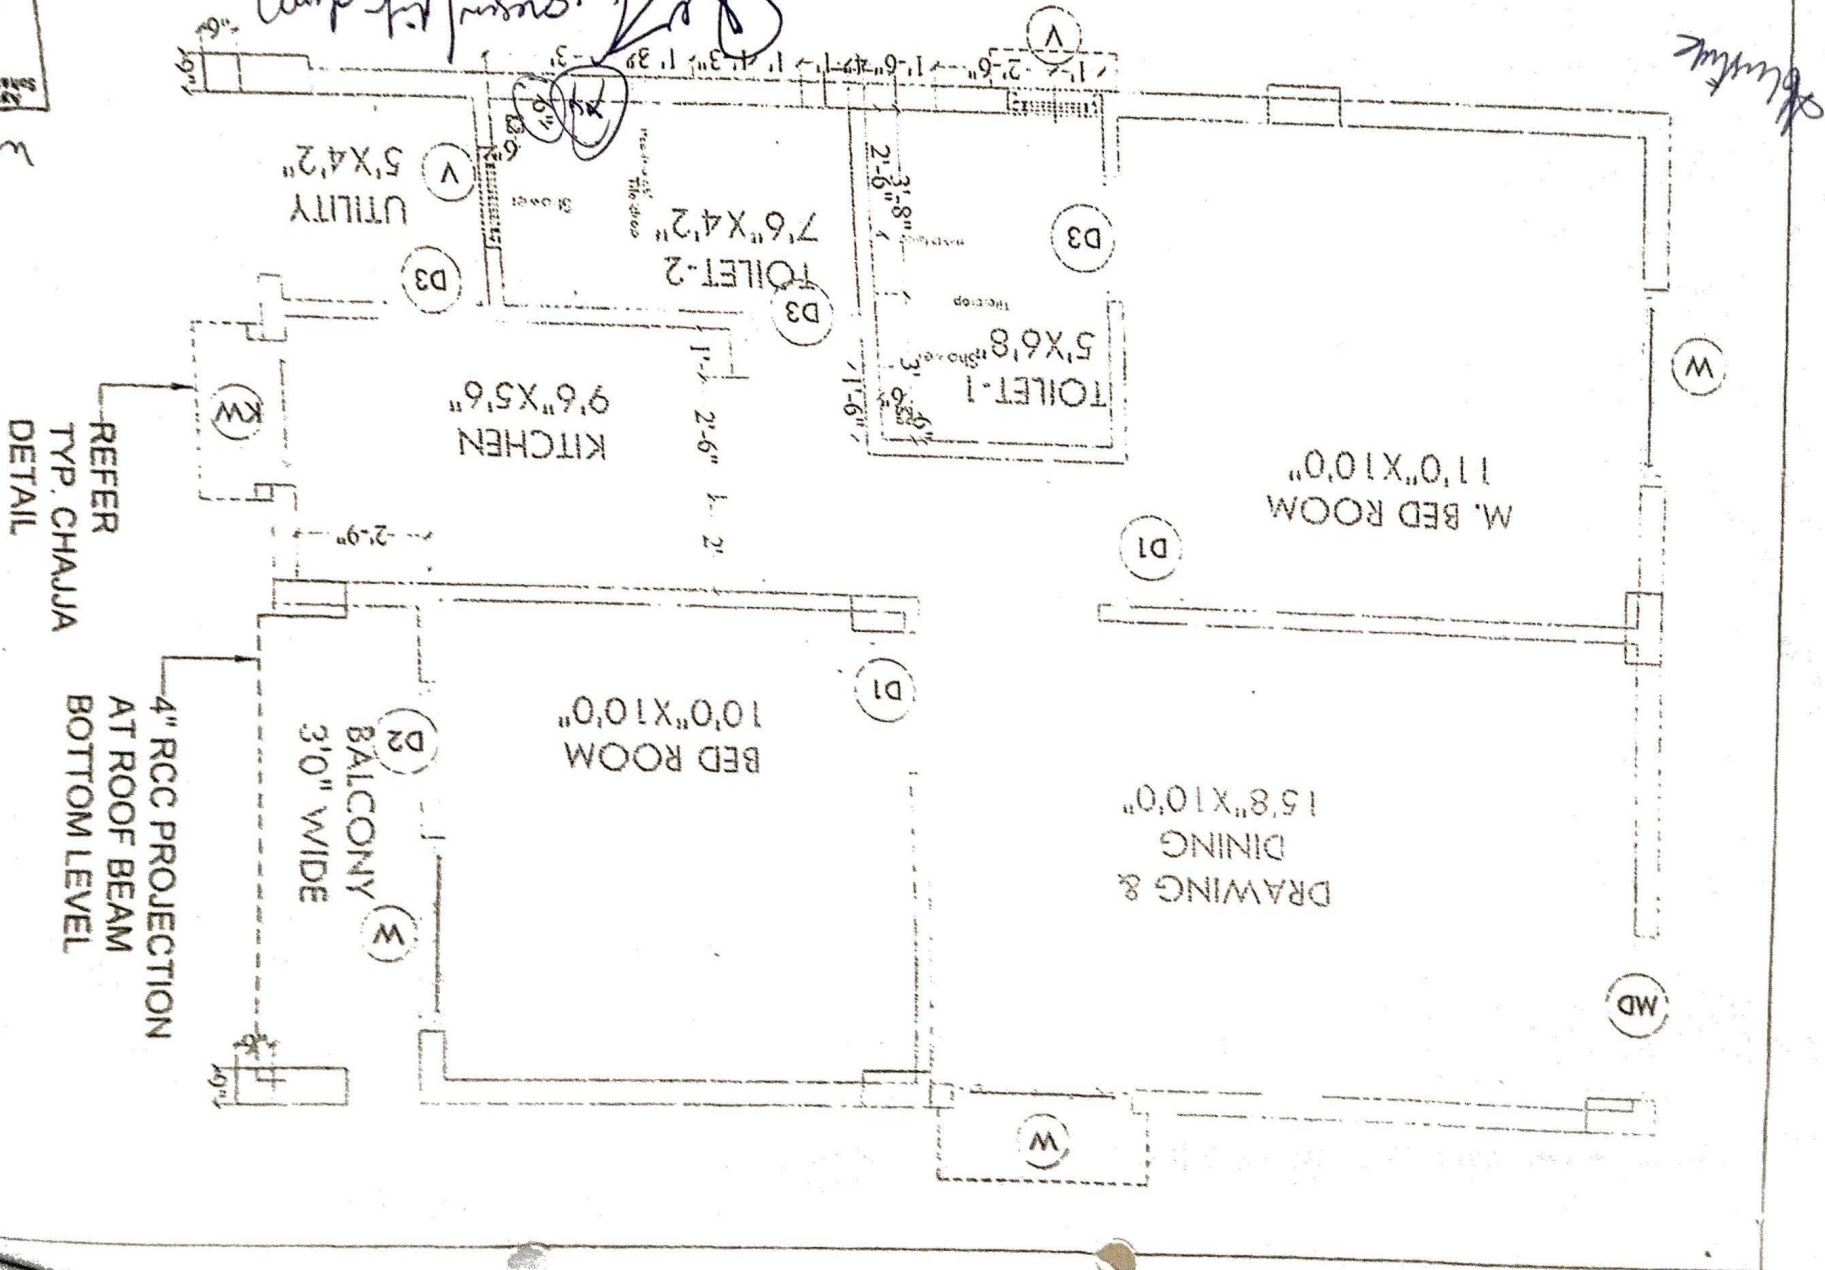

Approved for Construction
Soham Modi, Managing Dir.
14 SEP 2021
□ Original
□ Copy
Plan to Ref.

FLAT NOS. 112, 114, 116, 118, 120 & 122

ELECTRICAL PLAN



Direction
N

Owner & Developers

Mod. Realty Consume Valley LLP

Regd. No.

25.07.2001

Page No.

Project Name & Phase

Adm. Bldg.


25.07.2001

Scale

1:100

Handwritten signature

Handwritten signature

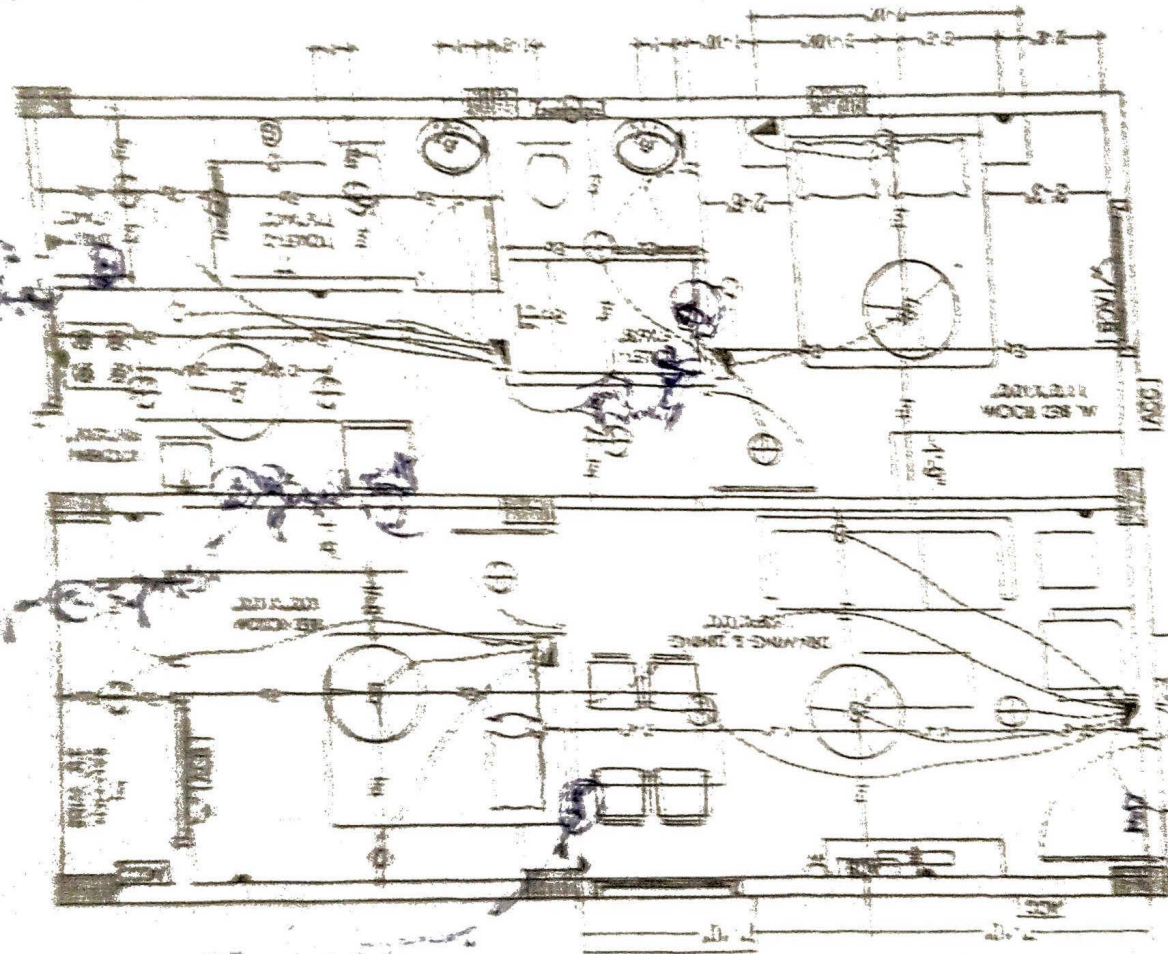

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32	33	34	35	36	37	38	39	40	41	42	43	44	45	46	47	48	49	50	51	52	53	54	55	56	57	58	59	60	61	62	63	64	65	66	67	68	69	70	71	72	73	74	75	76	77	78	79	80	81	82	83	84	85	86	87	88	89	90	91	92	93	94	95	96	97	98	99	100
---	---	---	---	---	---	---	---	---	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	-----

Handwritten signature
