


Construction Division
Additions & Alteration Charges Approval Form

Company Name:		MRMLLP	Site	Gulmohar Residency
Name of the customer		Y. Subash. XXXX		
Villa/ Flat No.		H-101.		
Sl.No	Description	Amount		
1	Total extra Charges	37241		
2	Total refundable amount	3040		
3	Net amount to be charges (if any)	34201		
4	Net amount to be refunded (if any)	—		
Remarks : Thirty four thousand Two hundred and one Rupees only.				
Approved by Project Manager		Approved by Design Team		Approved by MD
Date 17/06/24.		Date		Date
Sign: 		Sign:		Sign:

Note: 1. Enclose measurement & estimate sheet. 2. Send scanned copy by email to plans@modiproperties.com & CR. 3. Maintain originals in A&A of customers at site.

ATR on Quality Control Check Report, (Apartments)

Flat No	H-101	QC report stage	—	Sl. No.	42905
Company	MRMLLP	Project	GMR	Phase	—
Prepared by	P. Vithalrao	Sign	<i>P. Vithalrao</i>	Date	09/05/24
Project Manager	Sainivas	Sign	<i>Sainivas</i>	Date	09/05/24
Receipt by QC date		Sign		Other	
Receipt at HO date		Sign		Other	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No
Recommendation that was made by QC: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team					

Notes:

1. Attach a copy of the QC report to this sheet.
2. Circle each correction with a red pen – tick (✓) each circle for work completed and cross (X) each circle where work has not been completed.
3. Give remarks for each case where work has not completed on this sheet.
4. Make 2 copied of the ATR – send one to MD and other to QC.
5. Enclose required photographs – hard copy.

Remarks:	work completed

Quality Control Check Report.

Stage: After Finishing Stage III (Apartments)

Flat No	H-101.	Other		Sl. No.	42905
Company	MRM-LLP	Project	GMR.	Phase	
Prepared by	Saikrishna	Sign	Saikrishna	Date	25/04/24
Project Manager	Narendan	Sign		Date	25/04/24
Previous stage report no.			Report filed and signed by PM	☒ Yes ☐ No	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☐ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.					

Inspection should be done after:

- Completing stage II works
- Complete works like doors, windows, grills, electrical wiring, switches, french door glass, etc
- In case of modular kitchen provide platform, granite and dado and modular kitchen in this stage.
- Provide video door phone in this stage.
- Possession for wood work cannot be given until QC check for stage III is completed and all corrections mentioned in the report are made.

Miscellaneous check:


Modular kitchen to be provided	☒ Yes ☐ No	Modular kitchen provided	☐ Yes ☒ No
Modular kitchen workman ship	☐ Good ☐ Avg ☒ Poor	Modular kitchen granite & dado workman ship & finishing	☐ Good ☐ Avg ☒ Poor
Video door phone /wifi cam to be provided	☒ Yes ☐ No	Video door phone/wifi cam provided	☐ Yes ☒ No
Painting marks and drops are cleaned from floor, windows, walls.		☐ Good ☐ Avg ☒ Poor	

Quality Control Check Report.

Stage: After Finishing Stage III (Apartments)

Check Report.			Stage: After Finishing Stage III (Apartments)											
S No	Room		Rate the quality of (Good ✓, Avg X, Poor - needs correction XX, NA)											
			Door, door knob & door stopper fitting	Door, door knob & door stopper cleaning	Window grills & quality	Window grills fitting & finishing	Windows quality	Window fitting & finishing	Balcony railing quality & finishing	French door quality & fitting	CP jali quality and fitting	Edge building	Switch boards fitting & covering with plastic covers	Junction box covers painting
1	Bedroom 1	M.B	✓	✓	XX	X	✓	✓	✓	✓	✓	✓	✓	✓
2	Bedroom 2	G.B	✓	✓	XX	X	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 3	C.B	✓	✓	XX	X	✓	✓	✓	✓	✓	✓	✓	✓
4	Drawing		✓	✓	XX	X	✓	✓	✓	✓	✓	✓	✓	✓
5	Dining		✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Lobby		✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility + balcony 1		✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Utility / balcony 2		✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Utility + balcony 3		✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Kitchen		✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Toilet 1	M.S	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Toilet 2	C.T	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Toilet 3													
14	Other													
15	Other													
Remarks			NOTE 1) ✓ with out completion of stage-3 Bc wall wood works are slow 2) ✓ window frame fixing works are Pending. 3) ✓ Modular Kitchen works are Pending.											

Self
Quality Control Check Report. Stage: After Finishing Stage III (Apartments)

Flat No	H-101	Other	Stage III	SI No.	
Company	MMMLP	Project	GMR	Phase	
Prepared by	P. Nishaika	Sign		Date	24/04/24
Project Manager	Naseender	Sign		Date	24/04/24
Previous stage report no.		Report filed and signed by PM			☐ Yes ☐ No
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.					

Inspection should be done after :

- Completing stage II works.
- Complete works like doors, windows, grills, electrical wiring, switches, french door glass, etc.
- In case of modular kitchen provide platform, granite and dado and modular kitchen in this stage.
- Provide video door phone in this stage.
- Possession for wood work cannot be given until QC check for stage III is completed and all corrections mentioned in the report are made.

Miscellaneous check:

Modular kitchen to be provided	☐ Yes ☒ No	Modular kitchen provided	☐ Yes ☒ No
Modular kitchen workman ship	☐ Good ☒ Avg ☐ Poor	Modular kitchen granite & dado workman ship & finishing	☐ Good ☒ Avg ☐ Poor
Video door phone /wifi cam to be provided	☐ Yes ☒ No	Video door phone/wifi cam provided	☐ Yes ☒ No
Painting marks and drops are cleaned from floor, windows, walls.		☒ Good ☐ Avg ☐ Poor	

S No	Room	Rate the quality of (Good ✓, Avg X, Poor - needs correction XX, NA)											
		Door, door knob & door stopper fitting	Door, door knob & door stopper cleaning	Window grills & quality	Window grills fitting & finishing	Windows quality	Window fitting & finishing	Balcony railing quality & finishing	French door quality & fitting	CP job quality and fitting	Edge building	Switch boards fitting & covering with plastic covers	junction box covers painting
1	Bedroom 1 - H.B.	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Bedroom 2 - H.B.	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 3 - C.B.	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Utility - balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Utility - balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Toilet 1 - M/T	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Toilet 2 - C.T.	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other												
15	Other												
Remarks		Grills fixing customer scope, electrical work customer scope											

ATR on Quality Control Check Report. (Apartments)

Flat No	H-101	QC report stage	Stage - II	Sl. No.	42746
Company	NRMLLP	Project	GMR	Phase	-
Prepared by	Seinivas	Sign		Date	29/01/24
Project Manager	Narendar	Sign		Date	29/01/24
Receipt by QC date		Sign		Other	
Receipt at HO date		Sign		Other	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation that was made by QC:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team.

Notes:

1. Attach a copy of the QC report to this sheet.
2. Circle each correction with a red pen - tick (✓) each circle for work completed and cross (X) each circle where work has not been completed.
3. Give remarks for each case where work has not completed on this sheet.
4. Make 2 copied of the ATR - send one to MD and other to QC.
5. Enclose required photographs - hard copy.

Remarks:	Work Completed

Quality Control Check Report

Stage: After Finishing Stage II (Apartments)

Flat No	H-101	Other		SI No.	42746
Company	Mem-UP	Project	---	Phase	---
Prepared by	Sarkar	Sign	---	Date	27/6/2024
Project Manager	Abundant	Sign	---	Date	27/6/24
Previous stage report no.					
Checked By MD on		MD Sign		Report filed and signed by PM	☐ Yes ☒ No
Recommendation:				For filling	☐ Yes ☐ No
☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☐ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.					

Inspection should be done after:

- Completion of flooring, bathroom/utility tiles, first coat of paint.
- Completion of doors, windows, grills, electrical wiring, switches must be done in next stage
- False ceiling must be completed before flooring
- Kitchen platform, granite and dado must be completed where modular kitchen is not provided
- Provide granite soffit for main door and balconies in this stage.

Miscellaneous check

Main door fixed with lock & stopper	☒ Yes ☐ No		
Granite soffit for balcony required	☒ Yes ☐ No		
Balcony granite soffit workmanship	☐ Good ☐ Avg ☒ Poor	Granite soffit for balcony provided	☐ Yes ☒ No
Granite soffit for main door required	☒ Yes ☐ No	Balcony granite soffit edge polishing	☐ Good ☐ Avg ☒ Poor
Main door granite soffit workmanship	☐ Good ☒ Avg ☐ Poor	Granite soffit for main door provided	☒ Yes ☐ No
		Main door granite soffit edge polishing	☐ Good ☒ Avg ☐ Poor

Certified that all corrections mentioned in the QC Report have been completed. Work can Proceed to next Stage.

Project In-charge	Sign	Date

Page 1 of 3

Draft after finishing stage II check report apts. Dt 17-10-2020 ver5

Quality Control Check Report. Stage: After Finishing Stage II (Apartments)

Tiling & granite work		Rate the quality of (Good ✓, Avg X, Poor - needs correction XX, NA)												
S No	Room	Workmanship of tiling	White cement filling around CPVC lines	Corners finishing	Finishing near doors	Finishing on top of tiles	Finishing near ventilators	Step at bathroom entrance / utility	Step for shower / pot wash	Tile joint grouting	Granite platform finishing and edge polishing	Granite platform slope	Granite platform height	Finishing under granite platform
1	Toilet 1 M. Toi	✓	X	✓	X	X	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 2 C. Toi	✓	X	✓	X	X	✓	✓	✓	✓	✓	✓	✓	✓
3	Toilet 3	✓	X	✓	X	X	✓	✓	✓	X	✓	✓	✓	✓
4	Toilet 4	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Wash basin in dining area	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility	✓	X	X	✓	✓	✓	✓	✓	X	✓	✓	✓	✓
8	Other													
9	Other													
Remarks		NOTE: (1) For M. Toi & C. Toi, painting work not done. (2) Grouting work to be improved.												

S No	Room	Rate the quality of (Good ✓, Avg ✕, Poor - needs correction ✕✕, NA)										Door & frame painting quality	Door beading, lippam and painting quality.	Edge building
		Flooring & painting	Color variation of floor tiles	Flooring workmanship & grouting	Skirting size (3")	Skirting workmanship	Plastering above skirting	Plastering & finishing of walls	Crack filling	Loft Finishing	Windows check	General quality of painting & finishing		
1	Bedroom 1 M. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Bedroom 2 G. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 3 C. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕
4	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕
5	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕
8	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕
9	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✕
10	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✕	✓	✓	✓	✓
11	Other													
12	Other													
Remarks		NOTE: (1) 1 st coat of painting work not done in a flat.												
		(2) Flat to be clean.												

Quality Control Check Report. Stage: After Plumbing & Electrical (Apartments)

Flat No.	11-101	Other	-	SI No.	42273
Company	MFM-CLP	Project	GMK	Phase	-
Prepared by	Saikrishna	Sign	<i>[Signature]</i>	Date	26-08-2023
Project Manager	Shankar / Shrinivas	Sign	<i>[Signature]</i>	Date	26-08-2023
Previous stage report no.				Report filed and signed by PM?	☒ Yes ☐ No
Additions & alterations sheet date	4/265			All pages signed by engineer & customer?	☐ Yes ☐ No
Checked By MD on		MD Sign	UAI-50CP	For filling	☐ Yes ☐ No
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.					

Inspection should be done after:

- after cleaning the apartment
- before starting painting, tiling & flooring.
- electrical conduct, waterproofing & plumbing work is completed (for stage II only).
- additions & alterations is finalized and signed. In case there are no additions and alterations printout of email by PM to CR confirming the same must be filed.
- additions & alterations sheets to be transferred to QC file. QC to check if A&A are made as per request.

After Plumbing & Electrical Check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark X for minor mistake that requires minor correction.
3. Mark X X for major mistake that requires correction by replacement or re-fixing.
4. Mark X X X for major mistake that cannot be corrected.
5. Location of CPVC & PVC fittings must be checked as per measurements given in circular. Tolerance 1".
6. Location, height and spirit level of electrical points must be checked as per measurements given in circular & plan. Tolerance 1".
7. Civil work near pipes in balcony & utility must be neat and mortar should be removed from the pipes.
8. Water proofing must cover all pipes & check height above SFL.
9. Fasteners must be used as specified in circular. Especially check fixing of PVC pipes.
10. Height of DB box must be 6" below false ceiling level or 12" below slab level.
11. In case of many changes in civil work, electrical work and plumbing work, a new drawing must be prepared at HO and approved by MD.

Certified that all corrections mentioned in the QC Report have been completed. Work can Proceed to next Stage.

Project In-charge	Sign	Date
<i>[Signature]</i>		

Quality Control Check Report.

Stage: After Plumbing & Electrical (Apartments)

S No	Room	Civil work near pipes in balcony & utility (✓ or ✗)	CPVC & PVC Check ⁵ (✓ or ✗)	Electrical points check ⁶ (✓ or ✗)	Water proofing check ⁸ (✓ or ✗)	Proper use of fasteners check ⁹ (✓ or ✗)	Placement of DB ¹⁰ (✓ or ✗)	Placement of Generator changeover (✓ or ✗)
1	Bedroom 1 (1-3-2)	—	—	—	—	—	—	—
2	Toilet 1	—	—	—	—	—	—	—
3	Bedroom 2 (1-3-2)	—	✓	✓	—	—	—	—
4	Toilet 2	—	—	✓	✓	—	—	—
5	Bedroom 3 (1-3-2)	—	✓	✓	—	—	—	—
6	Toilet 3	—	—	✓	—	—	—	—
7	Drawing	—	—	—	—	—	—	—
8	Dining	—	—	✓	—	—	—	—
9	Lobby 1	—	—	—	—	—	✓	—
10	Utility balcony 1	✗	—	—	—	—	—	—
11	Utility balcony 2	✗	✓	✓	—	—	—	—
12	Utility balcony 3	—	✓	✓	✓	✓	—	—
13	Kitchen	—	—	—	—	—	—	—
14	Other	—	✓	✓	—	—	—	—
15	Other	—	—	—	—	—	—	—
Remarks (1) Level marking was not done. (2) Balcony still level was not done.								
Remarks on additions & alteration sheet:								
Signed by engineer,		☒ Yes ☐ No		Signed by customer,		☐ Yes ☐ No		
Revised drawing required from HO		☐ Yes ☐ No		Approved revised drawing attached		☐ Yes ☐ No		

Miscellaneous check	
Screeding done on walls upto 12" outside bathroom/utility	☒ Yes ☐ No
Bathroom /utility filled with 4" water for water proof check	☒ Yes ☐ No
Hole packing done around all pipes in ceiling and internal walls	☐ Yes ☒ No
Remarks:	

Quality Control Check Report. Stage: After Plastering (Apartments)

Flat No.	H-101	Other	-	Sl. No.	41965
Company	MEM LLP	Project	GMR	Phase	-
Prepared by	SAIKIRAN	Sign	<i>SAIKIRAN</i>	Date	05-05-2023
Project Manager	AHMED	Sign	<i>AHMED</i>	Date	05-05-2023
Previous stage report no.	40876	Report filed and signed by PM?	☒ Yes ☐ No		
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.					

Inspection should be done after:

- brickwork & 2 coats plastering is completed
- after cleaning the villa.
- Water proofing, screeding in bathrooms is completed.
- before starting painting, tiling & flooring.

Plastering Check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark X for minor mistake that requires minor correction.
3. Mark X X for major mistake that requires correction by replacement or re-fixing.
4. Mark X X X for major mistake that cannot be corrected.
5. 9" unplastered area from SFL should be left including in common areas and terraces.
6. Windows must be checked with templates. Plastering must be 3mm margin for lippum work. Tolerance 1/4"
7. Provision of tiles in bathrooms, kitchen & wash areas (rough plastering).
8. Check size of sink bowl. Hole should be 1" to 2" larger. (Tolerance: 1")
9. All doors frames should have 1/4" grooves.
10. Sill top must be of uniform thickness, correct height, at one level & without broken edges.

Certified that all corrections mentioned in the QC Report have been completed. Work can Proceed to next Stage.

Project In-charge	Sign	Date
<i>AHMED KHAN</i>	<i>[Signature]</i>	11/05/23

Quality Control Check Report, Stage: After Plastering (Apartments)

S No	Room	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	Remarks
		Bedroom 1 (M. Bed)	Toilet 1 (4-to)	Bedroom 2 (4. Bed)	Toilet 2 (4-to)	Bedroom 3 (C. Bed)	Toilet 3	Bedroom 4	Toilet 4	Drawing	Dining	Lobby 1	Lobby 2	Balcony	Utility	Reception	Kitchen	Other	
	Skirting Provision (✓ or X)	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
	Furnishing around door frame (✓ or X)	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
	Beams & columns finishing (✓ or X)	✓	X	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
	Finishing of lofts (✓ or X)	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
	Electricity junctions finishing (✓ or X)	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
	Windows check (✓ or X)	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
	Tiles provision (✓ or X)	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
	Sink provision & size (✓ or X)	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
	Grooves for door frames (✓ or X)	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
	Balcony & terrace sill top finishing (✓ or X)	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
	Screeding in bathroom & utility (✓ or X)	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
	Screeding in 6" above FFL? (✓ or X)	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	

Quality Control Check Report. Stage: After Brickwork (Apartments/ Lab Spaces)

Flat No.	H-101	Others	SI. No.	40876
Company	MM-CLP	Project	Phase	-
Prepared by	P. Bhaskar	Sign	Date	25-11-22
Project Manager	Ramprasad	Sign	Date	25-11-22
Previous Stage report no.	410062	Report filed and signed by PM?	☒ Yes ☐ No	
Apartment No.		Other	other	
Checked By MD on		MD Sign	For filling	☐ Yes ☐ No

Recommendation:

☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.

☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.

☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.

☐ Proceed with further work. ATR not required.

Inspection should be done after:

- brickwork is completed
- chicken mesh fixed
- after cleaning the apartment
- electrical conducting work is completed

Brickwork Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✕ for minor mistake that requires minor correction.
3. Mark ✕✕ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✕✕✕ for major mistake that cannot be corrected.
5. Wall thickness should be as per plan. Use of 4", 6" & 8" blocks must be checked.
6. All walls should have 2 beds of about 2" to 3" thickness with one no. 6 mm or 8 mm rod with M15 CC.
7. Chicken mesh should be used in each and every joint between RCC & Brickwork.
8. Joint between brickwork & beam on external side must be filled.
9. Check room dimensions with working plan. (Tolerance: 1")
10. Diagonals of each room shall be equal. (Tolerance: 2")
11. Balcony sill level should be 3"3" from S.F.L. (Tolerance: 1")
12. Check room height with specified height. (Tolerance: 1")
13. Check plumb of walls wherever it appears to be out of plumb. (Tolerance: 1/2")
14. Specify the No. of beams which are not aligned by more than 1" in a room.
15. Door frames must have black Japan coating and wood primer pellambar - at cost of painter

Quality Control Check Report. Stage: After Brickwork (Apartments/ Lab Spaces)

S No	Room	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	Remarks
	Bedroom 1 - M-Rd	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
	Toilet 1 - M-Rd	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
	Bedroom 2 - K-Rd	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
	Toilet 2 - K-Rd	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
	Bedroom 3 - G-Rd	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
	Toilet 3 - G-Rd	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	

draft brickwork check report for Apis dt 19-03-22 ver7

Quality Control Check Report

Stage: After Brickwork (Apartments/ Lab Spaces)

Quality of edges and corners in all rooms?

Specify rooms that need correction:

☐ Good ☒ Avg ☐ Bad

Misc. Checks

Was 3.75 CFI proportion box provided?

☒ Yes ☐ No

Condition of proportion box?

☐ Good ☒ Avg ☐ Bad

Was the Apartment cleaned before starting brick work?

☐ Yes ☐ No ☒ Can't say

Is the Apartment cleaned for plastering?

☒ Yes ☐ No

Wastage?

☐ High ☒ Medium ☐ Low

Storage of building material like bricks sand and cement.

☐ Good ☒ Avg ☐ Bad

Drum (200 ltrs) provided for curing in each flat?

☒ Yes ☐ No

Remarks:

Door Frames & Windows check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✕ for minor mistake that requires minor correction
3. Mark ✕✕ for major mistake that requires correction by replacement or re-fixing
4. Mark ✕✕✕ for major mistake that cannot be corrected.
5. Window template depth should be between 2 to 2 1/2" after plastering.
6. Lintel level should be 7" 3" from SFL & 7" from FFL. (Tolerance 1"). Lintel should be as per standard design.
7. Loffs should be at a height of 7" to 7 3/4" from FFL. Kitchen plat form thickness should be 2", SFL to bottom 31". (Tolerance 1")
8. Slopes of lofts and kitchen platforms to be checked by using 12" spirit level and check height from floor from 2 or 3 points.
9. Thickness of platforms & lofts should be between 2 & 2.5".
10. Provide single layer table brick at bottom of each door frame without threshold
11. Check Z angle template size (Z angle for bathroom ventilators not required in new projects).
12. Window opening must be checked with MS square pipe templates of 2 sizes for inner and outer openings.
13. Z angle template must be 1" from brick wall surface from the inner side.

Security Control Check Report		Stage: After Brickwork (Apartments Lab Spaces)														
S No	Room	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15
		Bedroom 1 (11-12)	Toilet 1 (11-12)	Bedroom 2 (11-12)	Toilet 2 (11-12)	Bedroom 3 (11-12)	Toilet 3 (11-12)	Drawing	Dining	Lobby 1	Utility / balcony 1	Utility / balcony 2	Utility / balcony 3	Kitchen	Other	Other
	Door size, face and position (✓ or ✗)	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
	Brick at bottom of door frame (✓ or ✗)	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
	Door frame hold fast provision and fasteners (✓ or ✗)	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
	Door lintel design & level (✓ or ✗)	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
	Door diagonal check (✓ or ✗)	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
	Door Plumb - two sides (✓ or ✗)	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
	Windows lintel design & level, Sill level (✓ or ✗)	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
	Windows size (✓ or ✗)	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
	Windows - template depth & diagonal (✓ or ✗)	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
	Windows - template red oxide painting (✓ or ✗)	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
	Lift & Kitchen platform height (✓ or ✗)	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
	Lift & Kitchen platform slope (✓ or ✗)	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
	Door size, face and position (✓ or ✗)	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓

Remarks: 1) Kitchen plumb was not checked & left unchecked. Not done

Quality Control Check Report.		Stage: After Brickwork (Apartments/ Lab Spaces)	
Flat No.	H-101	Others	SI No. 40876
Company	MRM-CLP	Project	Phase
Prepared by	P Bhargava	Sign	Date 25-11-22
Project Manager	Ramprasad	Sign	Date 25-11-22
Previous Stage report no.	40062	Report filed and signed by PM? ☒ Yes ☐ No	
Apartment No.		Other	other
Checked By MD on		MD Sign	For filling ☒ Yes ☐ No

Recommendation:

☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.

☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.

☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.

☐ Proceed with further work. ATR not required.

Inspection should be done after:

- brickwork is completed
- chicken mesh fixed
- after cleaning the apartment
- electrical conducting work is completed

Brickwork Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark X for minor mistake that requires minor correction.
3. Mark XX for major mistake that requires correction by replacement or re-fixing.
4. Mark XXX for major mistake that cannot be corrected.
5. Wall thickness should be as per plan. Use of 4", 6" & 8" blocks must be checked.
6. All walls should have 2 beds of about 2" to 3" thickness with one no. 6 mm or 8 mm rod with M15 CC.
7. Chicken mesh should be used in each and every joint between RCC & Brickwork.
8. Joint between brickwork & beam on external side must be filled.
9. Check room dimensions with working plan (Tolerance: 1")
10. Diagonals of each room shall be equal (Tolerance: 2")
11. Balcony sill level should be 3"3" from SFL (Tolerance: 1")
12. Check room height with specified height (Tolerance: 1")
13. Check plumb of walls wherever it appears to be out of plumb (Tolerance: 1/2")
14. Specify the No. of beams which are not aligned by more than 1" in a room.
15. Door frames must have black Japan coating and wood primer pellambar - at cost of painter

APPROVED BY
06 JAN 2023
SOHAM MODI
MANAGING DIRECTOR

All works
Completed

S No	Remarks
1	Bedroom-1 - Al-Bed
2	Toilet-1 - Al-Toi
3	Bedroom-2 K-Bed
4	Toilet-2 C-Toi
5	Bedroom-3 C-Rbd
6	Toilet-3
7	Drawing
8	Dining
9	Lobby-1
10	Utility / balcony-1
11	Utility / balcony-2
12	Utility / balcony-3
13	Kitchen
14	Other
15	Other

Quality Control Check Report, Stage: After Brickwork (Apartments/ Lab Spaces)

Quality of edges and corners in all rooms?

☐ Good ☒ Avg. ☐ Bad

Specify rooms that need correction:

Misc. Checks.

Was 3.75 CFT proportion box provided?

Condition of proportion box?

☒ Yes ☐ No

Was the Apartment cleaned before starting brick work?

☐ Good ☒ Avg. ☐ Bad

Is the Apartment cleaned for plastering?

☐ Yes ☐ No ☒ Cant' say

Wastage?

☒ Yes ☐ No

Storage of building material like bricks sand and cement.

☐ High ☒ Medium ☐ Low

Drum (200 ltrs) provided for curing in each flat?

☐ Good ☒ Avg. ☐ Bad

Remarks:

☒ Yes ☐ No

Door Frames & Windows check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. Window template depth should be between 2 to 2 ½" after plastering.
6. Lintel level should be 7'3" from SFL & 7' from FFL. (Tolerance 1"). Lintel should be as per standard design.
7. Lofts should be at a height of 7' to 7'3" from FFL. Kitchen plat form thickness should be 2". SFL to bottom 31" - (Tolerance 1")
8. Slopes of lofts and kitchen platforms to be checked by using 12" spirit level and check height from floor from 2 or 3 points.
9. Thickness of platforms & lofts should be between 2 & 2.5".
10. Provide single layer table brick at bottom of each door frame without threshold.
11. Check Z angle template size (Z angle for bathroom ventilators not required in new projects).
12. Window opening must be checked with MS square pipe templates of 2 sizes for inner and outer openings.
13. Z angle template must be 1" from brick wall surface from the inner side.

S No	Room	Door size, face and position (✓ or X)	Brick at bottom of door frame (✓ or X)	Door frame hold fast provision and fasteners (✓ or X)	Door lintel design & level (✓ or X)	Door diagonal check (✓ or X)	Door Plumb - two sides (✓ or X)	Windows lintel design & level, Sill level (✓ or X)	Windows size (✓ or X)	Windows - template depth & diagonal (✓ or X)	Windows - template test inside painting (✓ or X)	Loft & Kitchen platform height (✓ or X)	Loft & Kitchen platform slope (✓ or X)	Door size, face and position (✓ or X)
1	Bedroom 1 At 18d	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 At 16d	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 K-Rd	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 C-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 G-Rd	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
15	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
Remarks: 1) Kitchen plumbing was not tested & for left balcony not done														

GULMOHAR RESIDENCY

Sy. No. 19, Mallapur Village, Uppal, Hyderabad.
Owned & Developed by: M/s. Modi Realty Mallapur LLP.
Head office; 5-4-187/3&4 M G Road Secunderabad.

Details of Additions & Alterations

Flat No	101	Block no.	'H'
Flat Area	1360 sft	Type A	Deluxe / Luxury
Buyer Name	Mr.		
Phone No.		Email	

I hereby confirm that I have given the details of the minor additions and alterations that are required in the above referred flat in the pages attached herein. Please complete the changes suggested by me. I agree to pay the charges, if any, for the additions and alterations that I have asked you to make, as per the rates suggested by you. I shall deliver all the materials that are required to be provided by me at the site on or before _____. In case I fail to deliver these items to the site by the specified date, you may complete the works in the flat as per the standard items provided by you.

Buyers sign		Engg. Sign	
Date:		Date	16/11/23

Note:

1. Colour shades of paints may vary from batch to batch & company to company. The Builder will not take responsibility of quality of work for dark shades especially green & blue.
2. Shade / colour of natural material like marble and granite can't be guaranteed and may vary from lot to lot. Cracks like appearance in marble is a natural feature and Builder shall not be responsible for repairs or replacement.
3. Availability of bathroom or flooring tiles of the same type /colour/make can not be guaranteed and closest possible type/colour/make may be used in its place.
4. No further change shall be permitted from this day.
5. Please sign on all pages.

Buyers sign:


Engg. Sign:


16/11/23
Date:

Choice of colours:

Changes in flooring:

- ① 3 Bedrooms Automatic mowing - Kitchen floor
- ② Balcony - Oak and Dark (classy way)
- ③ Hall - Travertine marble
- ④ Utility - Black bay + slate white.


Buyers sign:


Engg. Sign:

16/11/22
Date:

Changes in electrical points: (mark on plan)

① Extra TV points @ Master & Guest Bedrooms.

Choice of Bathroom tiles, CP fittings & Sanitary ware:

MT - ultra sprinkler *Klang 21/11/2023*

CT - - do -

- extra wash basin point

Buyer's sign:

Engg Sign:

Date:

16/11/23



Changes in kitchen platform: (mark on plan)

- ① kitchen platform granite will given by customer later.
- ② Edge tiles + ss sink given by customer. Not by company - 3/1/24
- ③ Sink by company - 3/1/24.

Other Changes:

①

[Signature]


Buyers sign:

[Signature]

Engg. Sign:


16/11/25


Date:

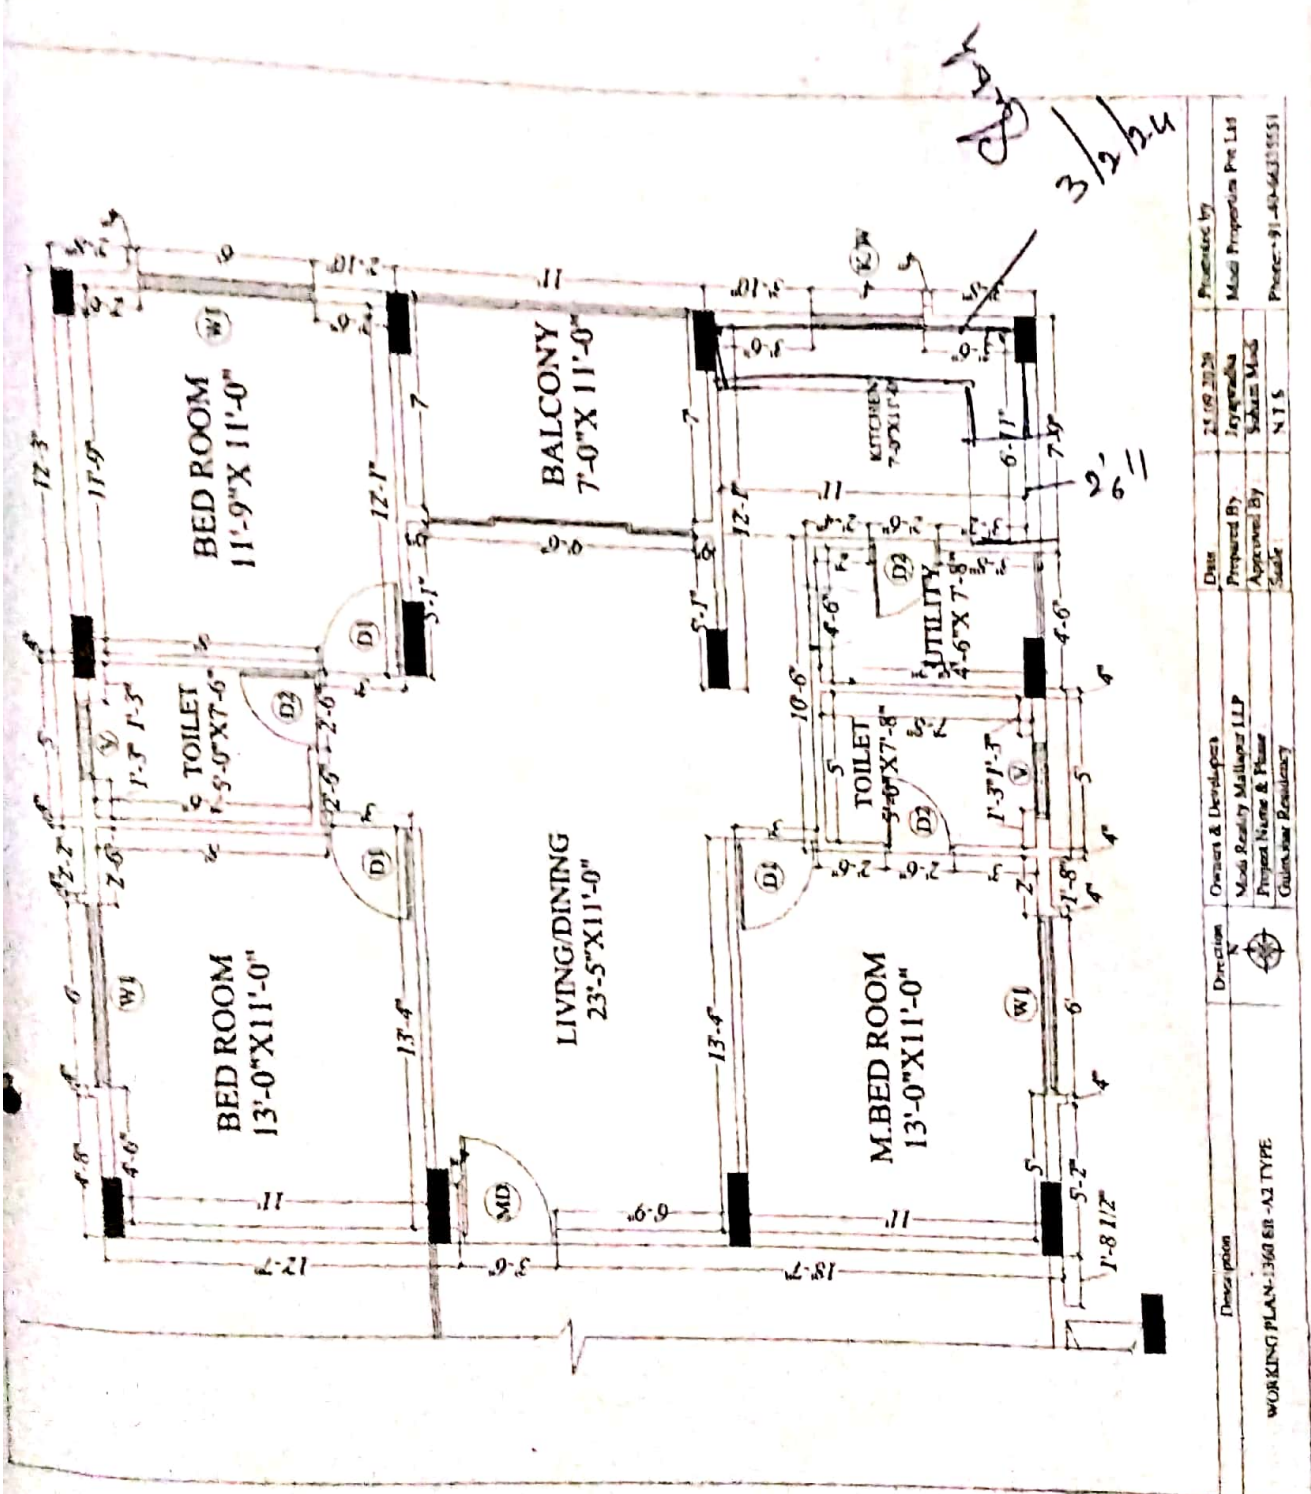

Revision	Drawn	Owner & Developer	Date	21.09.2020	Prepared by	21.09.2020	Produced by
WORKING PLAN-1360 BR-A2 TYPE	N	Maha Realty Mallapur LLP Project Name & Phase Gulmohar Residency	Prepared By	Jayaprakasha	Modi Properties Pvt Ltd		
			Approved By	Saham Modi			
			Scale	NTS			
							Phone: 91-40-66335551

000
000
000

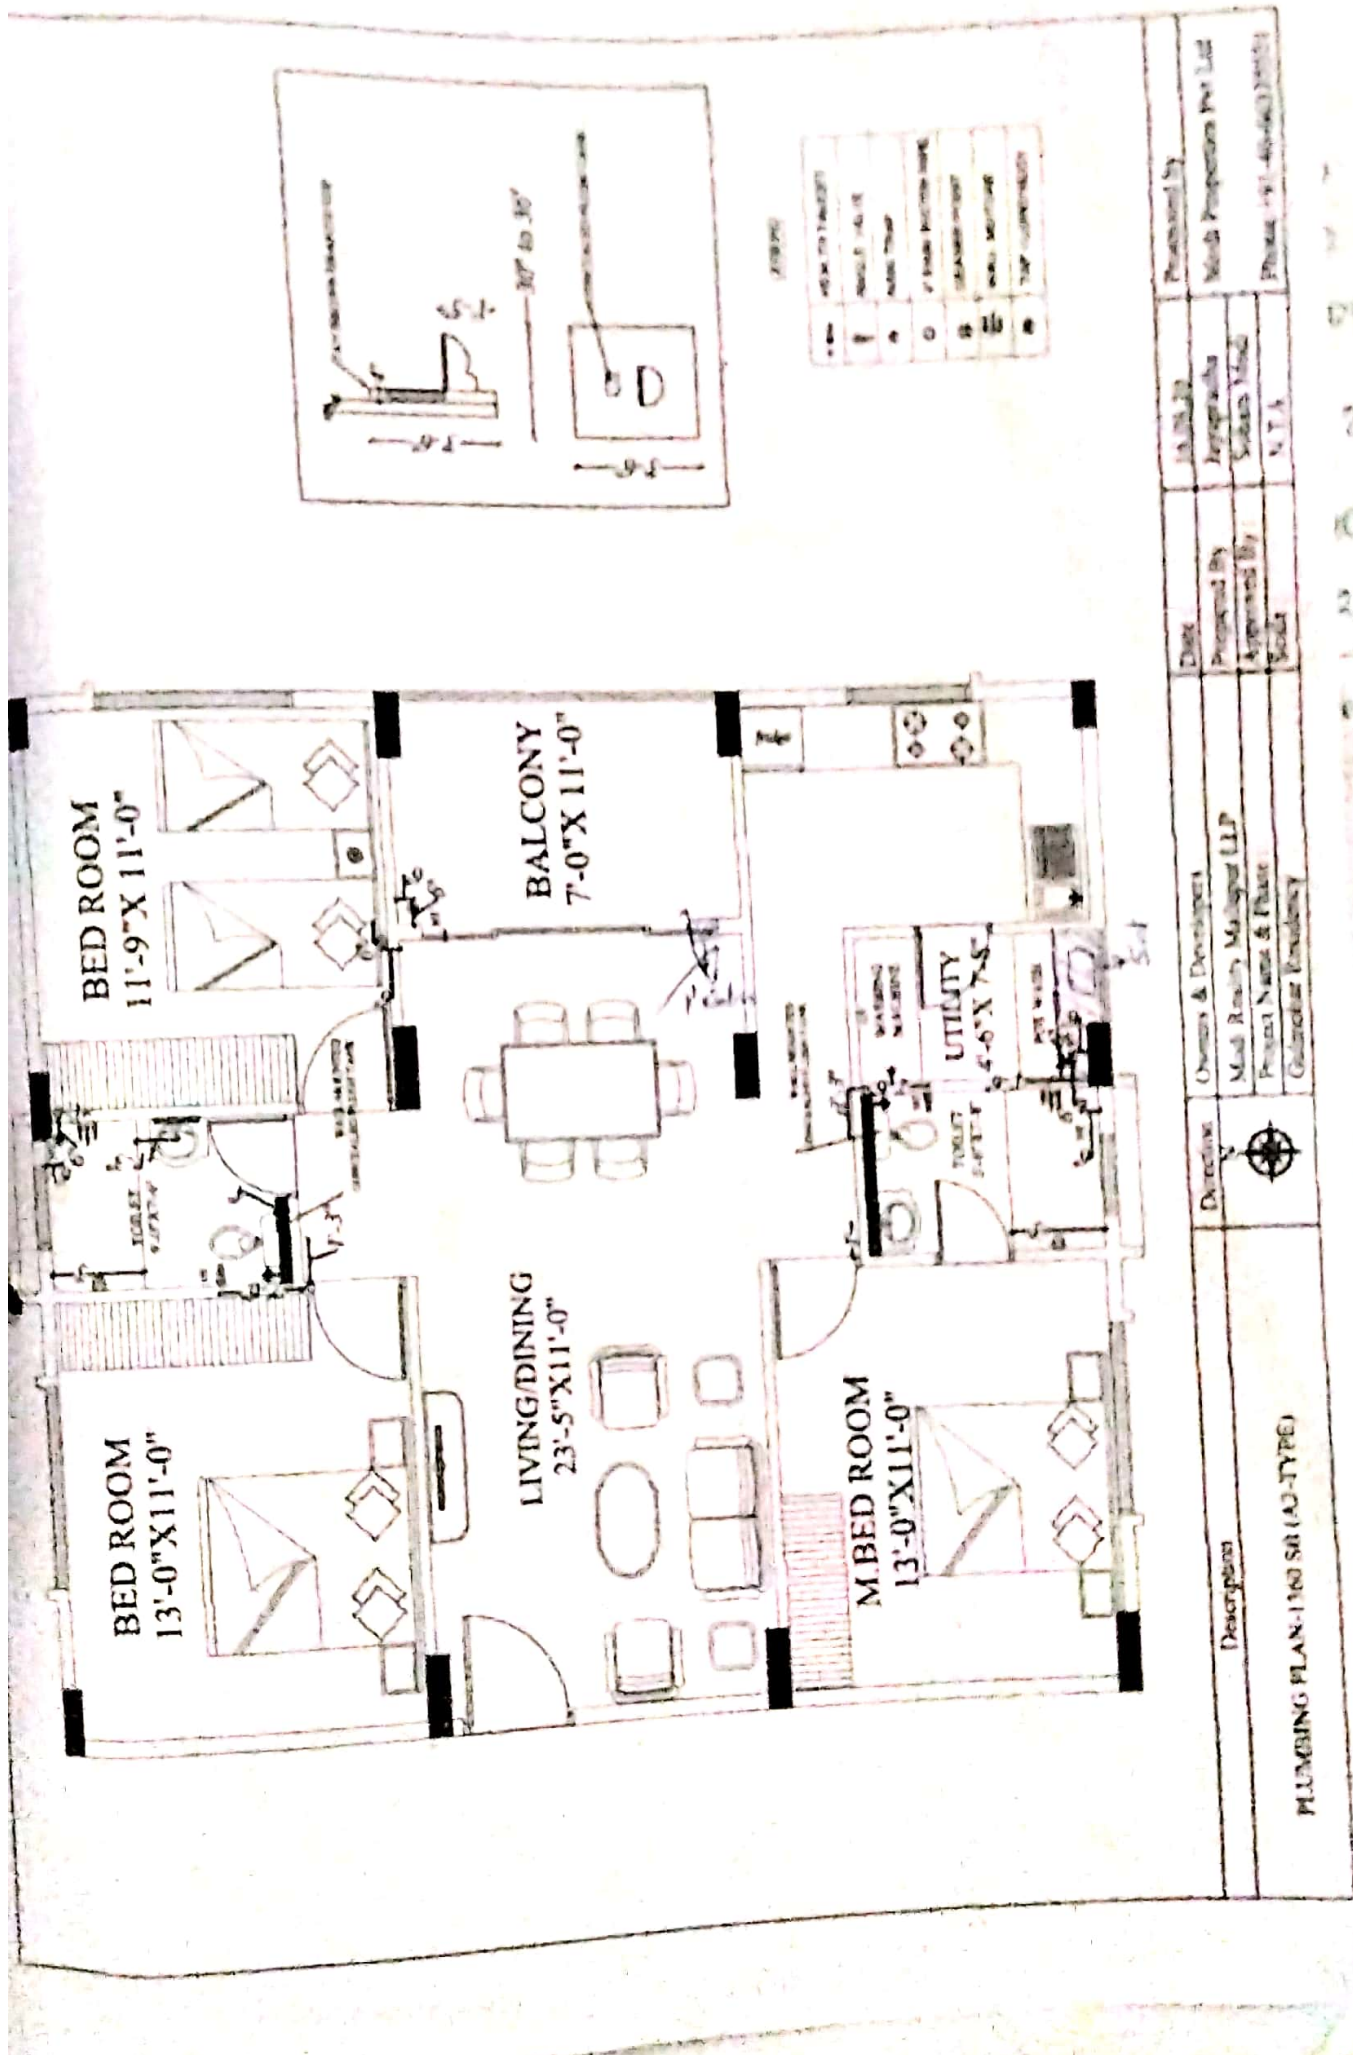

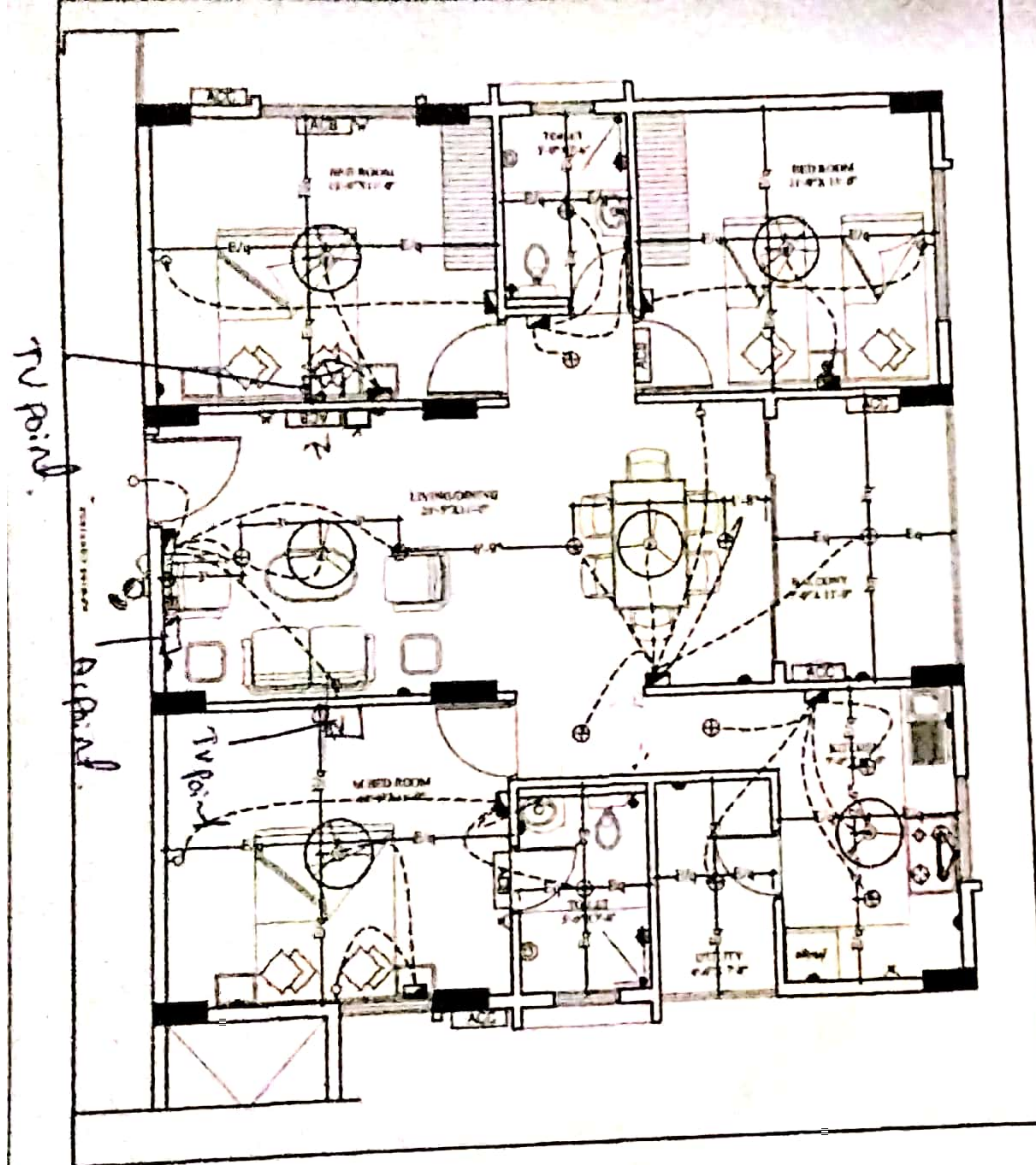

LEGEND:-

S.NO.	ITEM	SYMBOL	REMARKS
1.	Exhaustion duct & storage unit	⊠	1700x700
2.	Switch board	⊠	400x400
3.	Hot water heater unit	⊠	700x700
4.	Water supply unit	⊠	7
5.	Lighting fan	⊠	7
6.	Water pump unit	⊠	1000x1000
7.	Exhaust fan	⊠	700
8.	10 amp plug unit	⊠	2000x1000
9.	Telephone unit	⊠	7
10.	Telephone point	⊠	7
11.	Lighting unit	⊠	700
12.	Bed room	⊠	7
13.	Lighting unit	⊠	700
14.	Bed room	⊠	700
15.	AC Compressor	⊠	1700x700
16.	AC Room	⊠	1700x700
17.	Bed room unit & AC	⊠	1700x700

Note:- Switch board to be kept near the TV from center of the room.

Description	Direction	Owners & Developers	Date	21.09.2020	Promoted by
ELECTRICAL PLAN - 360 sq ft FLATS-A2 TYPE		Modi Realty Mallapur LLP	Prepared By	Jayarambha	Modi Properties Pvt Ltd
		Project Name & Phase	Approved By	Soham Modi	Phone: +91-80-66335551
		Gulmohar Residency	Scale	NTS	
