

Flat No	H-104	QC report stage	Stage - III	Sl. No.	43026
Company	NRMLP	Project	GRM	Phase	—
Prepared by	N. Sathesh	Sign	See	Date	15/04/24
Project Manager	S. Sathish	Sign	Shiny	Date	15/04/24
Receipt by QC date		Sign		Other	
Receipt at HO date		Sign		Other	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation that was made by QC:

☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.

☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.

Notes:

1. Attach a copy of the QC report to this sheet.
2. Circle each correction with a red pen – tick (✓) each circle for work completed and cross (X) each circle where work has not been completed.
3. Give remarks for each case where work has not completed on this sheet.
4. Make 2 copied of the ATR – send one to MD and other to QC.
5. Enclose required photographs – hard copy.

Remarks:

All works completed.

Flat No	H-104	Other		Sl. No.	43026
Company	MM-LLP	Project		Phase	-
Prepared by	Chao Mohammed	Sign		Date	12-07-24
Project Manager	Survival	Sign		Date	12-07-24
Previous stage report no.	43009	Report filed and signed by PM		☒ Yes ☐ No	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation:

☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.

☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team.

☐ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.

☐ Proceed with further work. ATR not required.

Inspection should be done after :

- Completing stage II works.
- Complete works like doors, windows, grills, electrical wiring, switches, french door glass, etc.
- In case of modular kitchen provide platform, granite and dado and modular kitchen in this stage.
- Provide video door phone in this stage.
- Possession for wood work cannot be given until QC check for stage III is completed and all corrections mentioned in the report are made.

Miscellaneous check:

Modular kitchen to be provided	☐ Yes ☒ No	Modular kitchen provided	☐ Yes ☒ No
Modular kitchen workman ship	☐ Good ☐ Avg ☐ Poor	Modular kitchen granite & dado workman ship & finishing	☐ Good ☐ Avg ☐ Poor
Video door phone /wifi cam to be provided	☐ Yes ☒ No	Video door phone/wifi cam provided	☐ Yes ☒ No
Painting marks and drops are cleaned from floor, windows, walls.		☐ Good ☐ Avg ☒ Poor	

Certified that all corrections mentioned in the QC Report have been completed. Work can Proceed to Next Stage.

Project In-charge	Sign	Date

		Rate the quality of (Good ✓, Avg. ✗, Poor – needs correction ✗✗, NA)											
S No	Room	Door, door knob & door stopper fitting	Door, door knob & door stopper cleaning	Window grills & quality	Window grills fitting & finishing	Windows quality	Window fitting & finishing	Balcony railing quality & finishing	French door quality & fitting	CP jali quality and fitting	Edge building	Switch boards fitting & covering with plastic covers	Junction box covers painting
1	Bedroom-1 M.Bed	✓	✗✓	✗✓	✗✓	✓	✗✓	—	—	—	✓	✗✗	✓
2	Bedroom-2 G.Bed	✓	✓	✓	✓	✓	✓	—	—	—	✓	✗✗	✓
3	Bedroom-3 C.Bed	✓	✓	✓	✗✓	✓	✓	—	—	—	✗✓	✗✓	✗✗
4	Drawing	✓	✓	✓	✓	✓	✗✓	—	—	—	✓	✗✗	✗✓
5	Dining	—	—	—	—	✓	✓	—	✓	—	✓	✓	✓
6	Lobby-1	—	—	—	—	—	—	—	—	—	✗✓	✗✓	✗✓
7	Utility / balcony-1	✓	✗✓	✓	✓	✓	✓	—	—	✗✗	✗✗	✗✓	—
8	Utility / balcony-2	—	—	—	—	—	—	✓	—	✗✗	✓	✓	✓
9	Utility / balcony-3	—	—	—	—	—	—	—	—	✗✗	✓	—	✓
10	Kitchen	—	—	✗✓	✗✓	✗✓	✗✓	—	—	—	✓	✗✓	—
11	Toilet-1 C.Toi	✓	✓	✗✓	✗✓	✗✓	✗✓	—	—	✗✗	✗✗	✗✓	✗✓
12	Toilet-2 M.Toi	✓	✗✓	✗✓	✗✓	✗✓	✗✓	—	—	✗✗	✗✓	✗✓	✗✓
13	Toilet-3	—	—	—	—	—	—	—	—	—	—	—	—
14	Other	—	—	—	—	—	—	—	—	—	—	—	—
15	Other	—	—	—	—	—	—	—	—	—	—	—	—
Remarks ①		Painting marks and drops are not cleaned from M.Bed room, Common bedroom, balcony, Utility area, M-Toilet.											
②		Common toilet flooring is very very dirty.											

Construction Division
Additions & Alteration Charges Approval Form

Name:	MRMLLP	Site	Gulmohar Residency
the customer	P. Laxayanya.		
at No.	H-104		
Description	Amount		
Total extra Charges	33143.		
Total refundable amount	-		
Net amount to be charges (if any)	33143.		
Net amount to be refunded (if any)			
Extra Charges for tiles.			
Thirty three thousand one hundred and forty three Rupees only.			
d by Project Manager		Approved by Design Team	Approved by MD
36106124.		Date	Date
③ Vinay		Sign:	Sign:

Enclose measurement & estimate sheet. 2. Send scanned copy by email to plans@modiproperties.com & CR. 3.
in originals in A&A of customers at site.

[illegible]

Quality Control Check Report. Stage: After Finishing Stage II (Apartments)

Flat No	H-104	Other		Sl. No.	4266/1
Company	MRM-LLP	Project	GMR	Phase	
Prepared by	Abhishek Gaudon	Sign	Abhishek	Date	24-06-24
Project Manager	Srinivas	Sign	@king	Date	24-06-24
Previous stage report no.	41792	Report filed and signed by PM			☒ Yes ☐ No
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- Completion of flooring, bathroom /utility tiles, first coat of paint.
- Completion of doors, windows, grills, electrical wiring, switches must be done in next stage
- False ceiling must be completed before flooring.
- Kitchen platform, granite and dado must be completed where modular kitchen is not provided.
- Provide granite soffit for main door and balconies in this stage.

Certified that all corrections mentioned in the QC Report have been completed. Work can Proceed to next Stage.

Project In-charge	Sign	Date
	@king	

Miscellaneous check:

Main door fixed with lock & stopper	☒ Yes ☐ No		
Granite soffit for balcony required	☒ Yes ☐ No	Granite soffit for balcony provided	☒ Yes ☐ No
Balcony granite soffit workmanship	☐ Good ☒ Avg ☐ Poor	Balcony granite soffit edge polishing	☐ Good ☒ Avg ☐ Poor
Granite soffit for main door required	☒ Yes ☐ No	Granite soffit for main door provided	☒ Yes ☐ No
Main door granite soffit workmanship	☒ Good ☐ Avg ☐ Poor	Main door granite soffit edge polishing	☐ Good ☒ Avg ☐ Poor

Quality Control Check Report. Stage: After Finishing Stage II (Apartments)

Tiling & granite work		Rate the quality of (Good ✓, Avg. ✕, Poor – needs correction ✕✕, NA)												
S No	Room	Workmanship of tiling	White cement filling around CPVC lines	Corners finishing	Finishing near doors	Finishing on top of tiles	Finishing near ventilators	Step at bathroom entrance / utility	Step for shower / pot wash	Tile joint grouting	Granite platform finishing and edge polishing	Granite platform slope	Granite platform height	Finishing under granite platform
1	Toilet 1 m-Toi	✓	✕✕	✓	✓	✓	✓	✓	✓	✓	—	—	—	—
2	Toilet 2 c-Toi	✓	✕✕	✓	✓	✓	✓	✓	✓	✓	—	—	—	—
3	Toilet 3	—	—	—	—	—	—	—	—	—	—	—	—	—
4	Toilet 4	—	—	—	—	—	—	—	—	—	—	—	—	—
5	Wash basin in dining area	—	—	—	—	—	—	—	—	—	—	—	—	—
6	Kitchen	✓	✕✕	✕	✓	✕	✓	—	—	✓	—	—	—	—
7	Utility	✓	✕✕	✕	✕	✕	✕	✓	✓	✓	—	—	—	—
8	Other													
9	Other													
Remarks														
① Provision for modular kitchen.														
② Flat should be cleaned properly.														
③ minor civil & paint touchup to be done properly.														

Quality Control Check Report. Stage: After Finishing Stage II (Apartments)

Flooring & painting		Rate the quality of (Good ✓, Avg. ✗, Poor - needs correction ✗✗, NA)												
S No	Room	Color variation of floor tiles	Flooring workmanship & grouting	Skirting size (3")	Skirting workmanship	Plastering above skirting	Plastering & finishing of walls	Crack filling	Loft Finishing	Windows check	General quality of painting & finishing	Door & frame painting quality	Door beading, lippam and painting quality	Edge building
1	Bedroom 1 M.BR	✓	✓	✓	✓	✓	✓	✓	—	✓	✓	✓	✓	✗
2	Bedroom 2 G.BR	✓	✓	✓	✓	✓	✓	✓	—	✓	✓	✓	✓	✗
3	Bedroom 3 K.BR	✓	✓	✓	✓	✓	✓	✓	—	✓	✓	✓	✓	✗
4	Drawing	✓	✓	✓	✗	✓	✓	✓	—	✓	✓	✓	✓	✗
5	Dining	✓	✓	✓	✗	✓	✓	✓	—	✓	✓	✓	✓	✗
6	Lobby-1	—	—	—	—	—	—	—	—	—	—	—	—	—
7	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	—	—	—	—	—	—
8	Utility / balcony 2	✓	✓	—	✗	✓	✓	✓	—	—	✓	✓	✓	✓
9	Utility / balcony 3	—	—	—	—	—	—	✗	—	✓	✗	✓	✓	✗
10	Kitchen	✓	✓	✓	✗	✓	✓	✗	✗	✓	✗	✗	✗	✗
11	Other													
12	Other													
Remarks		① Skirting in Drawing & Dining and few rooms zero level to wall must be corrected.												
		② Junction box & Switch box cracks, Gap filling not done												

Company	11-104	Project	Other	SI. No.	422A6
Prepared by	MAN-11P	Sign	GMR	Phase	—
Project Manager	Sarkis	Sign	Sarkis	Date	26-08-2023
Previous stage report no.		Sign	for [Signature]	Date	26-08-2023
Additions & alterations sheet date	41292	Report filed and signed by PM?	☒ Yes ☐ No		
Checked By MD on	UN-SOLD	All pages signed by engineer & customer?	☐ Yes ☐ No		
	MD Sign	For filling	☐ Yes ☐ No		
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.					

Inspection should be done after:

- after cleaning the apartment.
- before starting painting, tiling & flooring.
- electrical conduct, waterproofing & plumbing work is completed (for stage II only).
- additions & alterations is finalized and signed. In case there are no additions and alterations printout of email by PM to CR confirming the same must be filed.
- additions & alterations sheets to be transferred to QC file. QC to check if A&A are made as per request.

After Plumbing & Electrical Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✕ for minor mistake that requires minor correction.
3. Mark ✕✕ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✕✕✕ for major mistake that cannot be corrected.
5. Location of CPVC & PVC fittings must be checked as per measurements given in circular. Tolerance 1".
6. Location, height and spirit level of electrical points must be checked as per measurements given in circular & plan. Tolerance 1".
7. Civil work near pipes in balcony & utility must be neat and mortar should be removed from the pipes.
8. Water proofing must cover all pipes & check height above SFL.
9. Fasteners must be used as specified in circular. Especially check fixing of PVC pipes.
10. Height of DB box must be 6" below false ceiling level or 12" below slab level.
11. In case of many changes in civil work, electrical work and plumbing work, a new drawing must be prepared at HO and approved by MD.

Certified that all corrections mentioned in the QC Report have been completed. Work can Proceed to next Stage.

Project In-charge	Sign	Date
[Signature]		


S No	Room	near pipes in balcony & utility ⁷ (✓ or ✕)	C/PVC & PVC Check ⁵ (✓ or ✕)	Electrical points check ⁶ (✓ or ✕)	Water proofing check ⁸ (✓ or ✕)	Proper use of fasteners check ⁹ (✓ or ✕)	Placement of DB ¹⁰ (✓ or ✕)	Placement of Generator changeover (✓ or ✕)
1	Bedroom 1 M. Bed	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M. Toi	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 G. Bed	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 G. Toi	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 G. Bed	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓
9	Lobby 1	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3	✓	✓	✓	✓	✕	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓
14	Other	✓	✓	✓	✓	✓	✓	✓
15	Other	✓	✓	✓	✓	✓	✓	✓

Remarks NOTE :- 1) In Utility, fastener to be replaced properly.


Remarks on additions & alteration sheet:

Signed by engineer,	☐ Yes ☐ No —	Signed by customer,	☐ Yes ☐ No —
Revised drawing required from HO	☐ Yes ☐ No —	Approved revised drawing attached	☐ Yes ☐ No —

Screeding done on walls upto 12" outside bathroom/utility	☒ Yes ☐ No
Bathroom /utility filled with 4" water for water proof check	☐ Yes ☒ No
Hole packing done around all pipes in ceiling and internal walls	☐ Yes ☒ No
Remarks:	

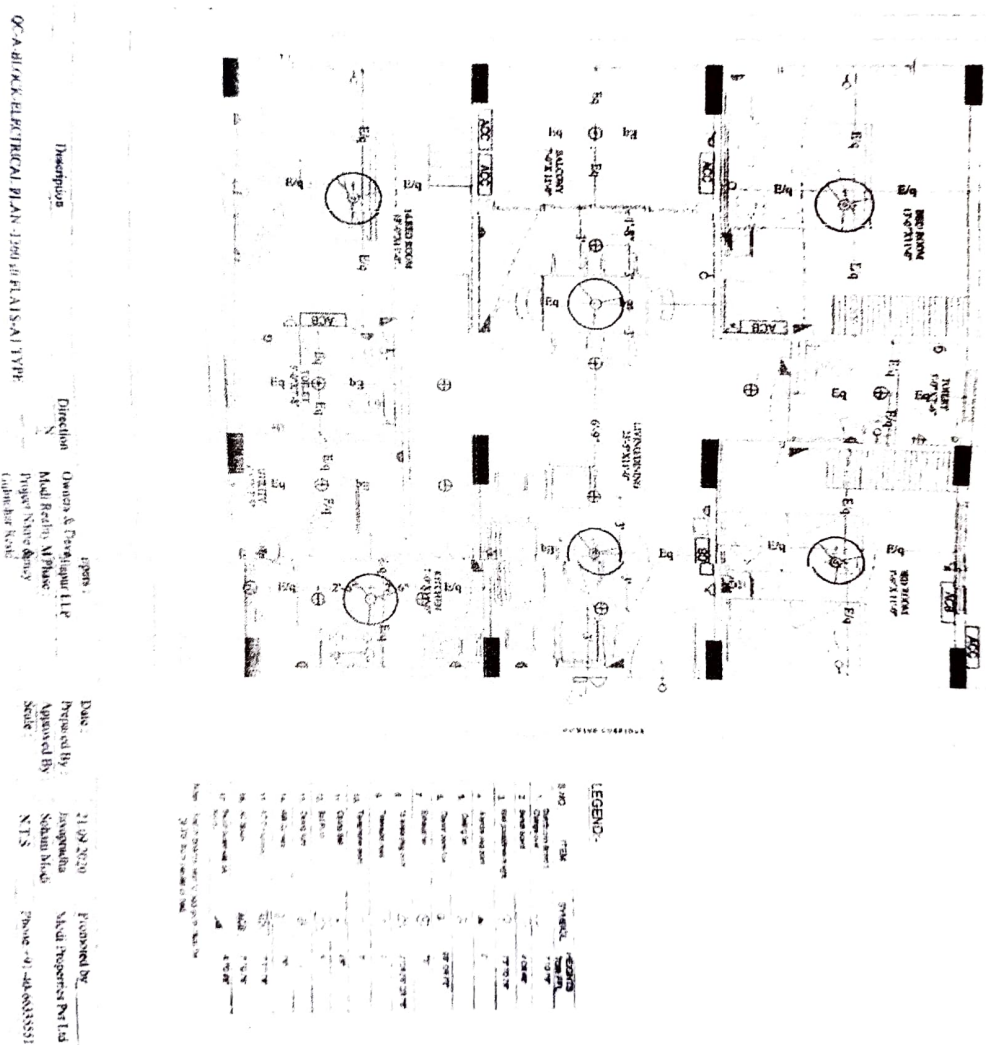

APPROVED FOR CONSTRUCTION
25 SEP 2000
JAMES HUI
MANAGING DIRECTOR

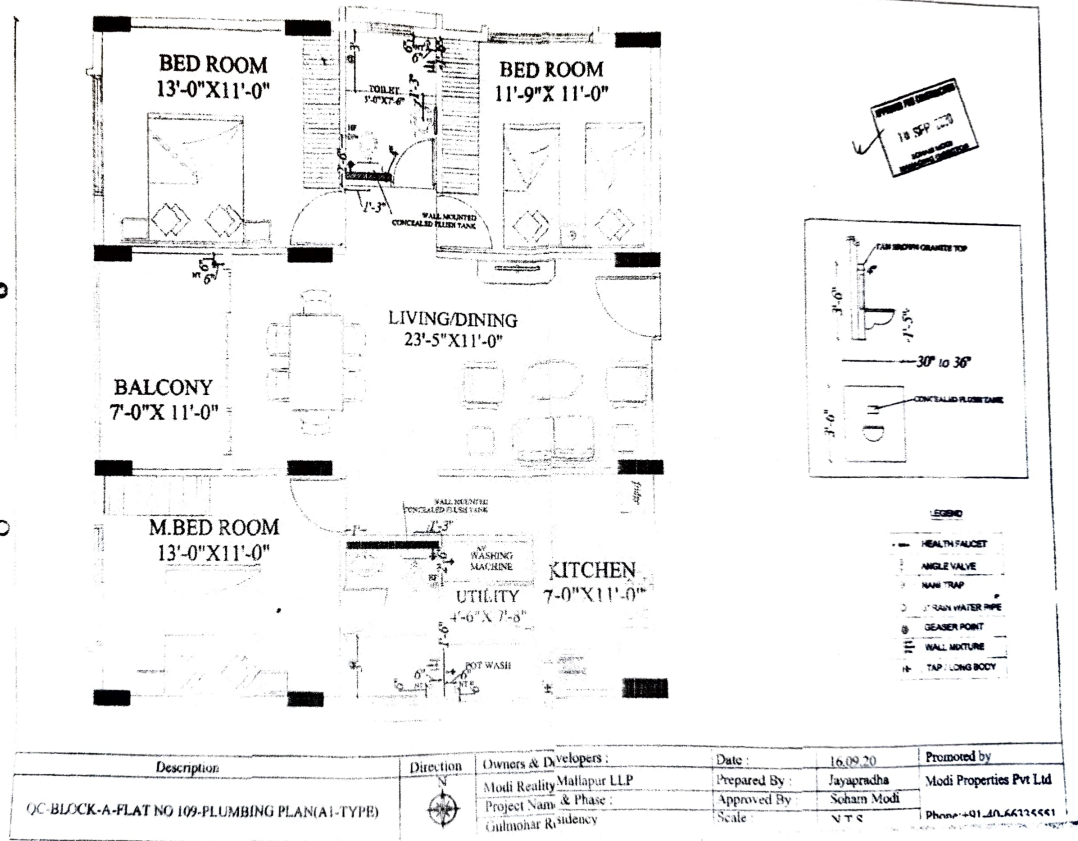

Flat No.		Stage: After Plastering (Apartments)			
Company	H-104	Other	-	Sl. No.	41792
Prepared by	MRM-CLIP	Project	GMR	Phase	-
Project Manager	P. Bhaskar	Sign	P.B.	Date	12-05-23
Previous stage report no.	Naxendar / Ahmed	Sign	Ahmed	Date	12-05-23
Checked By MD on	40905	Report filed and signed by PM?	Yes		
	MD Sign		For filling	☐ Yes ☐ No	
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☐ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.					

Inspection should be done after:

- brickwork & 2 coats plastering is completed
- after cleaning the villa.
- Water proofing, screeding in bathrooms is completed.
- before starting painting, tiling & flooring.

Plastering Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✕ for minor mistake that requires minor correction.
3. Mark ✕✕ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✕✕✕ for major mistake that cannot be corrected.
5. 9" unplastered area from SFL should be left including in common areas and terraces.
6. Windows must be checked with templates. Plastering must be 3mm margin for lippum work. Tolerance 1/2"
7. Provision of tiles in bathrooms, kitchen & wash areas (rough plastering).
8. Check size of sink bowl. Hole should be 1" to 2" larger. (Tolerance: 1")
9. All doors frames should have 1/2" grooves.
10. Sill top must be of uniform thickness, correct height, at one level & without broken edges.

Certified that all corrections mentioned in the QC Report have been completed. Work can Proceed to next Stage.

Project In-charge	Sign	Date
Ahmed Khan	Ahmed	12/05/23

S No	Room	Skirting Provision (✓ or ✗)	Furnishing around door frame (✓ or ✗)	Beams & columns finishing (✓ or ✗)	Finishing of lofts (✓ or ✗)	Electricity junctions finishing (✓ or ✗)	Windows check (✓ or ✗)	Tiles provision (✓ or ✗)	Sink provision & size (✓ or ✗)	Grooves for door frames (✓ or ✗)	Balcony & terrace sill top finishing (✓ or ✗)	Screeding in bathroom & utility (✓ or ✗)	Screeding in 6" above FFL? (✓ or ✗)
1	Bedroom 1 M. Bed	✓	✓	✗✗	-	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M. Toi	-	✓	✓	-	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 K. Bed	✓	✓	✓	-	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 C- Toi	-	✗	✗✗	-	✓	✓	✓	✓	✗	✓	✓	✓
5	Bedroom 3 Gr. Bed	✓	✓	✓	-	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	-	-	-	-	-	-	-	-	-	-	-	-
7	Bedroom 4	-	-	-	-	-	-	-	-	-	-	-	-
8	Toilet 4	-	-	-	-	-	-	-	-	-	-	-	-
9	Drawing	✓	-	✓	-	✓	-	-	-	-	-	-	-
10	Dining	✓	-	✓	-	✓	-	-	-	-	-	-	-
11	Lobby 1	-	-	-	-	-	-	-	-	-	-	-	-
12	Lobby 2	-	-	-	-	-	-	-	-	-	-	-	-
13	Terrace/ balcony 1	✓	-	✓	-	✓	-	-	-	✓	✗✗	-	-
14	Terrace / balcony 2	-	-	-	-	-	-	-	-	-	-	-	-
15	Terrace / balcony 3	-	-	-	-	-	-	-	-	-	-	-	-
16	Portico Utility	-	-	✓	+	✓	-	✓	-	✓	-	-	-
17	Kitchen	✓	-	✓	✓	✓	✗	✗✗	-	-	-	-	-
18	Other	-	-	-	-	-	-	-	-	-	-	-	-

Remarks

1) In flat dust was observed during checking 2) Gropa Hole's were not packed in the flat. 3) In both Toilet's Screeding instead (8") above FFL they have only provided (3") above FFL. 4) Minor chipping plastering not done in Balcony. 5) They have already done upper work in Balcony before checking.

Company	M-109	Others	Sl. No.	40905
Prepared by	MRAI-LLP	Project	Phase	—
Project Manager	R.S. SATHIRAN	Sign	Date	30-11-2022
Previous Stage report no.	RAM PRAJAD	Sign	Date	30-11-2022
Apartment No.	40003	Report filed and signed by PM?	☒ Yes ☐ No	
Checked By MD on		Other	other	
		MD Sign	For filling	☐ Yes ☐ No
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.				

Inspection should be done after:

- brickwork is completed
- chicken mesh fixed
- after cleaning the apartment
- electrical conducting work is completed

Brickwork Check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✕ for minor mistake that requires minor correction.
3. Mark ✕✕ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✕✕✕ for major mistake that cannot be corrected.
5. Wall thickness should be as per plan. Use of 4", 6" & 8" blocks must be checked.
6. All walls should have 2 beds of about 2" to 3" thickness with one no. 6 mm or 8 mm rod with M15 CC.
7. Chicken mesh should be used in each and every joint between RCC & Brickwork.
8. Joint between brickwork & beam on external side must be filled.
9. Check room dimensions with working plan. (Tolerance: 1")
10. Diagonals of each room shall be equal. (Tolerance: 2")
11. Balcony sill level should be 3'3" from SFL. (Tolerance: 1")
12. Check room height with specified height. (Tolerance: 1")
13. Check plumb of walls wherever it appears to be out of plumb. (Tolerance: 1/2")
14. Specify the No. of beams which are not aligned by more than 1" in a room.
15. Door frames must have black Japan coating and wood primer / pellambar - at cost of painter.

Certified that all corrections mentioned in the QC Report have been completed. Work can Proceed to next Stage.

Project In-charge: *[Signature]* Date: 03/12/23

S No	Room	Wall thickness (✓ or ✗)	Beds in walls (✓ or ✗)	Chicken mesh (✓ or ✗)	External brickwork & beam joint (✓ or ✗)	Room Dimensions (✓ or ✗)	Room Dimensions Difference in inches	Diagonal (✓ or ✗)	Diagonal Difference in inches	Balcony sill level (✓ or ✗)	Room Height (✓ or ✗)	Plumb of walls (Good/Avg./Bad)	Alignment of beams and walls - Nos.
1	Bedroom 1 M. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet-1 M. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 G. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet-2 G. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 C. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet-3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby-1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other												
15	Other												
Remarks													

Specify rooms that need correction:	☐ Good ☒ Avg. ☐ Bad

Misc. Checks

Was 3.75 CFT proportion box provided?	☒ Yes ☐ No
Condition of proportion box?	☐ Good ☒ Avg. ☐ Bad
Was the Apartment cleaned before starting brick work?	☐ Yes ☐ No ☒ Carit' say
Is the Apartment cleaned for plastering?	☐ Yes ☒ No
Wastage?	☐ High ☒ Medium ☐ Low
Storage of building material like bricks sand and cement.	☐ Good ☒ Avg. ☐ Bad
Drum (200 hrs) provided for curing in each flat?	☒ Yes ☐ No
Remarks:	

Door Frames & Windows check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark X for minor mistake that requires minor correction.
3. Mark X X for major mistake that requires correction by replacement or re-fixing.
4. Mark X X X for major mistake that cannot be corrected.
5. Window template depth should be between 2 to 2 1/2" after plastering.
6. Lintel level should be 7'3" from SFL & 7' from FFL. (Tolerance 1"). Lintel should be as per standard design.
7. Lofts should be at a height of 7' to 7'3" from FFL. Kitchen plat form thickness should be 2", SFL to bottom 31" (Tolerance 1")
8. Slopes of lofts and kitchen platforms to be checked by using 12" spirit level and check height from floor from 2 or 3 points.
9. Thickness of platforms & lofts should be between 2 & 2.5".
10. Provide single layer table brick at bottom of each door frame without threshold.
11. Check Z angle template size (Z angle for bathroom ventilators not required in new projects).
12. Window opening must be checked with MS square pipe templates of 2 sizes for inner and outer openings.
13. Z angle template must be 1" from brick wall surface from the inner side.

S No	Room	Door size, face and position (✓ or ✗)	Brick at bottom of door frame (✓ or ✗)	Door frame hold fast provision and fasteners (✓ or ✗)	Door lintel design & level (✓ or ✗)	Door diagonal check (✓ or ✗)	Door Plumb - two sides (✓ or ✗)	Windows lintel design & level, Sill level (✓ or ✗)	Windows size (✓ or ✗)	Windows - template depth & diagonal (✓ or ✗)	Windows - template red oxide painting (✓ or ✗)	Loft & Kitchen platform height (✓ or ✗)	Loft & Kitchen platform slope (✓ or ✗)	Door size, face and position (✓ or ✗)
1	Bedroom 1 m. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 m. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 4. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 C. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 C. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other													
15	Other													
Remarks: NOTE :- 1) kitchen platform was not casted.														

Company	MEM-CCP	Project	4003	St. No	4005
Prepared by	R.S. SAIKIRAN	Sign	R.S. SAIKIRAN	Phase	
Project Manager	RAM PRASAD	Sign	R.S. SAIKIRAN	Date	30-11-2022
Previous Stage report no.		4003	Report filed and signed by PM?	Date	30-11-2022
Apartment No.		Other		☒ Yes ☐ No	
Checked By MD on		MD Sign		other	
				For filling	☒ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.


Inspection should be done after:

- brickwork is completed
- chicken mesh fixed
- after cleaning the apartment
- electrical conducting work is completed

Brickwork Check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. Wall thickness should be as per plan. Use of 4", 6" & 8" blocks must be checked.
6. All walls should have 2 beds of about 2" to 3" thickness with one no. 6 mm or 8 mm rod with M15 CC.
7. Chicken mesh should be used in each and every joint between RCC & Brickwork.
8. Joint between brickwork & beam on external side must be filled.
9. Check room dimensions with working plan. (Tolerance: 1")
10. Diagonals of each room shall be equal. (Tolerance: 2")
11. Balcony sill level should be 3'3" from SFL. (Tolerance: 1")
12. Check room height with specified height. (Tolerance: 1")
13. Check plumb of walls wherever it appears to be out of plumb. (Tolerance: 1/2")
14. Specify the No. of beams which are not aligned by more than 1" in a room.
15. Door frames must have black Japan coating and wood primer /pellambar – at cost of painter.



All works Completed

S No	Room	Wall thickness (✓ or ✗)	Beds in walls (✓ or ✗)	Chicken mesh (✓ or ✗)	External brickwork & beam joint (✓ or ✗)	Room Dimensions (✓ or ✗)	Room Dimensions Difference in inches	Diagonal (✓ or ✗)	Diagonal Difference in inches	Balcony sill level (✓ or ✗)	Room Height (✓ or ✗)	Plumb of walls (Good/Avg./Bad)	Alignment of beams and walls - Nos.
1	Bedroom 1 M-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 G-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 C-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 C-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✗
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✗
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✗
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other												
15	Other												
Remarks													

Specify rooms that need correction:	☐ Good ☒ Avg. ☐ Bad

Misc. Checks.

Was 3.75 CFT proportion box provided?	☒ Yes ☐ No
Condition of proportion box?	☐ Good ☒ Avg. ☐ Bad
Was the Apartment cleaned before starting brick work?	☐ Yes ☐ No ☒ Cant' say
Is the Apartment cleaned for plastering?	☐ Yes ☒ No
Wastage?	☐ High ☒ Medium ☐ Low
Storage of building material like bricks sand and cement.	☐ Good ☒ Avg. ☐ Bad
Drum (200 ltrs) provided for curing in each flat?	☒ Yes ☐ No
Remarks:	

Door Frames & Windows check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✕ for minor mistake that requires minor correction.
3. Mark ✕✕ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✕✕✕ for major mistake that cannot be corrected.
5. Window template depth should be between 2 to 2 ½" after plastering.
6. Lintel level should be 7'3" from SFL & 7" from FFL. (Tolerance 1"). Lintel should be as per standard design.
7. Lofts should be at a height of 7' to 7'3" from FFL. Kitchen platform thickness should be 2", SFL to bottom 31".. (Tolerance 1")
8. Slopes of lofts and kitchen platforms to be checked by using 12" spirit level and check height from floor from 2 or 3 points.
9. Thickness of platforms & lofts should be between 2 & 2.5".
10. Provide single layer table brick at bottom of each door frame without threshold.
11. Check Z angle template size (Z angle for bathroom ventilators not required in new projects).
12. Window opening must be checked with MS square pipe templates of 2 sizes for inner and outer openings.
13. Z angle template must be 1" from brick wall surface from the inner side.

S No	Room	Door size, face and position (✓ or ✗)	Brick at bottom of door frame (✓ or ✗)	Door frame hold fast provision and fasteners (✓ or ✗)	Door lintel design & level (✓ or ✗)	Door diagonal check (✓ or ✗)	Door Plumb - two sides (✓ or ✗)	Windows lintel design & level. Sill level (✓ or ✗)	Windows size (✓ or ✗)	Windows - template depth & diagonal (✓ or ✗)	Windows - template red oxide painting (✓ or ✗)	Loft & Kitchen platform height (✓ or ✗)	Loft & Kitchen platform slope (✓ or ✗)	Door size, face and position (✓ or ✗)
1	Bedroom 1 M. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 G. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 C. Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 C. Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other							✓	✓	✓	✓	✓	✓	✓
15	Other													
Remarks:		NOTE :- 1) kitchen platform was not casted.												

GULMOHAR RESIDENCY

Sy. No. 19, Mallapur Village, Uppal, Hyderabad.
Owned & Developed by: M/s. Modi Realty Mallapur LLP.
Head office: 5-4-187/3&4 M G Road Secunderabad.

Details of Additions & Alterations

Flat No	H - 104	Block no.	H.
Flat Area	sft	Type	Deluxe / Luxury
Buyer Name	Mr. P. Lavanya		
Phone No.	7036053694	Email	lavanya.virginia@gmail.com.

9491448754.

I hereby confirm that I have given the details of the minor additions and alterations that are required in the above referred flat in the pages attached herein. Please complete the changes suggested by me. I agree to pay the charges, if any, for the additions and alterations that I have asked you to make, as per the rates suggested by you. I shall deliver all the materials that are required to be provided by me at the site on or before _____.

In case I fail to deliver these items to the site by the specified date, you may complete the works in the flat as per the standard items provided by you.

Buyers sign		Engg. Sign	
Date:		Date	20/12/23.

Note:

1. Colour shades of paints may vary from batch to batch & company to company. The Builder will not take responsibility of quality of work for dark shades especially green & blue.
2. Shade / colour of natural material like marble and granite can't be guaranteed and may vary from lot to lot. Cracks like appearance in marble is a natural feature and Builder shall not be responsible for repairs or replacement.
3. Availability of bathroom or flooring tiles of the same type /colour/make can not be guaranteed and closest possible type/colour/make may be used in its place.
4. No further change shall be permitted from this day.
5. Please sign on all pages.

Buyers sign:



Engg. Sign:



Date:

20/12/23.

Choice of colours:

Changes in flooring:

- ✓ 1) Natural wood, ^{dark} tiles in MRIP & RR (East side room)
- 2) Vitrified tiles — Guest bed room.
- ✓ 3) Ultra Spine — 2 toilets.
- 4) ~~White~~ bed room kitchen ~~vitrified~~
- 5) Hall — canite beige & kitchen
- 6) Balcony — Country Rose.
- 7) Utility — Black & white.

Wall breacking as per drawing.


Owner's sign: 

Engg. Sign: 

Date: 30/12/23.

Full

Working

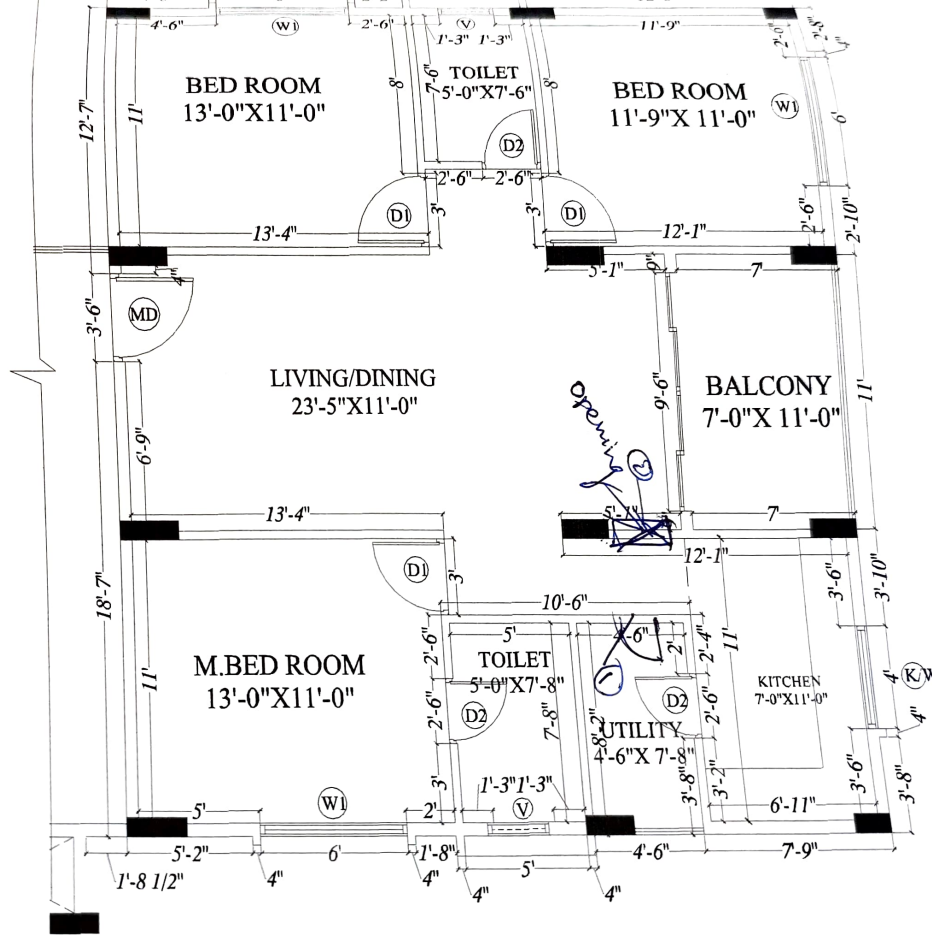

Description	Direction	Owners & Developers :	Date :	25.09.2020	Promoted by
WORKING PLAN-1360 Sit -A2 TYPE		Modi Reality Mallapur LLP	Prepared By :	Jayapradha	Modi Properties Pvt Ltd
		Project Name & Phase :	Approved By :	Soham Modi	
		Gulmohar Residency	Scale :	N.T.S	Phone: +91-40-66335551
