


Construction Division
Additions & Alteration Charges Approval Form

Company Name:		MRMLLP	Site	Gulmohar Residency
Name of the customer		Lakshmi Priyanka.		
Villa/ Flat No.		H-106.		
Sl.No	Description	Amount		
1	Total extra Charges	57190.		
2	Total refundable amount	57190.		
3	Net amount to be charges (if any)	—		
4	Net amount to be refunded (if any)	57190.		
Remarks :				
fifty Seven thousand One hundred and Ninety				
Rupees only.				
Approved by Project Manager		Approved by Design Team		Approved by MD
Date 21/02/2025		Date		Date
Sign: 		Sign:		Sign:

Note: 1. Enclose measurement & estimate sheet. 2. Send scanned copy by email to plans@modiproperties.com & CR. 3. Maintain originals in A&A of customers at site.

* Camera given on 03.05.25

ESTIMATE SHEET

Company Name:		MRMLLP		Approved by: Srinivas N		
Project:		Gulmohar Residency				
Work Description:		Extra Specs				
Flat No.		H 106				
Prepared By		Srinivas N				
Date:		21-02-2025				
S No.	Item Head	Item Description	Quantity	Units	Rate	Amount
1	Extra Charges	Master Bed Room	143	Sft	50	7150
		G B R	143	Sft	50	7150
		C B R	129	Sft	50	6450
		Living & Dining	259	Sft	50	12925
		Passage	30	Sft	50	1500
		Passage	15	Sft	50	750
		Skirting - of SBU/A 1360 sft	102	Sft	50	5075
		Balcony	77	Sft	45	3465
		Kitchen	77	Sft	45	3465
		Kitchen Platform	32	Sft	110	3520
		Dado Tiles	32	Sft	35	1120
		Bath Room Doors	42	Sft	110	4620
		Total				57190

ESTIMATE SHEET

Common Name	MIRMI P
Project	Cultural Residence
Work Description	Earth Spec
File No	H 106
Prepared By	N Simran
Date	21-02-2025

Approved by: Signature
Date: _____

S.No	Item Head	Item Description	A Length	B Width	C Height	D No.	E-AXBYCXD Quantity	F Units
1	Vitrified Tiles	Master Bed Room	13.00	11.00	1.00	1	143	Sft
2	Vitrified Tiles	G.R.R	13.00	11.00	1.00	1	143	Sft
3	Vitrified Tiles	C.B.R	11.75	11.00	1.00	1	129	Sft
4	Vitrified Tiles	Living & Dining	23.50	11.00	1.00	1.00	258.50	Sft
5	Vitrified Tiles	Passage	10.50	3.00	1.00	1.00	31.50	Sft
6	Vitrified Tiles	Passage	5.00	3.00	1.00	1.00	15.00	Sft
7	Vitrified Tiles	Skirting - cf SBUA 1360 sft	203.00	1.00	0.50	1.00	101.50	Sft
8	Vitrified Tiles	Balcony	7	11	1.00	1	77.00	Sft
9	Ceramic	Kitchen	7	11	1	1	77.00	Sft
10	Kitchen Platform	Granite	16	2	1	1	32.00	Sft
11	Dado Tiles	Ceramic	16	1	2	1	32.00	Sft
12	Bath Room Doors	Bath room Doors	3	1	7	2	42.00	Sft

Flat No.	H-106	Other		Sl. No.	42778
Company	MMR-UP	Project	GMR	Phase	
Prepared by	Sankin	Sign		Date	26-08-2023
Project Manager	Abhendra Srinivas	Sign	for @Srinivas	Date	26-08-2023
Previous stage report no.		41793	Report filed and signed by PM?	☒ Yes ☐ No	
Additions & alterations sheet date		UAI-SOLD	All pages signed by engineer & customer?	☐ Yes ☐ No	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- after cleaning the apartment.
- before starting painting, tiling & flooring.
- electrical conduct, waterproofing & plumbing work is completed (for stage II only).
- additions & alterations is finalized and signed. In case there are no additions and alterations printout of email by PM to CR confirming the same must be filed.
- additions & alterations sheets to be transferred to QC file. QC to check if A&A are made as per request.

After Plumbing & Electrical Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. Location of CPVC & PVC fittings must be checked as per measurements given in circular. Tolerance 1".
6. Location, height and spirit level of electrical points must be checked as per measurements given in circular & plan. Tolerance 1".
7. Civil work near pipes in balcony & utility must be neat and mortar should be removed from the pipes.
8. Water proofing must cover all pipes & check height above SFL.
9. Fasteners must be used as specified in circular. Especially check fixing of PVC pipes.
10. Height of DB box must be 6" below false ceiling level or 12" below slab level.
11. In case of many changes in civil work, electrical work and plumbing work, a new drawing must be prepared at HO and approved by MD.

Certified that all corrections mentioned in the QC Report have been completed. Work can Proceed to next Stage.

Project in charge	Sign	Date

S No	Room	Civil work near pipes in balcony & utility ⁷ (✓ or ✕)	CPVC & PVC Check ⁵ (✓ or ✕)	Electrical points check ⁶ (✓ or ✕)	Water proofing check ⁸ (✓ or ✕)	Proper use of fasteners check ⁹ (✓ or ✕)	Placement of DB ¹⁰ (✓ or ✕)	Placement of Generator changeover (✓ or ✕)
1	Bedroom 1 M. Bed	—	—	—	—	—	—	—
2	Toilet 1 M. Toi	—	✓	✓	✓	—	—	—
3	Bedroom 2 C. Bed	—	—	✓	✓	—	—	—
4	Toilet 2 C. Toi	—	✓	✓	✓	—	—	—
5	Bedroom 3 C. Bed	—	—	✓	✓	—	—	—
6	Toilet 3	—	—	✓	—	—	—	—
7	Drawing	—	—	—	—	—	—	—
8	Dining	—	—	✓	—	—	✓	—
9	Lobby 1	—	—	—	—	—	—	—
10	Utility / balcony 1	✕	✓	✓	—	✓	—	—
11	Utility / balcony 2	✕	✓	✓	✓	✕	—	—
12	Utility / balcony 3	—	—	—	—	—	—	—
13	Kitchen	—	✓	✓	—	—	—	—
14	Other	—	—	—	—	—	—	—
15	Other	—	—	—	—	—	—	—


Remarks **NOTE :- 1) In Utility, fasteners to be provide properly.**

Remarks on additions & alteration sheet:

Signed by engineer,	☐ Yes ☐ No	Signed by customer,	☐ Yes ☐ No
Revised drawing required from HO	☐ Yes ☐ No	Approved revised drawing attached	☐ Yes ☐ No

Miscellaneous check

Screeding done on walls upto 12" outside bathroom/utility	☒ Yes ☐ No
Bathroom /utility filled with 4" water for water proof check	☒ Yes ☐ No
Hole packing done around all pipes in ceiling and internal walls	☐ Yes ☒ No
Remarks:	

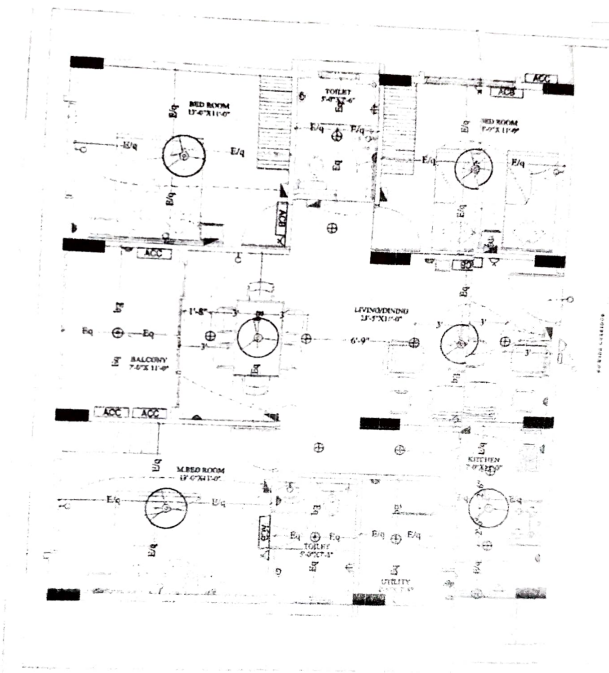

G-507
[electric]

LEGEND

S.NO	ITEM	SYMBOL	HEIGHTS
1	Common Switch	SW	1'10" TO 1'2"
2	Switch	SW	1'10" TO 1'2"
3	Common Switch	SW	1'10" TO 1'2"
4	Switch	SW	1'10" TO 1'2"
5	Common Switch	SW	1'10" TO 1'2"
6	Switch	SW	1'10" TO 1'2"
7	Common Switch	SW	1'10" TO 1'2"
8	Switch	SW	1'10" TO 1'2"
9	Common Switch	SW	1'10" TO 1'2"
10	Switch	SW	1'10" TO 1'2"
11	Common Switch	SW	1'10" TO 1'2"
12	Switch	SW	1'10" TO 1'2"
13	Common Switch	SW	1'10" TO 1'2"
14	Switch	SW	1'10" TO 1'2"
15	Common Switch	SW	1'10" TO 1'2"
16	Switch	SW	1'10" TO 1'2"
17	Common Switch	SW	1'10" TO 1'2"
18	Switch	SW	1'10" TO 1'2"
19	Common Switch	SW	1'10" TO 1'2"
20	Switch	SW	1'10" TO 1'2"

NOTE: SWITCHES SHOULD BE 1'10" TO 1'2" HEIGHTS
@ 1'10" TO 1'2" HEIGHTS

APPROVED FOR CONSTRUCTION
25 SEP 2020
Soham Modi
MANAGING DIRECTOR

Description	Direction	Owner's Representative	Date	Prepared By	Prepared By
QC-A-BLOCK-ELECTRICAL PLAN-1360 sq ft FLAT-A1 TYPE	N	Mahesh & Pooja LLP	21.09.2020	Soham Modi	Prepared By
		Project No. 1360	Approved By	N.T.S	Modi Properties Pvt Ltd
		Customer Name	Scale		Phone: 91-40-66335551

Quality Control Check Report. Stage: After Plastering (Apartments)

Fiat No.	H-106	Other		Sl. No.	41793
Company	MRM - (U.P.)	Project	G.M.P.	Phase	-
Prepared by	P. Bhattach	Sign	P.B.	Date	12-05-23
Project Manager	Ahmed	Sign	Ahmed	Date	12-05-23
Previous stage report no.		Report filed and signed by PM?			Yes
Checked By MD on	120875	MD Sign		For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☐ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- brickwork & 2 coats plastering is completed
- after cleaning the villa.
- Water proofing, screeding in bathrooms is completed.
- before starting painting, tiling & flooring.

Plastering Check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. 9" unplastered area from SFT should be left including in common areas and terraces.
6. Windows must be checked with templates. Plastering must be 3mm margin for lippun work. Tolerance: 1"
7. Provision of tiles in bathrooms, kitchen & wash areas (rough plastering).
8. Check size of sink bowl. Hole should be 1" to 2" larger. (Tolerance: 1")
9. All doors frames should have ½" grooves.
10. Sill top must me of uniform thickness, correct height, at one level & without broken edges

Certified that all corrections mentioned in the QC Report have been completed. Work can Proceed to next Stage.

Project In-charge	Sign	Date
Ahmed Khan	Ahmed	12/05/23

S No	Room	Skirting Provision (✓ or ✗)	Furnishing around door frame (✓ or ✗)	Beams & columns finishing (✓ or ✗)	Finishing of lofts (✓ or ✗)	Electricity junctions finishing (✓ or ✗)	Windows check (✓ or ✗)	Tiles provision (✓ or ✗)	Sink provision & size (✓ or ✗)	Grooves for door frames (✓ or ✗)	Balcony & terrace sill top finishing (✓ or ✗)	Screeding in bathroom & utility (✓ or ✗)	Screeding in 6" above FFL? (✓ or ✗)
1	Bedroom 1 M-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 M-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 C-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 G-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Bedroom 4	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Toilet 4	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Lobby 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Terrace/ balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Terrace/ balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
15	Terrace/ balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
16	Portico utility	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
17	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
18	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
Remarks: 1) During check we have observed dust in the flat 2) Some work was not parked in the flat 3) Before we checking they have already done the work in balcony and utility													

ATR on Quality Control Check Repot. (Apartments)

Flat No	H-106	QC report stage	After plastering	Sl. No.	4793
Company	M.R. M. C. P.	Project	C.R.P.	Phase	-
Prepared by	S.F. Goushee	Sign	<i>Goushee</i>	Date	28/7/23
Project Manager	Ahmed Khan	Sign	<i>Ahmed Khan</i>	Date	28/7/23
Receipt by QC date		Sign		Other	
Receipt at HO date		Sign		Other	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation that was made by QC:

☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.

☒ Stop further work. Proceed with work after submitting ATR on QC report to QC team.

Notes:

1. Attach a copy of the QC report to this sheet.
2. Circle each correction with a red pen - tick (✓) each circle for work completed and cross (X) each circle where work has not been completed.
3. Give remarks for each case where work has not completed on this sheet.
4. Make 2 copied of the ATR - send one to MD and other to QC.
5. Enclose required photographs - hard copy.

Remarks:

Company	H-106	Others	SL No.	10813
Prepared by	ARM-CLIP	Project	Phase	
Project Manager	P. Bhaskar	Sign	Date	25-11-22
Previous Stage report no.	Komprasad	Sign	Date	25-11-22
Apartment No.		Other	Report filed and signed by PM?	☒ Yes ☐ No
Checked By MD on		MD Sign	other	☒ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- brickwork is completed
- chicken mesh fixed
- after cleaning the apartment
- electrical conducting work is completed

Brickwork Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. Wall thickness should be as per plan. Use of 4" 6" & 8" blocks must be checked.
6. All walls should have 2 beds of about 2" to 3" thickness with one no. 6 mm or 8 mm rod with M15 CC.
7. Chicken mesh should be used in each and every joint between RCC & Brickwork.
8. Joint between brickwork & beam on external side must be filled.
9. Check room dimensions with working plan. (Tolerance: 1")
10. Diagonals of each room shall be equal. (Tolerance: 2")
11. Balcony sill level should be 3'3" from SFL. (Tolerance: 1")
12. Check room height with specified height. (Tolerance: 1")
13. Check plumb of walls wherever it appears to be out of plumb. (Tolerance: 1/2")
14. Specify the No. of beams which are not aligned by more than 1" in a room.
15. Door frames must have black Japan coating and wood primer /pellambar – at cost of painter.

APPROVED BY
06 JAN 2023
SOHAM MODI
MANAGING DIRECTOR

All works completed

S No	Room	Wall thickness (✓ or ✕)	Beds in walls (✓ or ✕)	Chicken mesh (✓ or ✕)	External brickwork & beam joint (✓ or ✕)	Room Dimensions (✓ or ✕)	Room Dimensions Difference in inches	Diagonal (✓ or ✕)	Diagonal Difference in inches	Balcony sill level (✓ or ✕)	Room Height (✓ or ✕)	Plumb of walls (Good/Avg./Bad)	Alignment of beams and walls - Nos.
1	Bedroom 1 M-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	Good	✓
2	Toilet 1 M-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	Good	✓
3	Bedroom 2 14-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	Good	✓
4	Toilet 2 C-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	Good	✓
5	Bedroom 3 Gr-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	Good	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	Good	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	Good	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	Good	✓
9	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	Good	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	Good	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	Good	✓
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	Good	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	Good	✓
14	Other												
15	Other												
Remarks	1) Brickwork workmanship in Gr-Bed to be improved.												

Specify rooms that need correction:	☐ Good ☒ Avg. ☐ Bad

Misc. Checks.

Was 3.75 CFT proportion box provided?	☒ Yes ☐ No
Condition of proportion box?	☐ Good ☒ Avg. ☐ Bad
Was the Apartment cleaned before starting brick work?	☐ Yes ☐ No ☒ Cant' say
Is the Apartment cleaned for plastering?	☒ Yes ☐ No
Wastage?	☐ High ☒ Medium ☐ Low
Storage of building material like bricks sand and cement.	☐ Good ☒ Avg. ☐ Bad
Drum (200 ltrs) provided for curing in each flat?	☒ Yes ☐ No
Remarks:	

Door Frames & Windows check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✕ for minor mistake that requires minor correction.
3. Mark ✕✕ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✕✕✕ for major mistake that cannot be corrected.
5. Window template depth should be between 2 to 2 ½" after plastering.
6. Lentil level should be 7'3" from SFL & 7' from FFL. (Tolerance 1"). Lentil should be as per standard design.
7. Lofts should be at a height of 7' to 7'3" from FFL. Kitchen plat form thickness should be 2", SFL to bottom 31" (Tolerance 1")
8. Slopes of lofts and kitchen platforms to be checked by using 12" spirit level and check height from floor from 2 or 3 points.
9. Thickness of platforms & lofts should be between 2 & 2.5".
10. Provide single layer table brick at bottom of each door frame without threshold.
11. Check Z angle template size (Z angle for bathroom ventilators not required in new projects).
12. Window opening must be checked with MS square pipe templates of 2 sizes for inner and outer openings.
13. Z angle template must be 1" from brick wall surface from the inner side.

S No	Room	Door size, face and position (✓ or ✗)	Brick at bottom of door frame ¹⁰ (✓ or ✗)	Door frame hold fast provision and fasteners. (✓ or ✗)	Door lenth design & level (✓ or ✗)	Door diagonal check (✓ or ✗)	Door Plumb - two sides (✓ or ✗)	Windows lenth design & level. Sill level (✓ or ✗)	Windows size (✓ or ✗)	Windows - template depth & diagonal ⁵ (✓ or ✗)	Windows - template red oxide painting (✓ or ✗)	Loft & Kitchen platform height (✓ or ✗)	Loft & Kitchen platform slope (✓ or ✗)	Door size, face and position (✓ or ✗)
1	Bedroom 1 M-Rd	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 K-Rd	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 C-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 G-Rd	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
15	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
Remarks:		1) kitchen platform work not started.												

Flat No.		Quality Control Check Report.		Stage: After Brickwork (Apartments/ Lab Spaces)	
Company	H-106	Others		Sl. No.	40873
Prepared by	MRM-CLLP	Project		Phase	
Project Manager	P. Bhaskar	Sign	G. 118	Date	25-11-22
Previous Stage report no.	Rampasad	Sign	P. S. R.	Date	25-11-22
Apartment No.		10062	Report filed and signed by PM?	☒ Yes ☐ No	
Checked By MD on		Other		other	
		MD Sign		For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- brickwork is completed
- chicken mesh fixed
- after cleaning the apartment
- electrical conducting work is completed

Brickwork Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✕ for minor mistake that requires minor correction.
3. Mark ✕✕ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✕✕✕ for major mistake that cannot be corrected.
5. Wall thickness should be as per plan. Use of 4", 6" & 8" blocks must be checked.
6. All walls should have 2 beds of about 2" to 3" thickness with one no. 6 mm or 8 mm rod with M15 CC.
7. Chicken mesh should be used in each and every joint between RCC & Brickwork.
8. Joint between brickwork & beam on external side must be filled.
9. Check room dimensions with working plan. (Tolerance: 1")
10. Diagonals of each room shall be equal. (Tolerance: 2")
11. Balcony sill level should be 3'3" from SFL. (Tolerance: 1")
12. Check room height with specified height. (Tolerance: 1")
13. Check plumb of walls wherever it appears to be out of plumb. (Tolerance: 1/2")
14. Specify the No. of beams which are not aligned by more than 1" in a room.
15. Door frames must have black Japan coating and wood primer / pellambar - at cost of painter.

Certified that all corrections mentioned in the QC Report have been completed. Work can proceed to next Stage.

Project In-charge: *[Signature]* Date: 25/11/22

Quality Control Check Report. Stage: After Brickwork (Apartments/ Lab Spaces)

S No	Room	Wall thickness (✓ or ✗)	Beds in walls (✓ or ✗)	Chicken mesh (✓ or ✗)	External brickwork & beam joint (✓ or ✗)	Room Dimensions (✓ or ✗)	Room Dimensions Difference in inches	Diagonal (✓ or ✗)	Diagonal Difference in inches	Balcony sill level (✓ or ✗)	Room Height (✓ or ✗)	Plumb of walls (Good/Avg./Bad)	Alignment of beams and walls - Nos.
1	Bedroom 1 M-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 M-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 C-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 G-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other												
15	Other												
Remarks		1) Brickwork workmanship in G-Bed to be improved.											

Quality Control Check Report. Stage: After Brickwork (Apartments/ Lab Spaces)

Quality of edges and corners in all rooms?

☐ Good ☒ Avg. ☐ Bad

Specify rooms that need correction:

Misc. Checks.

Was 3.75 CFT proportion box provided?

☐ Yes ☐ No

Condition of proportion box?

☐ Good ☒ Avg. ☐ Bad

Was the Apartment cleaned before starting brick work?

☐ Yes ☐ No ☒ Cant' say

Is the Apartment cleaned for plastering?

☒ Yes ☐ No

Wastage?

☐ High ☒ Medium ☐ Low

Storage of building material like bricks sand and cement.

☐ Good ☒ Avg. ☐ Bad

Drum (200 ltrs) provided for curing in each flat?

☒ Yes ☐ No

Remarks:

Door Frames & Windows check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✕ for minor mistake that requires minor correction.
3. Mark ✕✕ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✕✕✕ for major mistake that cannot be corrected.
5. Window template depth should be between 2 to 2 ½" after plastering.
6. Lintel level should be 7'3" from SFL & 7' from FFL. (Tolerance 1"). Lintel should be as per standard design.
7. Lofts should be at a height of 7' to 7'3" from FFL. Kitchen platform thickness should be 2", SFL to bottom 31". (Tolerance 1")
8. Slopes of lofts and kitchen platforms to be checked by using 12" spirit level and check height from floor from 2 or 3 points.
9. Thickness of platforms & lofts should be between 2 & 2.5".
10. Provide single layer table brick at bottom of each door frame without threshold.
11. Check Z angle template size (Z angle for bathroom ventilators not required in new projects).
12. Window opening must be checked with MS square pipe templates of 2 sizes for inner and outer openings.
13. Z angle template must be 1" from brick wall surface from the inner side.

Quality Control Check Report.

Stage: After Brickwork (Apartments/ Lab Spaces)

S No	Room	Door size, face and position (✓ or ✗)	Brick at bottom of door frame (✓ or ✗)	Door frame hold fast provision and fasteners. (✓ or ✗)	Door lintel design & level (✓ or ✗)	Door diagonal check (✓ or ✗)	Door Plumb - two sides (✓ or ✗)	Windows lintel design & level. Sill level (✓ or ✗)	Windows size (✓ or ✗)	Windows - template depth & diagonal (✓ or ✗)	Windows - template red oxide painting (✓ or ✗)	Loft & Kitchen platform height (✓ or ✗)	Loft & Kitchen platform slope (✓ or ✗)	Door size, face and position (✓ or ✗)
1	Bedroom 1 M-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 M-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 C-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 G-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other													
15	Other													
Remarks:		1) Kitchen platform wast not casted.												

GULMOHAR RESIDENCY

Sy. No. 19, Mallapur Village, Uppal, Hyderabad.
Owned & Developed by: M/s. Modi Realty Mallapur L.P.
Head office, 5-4-187/3&4 M G Road Secunderabad.

Details of Additions & Alterations

Flat No	106	Block no.	11
Flat Area	sft	Type	Deluxe / Luxury
Buyer Name	Mr. S Lakshmi	Pitfork	
Phone No.	9160086633	Email	yeshuacharya@gmail.com

I hereby confirm that I have given the details of the minor additions and alterations that are required in the above referred flat in the pages attached herein. Please complete the changes suggested by me. I agree to pay the charges, if any, for the additions and alterations that I have asked you to make, as per the rates suggested by you. I shall deliver all the materials that are required to be provided by me at the site on or before

In case I fail to deliver these items to the site by the specified date, you may complete the works in the flat as per the standard items provided by you.

Buyers sign		Engg. Sign	
Date:	09/01/25	Date	11/01/25

Note:

1. Colour shades of paints may vary from batch to batch & company to company. The Builder will not take responsibility of quality of work for dark shades especially green & blue.
2. Shade / colour of natural material like marble and granite can't be guaranteed and may vary from lot to lot. Cracks like appearance in marble is a natural feature and Builder shall not be responsible for repairs or replacement.
3. Availability of bathroom or flooring tiles of the same type /colour/make can not be guaranteed and closest possible type/colour/make may be used in its place.
4. No further change shall be permitted from this place.
5. Please sign on all pages.

Buyers sign: 

Engg. Sign: 

Date: 09-01-25

Choice of colours:

(iv) cream colour overall floor.

Changes in flooring:

hall, dining bedrooms and kitchen
own customer granite to be laid

2 bathrooms & utility default tiles
to be laid


external s.m.-floor - ultraspinked.

woodwork - floor - blackberry
wood - black outside

Buyers sign:

Engg. Sign:

Date: 04-1-25

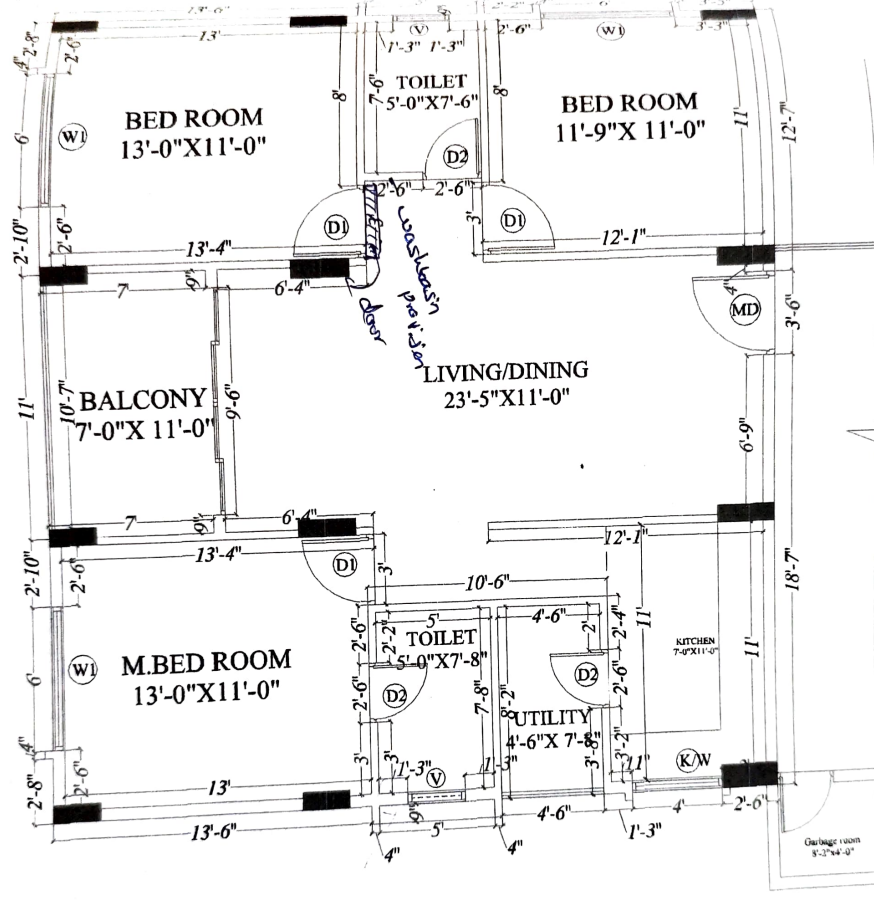

Description	Direction	Owners & Developers :	Date :	Promoted by
			Prepared By :	Modi Properties Pvt Ltd
		Modi Reality Mallapur LLP	Jayapradha	
		Project Name & Phase :	Sohan Modi	Phone: +91-40-66335551
			N.T.S	
