

Construction Division
Additions & Alteration Charges Approval Form

Company Name:	MRMLP		Site	Gulmohar Residency
Name of the customer	Nazreen			
Flat No.	H-302			

Description	Amount
Total extra Charges	1
Total refundable amount	1
Net amount to be charges (if any)	1
Net amount to be refunded (if any)	1

Notes:

Approved by Project Manager	Signature	Date	Sign:
Approved by Design Team	Signature	Date	Sign:
Approved by MD	Signature	Date	Sign:

1. Enclose measurement & estimate sheet. 2. Send scanned copy by email to plans@modiproperties.com & CR. 3. Submit originals in A&A of customers at site.

Company	H-302	Project	Stage III	Phase	
Prepared by	MR NLP	Sign	GMR	Date	12/08/24
Project Manager	Sanket	Sign	<i>[Signature]</i>	Date	12/08/24
Previous stage report no.		Report filed and signed by PM			☐ Yes ☐ No
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after :

- Completing stage II works.
- Complete works like doors, windows, grills, electrical wiring, switches, french door glass, etc.
- In case of modular kitchen provide platform, granite and dado and modular kitchen in this stage.
- Provide video door phone in this stage.
- Possession for wood work cannot be given until QC check for stage III is completed and all corrections mentioned in the report are made.

Miscellaneous check:

Modular kitchen to be provided	☐ Yes ☒ No	Modular kitchen provided	☐ Yes ☒ No
Modular kitchen workman ship	☐ Good ☒ Avg ☐ Poor	Modular kitchen granite & dado workman ship & finishing	☐ Good ☒ Avg ☐ Poor
Video door phone /wifi cam to be provided	☐ Yes ☒ No	Video door phone/wifi cam provided	☐ Yes ☒ No
Painting marks and drops are cleaned from floor, windows, walls.		☒ Good ☐ Avg ☐ Poor	

Rate the quality of (Good ✓, Avg. X, Poor - needs correction X X, NA)													
S No	Room	Door, door knob & door stopper fitting	Door, door knob & door stopper cleaning	Window grills & quality	Window grills fitting & finishing	Windows quality	Window fitting & finishing	Balcony railing quality & finishing	French door quality & fitting	CP jali quality and fitting	Edge building	Switch boards fitting & covering with plastic covers	Junction box covers painting
1	Bedroom 1 N.B	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Bedroom 2 C.B	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 3 G.B	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Toilet 1 N.T	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Toilet 2 C.T	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other												
15	Other												
Remarks													

Quality Control Check Report. Stage: After Finishing Stage II (Apartments)


Flat No	H-302	Other	—	Sl. No.	43083
Company	MRM-(LLP)	Project	GMR	Phase	—
Prepared by	Abhishek Gaudar	Sign	Abhishek	Date	13-08-24
Project Manager	Srinivas	Sign	② Srinivas	Date	13-08-24
Previous stage report no.	43082	Report filed and signed by PM		☒ Yes ☐ No	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- Completion of flooring, bathroom /utility tiles, first coat of paint.
- Completion of doors, windows, grills, electrical wiring, switches must be done in next stage
- False ceiling must be completed before flooring.
- Kitchen platform, granite and dado must be completed where modular kitchen is not provided.
- Provide granite soffit for main door and balconies in this stage.



Miscellaneous check			
Main door fixed with lock & stopper	☒ Yes ☐ No	Granite soffit for balcony provided	☒ Yes ☐ No
Granite soffit for balcony required	☒ Yes ☐ No	Balcony granite soffit edge polishing	☐ Good ☒ Avg ☐ Poor
Balcony granite soffit workmanship	☐ Good ☒ Avg ☐ Poor	Granite soffit for main door provided	☒ Yes ☐ No
Granite soffit for main door required	☒ Yes ☐ No	Main door granite soffit edge polishing	☐ Good ☒ Avg ☐ Poor
Main door granite soffit workmanship	☒ Good ☐ Avg ☐ Poor		

Tiling & granite work	Rate the quality of (Good ✓, Avg. X, Poor - needs correction XX, NA)														
S No	Room	Workmanship of tiling	White cement filling around CPVC lines	Corners finishing	Finishing near doors	Finishing on top of tiles	Finishing near ventilators	Step at bathroom entrance / utility	Step for shower / pot wash	Tile joint grouting	Granite platform finishing and edge polishing	Granite platform slope	Granite platform height	Finishing under granite platform	
1	Toilet 1 m-Toi	✓	XX	✓	✓	✓	XX	✓	✓	✓	✓	✓	✓	✓	
2	Toilet 2 c-Toi	✓	XX	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
3	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
4	Toilet 4	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
5	Wash basin in dining area	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
6	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
7	Utility	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
8	Other														
9	Other														
Remarks		① Flat should be cleaned properly. ② Balcony Granite Polishing & finishing must be improved.													

Certified that all measures have been taken to ensure the quality of the work.

Certified that all corrections mentioned in the QC Report have been completed. Work can proceed to next stage.

Project In-charge

Sign

Date

Tiling & granite work		Rate the quality of (Good ✓, Avg. X, Poor – needs correction XX, NA)												
S No	Room	Workmanship of tiling	White cement filling around CPVC lines	Corners finishing	Finishing near doors	Finishing on top of tiles	Finishing near ventilators	Step at bathroom entrance / utility	Step for shower / pot wash	Tile joint grouting	Granite platform finishing and edge polishing	Granite platform slope	Granite platform height	Finishing under granite platform
1	Toilet 1 m-Toi	✓	XX	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 2 c-Toi	✓	XX	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 4	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Wash basin in dining area	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Other													
9	Other													
Remarks		① Flat should be cleaned properly. ② Balcony Granite Polishing & finishing must be improved.												

Certified that all corrections mentioned in the QC Report have been completed. Work can proceed to next stage.

Project In-charge

Sign

Date

Quality Control Check Report. Stage: After Finishing Stage II (Apartments)

Flooring & painting		Rate the quality of (Good ✓, Avg. X, Poor – needs correction XX, NA)												
S No	Room	Color variation of floor tiles	Flooring workmanship & grouting	Skirting size (3")	Skirting workmanship	Plastering above skirting	Plastering & finishing of walls	Crack filling	Loft Finishing	Windows check	General quality of painting & finishing	Door & frame painting quality	Door beading, lippam and painting quality.	Edge building
1	Bedroom 1	M-BED	✓	✓	✓	✓	✓	✓	—	✓	✓	✓	✓	✓
2	Bedroom 2	M-BED	✓	✓	✓	✓	✓	✓	—	✓	✓	✓	✓	✓
3	Bedroom 3	C-BED	✓	✓	✓	✓	✓	✓	—	✓	✓	✓	✓	✓
4	Drawing		✓	✓	✓	✓	✓	✓	—	✓	✓	✓	✓	✓
5	Dining		✓	✓	✓	✓	✓	✓	—	✓	✓	✓	✓	✓
6	Lobby 1		—	—	—	—	—	—	—	—	—	—	—	X
7	Utility / balcony 1		✓	X	✓	X	✓	✓	—	—	✓	—	—	X
8	Utility / balcony 2		✓	X	—	—	✓	X	—	✓	✓	—	—	X
9	Utility / balcony 3		—	—	—	—	—	—	—	✓	✓	✓	✓	X
10	Kitchen		✓	✓	✓	✓	✓	X	✓	✓	✓	—	—	X
11	Other													
12	Other													
Remarks		① Civil touchups Around Junction box must be done at G-BED												

Certified that all corrections mentioned in the QC Report have been completed. Work can Proceed to next Stage.

Project In-charge: [Signature]

Sign: [Signature] Date:

Page 3 of 3

Quality Control Check Report. Stage: After Plumbing & Electrical (Apartments)

Flat No.	H-302	Other		Sl. No.	43032
Company	MRM-(LLP)	Project	GMR	Phase	
Prepared by	Abhishek Bhatnagar	Sign	<i>Abhishek</i>	Date	17-07-24
Project Manager	Srinivas	Sign	<i>Srinivas</i>	Date	17-07-24
Previous stage report no.	41887	Report filed and signed by PM?	☒ Yes ☐ No		
Additions & alterations sheet date	05-07-24	All pages signed by engineer & customer?	☒ Yes ☐ No		
Checked By MD on	MD Sign	For filing	☐ Yes ☐ No		

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- after cleaning the apartment.
- before starting painting, tiling & flooring.
- electrical conduct, waterproofing & plumbing work is completed (for stage II only).
- additions & alterations is finalized and signed. In case there are no additions and alterations printout of email by PM to CR confirming the same must be filed.
- additions & alterations sheets to be transferred to QC file. QC to check if A&A are made as per request.

After Plumbing & Electrical Check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark X for minor mistake that requires minor correction.
3. Mark X X for major mistake that requires correction by replacement or re-fixing.
4. Mark X X X for major mistake that cannot be corrected.
5. Location of CPVC & PVC fittings must be checked as per measurements given in circular. Tolerance 1".
6. Location, height and spirit level of electrical points must be checked as per measurements given in circular & plan. Tolerance 1".
7. Civil work near pipes & utility must be neat and mortar should be removed from the pipes.
8. Water proofing must cover all pipes & check height above SFL.
9. Fasteners must be used as specified in circular. Especially check fixing of PVC pipes.
10. Height of DB box must be 6" below false ceiling level or 12" below slab level.
11. In case of many changes in civil work, electrical work and plumbing work, a new drawing must be prepared at HO and approved by MD.

Certified that all corrections mentioned
in the QC Report have been completed.
Project In-charge *Srinivas* Date *17-07-24*

S No	Room	Civil work near pipes in balcony & utility ⁷ (✓ or ✕)	CPVC & PVC Check ⁵ (✓ or ✕)	Electrical points check ⁶ (✓ or ✕)	Water proofing check ⁸ (✓ or ✕)	Proper use of fasteners check ⁹ (✓ or ✕)	Placement of DB ¹⁰ (✓ or ✕)	Placement of Generator changeover (✓ or ✕)
1	Bedroom 1 M-BED	—	—	✓	—	—	—	—
2	Toilet 1 M-Toi	—	✓	✓	✓	—	—	—
3	Bedroom 2 K-BED	—	—	✓	—	—	—	—
4	Toilet 2 C-Toi	—	✕	✓	✓	—	—	—
5	Bedroom 3 G-BED	—	—	✓	—	—	—	—
6	Toilet 3	—	—	—	—	—	—	—
7	Drawing	—	—	✓	—	—	✓	—
8	Dining	—	—	✓	—	—	—	—
9	Lobby 1	—	—	—	—	—	—	—
10	Utility / balcony 1	✓	✓	✓	—	✓	—	—
11	Utility / balcony 2	✓	✓	✓	✓	✓	—	—
12	Utility / balcony 3	—	—	—	—	—	—	—
13	Kitchen	—	✓	✓	—	—	—	—
14	Other							
15	Other							

Remarks ① C-Toi CPVC Pipe should be fixed properly.

Remarks on additions & alteration sheet:

Signed by engineer.	☐ Yes ☐ No	Signed by customer.	☐ Yes ☐ No
Revised drawing required from H/O	☐ Yes ☐ No	Approved revised drawing attached	☐ Yes ☐ No

Flat No.	11-302	Other	—	Sl. No.	41887
Company	MRM-CLLP	Project	GMR	Phase	—
Prepared by	P. Bhargava	Sign	<i>[Signature]</i>	Date	30-05-23
Project Manager	Ahmed	Sign	<i>[Signature]</i>	Date	30-05-23
Previous stage report no.					
Checked By MD on	11/2/38	MD Sign		Report filed and signed by PM?	☒ Yes ☐ No
Recommendation:				For filling	☐ Yes ☐ No

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- brickwork & 2 coats plastering is completed
- after cleaning the villa.
- Water proofing, screeding in bathrooms is completed.
- before starting painting, tiling & flooring.

Plastering Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. 9" unplastered area from SFL should be left including in common areas and terraces.
6. Windows must be checked with templates. Plastering must be 3mm margin for luppum work. Tolerance 1/4".
7. Provision of tiles in bathrooms, kitchen & wash areas (rough plastering).
8. Check size of sink bowl. Hole should be 1" to 2" larger. (Tolerance: 1")
9. All doors frames should have 1/2" grooves.
10. Sill top must be of uniform thickness, correct height, at one level & without broken edges.

Certified that all corrections mentioned in the QC Report have been completed. Work can Proceed to next Stage.

Project In-charge	Sign	Date
<i>[Signature]</i>		

S No	Room	Skirting Provision (✓ or ✗)	Furnishing around door frame (✓ or ✗)	Beams & columns finishing (✓ or ✗)	Finishing of lofts (✓ or ✗)	Electricity junctions finishing (✓ or ✗)	Windows check (✓ or ✗)	Tiles provision (✓ or ✗)	Sink provision & size (✓ or ✗)	Grooves for door frames (✓ or ✗)	Balcony & terrace sill top finishing (✓ or ✗)	Screeding in bathroom & utility (✓ or ✗)	Screeding in 6" above FFL? (✓ or ✗)
1	Bedroom 1 M-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M-Toi	✓	✓	✓	✓	✓	✗	✓	✓	✓	✓	✓	✓
3	Bedroom 2 K-Bed	✓	✓	✗	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 C-Toi	✓	✓	✓	✓	✓	✗	✓	✓	✓	✓	✓	✓
5	Bedroom 3 Gr-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Bedroom 4	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Toilet 4	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Lobby 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Balcony	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Utility	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
15	Portico	✓	✓	✓	✓	✓	✓	✓	✓	✓	✗	✓	✓
16	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
17	Other	✓	✓	✓	✓	✓	✓	✗	✓	✓	✓	✓	✓
Remarks													

Company	MRM - UP	Project	GTMR	Phase	41238
Prepared by	K. Snela	Sign	Snela	Date	28-01-2023
Project Manager	Ram prasad	Sign	Ram prasad	Date	28-01-2023
Previous Stage report no.	40408	Report filed and signed by PM?	☒ Yes ☐ No		
Apartment No.		Other	other		
Checked By MD on		MD Sign	For filling ☐ Yes ☐ No		

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- brickwork is completed
- chicken mesh fixed
- after cleaning the apartment
- electrical conducting work is completed

Brickwork Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. Wall thickness should be as per plan. Use of 4", 6" & 8" blocks must be checked.
6. All walls should have 2 beds of about 2" to 3" thickness with one no. 6 mm or 8 mm rod with M15 CC.
7. Chicken mesh should be used in each and every joint between RCC & Brickwork.
8. Joint between brickwork & beam on external side must be filled.
9. Check room dimensions with working plan. (Tolerance: 1")
10. Diagonals of each room shall be equal. (Tolerance: 2")
11. Balcony sill level should be 3'3" from SFL. (Tolerance: 1")
12. Check room height with specified height. (Tolerance: 1")
13. Check plumb of walls wherever it appears to be out of plumb. (Tolerance: 1/2")
14. Specify the No. of beams which are not aligned by more than 1" in a room.
15. Door frames must have black Japan coating and wood primer /pellambar - at cost of painter.

Certified that all corrections mentioned in the QC Report have been completed.

Project In-charge: *[Signature]* Sign: *[Signature]* Date: 03/02/23

S No	Room	Wall thickness (✓ or ✗)	Beds in walls (✓ or ✗)	Chicken mesh (✓ or ✗)	External brickwork & beam joint (✓ or ✗)	Room Dimensions (✓ or ✗)	Room Dimensions Difference in inches	Diagonal (✓ or ✗)	Diagonal Difference in inches	Balcony sill level (✓ or ✗)	Room Height (✓ or ✗)	Plumb of walls (Good/ Avg/ Bad)	Alignment of beams and walls - Nos.
1	Bedroom 1 m. bed	✓	✓	✓	✗	✓	1	✓	1	1	✓	Avg	✓
2	Toilet 1 m. toi	✓	✓	✓	✗	✓	1	✓	1	1	✓	1	✓
3	Bedroom 2 K. bed	✓	✓	✗	✗	✓	1	✓	1	1	✓	1	✗
4	Toilet 2 C. Toi	✓	✓	✓	✗	✓	1	✓	1	1	✓	1	✓
5	Bedroom 3 A. bed	✓	✓	✓	✗	✓	1	✓	1	1	✓	1	✓
6	Toilet 3	1	1	1	1	1	1	1	1	1	1	1	1
7	Drawing	✓	✓	✓	✗	✓	1	✓	1	1	✓	1	✓
8	Dining	✓	✓	✓	1	✓	1	✓	1	1	✓	1	✓
9	Lobby 1	1	1	1	1	1	1	✓	1	1	✓	1	✓
10	Utility / balcony 1	✓	✓	✓	✗	✓	1	✓	1	✓	✓	1	✓
11	Utility / balcony 2	✓	✓	✓	✗	✓	1	✓	1	1	✓	1	✓
12	Utility / balcony 3	1	1	1	1	1	1	✓	1	1	1	1	1
13	Kitchen	✓	✓	✓	✗	✓	1	✓	1	1	✓	1	✓
14	Other											1	✓
15	Other												
Remarks													

Specify rooms that need correction:	☐ Good ☒ Avg. ☐ Bad

Misc. Checks.

Was 3.75 CFT proportion box provided?	☒ Yes ☐ No
Condition of proportion box?	☐ Good ☒ Avg. ☐ Bad
Was the Apartment cleaned before starting brick work?	☐ Yes ☐ No ☒ Cant' say
Is the Apartment cleaned for plastering?	☒ Yes ☐ No
Wastage?	☐ High ☒ Medium ☐ Low
Storage of building material like bricks sand and cement.	☐ Good ☒ Avg. ☐ Bad
Drum (200 ltrs) provided for curing in each flat?	☒ Yes ☐ No
Remarks:	

Door Frames & Windows check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✕ for minor mistake that requires minor correction.
3. Mark ✕✕ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✕✕✕ for major mistake that cannot be corrected.
5. Window template depth should be between 2 to 2 1/2" after plastering.
6. Lintel level should be 7'3" from SFL & 7' from FFL. (Tolerance 1"). Lintel should be as per standard design.
7. Lofts should be at a height of 7' to 7'3" from FFL. Kitchen plat form thickness should be 2". SFL to bottom 31" (Tolerance 1")
8. Slopes of lofts and kitchen platforms to be checked by using 12" spirit level and check height from floor from 2 or 3 points.
9. Thickness of platforms & lofts should be between 2 & 2.5".
10. Provide single layer table brick at bottom of each door frame without threshold.
11. Check Z angle template size (Z angle for bathroom ventilators not required in new projects).
12. Window opening must be checked with MS square pipe templates of 2 sizes for inner and outer openings.
13. Z angle template must be 1" from brick wall surface from the inner side.

S No	Room	Door size, face and position (✓ or ✗)	Brick at bottom of door frame (✓ or ✗)	Door frame hold fast provision and fasteners (✓ or ✗)	Door lintel design & level (✓ or ✗)	Door diagonal check (✓ or ✗)	Door Plumb - two sides (✓ or ✗)	Windows lintel design & level, Sill level (✓ or ✗)	Windows size (✓ or ✗)	Windows - template depth & diagonal (✓ or ✗)	Windows - template red oxide painting (✓ or ✗)	Loft & Kitchen platform height (✓ or ✗)	Loft & Kitchen platform slope (✓ or ✗)	Door size, face and position (✓ or ✗)
1	Bedroom 1 m.bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 m.Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 K.bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 c.Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 G.bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
15	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
Remarks:		Note: 1) Kitchen platform was not casted.												
		2) Loft hacking was not done.												

GULMOHAR RESIDENCY

Sy. No. 19, Mallapur Village, Uppal, Hyderabad.
Owned & Developed by: M/s. Modi Realty Mallapur L.L.P.
Head office; 5-4-187/3&4 M G Road Secunderabad.

Details of Additions & Alterations

Flat No	4-302	Block no.	,
Flat Area	sft	Type	Deluxe / Luxury
Buyer Name	Mr. Nageshwar		
Phone No.	Email		

I hereby confirm that I have given the details of the minor additions and alterations that are required in the above referred flat in the pages attached herein. Please complete the changes suggested by me. I agree to pay the charges, if any, for the additions and alterations that I have asked you to make, as per the rates suggested by you. I shall deliver all the materials that are required to be provided by me at the site on or before In case I fail to deliver these items to the site by the specified date, you may complete the works in the flat as per the standard items provided by you.

Buyers sign	Nageshwar	Engg. Sign	
Date:	05/07/2024	Date	05/07/2024

ote:

1. Colour shades of paints may vary from batch to batch & company to company. The Builder will not take responsibility of quality of work for dark shades especially green & blue.

Shade / colour of natural material like marble and granite can't be guaranteed and may vary from lot to lot. Cracks like appearance in marble is a natural feature and Builder shall not be responsible for repairs or replacement.

Availability of bathroom or flooring tiles of the same type /colour/make can not be guaranteed and closest possible type/colour/make may be used in its place.
No further change shall be permitted from this day.
Please sign on all pages.

s sign:


Engg. Sign:

Date: 5-7-24

Choice of colours:

Changes in flooring:

- 1) 2'x2' tiles in living, 3 bedrooms
- 2) Country almond in kitchen flooring
- 3) Country chocolate in kitchen dado.
- 4) Country rosea in balcony balcony flooring
- 5) Black honey flooring, black side wall in utility
- 6) ultra sparkle tiles in bath towels.
- 7) ~~in~~ no need of pattern over in bath towels.
- 8 Country almond in utility.

Buyers sign:



Engg. Sign:



Date:

05/7/24

Changes in electrical points: (mark on plan)

Choice of Bathroom tiles, CP fittings & Sanitary ware:

12' Bathroom Tiles, CP fittings & Sanitary ware.

11

Buyers sign:

Buyers Sign:

Date:

5/7/24

Changes in kitchen platform: (mark on plan)

Kitchen chimney hole By company /
Pambabu sir.

Kitchen platform chomfearing / proven
prabot sir.

Other Changes:

Buyers sign:



Engg. Sign:



Date:



5/7/24



	HEALTH FAUCET
	ANGLE VALVE
	NANI TRAP
	3" RAIN WATER PIPE
	GEASER POINT
	WALL MIXTURE
	TAP / LONG BODY

Description	Direction	Owners & Developers :	Date :	16.09.20	Promoted by
PLUMBING PLAN-1360 Sft (A2-TYPE)		Modi Reality Mallapur LLP	Prepared By :	Jayapradha	Modi Properties Pvt Ltd
		Project Name & Phase :	Approved By :	Soham Modi	
		Gulmohar Residency	Scale :	N.T.S	Phone:+91-40-66335551

5/12/24

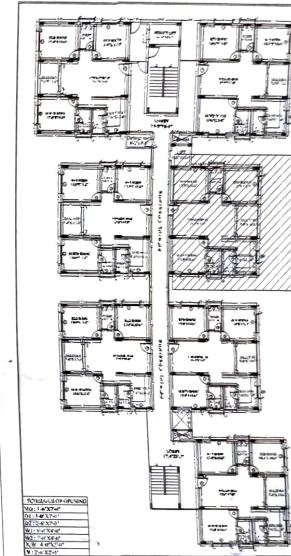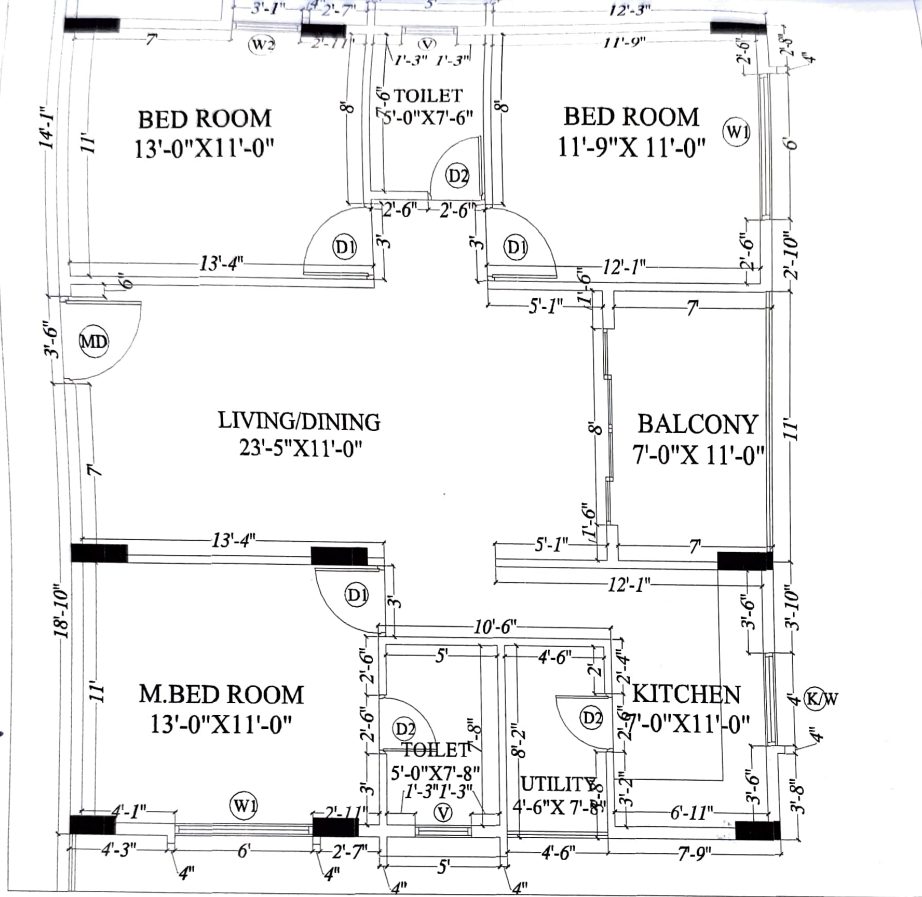

Description	Direction	Owners & Developers :	Date :	26.10.2022	Promoted by
H-BLOCK-Flat no-2-B2-Type-West facing- Working plan		Modi Reality Mallapur LLP	Prepared By :	Jayapradha	Modi Properties Pvt Ltd
		Project Name & Phase :	Approved By :	Soham Modi	
		Gulmohar Residency	Scale :	N.T.S	
					Phone:+91-40-66335551

From: Gulmohar Residency <info@modiproperties.com>
Sent: 16 April 2025 18:36
To: cr@modiproperties.com; feedback@modiproperties.com;
kprasad@modiproperties.com; gbrambabu@modiproperties.com; gmr-
const@modiproperties.in; samads86@gmail.com
Subject: Complaints And Suggestions from Gulmohar Residency

Complaint Id : 306654

Project Name : Gulmohar Residency

Block No / Phase : Block H

Flat No/Villa :302

Nature of complaint :Day to Day Maintenance

Customer Name : Mohammed samad

Email : samads86@gmail.com

Complaints :

1. leakages in flat and stair case
2. water quality foul smell in water
3. no security checks when entering in community
4. garbage collection was not regular request a dedicated dustbin for h block
5. water shortage causing inconvenience everyday
6. 3rd lift was not yet installed which was promised by builder
7. no proper lights in parking,uneven drive way surface causing issues and especially at night times
8. cctv camera was not fixed in lift
9. water logging in h block entrance
10. generators often fail to switch on automatically due to damaged batteries,power fluctuations causing damage electrical items in home

Note:

1. Please allow atleast two weeks for us to attend your complaint.
2. In general written response / reply to complaints shall not be given.
3. In case the complaint is not attended to for over two weeks customers are requested to send a reminder using the form given.

ACTION TAKEN REPORT (FOR COMPLAINTS)

Flat / bungalow No.	H 302	ATR Date	27-05-2025
Project	GMR	Complaint Date	16-04-2025
Customer Name	Samad		
Prepared By	Anil		
Project Manager's Sign	Ahmed	Admin Officer's Sign	S.Shravya

Note: Original ATR should be sent to CR & a copy to MD. CR to file original in customer's file.

[illegible]

Note: 1. Keep the report brief. 2. Do not repeat the complaint. 3. Use terms like “Work completed”, “Changes not permitted – work not taken up”, “Kept pending at customer’s request”, “Beyond our scope of work”, etc.

Quality Control Check Report for ATR on Complaints .

Flat / bungalow No.	H-302	ATR Date	27-05-2025		
Project	GMR	Complaint Date	16-04-2025		
Customer Name	Samad				
Prepared by	Saikiran	Date	28-05-2025	Sign	Saikiran
Project Manager	Ahmed	Date	28-05-2025	Sign	Ahmed
HO receipt date		Sign			
Checked by MD on		MD Sign			
MD's Remarks:					
CR to send letter to customer	☐ Yes ☐ No	For filling	☐ Yes ☐ No		

Note: CR will send a copy of ATR and complaint to QC immediately after the receipt of the ATR. QC will send their report on the ATR to the MD within 3 working days. Aruna to file to file it in MDs pending complaints file.

Complaint S No.	Quality of action taken by Site Engg on complaint?	If action on the complaint was not taken then, was the reason for not taking action justified?
1.	☐ Good ☐ Avg. ☐ Bad	Yes
2.	Avg	☐ Yes ☐ No
3.	Avg	☐ Yes ☐ No
4.	Avg	☐ Yes ☐ No
5.	Avg	☐ Yes ☐ No
6.	Avg	☐ Yes ☐ No
7.	☐ Good ☐ Avg. ☐ Bad	Yes
8.	☐ Good ☐ Avg. ☐ Bad	Yes
9.	Avg	☐ Yes ☐ No
10.	Avg	☐ Yes ☐ No
11.	☐ Good ☐ Avg. ☐ Bad	☐ Yes ☐ No
12.	☐ Good ☐ Avg. ☐ Bad	☐ Yes ☐ No
Remarks:		
