

Internal memo no. 903/35/A
Annexure - B
RMC pour report

Company/ firm:	Modi Reality Mallapur LLP	Block No.:	
Project:	Gulmohar Residency	Flat / Villa no.:	-
Supplier:	KN Infra	Slab no.:	For E block east side drive way slab
Requisition nos.:	20250528019	A. Estimated quantity:	200 M3
PO nos.:	20250528018	B. Requisition quantity:	200 M3
	Sign of Admin	C. Actual quantity poured	37.5 M3
	Sign of Project Manager	D. Difference (C-A)	162.5 M3

Details of RMC pour

Sl.	Date	Time of dispatch from RMC plant	Time of receipt at site	Time of pour	Quantity poured	Dc No. / Batch no.	Specified wt @2400 kgs/m3	Measured weight (kgs)	Short fall in weight in kgs	Deduction for shortfall in Rs.	7 day cube test strength in kN/m2	28 days cube test strength in kN/m2
1.	02.08.25	14:20	15:15	15:25	08	0014	19200	19200	-			
2.	02.08.25	14:45	15:50	16:00	08	0015	19200	18930	270			
3.	02.08.25	16:25	17:35	17:50	08	0016	19200	19150	50			
4.	02.08.25	16:45	17:50	18:05	08	0017	19200	18930	270			
5.	02.08.25	17:40	18:50	19:05	5.5	0018	13200	13600	-			
6.												
7.												
8.												
9.												
10.												
Total:							90000	89810	590			
Remarks	As per ordered quantity 200 M3 Received 37.5 M3											

Note: 1. Report to be sent on a daily basis to purchase@modiproperties.com and report-audit@modiproperties.com. 2. Report must be prepared during pour and not later. 3. Report must be sent within one working day. 4. Multiple report can be sent for one PO. 5. Weigh all vehicles. 6. 6 cubic meters vehicle should have a net weight of 14,110 kgs @ 2,400kgs/ m3. If the shortfall is more than 50 kgs per load purchase to debit supplier shortfall amount on pro-rata basis. 7. Site to calculate shortfall. 8. Maintain original report + weightment slips + pour reports + test reports + photographs



KN INFRA

Survey No: 294, Ramapally (V), Keesara(M)
Medchel Dist - 501 301

Email : kninfra1@gmail.com


Ph. No: 9100999994/9100755567

GLOBAL RMC
ENGINEER'S CONCRETE

DELIVERY CHALLAN

Customer Name: GULMOHAR RESIDENCY		D.C. No: 0014	Date: 02.08.2025		
Delivery Site: MALLAPUR		Truck No: TS08UG4351	Mode: PUMP		
S.No:	Description	Qty	Units	Cum. Qty	Remarks
1	M-20 RMC	8	Cum	8	-
Other Documents Enclosed:					
1)					
2)					
Note: No alterations will be accepted without supplier & Customer Signatures alongwith reasons.					
Received above material in good condition					
Customer Signature					
fo K N INFRA					
Authorized Signatory					

Rs 2025052808

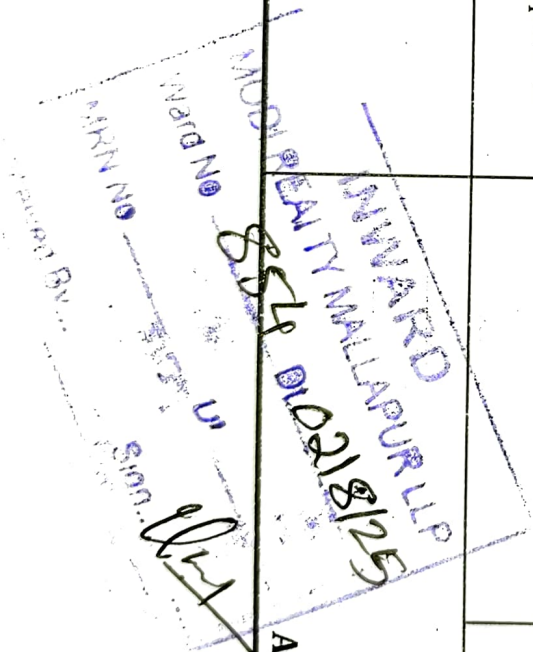

KN INFRA

Survey No: 294, Ramapally (V), Keesara(M)

Medchel Dist - 501 301

GLOBAL RMC
ENGINEER'S CONCRETE

Email : kninfra1@gmail.com

Ph. No: 9100999994/9100755567

DELIVERY CHALLAN

Customer Name: GULMOHAR RESIDENCY			D.C. No: 0015		Date: 02.08.2025
Delivery Site: MALLAPUR			Truck No: TS08UG4354		Mode: PUMP
S.No:	Description	Qty	Units	Cum. Qty	Remarks
2	M-20 RMC	8	Cum	16	-
Other Documents Enclosed: 1) 2)			For Office use only		
			Driver Name: P.MALLESH		
Note: No alterations will be accepted without supplier & Customer Signatures alongwith reasons.			Signature:		
Received above material in good condition			fo K N INFRA		
Customer Signature			Authorised Signatory		

INWARD
MODI REALTY MALLAPUR LLP
Ward No. **855** Dt. **02/8/25**
MRN No. **855**
Received By... **Sign.**

KN INFRA

Survey No: 294, Ramapally (V), Keesara(M)
Medchel Dist - 501 301

GLOBAL RMC
ENGINEER'S CONCRETE

Email : kninfra1@gmail.com

Ph. No: 9100999994/9100755567

DELIVERY CHALLAN

Customer Name: GULMOHAR RESIDENCY			D.C. No: 0016		Date: 02.08.2025
Delivery Site: MALLAPUR			Truck No: TS08UG5054		Mode: PUMP
S.No:	Description	Qty	Units	Cum. Qty	Remarks
3	M-20 RMC	8	Cum	24	-
Other Documents Enclosed:			For Office use only		
1)			Driver Name:		<i>C. Sridhar</i>
2)			Signature:		
Note: No alterations will be accepted without supplier & Customer Signatures alongwith reasons.					
Received above material in good condition			fo K N INFRA		
Customer Signature			INWARD MODI REALTY MALLAPUR LLP 856 DL 02/8/25 Authorized Signatory <i>[Signature]</i>		

Ward No. **856**
MRN No. **DL 02/8/25**
Received By... *[Signature]*
Sign. *[Signature]*

KN INFRA

Survey No: 294, Ramapally (V), Keesara(M)

Medchel Dist - 501 301

Email : kninfra1@gmail.com

Ph. No: 9100999994/9100755567

GLOBAL RMC
ENGINEER'S CONCRETE

DELIVERY CHALLAN

Customer Name: GULMOHAR RESIDENCY			D.C. No: 0017		Date: 02.08.2025
Delivery Site: MALLAPUR			Truck No: TS08UG4350		Mode: PUMP
S.No:	Description	Qty	Units	Cum. Qty	Remarks
4	M-20 RMC	8	Cum	32	-
Other Documents Enclosed: 1) 2)			For Office use only		
			Driver Name: SAMPATH REDDY		
Note: No alterations will be accepted without supplier & Customer Signatures alongwith reasons.			Signature:		
Received above material in good condition			fo K N INFRA		
Customer Signature			Authorised Signatory		

INWARD
MODI REALTY MALLAPUR LLP
857 **02/8/25**
Ward No. **857**
MARN No. **857**
Signature: **[Signature]**

KN INFRA

Survey No: 294, Ramapally (V), Keesara(M)
Medchel Dist - 501 301

Email : kninfra1@gmail.com

Ph. No: 9100999994/9100755567



DELIVERY CHALLAN

Customer Name: GULMOHAR RESIDENCY			D.C. No: 0018		Date: 02.08.2025
Delivery Site: MALLAPUR			Truck No: TS08UG7853		Mode: PUMP
S.No:	Description	Qty	Units	Cum. Qty	Remarks
5	M-20 RMC	5.5	Cum	37.5	-
Other Documents Enclosed:			For Office use only		
1)			Driver Name:		BR.SANTOSH
2)			Signature:		
Note: No alterations will be accepted without supplier & Customer Signatures alongwith reasons.					
Received above material in good condition			fo K N INFRA		
Customer Signature			Authorised Signatory		

INWARD
MODI REALTY MALLAPUR LLP
Ward No **859**
MRN No **02/8/25**
Sign. *[Signature]*
