


Construction Division
Additions & Alteration Charges Approval Form

Company Name:	MRMLLP	Site	Gulmohar Residency
Name of the customer	H-607		
Villa/ Flat No.	Inanisha . A.C.		
Sl.No	Description	Amount	
1	Total extra Charges	15768	
2	Total refundable amount	11305	
3	Net amount to be charges (if any)	4463.	
4	Net amount to be refunded (if any)	—	

Remarks : Extra Charges.

four thousand Six hundred and three rupees only.

Approved by Project Manager	Approved by Design Team	Approved by MD
Date 10-01-2025	Date	Date
Sign: 	Sign:	Sign:

Note: 1. Enclose measurement & estimate sheet. 2. Send scanned copy by email to plans@modiproperties.com & CR. 3. Maintain originals in A&A of customers at site.



ESTIMATE SHEET									
Company Name:		MRMLLP		Project:		Gulmohar Residency		Work Description:	
Flat No.		H 607		Prepared By		Srinivas N		Date:	
S No.		Item Head		Item Description		Quantity		Units	
I	Extra Charges	Statura Regal 4' x 2'		Sft		149		35	
		G B R		Sft		121		35	
		C B R		Sft		121		35	
		Skirting		Sft		60		35	
2	Refund Amount	Living and Dining		Sft		264		35	
		Skirting		Sft		48		35	
		Kitchen Dado tiles		Sft		11		35	
Total								4463	
								11305	
								385	
								1680	
								9240	
								15768	
								2100	
								4235	
								4235	
								5198	
		Amount		Rate		Quantity		Units	

[illegible]

Quality Control Check Report. Stage: After Finishing Stage II (Apartments)

Flat No	H-607			Other	Sl. No.	42-798
Company	MRMIP			Project	Phase	
Prepared by	Sankar Khona			Sign	Date	17/02/24
Project Manager	Narendar			Sign	Date	17/02/24
Previous stage report no.				Report filed and signed by PM		☐ Yes ☒ No
Checked By MD on	42609			MD Sign	For filling	☐ Yes ☒ No
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required. Inspection should be done after: • Completion of flooring, bathroom /utility tiles, first coat of paint. • Completion of doors, windows, grills, electrical wiring, switches must be done in next stage • False ceiling must be completed before flooring. • Kitchen platform, granite and dado must be completed where modular kitchen is not provided. • Provide granite soffit for main door and balconies in this stage.						

Miscellaneous check:

Main door fixed with lock & stopper	☒ Yes ☐ No	Granite soffit for balcony provided	☒ Yes ☐ No
Granite soffit for balcony required	☒ Yes ☐ No	Balcony granite soffit edge polishing	☒ Good ☐ Avg ☐ Poor
Balcony granite soffit workmanship	☐ Good ☒ Avg ☐ Poor	Granite soffit for main door provided	☐ Yes ☒ No
Granite soffit for main door required	☒ Yes ☐ No	Main door granite soffit edge polishing	☐ Good ☒ Avg ☐ Poor
Main door granite soffit workmanship	☐ Good ☒ Avg ☐ Poor		

Stage: After Finishing Stage II (Apartments)														
S No	Room	Rate the quality of (Good ✓, Avg. ✕, Poor – needs correction ✕✕, NA)												
		Workmanship of tiling	White cement filling around CPVC lines	Comers finishing	Finishing near doors	Finishing on top of tiles	Finishing near ventilators	Step at bathroom entrance / utility	Step for shower / pot wash	Tile joint grouting	Granite platform finishing and edge polishing	Granite platform slope	Granite platform height	Finishing under granite platform
1	Toilet 1	M.T	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 2	C.T	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Toilet 3		✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 4		✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Wash basin in dining area		✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Kitchen		✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Utility		✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Other													
9	Other													
Remarks														



Quality Control Check Report.

Stage: After Finishing Stage II (Apartments)

Sanity Control Check Repot.		Stage: After Finishing Stage II (Apartments)													
Flooring & painting		Rate the quality of (Good ✓, Avg X, Poor - needs correction X X, N/A)													
S No	Room	Color variation of floor tiles	Flooring workman ship & grouting	Skirting size (3")	Skirting workmanship	Plastering above skirting	Plastering & finishing of walls	Crack filling	Loft Finishing	Windows check	General quality of painting & finishing	Door & frame painting quality	Door heading, lipping and painting quality	Edge building	
1	Bedroom 1 M.B	✓	✓	✓	✓	✓	✓	✓	✓	✓	X	✓	✓	✓	
2	Bedroom 2 C.B	✓	✓	✓	✓	✓	✓	✓	✓	✓	X	✓	✓	✓	
3	Bedroom 3 G.B	✓	✓	✓	✓	✓	✓	✓	✓	✓	X	✓	✓	✓	
4	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	X	✓	✓	✓	
5	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	X	✓	✓	✓	
6	Lobby T	✓	✓	✓	✓	✓	✓	✓	✓	✓	X	✓	✓	✓	
7	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
8	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
9	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
10	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
11	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
12	Other	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
Remarks		NOTE 1) Painting works to be done at entire flat.													

Draft after finishing stage II, check report. apts. Dt 17-10-2020 ver5

Quality Control Check Report. Stage: After Finishing Stage III (Apartments)

Flat No	M-607	Other	-	Sl. No.	42818
Company	MPM-Up	Project	Gar R	Phase	-
Prepared by	Sarkar	Sign		Date	27/02/2024
Project Manager	Narender	Sign		Date	27/02/2024
Previous stage report no.		612798	Report filed and signed by PM		☐ Yes ☒ No
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.					

Inspection should be done after :

- Completing stage II works.
- Complete works like doors, windows, grills, electrical wiring, switches, french door glass, etc.
- In case of modular kitchen provide platform, granite and dado and modular kitchen in this stage.
- Provide video door phone in this stage.
- Possession for wood work cannot be given until QC check for stage III is completed and all corrections mentioned in the report are made.

Miscellaneous check:

Modular kitchen to be provided	☒ Yes ☐ No	Modular kitchen provided	☐ Yes ☐ No
Modular kitchen workman ship	☐ Good ☒ Avg ☐ Poor	Modular kitchen granite & dado workman ship & finishing	☐ Good ☐ Avg ☐ Poor
Video door phone /wifi cam to be provided	☒ Yes ☐ No	Video door phone/wifi cam provided	☐ Yes ☒ No
Painting marks and drops are cleaned from floor, windows, walls.		☐ Good ☐ Avg ☒ Poor	

Quantity Control Check Report. Stage: After Finishing Stage III (Apartments)

Rate the quality of (Good ✓, Avg. X, Poor – needs correction ✗ X, NA)													
S No	Room	Door, door knob & door stopper fitting	Door, door knob & door stopper cleaning	Window grills & quality	Window grills fitting & finishing	Windows quality	Window fitting & finishing	Balcony railing quality & finishing	French door quality & fitting	CP jali quality and fitting	Edge building	Switch boards fitting & covering with plastic covers	Junction box covers painting
1	Bedroom 1 M. Bed	✓	✓	✓	✗	✓	✓	1	1	1	✓	✓	✓
2	Bedroom 2 C. Bed	✓	✓	✓	✗	✓	✓	1	1	1	✓	✓	✓
3	Bedroom-3 C. Bed	✓	✓	✓	✗	✓	✓	1	1	1	✓	✓	✓
4	Drawing	✓	✓	1	1	1	1	1	1	1	✓	✓	✓
5	Dining	1	1	1	1	1	1	1	1	1	1	1	1
6	Lobby 1	1	1	1	1	1	1	1	1	1	1	1	1
7	Utility / balcony 1	1	1	1	1	1	1	1	1	1	1	1	1
8	Utility / balcony 2	✓	✓	1	1	1	1	1	1	1	1	1	1
9	Utility / balcony 3	1	1	1	1	1	1	1	1	1	1	1	1
10	Kitchen	1	1	✓	✓	✓	✓	1	1	1	✓	✓	✓
11	Toilet 1 M. Toi	✓	✓	✓	✓	✓	✓	1	1	1	✓	✓	✓
12	Toilet 2 C. Toi	✓	✓	✓	✓	✓	✓	1	1	1	✓	✓	✓
13	Toilet 3	1	1	1	1	1	1	1	1	1	1	1	1
14	Other												
15	Other												
Remarks		S-Board missed (or) not fixed in C. Bed.											
(2) At couple of places Junction Box covers not provided.													

Quality Control Check Report. Stage: After Plumbing & Electrical (Apartments)

Flat No.	H-607	Other	Sl. No.	42609
Company	MRM-CLP	Project	Phase	-
Prepared by	P. Bhaskar	Sign	Date	18-11-23
Project Manager	Saminathan / Ahmed	Sign	Date	18-11-23
Previous stage report no.	42515	Report filed and signed by PM?	Yes ☒ No ☐	
Additions & alterations sheet date	20/06/23	All pages signed by engineer & customer?	Yes ☐ No ☒	
Checked By MD on	MD Sign	For filling	Yes ☐ No ☐	

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- after cleaning the apartment.
- before starting painting, tiling & flooring.
- electrical conduct, waterproofing & plumbing work is completed (for stage II only).
- additions & alterations is finalized and signed. In case there are no additions and alterations printout of email by PM to CR confirming the same must be filed.
- additions & alterations sheets to be transferred to QC file. QC to check if A&A are made as per request.

After Plumbing & Electrical Check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected
5. Location of CPVC & PVC fittings must be checked as per measurements given in circular. Tolerance 1"
6. Location, height and spirit level of electrical points must be checked as per measurements given in circular & plan. Tolerance 1"
7. Civil work near pipes in balcony & utility must be neat and mortar should be removed from the pipes.
8. Water proofing must cover all pipes & check height above SFL.
9. Fasteners must be used as specified in circular. Especially check fixing of PVC pipes.
10. Height of DB box must be 6" below false ceiling level or 12" below slab level
11. In case of many changes in civil work, electrical work and plumbing work, a new drawing must be prepared at HO and approved by MD.

Quality Control Check Repot. Stage: After Plumbing & Electrical (Apartments)

S No	Room	Civil work near pipes in balcony & utility ⁷ (✓ or ✕)	CPVC & PVC Check ⁵ (✓ or ✕)	Electrical points check ⁶ (✓ or ✕)	Water proofing check ⁸ (✓ or ✕)	Proper use of fasteners check ⁹ (✓ or ✕)	Placement of DB ¹⁰ (✓ or ✕)	Placement of Generator changeover (✓ or ✕)
1	Bedroom 1 M. Bed	—	—	—	—	—	—	—
2	Toilet 1 M. Tor	—	—	✓	—	—	—	—
3	Bedroom 2 K. Bed	—	✓	✓	✓	✓	—	—
4	Toilet 2 C. Tor	—	—	✓	—	—	—	—
5	Bedroom 3 G. Bed	—	✓	✓	✓	✓	—	—
6	Toilet 3	—	—	✓	—	—	—	—
7	Drawing	—	—	—	—	—	—	—
8	Dining	—	—	✓	—	—	✓	—
9	Lobby 1	—	—	✓	—	—	—	—
10	Utility balcony 1	✓	✓	✓	✓	✓	—	—
11	Utility balcony 2	✓	✓	✓	—	✓	—	—
12	Utility balcony 3	—	—	—	—	—	—	—
13	Kitchen	—	✓	✓	—	—	—	—
14	Other							
15	Other							
Remarks								
Remarks on additions & alteration sheet:								
Signed by engineer,		☐ Yes ☒ No		Signed by customer,		☐ Yes ☒ No		
Revised drawing required from HO		☐ Yes ☐ No		Approved revised drawing attached		☐ Yes ☐ No		

Quality Control Check Repot. Stage: After Plumbing & Electrical (Apartments)

Miscellaneous check

Screeding done on walls upto 12" outside bathroom/utility

☒ Yes ☐ No

Bathroom /utility filled with 4" water for water proof check

☐ Yes ☒ No

Hole packing done around all pipes in ceiling and internal walls

☒ Yes ☐ No

Remarks:



Self
Quality Control Check Repot. Stage: After Plumbing & Electrical (Apartments)

Flat No.	H-607	Other	—	Sl. No.	—
Company	NRM LLP	Project	—	Phase	—
Prepared by	V. Ganbhatta	Sign	GMB	Date	19/11/2023
Project Manager	Narendra	Sign	Ku	Date	19/11/2023
Previous stage report no.	42515	Report filed and signed by PM?		☒ Yes ☐ No	
Additions & alterations sheet date	—	All pages signed by engineer & customer?		☒ Yes ☐ No	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No
Recommendation: ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC. ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team. ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required. ☐ Proceed with further work. ATR not required.					

Inspection should be done after:

- after cleaning the apartment.
- before starting painting, tiling & flooring.
- electrical conduct, waterproofing & plumbing work is completed (for stage II only).
- additions & alterations is finalized and signed. In case there are no additions and alterations printout of email by PM to CR confirming the same must be filed.
- additions & alterations sheets to be transferred to QC file. QC to check if A&A are made as per request.

After Plumbing & Electrical Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. Location of CPVC & PVC fittings must be checked as per measurements given in circular. Tolerance 1".
6. Location, height and spirit level of electrical points must be checked as per measurements given in circular & plan. Tolerance 1".
7. Civil work near pipes in balcony & utility must be neat and mortar should be removed from the pipes.
8. Water proofing must cover all pipes & check height above SFL.
9. Fasteners must be used as specified in circular. Especially check fixing of PVC pipes.
10. Height of DB box must be 6" below false ceiling level or 12" below slab level.
11. In case of many changes in civil work, electrical work and plumbing work, a new drawing must be prepared at HO and approved by MD.



SNo	Room	Civil work near pipes in balcony & utility ⁷ (✓ or ✕)	CPVC & PVC Check ⁵ (✓ or ✕)	Electrical points check ⁶ (✓ or ✕)	Water proofing check ⁸ (✓ or ✕)	Proper use of fasteners check ⁹ (✓ or ✕)	Placement of DB ¹⁰ (✓ or ✕)	Placement of Generator changeover (✓ or ✕)
1	Bedroom 1 M. Bed	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M. Toilet	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 G. Bed	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 G. Toilet	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 C. Bed	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	—	—	—	—	—	—	—
7	Drawing	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓
9	Lobby 1	—	—	—	—	—	—	—
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3	—	—	—	—	—	—	—
13	Kitchen	✓	✓	✓	✓	✓	✓	✓
14	Other	—	—	—	—	—	—	—
15	Other	—	—	—	—	—	—	—
Remarks								
Remarks on additions & alteration sheet:								
Signed by engineer,		☒ Yes ☐ No		Signed by customer,		☒ Yes ☐ No		
Revised drawing required from HO		☒ Yes ☐ No		Approved revised drawing attached		☒ Yes ☐ No		

Miscellaneous check

Screeding done on walls upto 12" outside bathroom/utility	☒ Yes ☐ No
Bathroom /utility filled with 4" water for water proof check	☒ Yes ☐ No
Hole packing done around all pipes in ceiling and internal walls	☒ Yes ☐ No
Remarks:	

Quality Control Check Report. Stage: After Brickwork (Apartments/ Lab Spaces)

Flat No.	H-602	Others	-	Sl. No.	41833
Company	ARM LLP	Project	GMR	Phase	-
Prepared by	SAIKIRAN	Sign	<i>[Signature]</i>	Date	25-05-2023
Project Manager	AMAR	Sign	<i>[Signature]</i>	Date	25-05-2023
Previous Stage report no.	40924	Report filed and signed by PM?			☐ Yes ☒ No
Apartment No.		Other		other	
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- brickwork is completed
- chicken mesh fixed
- after cleaning the apartment
- electrical conducting work is completed

Brickwork Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark X for minor mistake that requires minor correction.
3. Mark X X for major mistake that requires correction by replacement or re-fixing.
4. Mark X X X for major mistake that cannot be corrected.
5. Wall thickness should be as per plan. Use of 4", 6" & 8" blocks must be checked.
6. All walls should have 2 beds of about 2" to 3" thickness with one no. 6 mm or 8 mm rod with M15 CC.
7. Chicken mesh should be used in each and every joint between RCC & Brickwork.
8. Joint between brickwork & beam on external side must be filled,
9. Check room dimensions with working plan. (Tolerance: 1")
10. Diagonals of each room shall be equal. (Tolerance: 2")
11. Balcony sill level should be 3'3" from SFL. (Tolerance: 1")
12. Check room height with specified height. (Tolerance: 1")
13. Check plumb of walls wherever it appears to be out of plumb. (Tolerance: 1/2")
14. Specify the No. of beams which are not aligned by more than 1" in a room.
15. Door frames must have black Japan coating and wood primer /pellambar – at cost of painter.

Certified that all corrections mentioned in the QC Report have been completed. Work can Proceed to next Stage.

Project In-charge	Sign	Date
<i>[Signature]</i>		

S No	Room	Wall thickness (✓ or ✗)	Beds in walls (✓ or ✗)	Chicken mesh (✓ or ✗)	External brickwork & beam joint (✓ or ✗)	Room Dimensions (✓ or ✗)	Room Dimensions Difference in inches	Diagonal (✓ or ✗)	Diagonal Difference in inches	Balcony sill level (✓ or ✗)	Room Height (✓ or ✗)	Plumb of walls (Good/Avg./Bad)	Alignment of beams and walls - Nos.
1	Bedroom 1 M-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M-toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 G-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 C-toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 C-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✗
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other												
15	Other												
Remarks													

Quality of edges and corners in all rooms?

☐ Good ☒ Avg. ☐ Bad

Specify rooms that need correction:

Misc. Checks.

Was 3.75 CFT proportion box provided?

☒ Yes ☐ No

Condition of proportion box?

☐ Good ☒ Avg. ☐ Bad

Was the Apartment cleaned before starting brick work?

☐ Yes ☐ No ☒ Cant' say

Is the Apartment cleaned for plastering?

☒ Yes ☐ No

Wastage?

☐ High ☒ Medium ☐ Low

Storage of building material like bricks sand and cement.

☐ Good ☒ Avg. ☐ Bad

Drum (200 ltrs) provided for curing in each flat?

☒ Yes ☐ No

Remarks:

Door Frames & Windows check

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction
2. Mark ✕ for minor mistake that requires minor correction.
3. Mark ✕✕ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✕✕✕ for major mistake that cannot be corrected.
5. Window template depth should be between 2 to 2 1/2" after plastering.
6. Lintel level should be 7'3" from SFL & 7' from FFL. (Tolerance 1"). Lintel should be as per standard design.
7. Lofts should be at a height of 7' to 7'3" from FFL. Kitchen platform thickness should be 2", SFL to bottom 31".. (Tolerance 1")
8. Slopes of lofts and kitchen platforms to be checked by using 12" spirit level and check height from floor from 2 or 3 points.
9. Thickness of platforms & lofts should be between 2 & 2.5".
10. Provide single layer table brick at bottom of each door frame without threshold.
11. Check Z angle template size (Z angle for bathroom ventilators not required in new projects).
12. Window opening must be checked with MS square pipe templates of 2 sizes for inner and outer openings.
13. Z angle template must be 1" from brick wall surface from the inner side.

Draft Brickwork Check Report.														
Stage: After Brickwork (Apartments/ Lab Spaces)														
S No	Room	Door size, face and position (✓ or ✗)	Brick at bottom of door frame (✓ or ✗)	Door frame hold fast provision and fasteners. (✓ or ✗)	Door lintel design & level (✓ or ✗)	Door diagonal check (✓ or ✗)	Door Plumb - two sides (✓ or ✗)	Windows lintel design & level. Still level (✓ or ✗)	Windows size (✓ or ✗)	Windows - template depth & diagonal (✓ or ✗)	Windows - template red oxide painting (✓ or ✗)	Loft & Kitchen platform height (✓ or ✗)	Loft & Kitchen platform slope (✓ or ✗)	Door size, face and position (✓ or ✗)
1	Bedroom 1 M-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
2	Toilet 1 M-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 G-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
4	Toilet 2 C-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 C-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Utility / balcony 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Utility / balcony 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Utility / balcony 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
14	Other													
15	Other													
Remarks:		NOTE :- 1) Kitchen platform was not casted.												
		2) Loft backing was not done.												

Quality Control Check Report. Stage: After Plastering (Apartments)

Flat No.	H-607	Other	—	Sl. No.	42515
Company	ARM-CLP	Project	GMR	Phase	—
Prepared by	P. Bhaskar	Sign	Bms	Date	28-10-23
Project Manager	Narendar	Sign	[Signature]	Date	28-10-23
Previous stage report no.	41833	Report filed and signed by PM?	☒ Yes ☐ No		
Checked By MD on		MD Sign		For filling	☐ Yes ☐ No

Recommendation:

- ☐ Stop further work. Submit ATR on QC report to QC team. Proceed only after recheck by QC.
- ☐ Stop further work. Proceed with work after submitting ATR on QC report to QC team.
- ☒ Proceed with further work only after making corrections pointed out in the QC report. ATR not required.
- ☐ Proceed with further work. ATR not required.

Inspection should be done after:

- brickwork & 2 coats plastering is completed
- after cleaning the villa.
- Water proofing, screeding in bathrooms is completed.
- before starting painting, tiling & flooring.

Plastering Check.

Notes:

1. Mark ✓ for correct or minor mistake which does not require correction.
2. Mark ✗ for minor mistake that requires minor correction.
3. Mark ✗✗ for major mistake that requires correction by replacement or re-fixing.
4. Mark ✗✗✗ for major mistake that cannot be corrected.
5. 9" unplastered area from SFL should be left including in common areas and terraces.
6. Windows must be checked with templates. Plastering must be 3mm margin for lippum work. Tolerance 1/4".
7. Provision of tiles in bathrooms, kitchen & wash areas (rough plastering).
8. Check size of sink bowl. Hole should be 1" to 2" larger. (Tolerance: 1")
9. All doors frames should have 1/2" grooves.
10. Sill top must be of uniform thickness, correct height, at one level & without broken edges.

Certified that all corrections mentioned in the QC Report have been completed. Work can Proceed to next Stage.

Project In-charge	Sign	Date
[Signature]	[Signature]	28/10/23

Quality Control Check Report. Stage: After Plastering (Apartments)

S No	Room	Skirting Provision (✓ or ✗)	Furnishing around door frame (✓ or ✗)	Beams & columns finishing (✓ or ✗)	Finishing of lofts (✓ or ✗)	Electricity junctions finishing (✓ or ✗)	Windows check (✓ or ✗)	Tiles provision (✓ or ✗)	Sink provision & size (✓ or ✗)	Grooves for door frames (✓ or ✗)	Balcony & terrace sill top finishing (✓ or ✗)	Screeding in bathroom & utility (✓ or ✗)	Screeding in 6" above FFL? (✓ or ✗)
1	Bedroom 1 M-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✗	✓	✓	✓
2	Toilet 1 M-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
3	Bedroom 2 K-Bed	✓	✓	✓	✓	✓	✗	✓	✓	✓	✓	✓	✓
4	Toilet 2 C-Toi	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
5	Bedroom 3 G-Bed	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
6	Toilet 3	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
7	Bedroom 4	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
8	Toilet 4	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
9	Drawing	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
10	Dining	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
11	Lobby 1	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
12	Lobby 2	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
13	Balcony	✓	✓	✓	✓	✓	✓	✓	✓	✓	✗	✓	✓
14	Utility	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
15	Portico	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
16	Kitchen	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
17	Other												
Remarks													

GULMOHAR RESIDENCY

By: No. 19, Malleswari Villages, 1st stage, Hyderabad.
Owned & Developed by: M/s. Mohi Resale Malleswari P.L.P.
Head office: 5-A-187/3B/A M.C. Road Secunderabad.

Details of Additions & Alterations

Flat No	44 603	Block no.	44
Flat Area	1260 sq ft	Type	Deluxe / Luxury
Buyer Name	Mr. J. Jeyaraj		
Phone No.	078354211050	Email	jeyaraj@rediffmail.com

I hereby confirm that I have given the details of the minor additions and alterations that are required in the above referred flat in the pages attached hereto. Please complete the changes suggested by me. I agree to pay the charges, if any, for the additions and alterations that I have asked you to make, as per the rates suggested by you. I shall deliver all the materials that are required to be provided by me as the site on or before _____.

In case I fail to deliver these items to the site by the specified date, you may complete the works in the flat as per the standard items provided by you.

Buyer's sign	J. Jeyaraj	Engg. Sign	
Date:	20/06/22	Date	

Note:

1. Colour shades of paints may vary from batch to batch & company to company. The Builder will not take responsibility of quality of work for dark shades especially green & blue.
2. Shade / colour of natural material like marble and granite can't be guaranteed and may vary from lot to lot. Cracks like appearance in marble is a natural feature and Builder shall not be responsible for repairs or replacement.
3. Availability of bathroom or flooring tiles of the same type / colour/make can not be guaranteed and closest possible type/colour/make may be used in its place.
4. No further change shall be permitted from this day.
5. Please sign on all pages.

Buyer's sign:

Engg. Sign:

Date:

Choice of colours:

Changes in flooring:

① ~~use 3 bed room~~ - use 3 bed room - include.

① Statuario Pearl - 3 Bed room.

Buyers sign:

Engg. Sign:

Date:

D = 305



Changes in electrical points: (mark on plan)

Choice of Bathroom tiles, CP fittings & Sanitary ware:

- (1) MB - Halapya Brains
- (2) CB / O'Hara
- (3)

Buyers sign:

Engg. Sign:

Date:



Changes in kitchen platform: (mark on plan)

① Kitchen as per 15-104
floor/ceiling - Same

② Balcony - as per 15-104

③ Utility.
→ flooring Tiles - black honey
→ wall Tiles - Blanco white

Hall & dining bay customer,
kitchen door

Other Changes:

④ Utility. as per 15-104



→ flooring - black honey
→ wall - Blanco white

Buyers sign:

Engg. Sign:

Date:



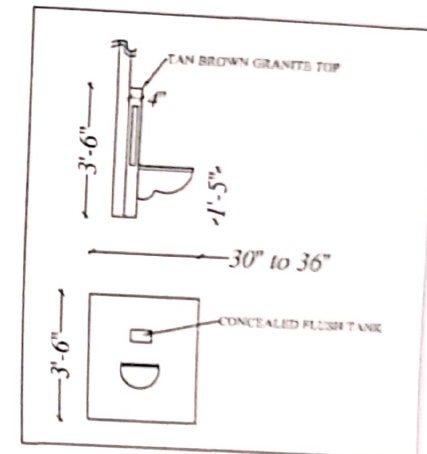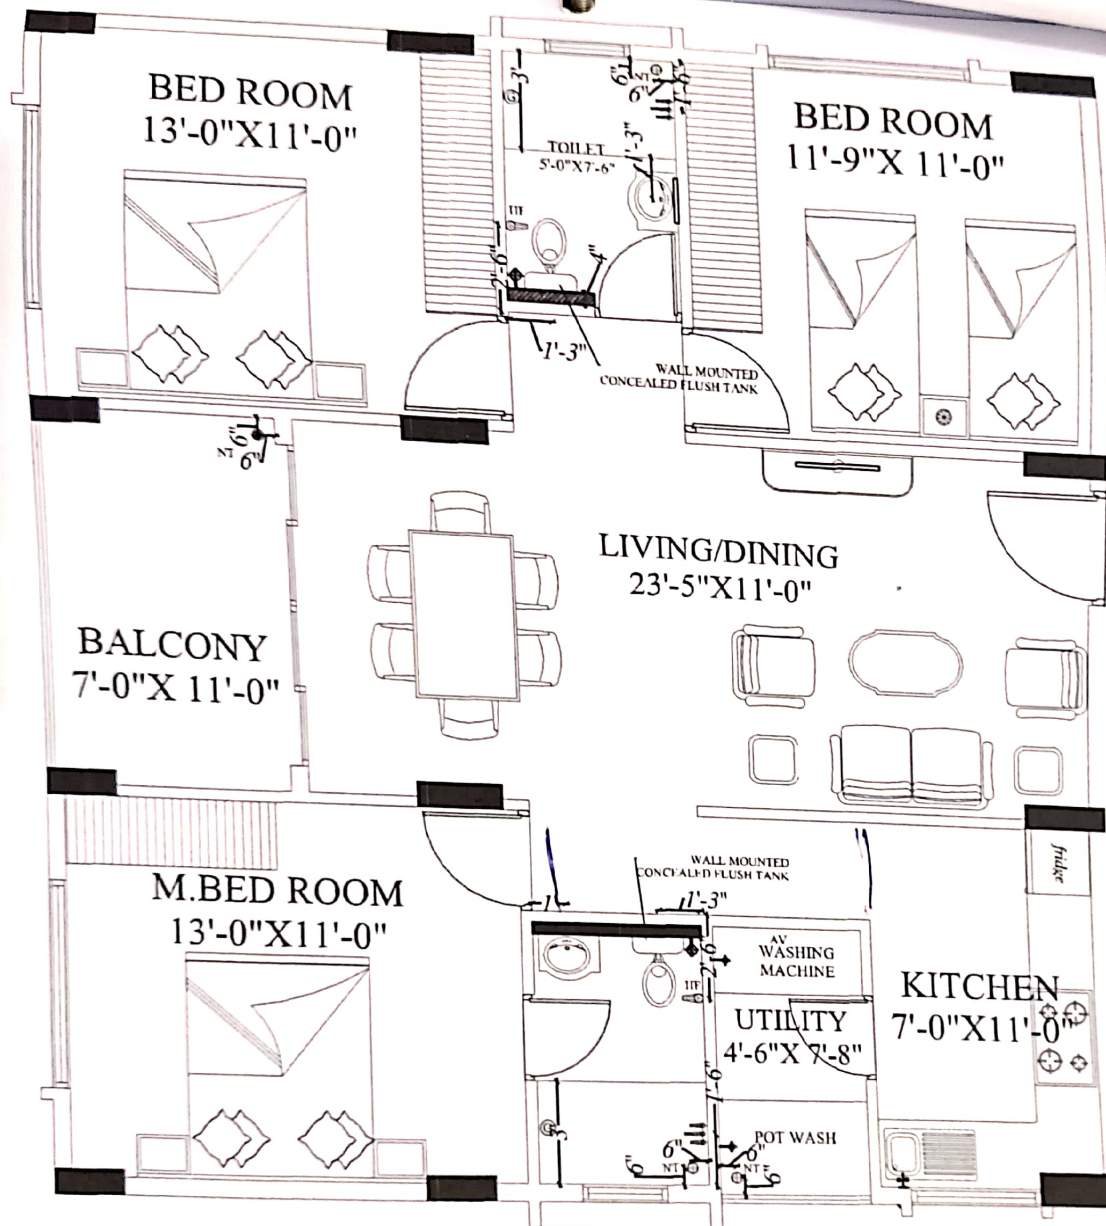


LEGEND

+	HEALTH FAUCET
⚡	ANGLE VALVE
⊙	NANI TRAP
○	3" RAIN WATER PIPE
⊙	GEASER POINT
	WALL MIXTURE
+	TAP / LONG BODY

Description	Direction	Owners & Developers :	Date :	16.09.20	Promoted by
PLUMBING PLAN-1360 Sft (A1-TYPE)		Modi Reality Mallapur LLP	Prepared By :	Jayapradha	Modi Properties Pvt Ltd
		Project Name & Phase :	Approved By :	Soham Modi	
		Gulmohar Residency	Scale :	N.T.S	Phone: +91-40-66335551



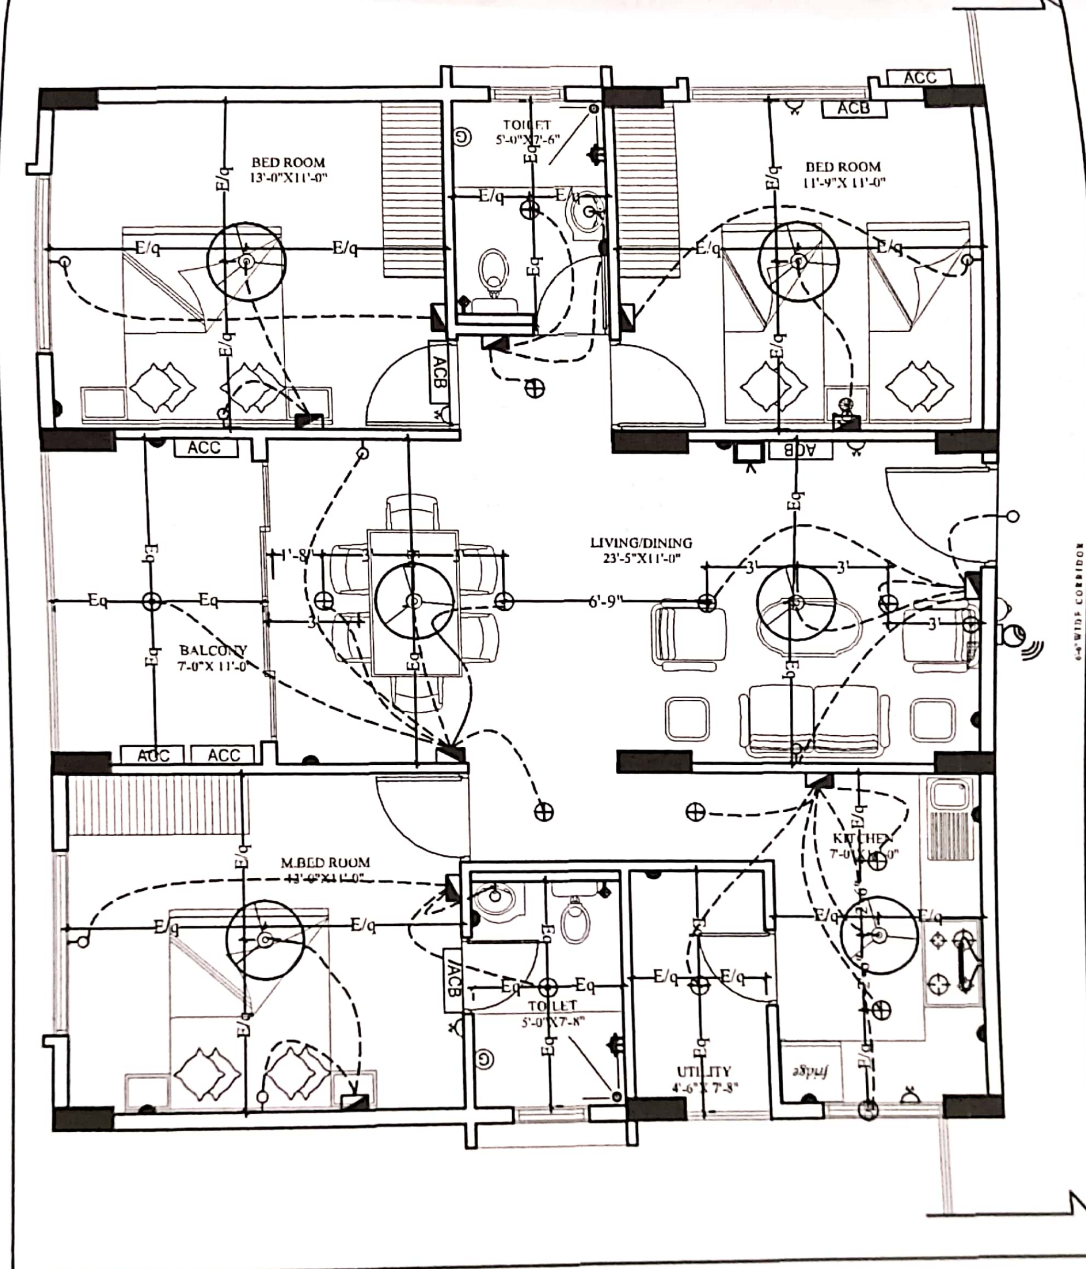


LEGEND:-


S.NO	ITEM	SYMBOL	HEIGHTS from FFL
1.	Distribution Board & Change over		7' TO 7'6"
2.	Switch board		4' OR 4'6"
3.	Wall point/Bracket light		7' TO 7'6"
4.	5 amp plug point		2'
5.	Ceiling fan		-
6.	Gaspar point-15A		6'6" OR 7'6"
7.	Exhaust fan		7'6"
8.	15 amp plug point		2' OR 3'6" OR 7'6"
9.	Television point		3'
10.	Telephone point		2'
11.	Calling Bell		4'6"
12.	Bell Push		5'
13.	Ceiling light		-
14.	WB Camera		7'6"
15.	AC Compressor		7' TO 7'6"
16.	AC Blower		7' TO 7'6"
17.	Switch board with 5A branch		4' TO 4'6"

Note - Switch boards next to bed with must be 3'6" from corner of bed.

Description	Direction	Owners & Developers :	Date :	21.09.2020	Promoted by
ELECTRICAL PLAN -1360 sft FLATS-A1 TYPE		Modi Reality Mallapur LLP	Prepared By :	Jayapradha	Modi Properties Pvt Ltd
		Project Name & Phase :	Approved By :	Soham Modi	
		Gulmohar Residency	Scale :	N T S	
		Phone: +91-40-6633555			

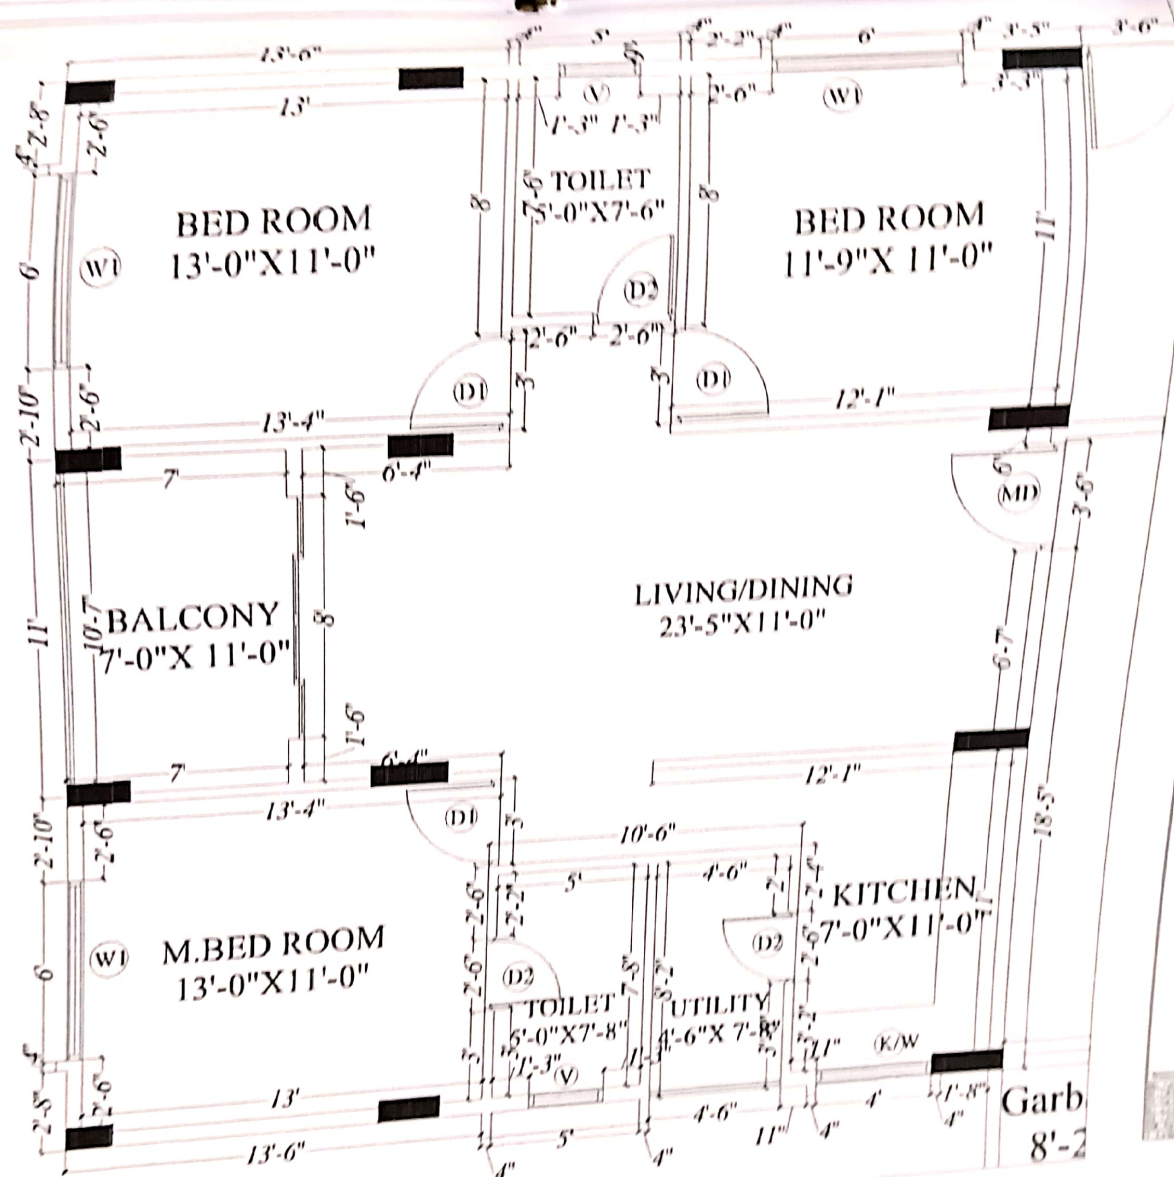

Description H-BLOCK-Flat no-7-B2-Type-West Living-Walkway plan	Direction N 	Owners & Developers : Modi Reality Mallapur LLP Project Name & Phase : Gulmohar Residency	Date : 26.10.2022 Prepared By : Jayapradha Approved By : Soham Modi Scale : 1:100	Promoted by Modi Properties Pvt Ltd Phone : +91-40-66133551
--	---	---	---	--

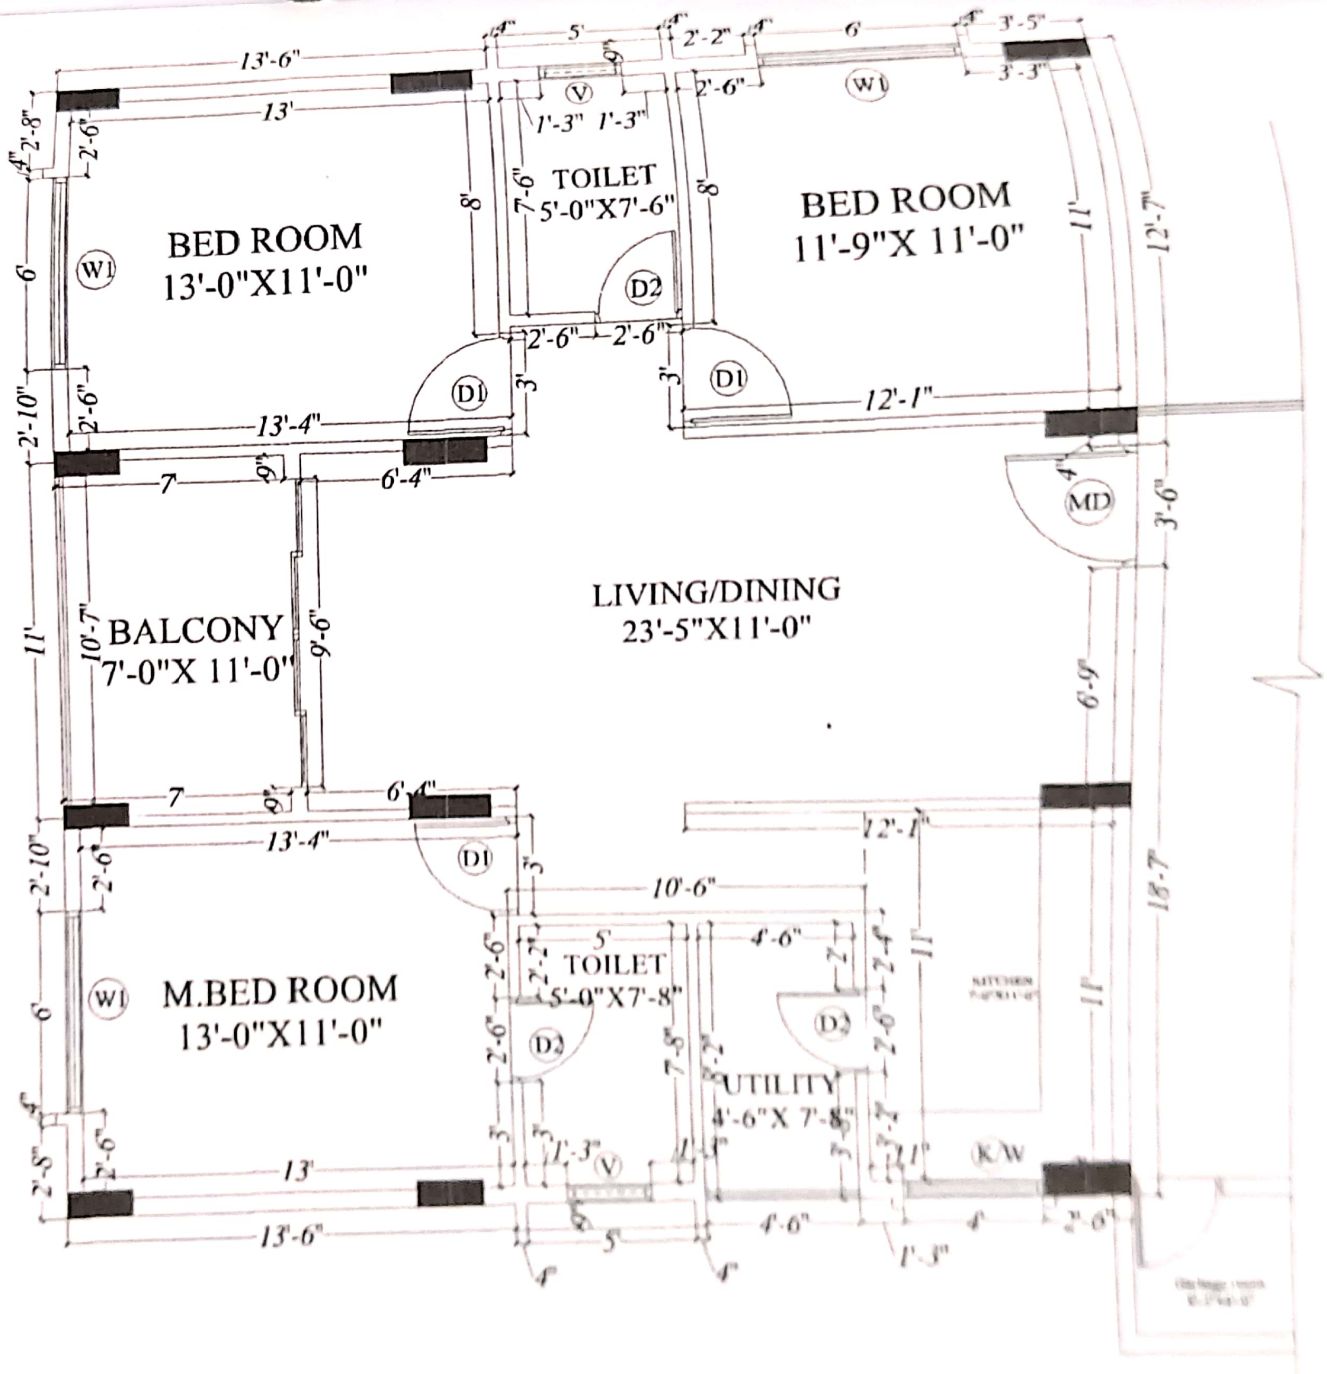

WORKING PLAN-1360 Sfr -A1 TYPE



Owners & Developers
Mush Realty Malappur LLP
Project Name & Phase
Gulmohar Residency

Date
Prepared By
Approved By
Scale

13.09.2020
Jayapandha
Sulaiman Mudi
N.T.S

Prepared by
Mush Properties Pvt Ltd
Phone: +91-40-00333351
