

MODI PROPERTIES PVT.LTD.

5-4-187/3&4, II Floor, M.G. Road,
Secunderabad - 500 003.
Phone : +91 - 40 - 66335551

MAYFLOWER PLATINUM

Sy. No. 82/1,
Mallapur Main Road,
Hyderabad - 500 076.

Sl. No.

1001

Date :

03/05/2019

Consultant Inspection Report

1) Inspection of fabrication has been done

Asked to proceed for the concreting,

Use - Cement block for the core
spacing.

2) Check the centerline alignment
while concreting.

M. A. S.

Engineer Sign.

Consultant Sign.

MODI PROPERTIES PVT.LTD.

5-4-187/3&4, II Floor, M.G. Road,
Secunderabad - 500 003.
Phone : +91 - 40 - 66335551

MAYFLOWER PLATINUM



Sy. No. 82/1,
Mallapur Main Road,
Hyderabad - 500 076.

Sl. No. **1002**

Date : 28/05/2019

Consultant Inspection Report We have visited the site
as requested by project manager to get
clarification on "RAFT-5", so the clarification
is the projected top on the column ^{also} "Drop"
Therefore their reinforcement need not go down to
the bottom matt.

The fabrication and laying of the reinforcement is
Satisfactory. we suggest go for concreting with
nessary precautions as written in the notes
Such as mix, cover, water cement ratio etc.



Engineer Sign.

Consultant Sign.

MODI PROPERTIES PVT.LTD.

5-4-187/3&4, II Floor, M.G. Road,
Secunderabad - 500 003.
Phone : +91 - 40 - 66335551

MAYFLOWER PLATINUM

Sy. No. 82/1,
Mallapur Main Road,
Hyderabad - 500 076.

Sl. No. **1003**

Date : 17/7/19

Consultant Inspection Report Ar. Ram Mohan Reddy &
Ar. Anita Raj visited the site. 17

Inspected the site to check the status
of work and clarify the doubts.

Clarified few doubts of Stair Case orientation.
and informed to site engineer Subba Reddy.

Per U/C

Ar. G. Ram Mohan Reddy.

ARDES

Engineer Sign.

Consultant Sign.

MODI PROPERTIES PVT.LTD.

5-4-187/3&4, II Floor, M.G. Road,
Secunderabad - 500 003.
Phone : +91 - 40 - 66335551

MAYFLOWER PLATINUM

Sy. No. 82/1,
Mallapur Main Road,
Hyderabad - 500 076.

Sl. No. **1004**

Date : 20/07/2019

Consultant Inspection Report _____

As per my visit. The site progress seems to be satisfactory.

- 1) The Quality of the work found satisfactory.
- 2) The Beam Reinforcement details to be issued after verification.
- 3) Sump Reinforcement details are discussed. The required drawing will be issued.

Engineer Sign.

Consultant Sign.

MODI PROPERTIES PVT.LTD.

5-4-187/3&4, II Floor, M.G. Road,
Secunderabad - 500 003.
Phone : +91 - 40 - 66335551

MAYFLOWER PLATINUM

Sy. No. 82/1,
Mallapur Main Road,
Hyderabad - 500 076.

Sl. No. **1005**

Date : 17/08/2019


Consultant Inspection Report

The inspection Subharedy has requested to have site visit to discuss the site evolution conditions and alterations.

1) The retaining wall at N-E area along the track decided in line with the building columns.

2) Eastern side of the parking area is cancelled due to existing heavy rock. The required changes in the structural design shall be carried out only after finalization.

3) Rest of the site progress found satisfactory.



Engineer Sign.

Consultant Sign.

MODI PROPERTIES PVT.LTD.

5-4-187/3&4, II Floor, M.G. Road,
Secunderabad - 500 003.
Phone : +91 - 40 - 66335551

MAYFLOWER PLATINUM

Sy. No. 82/1,
Mallapur Main Road,
Hyderabad - 500 076.

1006

Sl. No.

Date : _____

Consultant Inspection Report _____

We have visited the site as requested
by Subbareddy garu.

The fabrication and basement 2 Slab and
beam reinforcement is satisfactory advised to
bar bend at the junction, and all clear
cover are good. Beam no 23a, grid (9+1)
we will revise in drawing.

Requested us to visit again Friday/
Saturday to inspect remaining beams, & slabs.

Santosh
Shruthi Engineer

Engineer Sign.

Consultant Sign.

MODI PROPERTIES PVT.LTD.

5-4-187/3&4, II Floor, M.G. Road,
Secunderabad - 500 003.
Phone : +91 - 40 - 66335551

MAYFLOWER PLATINUM

Sy. No. 82/1,
Mallapur Main Road,
Hyderabad - 500 076.

Sl. No. **1007**

Date : 9/09/2019

Consultant Inspection Report

Today we have visited the site.
to inspect the Beam Layout. The
Beam Layout of 103rd slab is under
progress.

ii). We have suggested to fill with
Broken Ballast stone along the
track side compound wall up to depth
of 5-0" Lvl. down from the track Lvl.

(iii) Suggested to ~~increase~~ increase the
slab depth 8" to accommodate pre-
Engine Load on west side drive
way slab, so that Beams Lvl can
sustain the Load.

Engineer Sign.

Consultant Sign.

MODI PROPERTIES PVT.LTD.

5-4-187/3&4, II Floor, M.G. Road,
Secunderabad - 500 003.
Phone : +91 - 40 - 66335551

MAYFLOWER PLATINUM

Sy. No. 82/1,
Mallapur Main Road,
Hyderabad - 500 076.

Sl. No. **1008**

Date : 28/09/19

Consultant Inspection Report

- 1) Inspected the Slab layout—in site and checked the cut-outs in the slab (Ground floor).
- 2) BS-3 Staircase Section and plan Related Queries have been solved in the site.
- 3) Column cut elements in the upper floors plans have to be reflected in upper floors and sent to site.
- 4) Ramp from Road level to Basement-II Related Queries - Ramp slope -

Engineer Sign.

M. V. Chinn
Consultant Sign.

MODI PROPERTIES PVT.LTD.

5-4-187/3&4, II Floor, M.G. Road,
Secunderabad - 500 003.
Phone : +91 - 40 - 66335551

MAYFLOWER PLATINUM

Sy. No. 82/1,
Mallapur Main Road,
Hyderabad - 500 076.

Sl. No. **1009**

Date : 28/9/2019

Consultant Inspection Report we have visited the site to

inspect base & reinforcement we found
Satisfactory advised to maintain proper 4g
slab extension reinforcement on both side
of the beam/support.

Also advised to avoid the lapping
of column reinforcement at junction of beam
column.

Kalbauri Consultants
Engineer Sign.

Consultant Sign.

MODI PROPERTIES PVT.LTD.

5-4-187/3&4, II Floor, M.G. Road,
Secunderabad - 500 003.
Phone : +91 - 40 - 66335551

MAYFLOWER PLATINUM

Sy. No. 82/1,
Mallapur Main Road,
Hyderabad - 500 076.

Sl. No. **1010**

Date : 2/11/2019.


Consultant Inspection Report

Today visited the site to see the
various of filling to avoid vibrations
from the Railway track the following
points are suggested.

1) Filling nearby building line
is mandatory by required. Material
- the drawing will be Issued very soon

2) The drive way slab drawings
are Issued. ~~But~~ But - there is restriction
of Beam depth which we need to
cross check structural point of view
after cross checking we will issue
the same drawing at the earliest

Engineer Sign.


Consultant Sign.

MODI PROPERTIES PVT.LTD.

5-4-187/3&4, II Floor, M.G. Road,
Secunderabad - 500 003.
Phone : +91 - 40 - 66335551

MAYFLOWER PLATINUM


Sy. No. 82/1,
Mallapur Main Road,
Hyderabad - 500 076.

1011

Sl. No.

Date : _____

Consultant Inspection Report _____

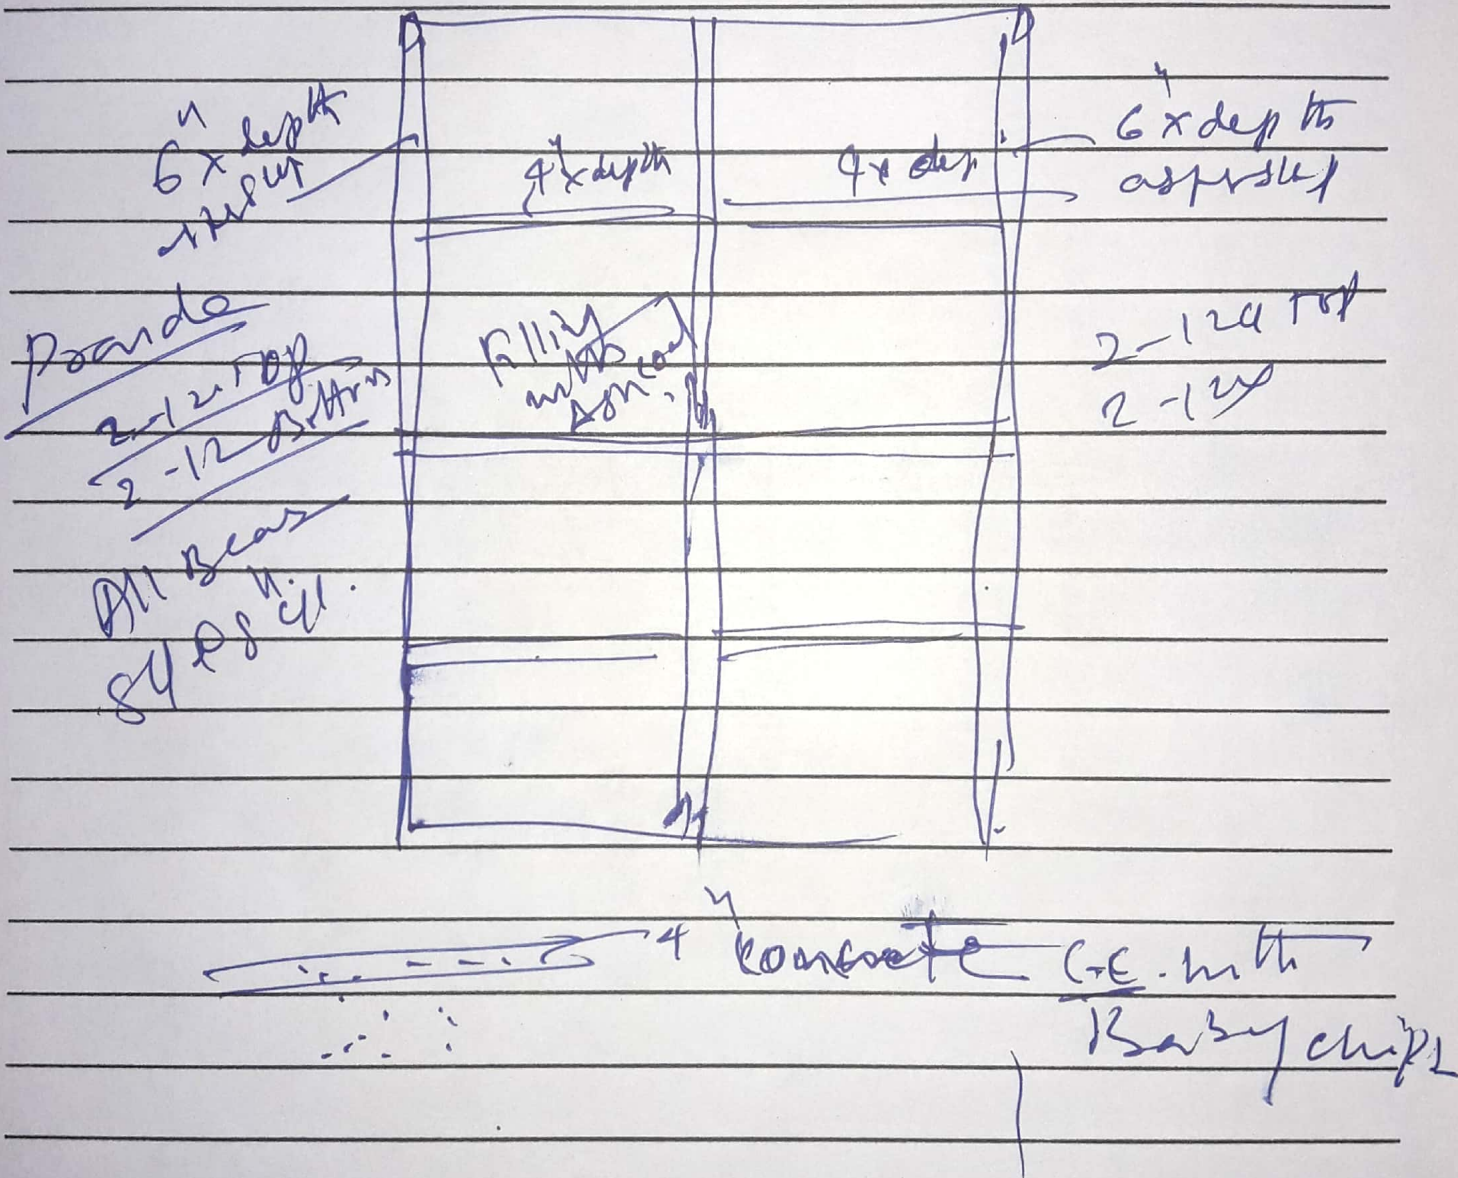

Engineer Sign.

Consultant Sign.
