

Modi Realty Mallapur LLP (20-21)

MG Road, RAnigunj


Secunderabad

State Name : Telangana, Code : 36

Payment VoucherNo. : **PAY/11637** 11647

Dated : 15-Jan-2021

Particulars	Amount
Account : CONT-G Sunitha	40,000.00 25,000
Through : BANK-Kotak Mahindra Bank Rera A/c	
On Account of : being neft trasnaction to Sunitha for releasing credit balance amount vide vocuher no 786 enclosed.	
Amount (in words) : Indian Rupees Forty Thousand Only	25,000 ₹ 40,000.00


Prepared by: gmr@modiproperties.com

Approved by

Receiver's Signature

Attendance Details
Gulmohar Residency
 Survey No.19, Mallapur, Hyderabad.


Advice for Payment No : 786

Date : 15/01/2021

Contractor Name	From Date	To Date
Sunitha (Painting)	07/01/2021	13/01/2021

Skill Name	Attendance		Department		Job Work		On A/c	
	Value	Amount	Auto	Manual	Auto	Manual	Auto	Manual
Totals...	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00

Advice For Payment	
PARTICULARS	AMOUNT
On A/c Description :	
Towards releasing credit balance amount	40000.00
credit balance amount Rs.61813/-	25,000
Department Description :	
	0.00
Job Work Description :	
	0.00
	25000
Total Amount %	40000.00
TDS : @ 0	0.00
Less Rent :	0.00
Less Loan :	0.00
Other Deductions Description :	
	0.00
Net Amount :	25000
	40000.00
Rupees : Fourty Thousand Only.	



[Signature]
 Approved By Accounts

Approved By Managing Director

Modi Realty Mallapur LLP (20-21)

MG Road, RAnigunj

Secunderabad

State Name : Telangana, Code : 36

Payment VoucherNo. : **PAY/11637-11648**

Dated : 15-Jan-2021


Particulars	Amount
Account : OE-Water Supply UD	24,000.00
Through : BANK-Kotak Mahindra Bank Rera A/c	
On Account of : being neft tarsnaction to A.Sathyanarayana for supply of bore water for site & labour qaurters work purpose vid evouche rno 5545 enclosed.	
Amount (in words) : Indian Rupees Twenty Four Thousand Only	
	₹ 24,000.00



Prepared by: gmr@modiproperties.com

Approved by

Receiver's Signature





Building Material Voucher

15/01/2021 13:15:59 Pages : 1 of 2

Company Name : Modi Reality Mallapur LLP
 Project Name : Gulmohar Residency
 Supplier Name : A. Sathyanarayana

Voucher No : 5545
 From Date : 07/01/2021
 To Date : 13/01/2021

Inward No	Recd Date	Recd Time	DC No.	DC Date	Qty	Rate	GST%	Gross
6125 - Building material - Water Tanker - NA - nos								
2661	07-01-2021	8.03			1.000	500.00	0.00	500.00
2662	07-01-2021	9.01			1.000	500.00	0.00	500.00
2663	07-01-2021	10.43			1.000	500.00	0.00	500.00
2664	07-01-2021	11.21			1.000	500.00	0.00	500.00
2665	07-01-2021	12.34			1.000	500.00	0.00	500.00
2666	07-01-2021	17.20			1.000	500.00	0.00	500.00
2667	08-01-2021	7.47			1.000	500.00	0.00	500.00
2668	08-01-2021	8.39			1.000	500.00	0.00	500.00
2669	08-01-2021	11.58			1.000	500.00	0.00	500.00
2670	08-01-2021	13.52			1.000	500.00	0.00	500.00
2671	08-01-2021	15.13			1.000	500.00	0.00	500.00
2672	08-01-2021	16.41			1.000	500.00	0.00	500.00
2673	08-01-2021	17.54			1.000	500.00	0.00	500.00
2674	09-01-2021	08:45			1.000	500.00	0.00	500.00
2675	09-01-2021	09:57			1.000	500.00	0.00	500.00
2676	09-01-2021	11:06			1.000	500.00	0.00	500.00
2677	09-01-2021	12:17			1.000	500.00	0.00	500.00
2678	09-01-2021	15:02			1.000	500.00	0.00	500.00
2679	09-01-2021	16:05			1.000	500.00	0.00	500.00
2680	09-01-2021	17:30			1.000	500.00	0.00	500.00
6281	10-01-2021	09:31			1.000	500.00	0.00	500.00
2682	10-01-2021	10:30			1.000	500.00	0.00	500.00
2683	10-01-2021	11:37			1.000	500.00	0.00	500.00
2684	10-01-2021	12:55			1.000	500.00	0.00	500.00
2685	10-01-2021	15:45			1.000	500.00	0.00	500.00
2686	10-01-2021	16:58			1.000	500.00	0.00	500.00
2687	11-01-2021	10.16			1.000	500.00	0.00	500.00
2688	11-01-2021	10.37			1.000	500.00	0.00	500.00
2689	11-01-2021	12.38			1.000	500.00	0.00	500.00
2690	11-01-2021	14.13			1.000	500.00	0.00	500.00
2691	11-01-2021	15.50			1.000	500.00	0.00	500.00
2692	11-01-2021	16.30			1.000	500.00	0.00	500.00
2693	11-01-2021	17.40			1.000	500.00	0.00	500.00
2694	12-01-2021	8.16			1.000	500.00	0.00	500.00
2695	12-01-2021	9.37			1.000	500.00	0.00	500.00
2696	12-01-2021	11.41			1.000	500.00	0.00	500.00
26978	12-01-2021	14.04			1.000	500.00	0.00	500.00
2698	12-01-2021	16.41			1.000	500.00	0.00	500.00
2699	12-01-2021	17.25			1.000	500.00	0.00	500.00
2700	12-01-2021	18.36			1.000	500.00	0.00	500.00



Accounts Manager

Managing Director

Building Material Voucher




15/01/2021 13:15:59

Pages : 2 of 2

2701	13-01-2021	6:50			1.000	500.00	0.00	500.00
2702	13-01-2021	07:36			1.000	500.00	0.00	500.00
2703	13-01-2021	09:45			1.000	500.00	0.00	500.00
2704	13-01-2021	12:46			1.000	500.00	0.00	500.00
2705	13-01-2021	13:49			1.000	500.00	0.00	500.00
2706	13-01-2021	13:49			1.000	500.00	0.00	500.00
2707	13-01-2021	15:02			1.000	500.00	0.00	500.00
2708	13-01-2021	17:22			1.000	500.00	0.00	500.00
					48.000			24000.00
Building Material Total								24000.00

Advice for Payment

PARTICULARS	Amount
Payment towards Building Material	24000.00
Towards supply of bore water for site A , B, C, F, & G blocks , rock cutting work at D-Block and labour quarters use purpose.	
Additional Payments :	0.00
Deductions :	0.00
Total	24000.00
Rupees : Twenty Four Thousand Only.	



Accounts Manager

Managing Director

Payment Voucher

No. : **PAY/11637/11649**

Dated : **15-Jan-2021**

Particulars	Amount
Account :	
EUC-Orsu Swamy	18,700.00
TDS-1.50% Contract	280.00
Through :	
BANK-Kotak Mahindra Bank Rera A/c	
On Account of :	
being neft tarsnaction to Orsu Swamy for rock cutting work done at C-Block vide vouche rno 7497 enclosed.	
Amount (in words) :	
Indian Rupees Eighteen Thousand Nine Hundred Eighty Only	
	₹ 18,980.00

18,419



Prepared by: gmr@modiproperties.com

Approved by


Receiver's Signature



Modi Realty Mallapur LLP					HC 86676
Gulmohar Residency					2559
HC Date	Veh No	Start Time	End Time	Pay Type	
09-01-2021	ap36x5179	09:15	17:30	JW	
Equipment					
Compressor for rock cutting					
Units	Min Rate	Max Rate	Qty	Rate	Value
per hour	550.00	550.00	7	550	3850.00
Supplier Name					
O.Swamy					
Work Description :-					
Towards rocks cutting work done at C-Block .					
Rupees : Three Thousand Eight Hundred Fifty Only.					

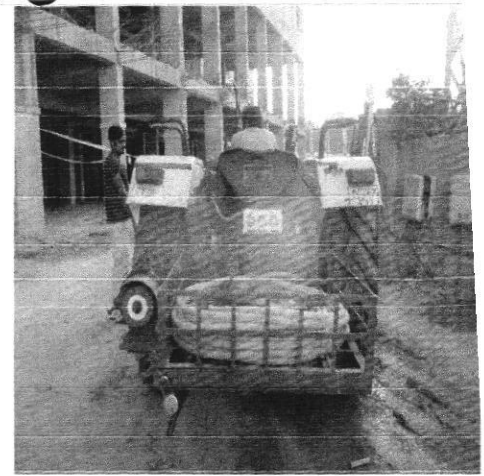

Printed On 11/01/2021 14:37:28



J/w

Material Shifting Authorization Form

No. A 16240

Date	09/01/21	Time	9:30
Authorized By	Gravani A	Engg. Sign	S
Material to be shifted	Towards Rock cutting work done		
Shift from	C- Block		
Shift to			
Vehicle Type	☐ Tractor ☐ JCB ☐ Blade Tractor ☒ Other <u>Compressor</u>		
Vehicle No.	AP36X5179	Vehicle Owner	O. Swamy
Hire charges register serial no.	2559		
Security / Supervisor Sign	S	Start Time	9:15
		Stop Time	17:30

4987

5816

Modi Reality Mallapur LLP

Gulmohar Residency

HC 86678

HC Date	Veh No	Start Time	End Time	Pay Type
09-01-2021	ap27tu6326	10:34	17:36	JW

2560

Equipment

Compressor for rock cutting

Units	Min Rate	Max Rate	Qty	Rate	Value
per hour	550.00	550.00	6	550	3300.00


Supplier Name

O.Swamy


Work Description :-

Towards rock cutting work done at D-Block .

Rupees : Three Thousand Three Hundred Only.

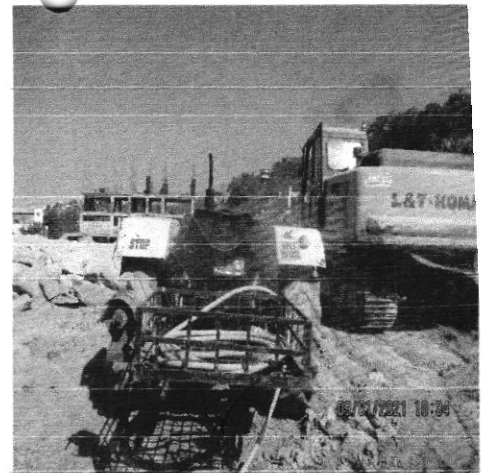


Printed On 11/01/2021 14:37:28



Material Shifting Authorization Form

No. A 16242

Date	09/01/21	Time	10:50
Authorized By	Sravani A	Engg. Sign	
Material to be shifted	Towards Rock Cutting work done		
Shift from	D - Block		
Shift to			
Vehicle Type	☐ Tractor ☐ JCB ☐ Blade Tractor ☒ Other <u>Compressor</u>		
Vehicle No.	AP27TU 6326	Vehicle Owner	V. Raju
Hire charges register serial no.	 2560		
Security / Supervisor Sign		Start Time	10:34
		Stop Time	17:36

9993

5017

Advice for Payment

Company Name : Modi Reality Mallapur LLP

Project Name : Gulmohar Residency

Supplier Name : O.Swamy

Voucher No : 7497

PARTICULARS

Amount

Hire Charges - Job Work Payment

Amount Payable :- 18700.00

Towards rock cutting and drilling holes work done at C-Block for level.

18700.00

Hire Charges - On A/C Payment

Amount Payable :- 0.00

0.00

Other Additions :

0.00

Gross 18700.00

TDS% 1.50

TDS Amount 280.50

CGST% 0.00

0.00

SGST% 0.00

0.00

0.00

Total GST Amount 0.00

Other Deductions :

0.00

Total 18419.50

Rupees : Eighteen Thousand Four Hundred Nineteen and Paise Fifty Only.

VERIFIED BY

V RAVI
MANAGER-AUDIT

Certified by:

Asst. Engineer
MODI REALTY (MALLAPUR) LLP15 JAN 2021
Project Manager

Accounts Manager

Managing Director

Hire Charges Voucher

Company Name : Modi Reality Mallapur LLP

Project Name : Gulmohar Residency



Supplier Name : O.Swamy

15/01/2021 14:10:58

Pages : 1 of 2

Voucher No :	7497
From Date :	07/01/2021
To Date :	13/01/2021

	HC No	HC Date	Equipment Name / Particulars	S.Time	E.Time	Qty	Rate		Gross
86676	2559	09-01-2021	Compressor for rock cutting ap36x5179 Units : per hour Rate : 550 Towards rocks cutting work done at C-Block .	09:15	17:30	7	550	JW	3850.00
86678	2560	09-01-2021	Compressor for rock cutting ap27tu6326 Units : per hour Rate : 550 Towards rock cutting work done at D-Block .	10:34	17:36	6	550	JW	3300.00
86734	2561	11-01-2021	Compressor for rock cutting AP36X5179 Units : per hour Rate : 550 Towards rock cutting work at C - block.	09:38	17:31	6.5	550	JW	3575.00
86763	2565	12-01-2021	Compressor for rock cutting AP36X5179 Units : per hour Rate : 550 Towards rock cutting work done at C - block.	09:26	17:27	7	550	JW	3850.00
86780	2568	13-01-2021	Compressor for rock cutting ap36x5179 Units : per hour Rate : 550 towards rock cutting work done at C-Block .	09:31	17:27	7.5	550	JW	4125.00



Project Manager

Accounts Manager

Managing Director

Modi Realty Mallapur LLP (20-21)

MG Road, RAnigunj

Secunderabad

State Name : Telangana, Code : 36

Payment VoucherNo. : **PAY/11637** 11650

Dated : 15-Jan-2021

Particulars	Amount
Account :	
EUC-Kamlesh Varma	1,050.00
TDS-1.50% Contract	(-)16.00
Through :	
BANK-Kotak Mahindra Bank Rera A/c	
On Account of :	
being neft tarsnaction to Kamlesh varma for chipping work done vide vouche no 7496 enclosed.	
Amount (in words) :	
Indian Rupees One Thousand Thirty Four Only	
	₹ 1,034.00




Prepared by: gmr@modiproperties.com

Approved by



Receiver's Signature



Modi Realty Mallapur LLP					HC 86779
Gulmohar Residency					2567
HC Date	Veh No	Start Time	End Time	Pay Type	
13-01-2021	-	09:24	17:40	JW	
Equipment					
Chipping machine (per hour)					
Units	Min Rate	Max Rate	Qty	Rate	Value
per hour	150.00	150.00	7	150	1050.00
Supplier Name					
Kamles Varma					
Work Description :-					
Towards wall chipping work done at B-Block .					
Rupees : One Thousand Fifty Only.					

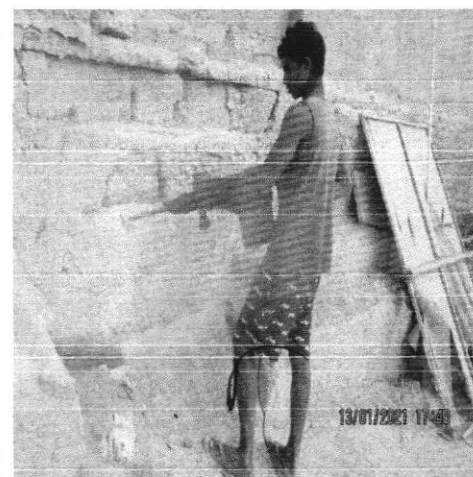

Printed On 15/01/2021 15:11:03



Material Shifting Authorization Form

No. A 16250

Date	13/01/21	Time	9:30
Authorized By	Saravansi	Engg. Sign	[Signature]
Material to be shifted	Towards wall chipping work		
Shift from	B - Block		
Shift to			
Vehicle Type	☐ Tractor ☐ JCB ☐ Blade Tractor ☒ Other <u>Chipping Machine</u>		
Vehicle No.	-	Vehicle Owner	Kamlesh Verma
Hire charges register serial no.	2567		
Security / Supervisor Sign	[Signature]	Start Time	9:24
		Stop Time	17:40

5272

5338

Company Name : Modi Reality Mallapur LLP		Voucher No : 7496	
Project Name : Gulmohar Residency			
Supplier Name : Kamles Varma			
PARTICULARS		Amount	
Hire Charges - Job Work Payment		Amount Payable :-	1050.00
Towards wall chipping work done at B-Block .			1050.00
Hire Charges - On A/C Payment		Amount Payable :-	0.00
			0.00
Other Additions :			0.00
			0.00
		Gross	1050.00
		TDS% 1.50	15.75
		TDS Amount	15.75
		CGST% 0.00	0.00
		SGST% 0.00	0.00
		Total GST Amount	0.00
Other Deductions :			0.00
			0.00
		Total	1034.25
Rupees : One Thousand Thirty Four and Paise Twenty Five Only			

Rupees : One Thousand Thirty Four and Paise Twenty Five Only

~~Certified by:~~

A. Sravani
Asst. Engineer
MODI REALTY (MALLAPUR) LLP

V. RAVI
MANAGER-AUDIT

APPROVED BY
15 JAN 2021
M. RAM KRASAD
PROJECT MANAGER
Project Manager

Accounts Manager

Managing Director

Hire Charges Voucher


Company Name : Modi Reality Mallapur LLP
Project Name : Gulmohar Residency
Supplier Name : Kamles Varma

15/01/2021 14:10:58

Pages : 1 of 2

Voucher No :	7496
From Date :	07/01/2021
To Date :	13/01/2021

	HC No	HC Date	Equipment Name / Particulars	S.Time	E.Time	Qty	Rate		Gross
86779	2567	13-01-2021	Chipping machine (per hour)	09:24	17:40	7	150	JW	1050.00
			Units : per hour			Rate : 150			
			Towards wall chipping work done at B-Block ,						



Accounts Manager

Managing Director

Payment Voucher

No. : PAY/11637-1165)

Dated : 15-Jan-2021

Particulars	Amount
Account :	
EUC-Surasani Associates	4,000.00
TDS-1.50% Contract	(-)60.00
Through :	
BANK-Kotak Mahindra Bank Rera A/c	
On Account of :	
being neft transaction to sursani associates for total station work done vide vouche rno 7495 enclsod.	
Amount (in words) :	
Indian Rupees Three Thousand Nine Hundred Forty Only	
	₹ 3,940.00


Prepared by: gmr@modiproperties.com

Approved by

Receiver's Signature



Modi Reality Mallapur LLP
Gulmohar Residency

HC 86659

HC Date	Veh No	Start Time	End Time	Pay Type
08-01-2021		10:10	17:21	JW

2558

Equipment

Total Station Survey (per day)

Units	Min Rate	Max Rate	Qty	Rate	Value
per day	4000.00	4000.00	1	4000	4000.00


Supplier Name

Surasani Associates

Work Description :-

Towards marking work done at C - block

Rupees : Four Thousand Only.

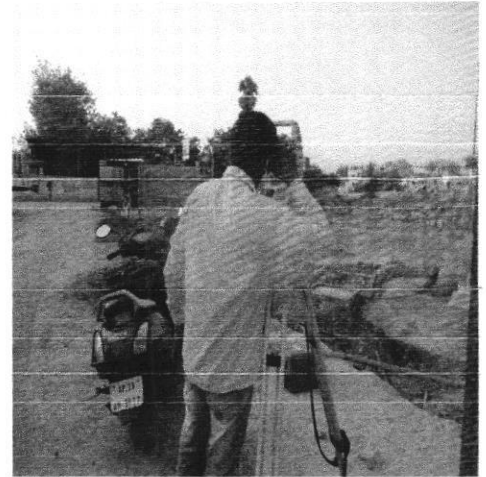

Printed On 11/01/2021 14:37:28

APPROVED BY
11 JAN 2021
M. HAMPIRASAD
PROJECT MANAGER

Certified by:
A. Sravani
Asst. Engineer
MODI REALTY (MALLAPUR) LLP

CHECKED (Security)
[Signature]
MODI REALTY MALLAPUR LLP

NOTE: No date & amt in photoprnt.

VERIFIED BY
15 JAN 2021
V. RAVI
MANAGER-AUDIT

Material Shifting Authorization Form

No. A 16237

Date	08/01/21	Time	10:30
Authorized By	Sravani A	Engg. Sign	
Material to be shifted	Towards Marking work Done		
Shift from	C- Block		
Shift to			
Vehicle Type	☐ Tractor ☐ JCB ☐ Blade Tractor ☒ Other <u>Total Stations</u>		
Vehicle No.	-	Vehicle Owner	Sursani Associates
Hire charges register serial no.	2558		
Security / Supervisor Sign		Start Time	10:10
		Stop Time	17:21

4960

4976

Advice for Payment

Company Name : Modi Reality Mallapur LLP

Project Name : Gulmohar Residency

Supplier Name : Surasani Associates

Voucher No : 7495

PARTICULARS							Amount
Hire Charges - Job Work Payment							
Towards total station marking given work done at C-Block .							
							4000.00
Hire Charges - On A/C Payment							
							0.00
Other Additions :							
							0.00
							Gross 4000.00
							TDS% 1.50 TDS Amount 60.00
							CGST% 0.00 0.00 SGST% 0.00 0.00 Total GST Amount 0.00
Other Deductions :							
							0.00
							Total 3940.00

Rupees : Three Thousand Nine Hundred Fourty Only.



Accounts Manager

Managing Director

Hire Charges Voucher

15/01/2021 14:10:58

Pages : 1 of 2

Company Name : Modi Reality Mallapur LLP

Project Name : Gulmohar Residency



Supplier Name : Surasani Associates

Voucher No : 7495

From Date : 07/01/2021

To Date : 13/01/2021

	HC No	HC Date	Equipment Name / Particulars	S.Time	E.Time	Qty	Rate		Gross
86659	2558	08-01-2021	Total Station Survey (per day)	10:10	17:21	1	4000	JW	4000.00
			Units : per day	Rate : 4000					
			Towards marking work done at C - block						



Accounts Manager

Managing Director

Modi Realty Mallapur LLP (20-21)

MG Road, RAnigunj

Secunderabad

State Name : Telangana, Code : 36

Payment VoucherNo. : **PAY/11637** 11652

Dated : 15-Jan-2021

Particulars	Amount
Account :	
CONJBDW-Usha Varma	4,000.00
TDS-0.75% Contract	(-)30.00
Through :	
BANK-Kotak Mahindra Bank Rera A/c	
On Account of :	
being neft transaction to usha varma for civil work done for septic tank chambers as per job work sheet vide vouche rno 801 enclosed.	
Amount (in words) :	
Indian Rupees Three Thousand Nine Hundred Seventy Only	
	₹ 3,970.00

Prepared by: gmr@modiproperties.com

Approved by

Receiver's Signature

Modi Realty Mallapur LLP (20-21)

MG Road, RAnigunj

Secunderabad

State Name : Telangana, Code : 36

Payment VoucherNo. : **PAY/11637-11653**Dated : **15-Jan-2021**

Particulars	Amount
Account :	
CONJBDW-Usha Varma	1,725.00
TDS-0.75% Contract	(-)13.00
Through :	
BANK-Kotak Mahindra Bank Rera A/c	
On Account of :	
being neft trasnaction to Usha Varma for civil work done vide vouche rno 800 enclsod.	
Amount (in words) :	
Indian Rupees One Thousand Seven Hundred Twelve Only	
	₹ 1,712.00


Prepared by: gmr@modiproperties.com

Approved by

Receiver's Signature




Payment Voucher

No. : PAY/11637 11654

Dated : 15-Jan-2021

Particulars	Amount
Account :	
CONJBDW-Srikanth Jena(Plumber)	3,300.00
TDS-0.75% Contract	(-)25.00
Through :	
BANK-Kotak Mahindra Bank Rera A/c	
On Account of :	
being nft transaction to Srikanth jena for plumbing work done vide voucher no 799 enclosed.	
Amount (in words) :	
Indian Rupees Three Thousand Two Hundred Seventy Five Only	
	₹ 3,275.00

 
Prepared by: gmr@modiproperties.com

Approved by

Receiver's Signature

Modi Realty Mallapur LLP (20-21)

MG Road, RAnigunj


Secunderabad

State Name : Telangana, Code : 36

Payment VoucherNo. : **PAY/11637** 11658


Dated : 15-Jan-2021

Particulars	Amount
Account :	
CONJBDW-Thirupathi Raju (Electrician)	950.00
TDS-0.75% Contract	(-)7.00
Through :	
BANK-Kotak Mahindra Bank Rera A/c	
On Account of :	
being neft transaction to Thirupathi raju for electrical work done as pe job work sheet vi voucher no 785 enclosed.	
Amount (in words) :	
Indian Rupees Nine Hundred Forty Three Only	
	₹ 943.00

 
Prepared by: gmr@modiproperties.com

Approved by

Receiver's Signature



Modi Realty Mallapur LLP (20-21)

MG Road, RAnigunj

Secunderabad

State Name : Telangana, Code : 36

Payment VoucherNo. : **PAY/11664** 11656

Dated : 15-Jan-2021

Through : BANK-Kotak Mahindra Bank Rera A/c

Particulars	Amount
Account :	
CONT-Surasani Constructions	18,000.00
TDS-1.50% Contract	(-)-270.00
On Account of :	
Being amount transfered towards advance payment against Anx-B for Club house	
Amount (in words) :	
Indian Rupees Seventeen Thousand Seven Hundred Thirty Only	
	₹ 17,730.00

Prepared by: rajyalakshmi

Approved by

Receiver's Signature

Anx - A - Attendance details

Annexure - A - Send Weekly Details of labour charges					
Name of contractor:		S.Karunakar Reddy			
Company name:		Surasani Constructions (Club House)			
Project name:		Gulmohar Residency			
Date:		15.01.2021			
Period		From:	07.01.2021	To:	13.01.2021
Sl. No.	Work Type	Worker Type	Quantity	Rate	Amount
1	Civil work	Mason	-	575.00	-
2	Civil work	Male helper	-	400.00	-
3	Civil work	Female helper	-	350.00	-
4	RCC work	Mason	-	550.00	-
5	RCC work	Male helper	-	400.00	-
6	RCC work	Female helper	-	-	-
7	Earth work	Mason	-	-	-
8	Earth work	Male helper	-	450.00	-
9	Earth work	Female helper	-	400.00	-
10	Electrician	Mason	-	550.00	-
11	Electrician	Male helper	-	400.00	-
12					-
13					-
14					-
15					-
16					-
17					-
18					-
19					-
20					-
Total					-
Payment approved by MD:					
Prepared by:		MDs approval			
Name	A.Sravani				
Date	15.01.2021				

APPROVED BY
15 JAN 2021
M. KAVI PRASAD
PROJECT MANAGER

Certified by:
A. Sravani
Asst. Engineer
MODI REALTY (MALLAPUR) LLP

Anx - B - Hire charges

Annexure - B - Send Weekly					
Details of hire charges					
Name of contractor:		S.Karunakar Reddy			
Company name:		Surasani Constructions (Club House)			
Project name:		Gulmohar Residency			
Date:		15.01.2021			
Period		From:	07.01.2021	To:	13.01.2021
Sl. No.	Equipment Type	Quantity	Rate	Units	Amount
1	JCB	21.50	800.00	hours	17,200
2	Tractor with Tipper	0.50	1,800.00	nos	900
3					-
4					-
5					-
6					-
7					-
8					-
9					-
10					-
11					-
12					-
13					-
14					-
15					-
16					-
17					-
18					-
19					-
20					-
21					-
22					-
23					-
24					-
25					-
Total					18,100
Payment approved by MD:					
Prepared by:					MDs approval
Name	A.Sravani				
Date	15.01.2021				

APPROVED BY
15 JAN 2021
M. RAJ PRASAD
PROJECT MANAGER

Certified by:
A. Sravani
Asst. Engineer
MODI REALTY (MALLAPUR) LLP

Anx - C - Material received

Annexure - C - send weekly

Details of material received

Name of contractor: S.Karunakar Reddy

Company name: Surasani Constructions (Club House)

Project name: Gulmohar Residency

Date: 15.01.2021

Period From: 07.01.2021 To: 13.01.2021

Sl. No.	Material type	Received date	Inward no.	Quantity	Units	Rate	Amount
1							-
2							-
3							-
4							
5							
6							
7							
8							
9							
10							
11							
12							
13							
14							
15							
16							
17							
18							
19							
20							
21							
22							
23							
24							-
Total							-
Payment approved by MD:							
Prepared by:		Approved by:		MDs approval			
Name	A.Sravani						
Date	15.01.2021						

APPROVED BY
 15 JAN 2021
 M. KAMARUDDIN
 PROJECT MANAGER

Certified by:
 A. Sravani
 Asst. Engineer
 MODI REALTY (MALLAPUR) LLP

Uddi Realty Mallapur LLP (20-21)
MG Road, RAnigunj
Secunderabad
State Name : Telangana, Code : 36

Payment Voucher

No. : **PAY/11663** 11657

Dated : 16-Jan-2021

Particulars	Amount
Account :	
CONT-Pointech Associates	4,60,000.00
TDS-1.50% Contract	(-)6,900.00
Through :	
BANK-Kotak Mahindra Bank Rera A/c	
On Account of :	
Being amount transfered towards advance payment against Anx-A & C	
Amount (in words) :	
Indian Rupees Four Lakh Fifty Three Thousand One Hundred Only	
	₹ 4,53,100.00

Prepared by: rajyalakshmi

Approved by

Receiver's Signature

Anx - A - Attendance details

Annexure - A - Send Weekly Details of labour charges					
Name of contractor:		P. Srinivasa			
Company name:		Pointec Associates			
Project name:		Gulmohar Residency			
Date:		15.01.2021			
Period		From:	07.01.21	To:	13.01.21
Sl. No.	Work Type	Worker Type	Quantity	Rate	Amount
1	Civil work	Mason	20	575.00	11,500
2	Civil work	Male helper	20	400.00	8,000
3	Civil work	Female helper	-	350.00	-
4	RCC work	Mason	65	550.00	35,750
5	RCC work	Male helper	60	400.00	24,000
6	RCC work	Female helper	-	-	-
7	Earth work	Mason	-	-	-
8	Earth work	Male helper	-	450.00	-
9	Earth work	Female helper	-	400.00	-
10	Electrician	Mason	-	550.00	-
11	Electrician	Male helper	-	400.00	-
12					-
13					-
14					-
15					-
16					-
17					-
18					-
19					-
20					-
Total					79,250
Payment approved by MD:					
Prepared by:		MDs approval			
Name	A.Sravani				
Date	15.01.2021				

APPROVED BY
15 JAN 2021
M. K. Srinivas
PROJECT MANAGER

Certified by:
A. Sravani
Asst. Engineer
MODI REALTY (MALLAPUR) LLP

Anx - B - Hire charges

e - B - Send Weekly					
s of hire charges					
ne of contractor:		P. Srinivasa			
ompany name:		Pointec Associates			
Project name:		Gulmohar Residency			
Date:	15.01.2021				
Period	From:	07.01.21	To:	13.01.21	
Sl. No.	Equipment Type	Quantity	Rate	Units	Amount
1	JCB	-	800.00	nos	-
2	Tractor with Tipper	-	1,800.00	nos	-
3	Compressor rock drilling holes	-	550.00	per hour	-
4					-
5					-
6					-
7					-
8					-
9					-
10					-
11					-
12					-
13					-
14					-
15					-
16					-
17					-
18					-
19					-
20					-
21					-
22					-
23					-
24					-
25					-
Total					-
Payment approved by MD:					
Prepared by:					MDs approval
Name	A. Sravani				
Date	15.01.2021				

APPROVED BY
15 JAN 2021
M. RAM KRASAD
PROJECT MANAGER

Certified by:
A. Sravani
Asst. Engineer
MODI REALTY (MALLAPUR) LLP

Anx - C - Material received

C - send weekly
of material received
of contractor:
Company name:
Project name:
Date:
Period:

P. Srinivasa
Pointec Associates
Gulmohar Residency
15.01.2021
From: 07.01.21 To: 13.01.21

Sl. No.	Material type	Received date	Inward no.	Quantity	Units	Rate	Amount
1	Steel	09.01.21	76	12,200.00	kgs	59.00	719,800.00
2	Solid bricks 6"x8"x16"	09.01.21	77	400.00	No's	30.00	12,000.00
3	Solid bricks 4"x8"x16"	13.01.21	78	400.00	No's	20.00	8,000.00
4	Robo sand coarse	07.01.21	7	430.00	cft	24.00	10,320.00
5	20mm metal	08.01.21	8	480.00	cft	19.00	9,120.00
6							-
7							-
8							-
9							-
10							-
11							-
12							-
13							-
14							-
15							-
16							-
17							-
18							-
19							-
20							-
21							-
22							-
23							-
24							-
25							-
26							-
27							-
28							-
Total							759,240.00
Payment approved by MD:							
Prepared by:							
Name	A. Sravani						
Date	15.01.2021						
Approved by:							
MDs approval							

APPROVED BY
15 JAN 2021
SOHAM MODI
MANAGING DIRECTOR

7500
580 * 2 = 1160
360 * 2 = 720
115/1

APPROVED BY
15 JAN 2021
PROJECT MANAGER

Certified by:
A. Sravani
Asst. Engineer
MODI REALTY (MALLAPUR) LLP

Modi Realty Mallapur LLP (20-21)

MG Road, RAnigunj

Secunderabad

State Name : Telangana, Code : 36

Payment VoucherNo. : **PAY/11666** 11658

Dated : 16-Jan-2021

Through : BANK-Kotak Mahindra Bank Rera A/c

Particulars	Amount
Account :	
CONT-Sree Srinivasa Constrctions	2,05,000.00
TDS-1.50% Contract	(-)3,075.00
On Account of :	
Being amount transfered towards advance payment for Anx-A & C for B block	
Amount (in words) :	
Indian Rupees Two Lakh One Thousand Nine Hundred Twenty Five Only	
	₹ 2,01,925.00

Prepared by: rajyalakshmi

Approved by

Receiver's Signature

Anx - A - Attendance details

Annexure - A - Send Weekly Details of labour charges					
Name of contractor:		B. Srinivasa Reddy			
Company name:		Sree Srinivasa Constructions			
Project name:		Gulmohar Residency			
Date:		15.01.2021			
Period		From:	07.01.2020	To:	13.01.2021
Sl. No.	Work Type	Worker Type	Quantity	Rate	Amount
1	Civil work	Mason	75	575.00	43,125
2	Civil work	Male helper	72	400.00	28,800
3	Civil work	Female helper	30	350.00	10,500
4	RCC work	Mason	40	550.00	22,000
5	RCC work	Male helper	46	400.00	18,400
6	RCC work	Female helper	-	-	-
7	Earth work	Mason	-	-	-
8	Earth work	Male helper	-	450.00	-
9	Earth work	Female helper	-	400.00	-
10	Electrician	Mason	-	550.00	-
11	Electrician	Male helper	-	400.00	-
12					-
13					-
14					-
15					-
16					-
17					-
18					-
19					-
20					-
Total					122,825
Payment approved by MD:					
Prepared by:					MDs approval
Name	A. Sravani				
Date	15.01.2021				

APPROVED BY
15 JAN 2021
M. R. P. K. S. R.
PROJECT MANAGER

Certified by:
A. Sravani
Asst. Engineer
MODI REALTY (MALLAPUR) LLP

Anx - B - Hire charges

Annexure - B - Send Weekly					
Details of hire charges					
Name of contractor:		B.Srinivasa Reddy			
Company name:		Sree Srinivasa Constructions			
Project name:		Gulmohar Residency			
Date:		15.01.2021			
Period		From:	07.01.2020	To:	13.01.2021
Sl. No.	Equipment Type	Quantity	Rate	Units	Amount
1	JCB	-	-	nos	-
2	Tractor with Tipper	-	-	nos	-
3					-
4					-
5					-
6					-
7					-
8					-
9					-
10					-
11					-
12					-
13					-
14					-
15					-
16					-
17					-
18					-
19					-
20					-
21					-
22					-
23					-
24					-
25					-
Total					-
Payment approved by MD:					
Prepared by:					MDs approval
Name	A.Sravani				
Date	15.01.2021				

APPROVED BY
15 JAN 2021
M. RAM KRASND
PROJECT MANAGER

Certified by:
A. Sravani
Asst. Engineer
MODI REALTY (MALLAPUR) LLP

Anx - C - Material received

Annexure - C - send weekly							
Details of material received							
Name of contractor:		B. Srinivasa Reddy					
Company name:		Sree Srinivasa Constructions					
Project name:		Gulmohar Residency					
Date:		15.01.2021					
Period		From:		07.01.2020		To: 13.01.2021	
Sl. No.	Material type	Received date	Inward no.	Quantity	Units	Rate	Amount
1	Solid bricks 6"x8"x16"	08.01.2021	569	400.00	No's	30.00	12,000.00
2	Solid bricks 6"x8"x16"	12.01.21	570	450.00	No's	30.00	13,500.00
3	Solid bricks 4"x8"x16"	12.01.21	571	700.00	No's	20.00	14,000.00
4	Robo sand fine	08.01.21	60	530	cft	32.00	16,960.00
5	Robo sand coarse	09.01.21	61	530.00	cft	24.00	12,720.00
6	Robo sand fine	11.01.21	62	400	cft	32.00	12,800.00
7							
8							
9							
10							
11							
12							
13							
14							
15							
16							
17							
18							
19							
20							
21							
22							
23							
24							
25							
26							
27							
28							
Total							81,980.00
Payment approved by MD:							
Prepared by:				Approved by:		MDs approval	
Name	A. Sravani						
Date	15.01.2021						

APPROVED BY
15 JAN 2021
M. R. V. PRASAD
PROJECT MANAGER

Certified by:
A. Sravani
Asst. Engineer
MODI REALTY (MALLAPUR) LLP

Annex - D - Milestone report

Annexure - D - send weekly
Mile stone report for CR-

Company name:

Modi Realty Mallapur LLP

Project name:

Gulmohar Residency

Date:

15.01.2021

Note:

Prepare the statement for all the villas in the project.

S No	Flat No	Type (3BHK)	SBUA	Work start date	Completion of plinth	Completion of RCC	Completion of brickwork and plastering	Completion of stage I	Completion of stage II	Completion of stage III	Completion of stage IV	Date of physical possession
1	B-001	3BHK	1660	03.10.19	27.01.20	27.01.2020	19.12.2020					
2	B-002	3BHK	1660	03.10.19	27.01.20	27.01.2020	19.12.2020					
3	B-003	3BHK	1660	08.08.19	21.12.19	21.12.2019	19.12.2020					
4	B-004	3BHK	1660	08.08.19	15.12.19	15.12.2019	20.08.2020					
5	B-005	3BHK	1660	11.08.19	15.12.19	15.12.2019	20.08.2020					
6	B-006	3BHK	1660	08.08.19	21.12.19	21.12.2019	10.10.2020					
7	B-007	3BHK	1660	04.10.19	11.01.20	11.01.2020	19.12.2020					
8	B-008	3BHK	1660	15.10.19	11.01.20	11.01.2020	19.12.2020					
9	B-201	3BHK	1660			19.09.20	29.12.2020					
10	B-202	3BHK	1660			19.09.20						
11	B-203	3BHK	1660			23.06.20						
12	B-204	3BHK	1660			23.06.20						
13	B-205	3BHK	1660			23.06.20						
14	B-206	3BHK	1660			23.06.20	29.12.2020					
15	B-207	3BHK	1660			19.09.20	19.12.2020					
16	B-208	3BHK	1660			19.09.20	19.12.2020					
17	B-301	3BHK	1660			23.10.20						
18	B-302	3BHK	1660			23.10.20						
19	B-303	3BHK	1660			23.10.20						
20	B-304	3BHK	1660			23.10.20						
21	B-305	3BHK	1660			23.10.20						
22	B-306	3BHK	1660			23.10.20						
23	B-307	3BHK	1660			23.10.20						
24	B-308	3BHK	1660			23.10.20						
25												
26												
27												
28												
29												
30												
31												

APPROVED BY

15 JAN 2021

M. R. PRASAD
PROJECT MANAGER

Certified by:

[Signature]
A. Sravani

Asst. Engineer
MODI REALTY (MALLAPUR) LLP

Modi Realty Mallapur LLP (20-21)
MG Road, RAnigunj
Secunderabad
State Name : Telangana, Code : 36

Payment Voucher

No. : **PAY/11667** 11659

Dated : 16-Jan-2021

Through : BANK-Kotak Mahindra Bank Rera A/c

Particulars	Amount
Account :	
CONT-Sree Srinivasa Constrctions	5,03,000.00
TDS-1.50% Contract	(-)7,545.00
On Account of :	
Being amount transfered towards advance payment for Anx-A & C for B block for G block	
Amount (in words) :	
Indian Rupees Four Lakh Ninety Five Thousand Four Hundred Fifty Five Only	
	₹ 4,95,455.00

Prepared by: rajyalakshmi

Approved by

Receiver's Signature

Anx - A - Attendance details

Annexure - A - Send Weekly					
Details of labour charges					
Name of contractor:		B.Srinivasa Reddy			
Company name:		Sree Srinivasa Constructions (G-Block)			
Project name:		Gulmohar Residency			
Date:		15.01.2021			
Period		From:	07.01.2021	To:	13.01.21
Sl. No.	Work Type	Worker Type	Quantity	Rate	Amount
1	Civil work	Mason	-	575.00	-
2	Civil work	Male helper	-	400.00	-
3	Civil work	Female helper	-	350.00	-
4	RCC work	Mason	70	550.00	38,500
5	RCC work	Male helper	65	400.00	26,000
6	RCC work	Female helper	-	-	-
7	Earth work	Mason	-	-	-
8	Earth work	Male helper	7	450.00	3,150
9	Earth work	Female helper	-	400.00	-
10	Electrician	Mason	-	550.00	-
11	Electrician	Male helper	-	400.00	-
12					-
13					-
14					-
15					-
16					-
17					-
18					-
19					-
20					-
Total					67,650
Payment approved by MD:					
Prepared by:					MDs approval
Name		A.Sravani			
Date		06.02.2020			

APPROVED BY
15 JAN 2021.
M. KAM PRASAD
PROJECT MANAGER

Certified by:
[Signature]
S. Srinivasa Reddy
MANAGING DIRECTOR

Anx - B - Hire charges

Send Weekly					
are charges					
contractor:		B.Srinivasa Reddy			
any name:		Sree Srinivasa Constructions (G-Block)			
ject name:		Gulmohar Residency			
Date:		15.01.2021			
Period		From:	07.01.2021	To:	13.01.21
Sl. No.	Equipment Type	Quantity	Rate	Units	Amount
1	JCB	-	-	nos	-
2	Tractor with Tipper	-	-	nos	-
3					-
4					-
5					-
6					-
7					-
8					-
9					-
10					-
11					-
12					-
13					-
14					-
15					-
16					-
17					-
18					-
19					-
20					-
21					-
22					-
23					-
24					-
25					-
Total					-
Payment approved by MD:					
Prepared by:					MDs approval
Name	A.Sravani				
Date	15.01.2021				

APPROVED BY
15 JAN 2021
M. RAM PRASAD
PROJECT MANAGER

Certified by:
A. Sravani
Asst. Engineer
MODI REALTY (MALLAPUR) LLP

Annex - C - Material received

Annexure - C - send weekly							
Details of material received							
Name of contractor:		B. Srinivasa Reddy					
Company name:		Sree Srinivasa Constructions (G-Block)					
Project name:		Gulmohar Residency					
Date:		15.01.2021					
Period		From:	07.01.2021	To:	13.01.21		
Sl. No.	Material type	Received date	Inward no.	Quantity	Units	Rate	Amount
1	Steel 8mm 10,16mm	09.01.21	27.00	7080.00	kgs	60.38	427,490.40
2	ms wire	11.01.21	28.00	100.00	kgs	85.00	8,500.00
3							-
4							-
5							-
6							-
7							-
8							-
9							-
10							-
11							-
12							-
13							-
14							-
15							-
16							-
17							-
18							-
19							-
20							-
21							-
22							-
23							-
24							-
25							-
26							-
27							-
28							-
Total							435,990.40
Payment approved by MD:							
Prepared by:		Approved by:					
Name	A. Sravani						
Date	15.01.2021						
							MDs approval

APPROVED BY
15 JAN 2021
M. S. Srinivasa Reddy
PROJECT MANAGER

Certified by:
A. Sravani
Asst. Engineer
MODI REALTY (MALLAPUR) LLP

Modi Realty Mallapur LLP (20-21)
MG Road, RAnigunj
Secunderabad
State Name : Telangana, Code : 36

Payment Voucher

No. : **PAY/11668-1166D**

Dated : 16-Jan-2021

Through : BANK-Kotak Mahindra Bank Rera A/c

Particulars	Amount
Account :	
CONT-Surasani Constructions	3,93,000.00
TDS-1.50% Contract	(-)5,895.00
On Account of :	
Being amount transfered towards advance payment against Anx-B for A-block	
Amount (in words) :	
Indian Rupees Three Lakh Eighty Seven Thousand One Hundred Five Only	
	₹ 3,87,105.00

Prepared by: rajyalakshmi

Approved by

Receiver's Signature

Anx - A - Attendance details

Annexure - A - Send Weekly Details of labour charges					
Name of contractor:		S Karunakar Reddy			
Company name:		Surasani Constructions			
Project name:		Gulmohar Residency			
Date:		15.01.2021			
Period:		From:	07.01.21	To:	13.01.2021
Sl. No.	Work Type	Worker Type	Quantity	Rate	Amount
1	Civil work	Mason	65	575.00	37,375
2	Civil work	Male helper	60	400.00	24,000
3	Civil work	Female helper	30	350.00	10,500
4	RCC work	Mason	45	550.00	24,750
5	RCC work	Male helper	40	400.00	16,000
6	RCC work	Female helper	-	-	-
7	Earth work	Mason	-	-	-
8	Earth work	Male helper	-	450.00	-
9	Earth work	Female helper	-	400.00	-
10	Electrician	Mason	-	550.00	-
11	Electrician	Male helper	-	400.00	-
12					-
13					-
14					-
15					-
16					-
17					-
18					-
19					-
20					-
Total					112,625
Payment approved by MD:					
Prepared by:		MDs approval			
Name	A Sravani				
Date	15.01.2021				


1136
APPROVED BY
16 JAN 2021
SOHAM MOULI
MANAGING DIRECTOR


APPROVED BY
15 JAN 2021
PROJECT MANAGER

Certified by:
A Sravani
Asst. Engineer
MODI REALTY (MALLAPUR) LLP

Anx - B - Hire charges

Annexure - B - Send Weekly					
Details of hire charges					
Name of contractor:		S. Karunakar Reddy			
Company name:		Surasani Constructions			
Project name:		Gulmohar Residency			
Date:	15.01.2021				
Period	From:	07.01.21	To:	13.01.2021	
Sl. No.	Equipment Type	Quantity	Rate	Units	Amount
1	JCB	-	800.00	nos	-
2	Tractor with Tipper	-	1,800.00	nos	-
3					-
4					-
5					-
6					-
7					-
8					-
9					-
10					-
11					-
12					-
13					-
14					-
15					-
16					-
17					-
18					-
19					-
20					-
21					-
22					-
23					-
24					-
25					-
Total					-
Payment approved by MD:					
Prepared by:					MDs approval
Name	A. Sravani				
Date	15.01.2021				

APPROVED BY

 15 JAN 2021
 M. RAM PRASAD
 PROJECT MANAGER

Certified by:

 A. Sravani
 Asst. Engineer
 MODI REALTY (MALLAPUR) LLP

Anx - C - Material received

Annexure - C - send weekly							
Details of material received							
Name of contractor:		S.Karunakar Reddy					
Company name:		Surasani Constructions					
Project name:		Gulmohar Residency					
Date:		15.01.2021					
Period		From:		07.01.21		To: 13.01.2021	
Sl. No.	Material type	Received date	Inward no.	Quantity	Units	Rate	Amount
1	Soild bricks 4"x8"x16"	08.01.21	1552	600.00	No's	20.00	12,000.00
2	Solid bricks 6"x8"x16"	11.01.21	1553	400.00	No's	30.00	12,000.00
3	Cement	13.01.21	1554	500.00	bags	320.00	160,000.00
4	Soild bricks 4"x8"x16"	13.01.21	1555	600	no's	20.00	12,000.00
5	Robo sand fine	07.01.21	73	480.00	cft	32.00	15,360.00
6	Robo sand fine	09.01.21	74	480.00	cft	32.00	15,360.00
7	Robo sand coarse	10.01.21	75	530.00	cft	24.00	12,720.00
8	20mm metal	11.01.21	76	530.00		19.00	10,070.00
9	robo sand fine	11.01.21	77	500.00	cft	32.00	16,000.00
10	robo sand coarse	13.01.21	78	600.00	cft	24.00	14,400.00
11							-
12							-
13							-
14							-
15							-
16							
17							
18							
19							
20							
21							
22							
23							
24							-
Total							279,910.00
Payment approved by MD:							
Prepared by:				Approved by:		MDs approval	
Name	A.Sravani						
Date	15.01.2021						

APPROVED BY
15 JAN 2021
M. Ravi Prasad
PROJECT MANAGER

Certified by:
A. Sravani
Asst. Engineer
MODI REALTY (MALLAPUR) LLP

Anx - D - Milestone report

Annexure - D - send weekly

Mile stone report for CR-

Company name:

Modi Realty Mallapur LLP

Project name:


Gulmohar Residency


Date:

15.01.2021

Note: Prepare the statement for all the villas in the project.

S No	Flat No	Type (3BHK)	SBUA	Work start date	Completion of plinth	Completion of RCC	Completion of brickwork and plastering	Completion of stage I	Completion of stage II	Completion of stage III	Completion of stage IV	Date of physical possession
1	A-001	3BHK	1360	28.08.19	27.12.19	03.06.20	23.09.20					
2	A-002	3BHK	1360	22.10.19	27.12.19	03.06.20	22.12.20					
3	A-003	3BHK	1360	08.08.19	27.12.19	11.07.20	22.12.20					
4	A-004	3BHK	1360	08.08.19	27.12.19	11.07.20	22.12.20					
5	A-005	3BHK	1360	17-09-19	18.12.19	11.07.20	22.12.20					
6	A-006	3BHK	1360	08.08.19	27.12.19	11.07.20	22.12.20					
7	A-007	3BHK	1360	08.08.19	08.01.20	11.07.20	22.12.20					
8	A-008	3BHK	1360	16.10.19	08.01.20	03.06.20	22.12.20					
9	A-009	3BHK	1360	28.08.19	27.12.19	03.06.20	23.09.20					
10												
11												
12												
13												
14												
15												
16												
17												
18												
19												
20												
21												
22												
23												
24												
25												
26												
27												
28												
29												
30												

APPROVED BY

 15 JAN 2021
 M. RAM PRASAD
 PROJECT MANAGER

Certified by:

 A. Sravani
 Asst. Engineer
 MODI REALTY (MALLAPUR) LLP
